


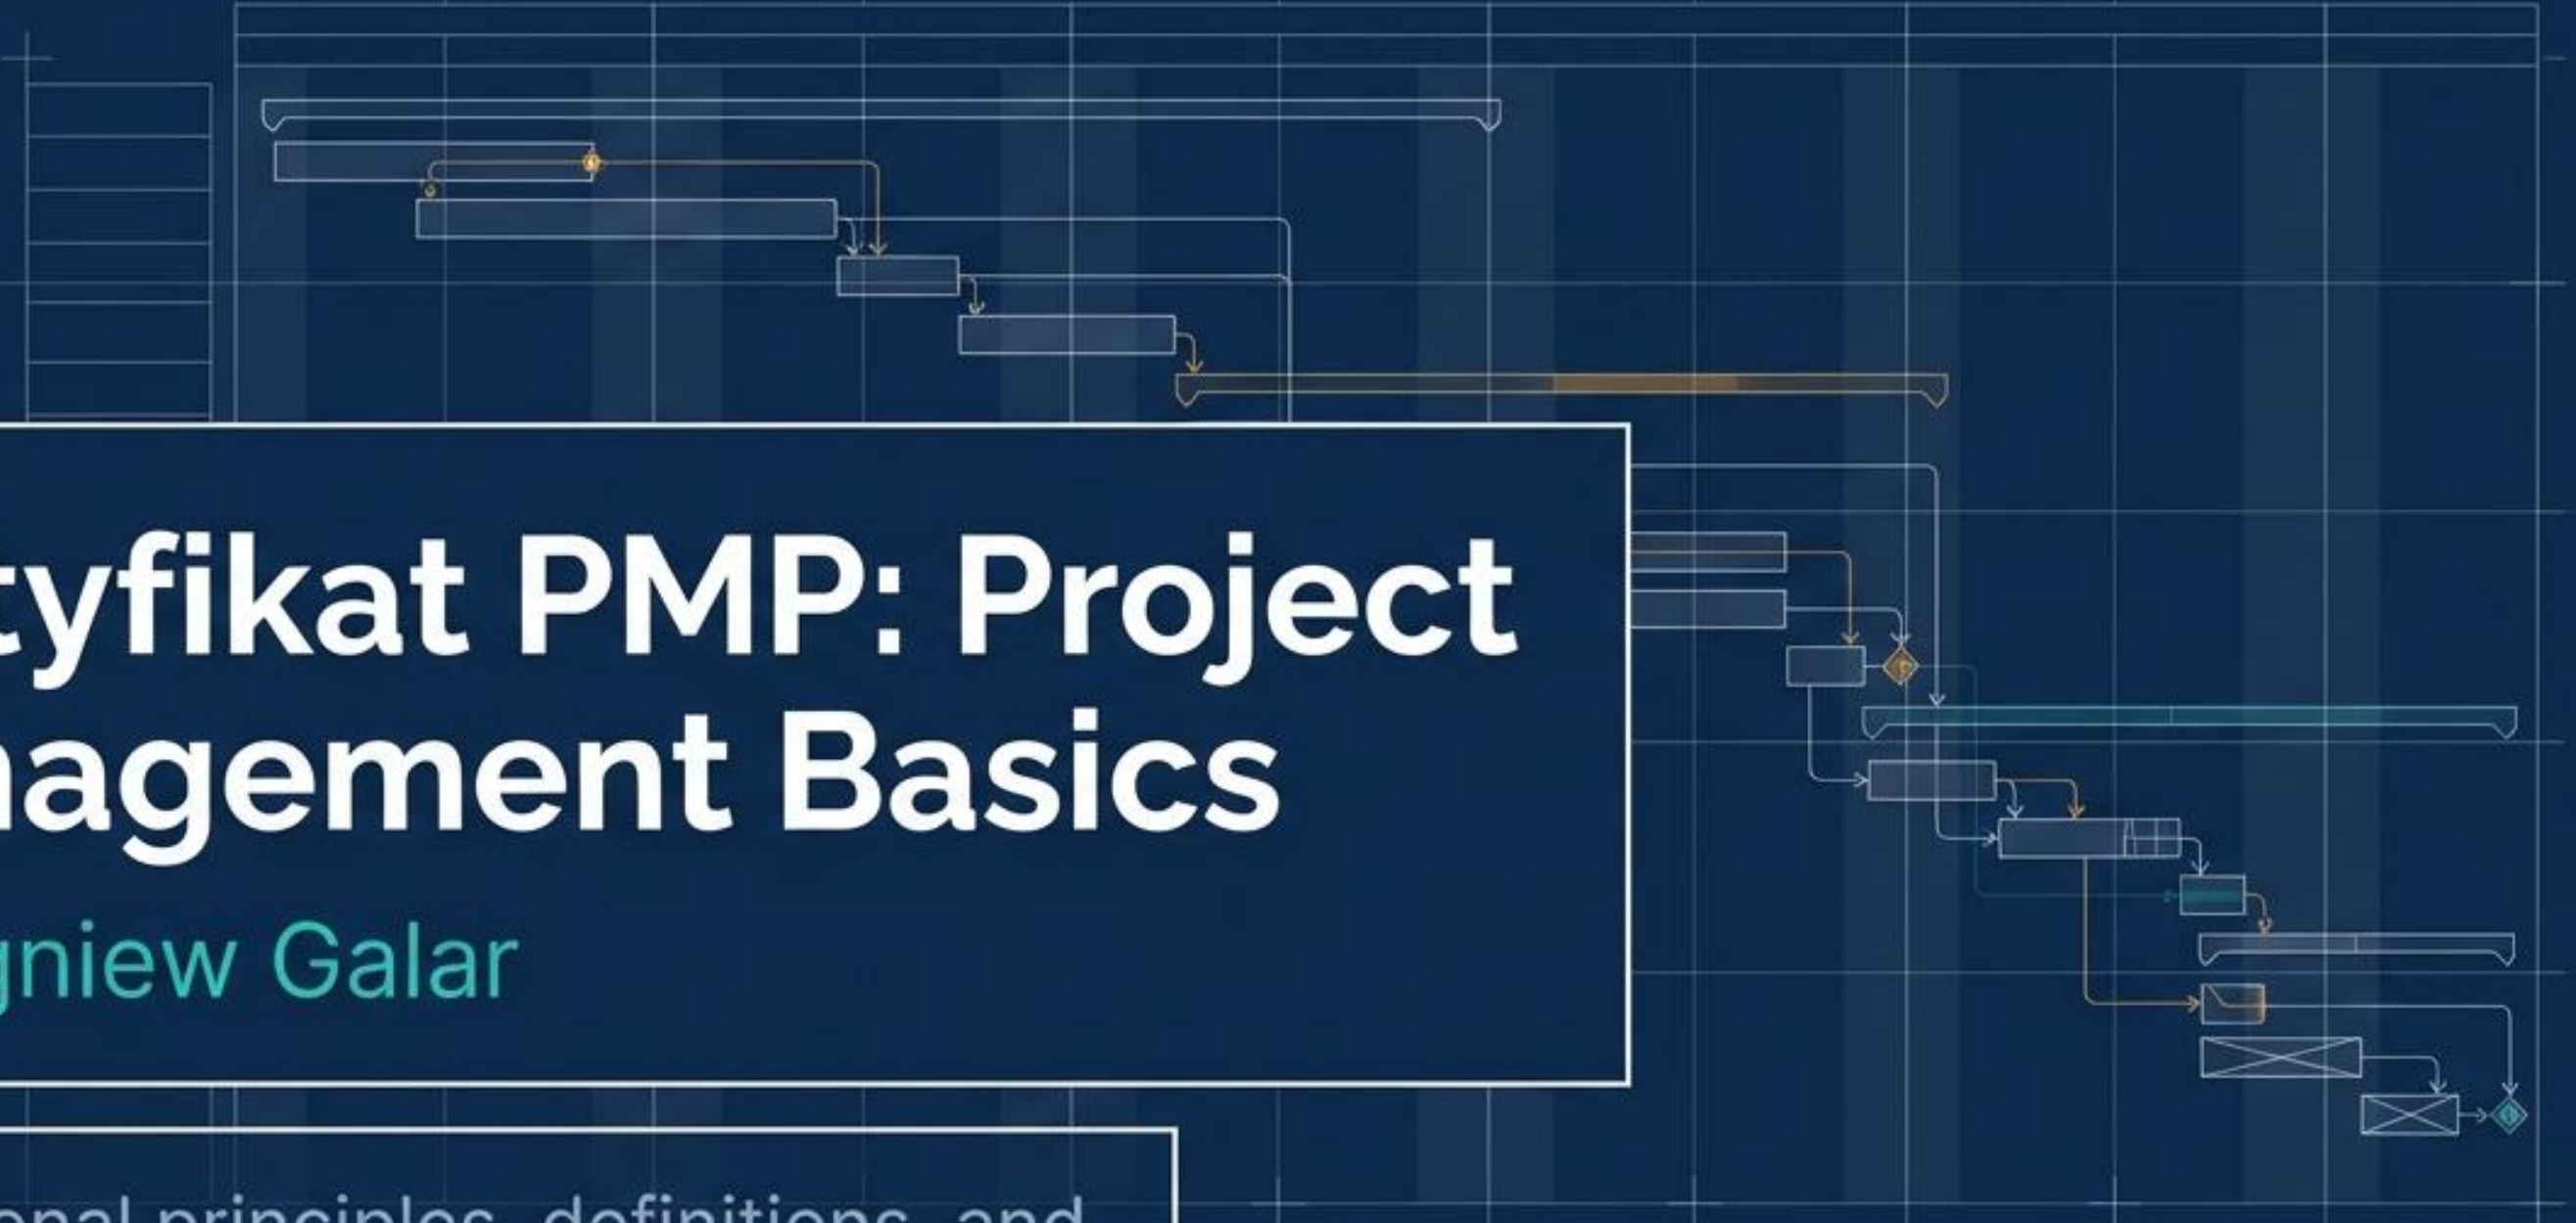

Certyfikat PMP: Project Management Basics

dr Zbigniew Galar


Foundational principles, definitions, and environmental structures aligned with PMI® and PMBOK® Guide standards.

A Universal Language for Execution

Core Concept

The PMBOK® Guide provides standardized terminology developed by global volunteers.

Translation Diagram

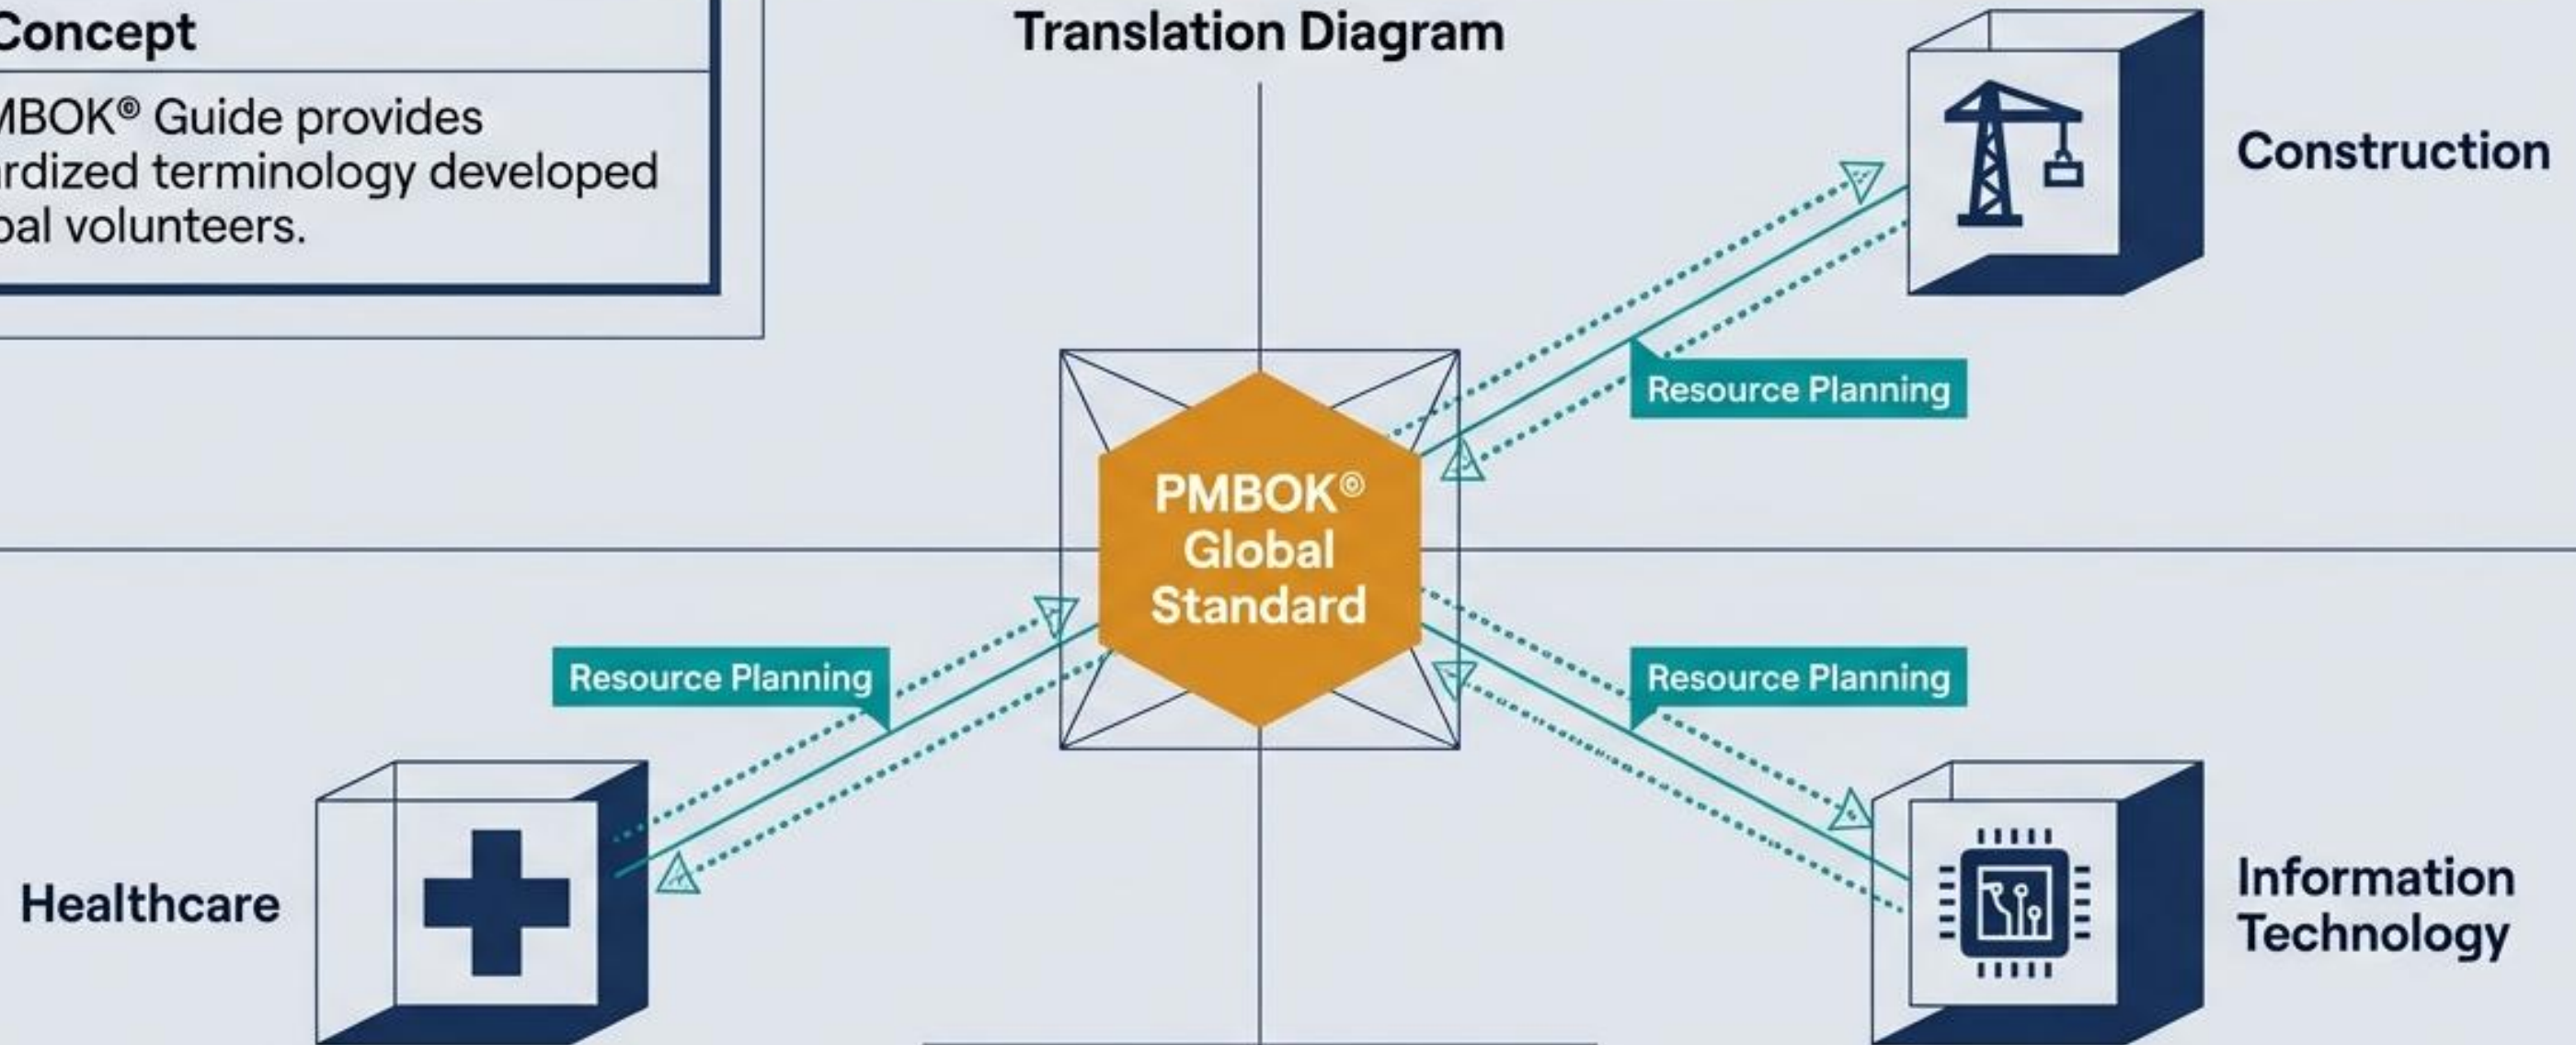

Key Takeaway

The underlying principles and processes of project management are interchangeable across industries, allowing professionals to manage work regardless of the specific technical domain.

Diagnostic: Is It a Project?

Diagnostic Checklist



Real World Scenario

The Wireless Kiosk Initiative

Concept: Install 12 mini-office kiosks in grocery stores by year-end.


Verdict: YES, IT IS A PROJECT.

It is unique (new delivery method), temporary (ends this year), and has clear completion criteria (12 operating kiosks).

The Mechanics of Progressive Elaboration

Definition Panel

Project characteristics are determined incrementally and continually refined in detail as the project progresses.

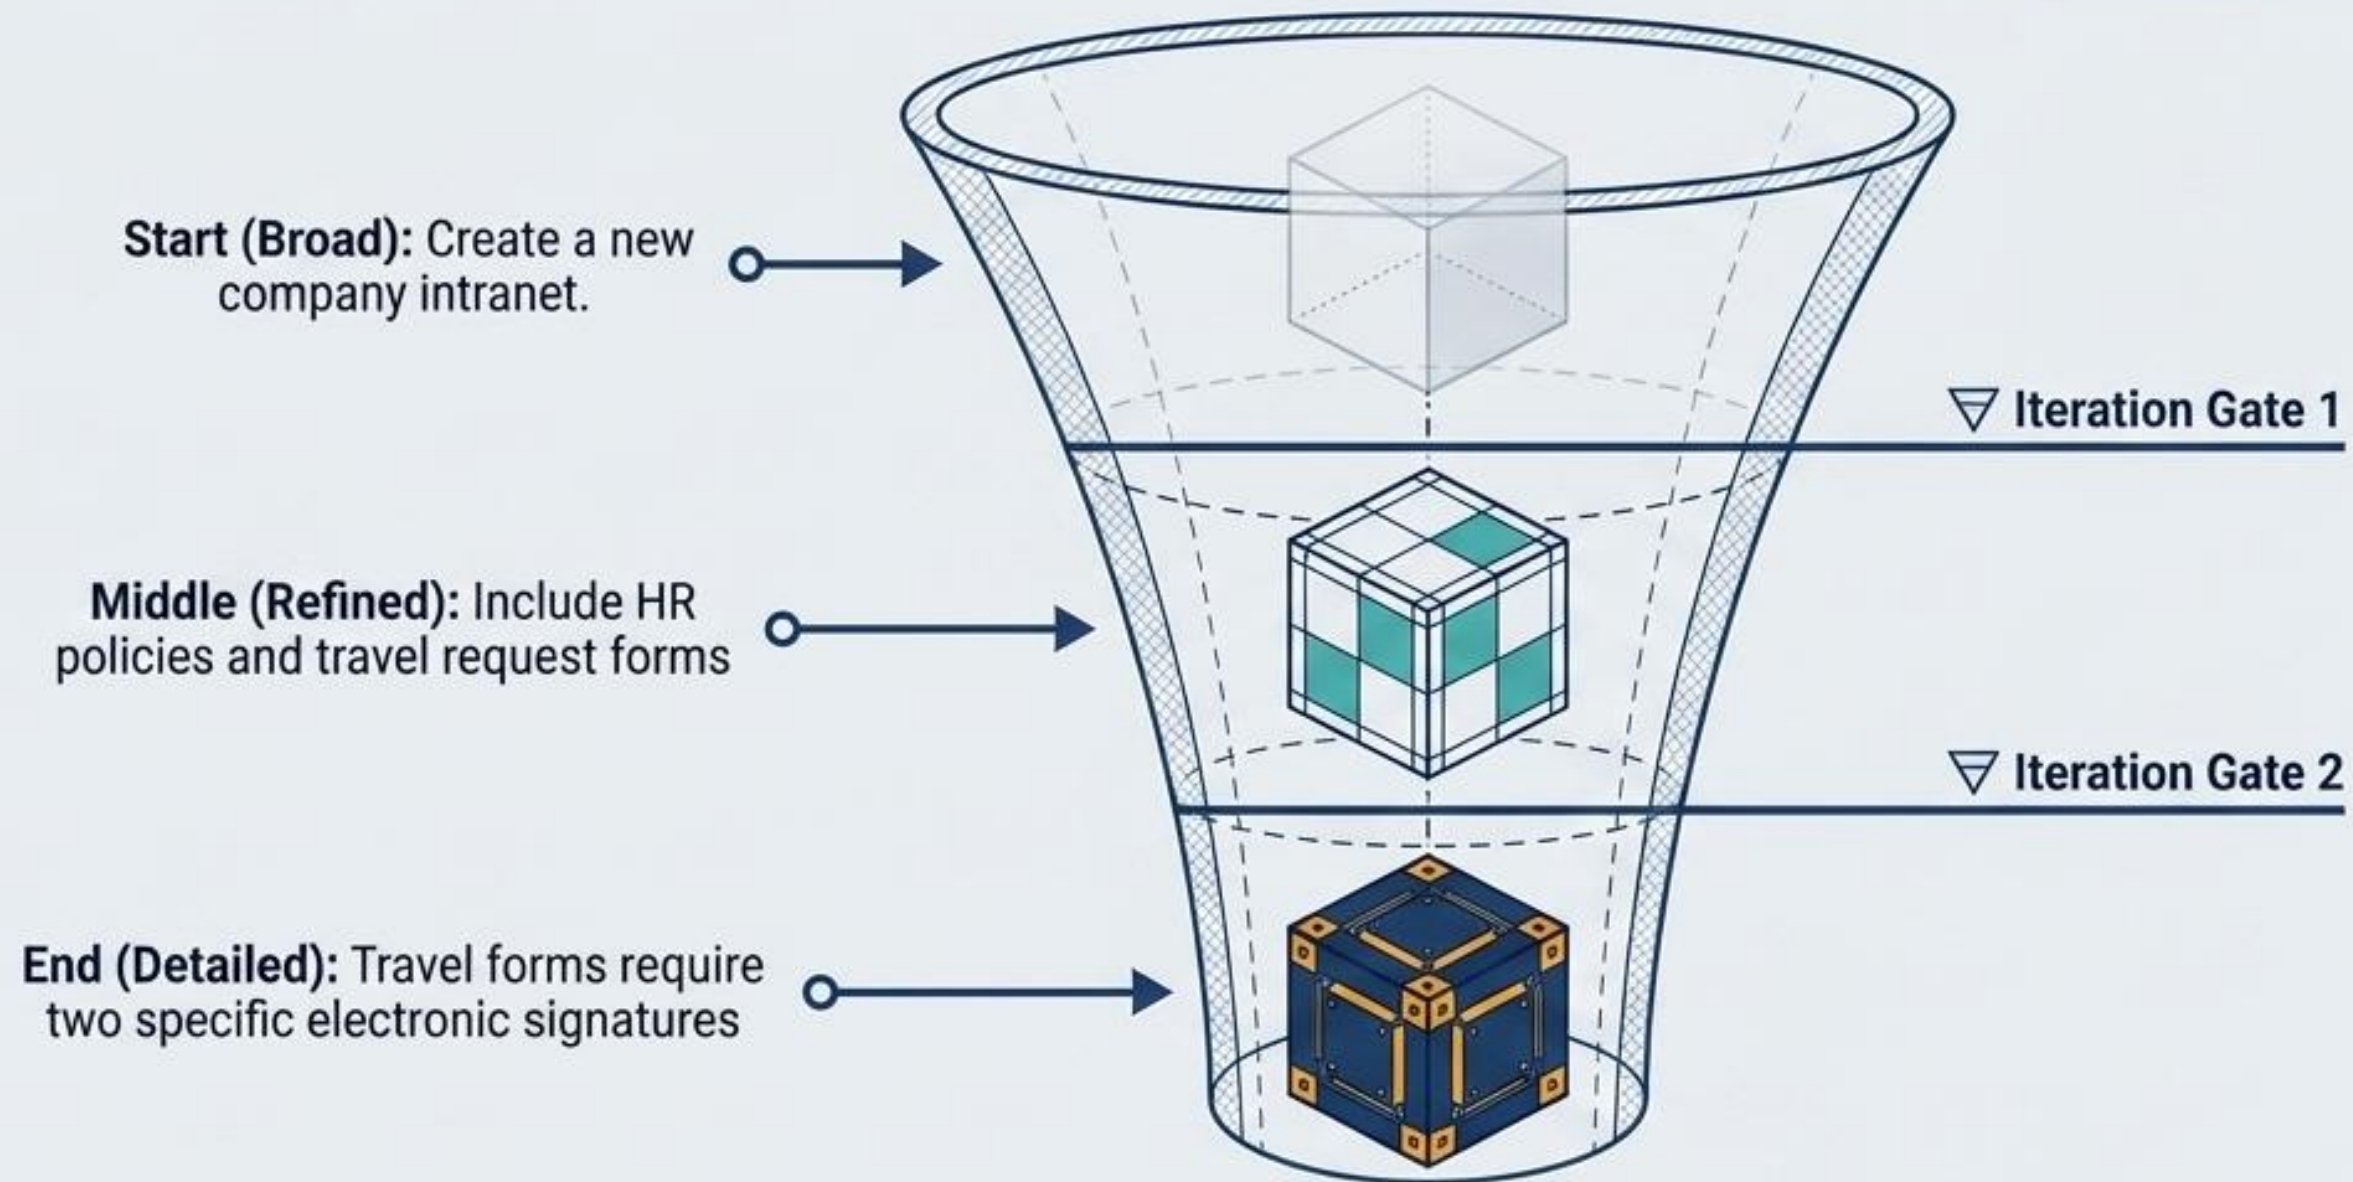

Note: Allows teams to manage greater levels of detail and adapt to inevitable changes throughout the life cycle.

The Delineation: Projects vs. Operations


	Projects	Operations
Nature of Work	Temporary & Unique.	Ongoing & Repetitive.
Primary Purpose	To meet specific goals and then conclude.	To keep the organization functioning and sustain the business.
Example (Automotive)	Designing a new SUV model.	Assembly line manufacturing of the SUV.
Required Skillsets	General management, interpersonal, and planning skills.	Business operations, manufacturing line, and retail management.

Projects often extend into operations (e.g., at phase ends, for process improvement, or during formal handoffs for ongoing maintenance).

Mapping the Stakeholder Ecosystem

Stakeholders are individuals or organizations with a vested interest who have something to gain or lose as a result of the project.


The Stakeholder Orbit

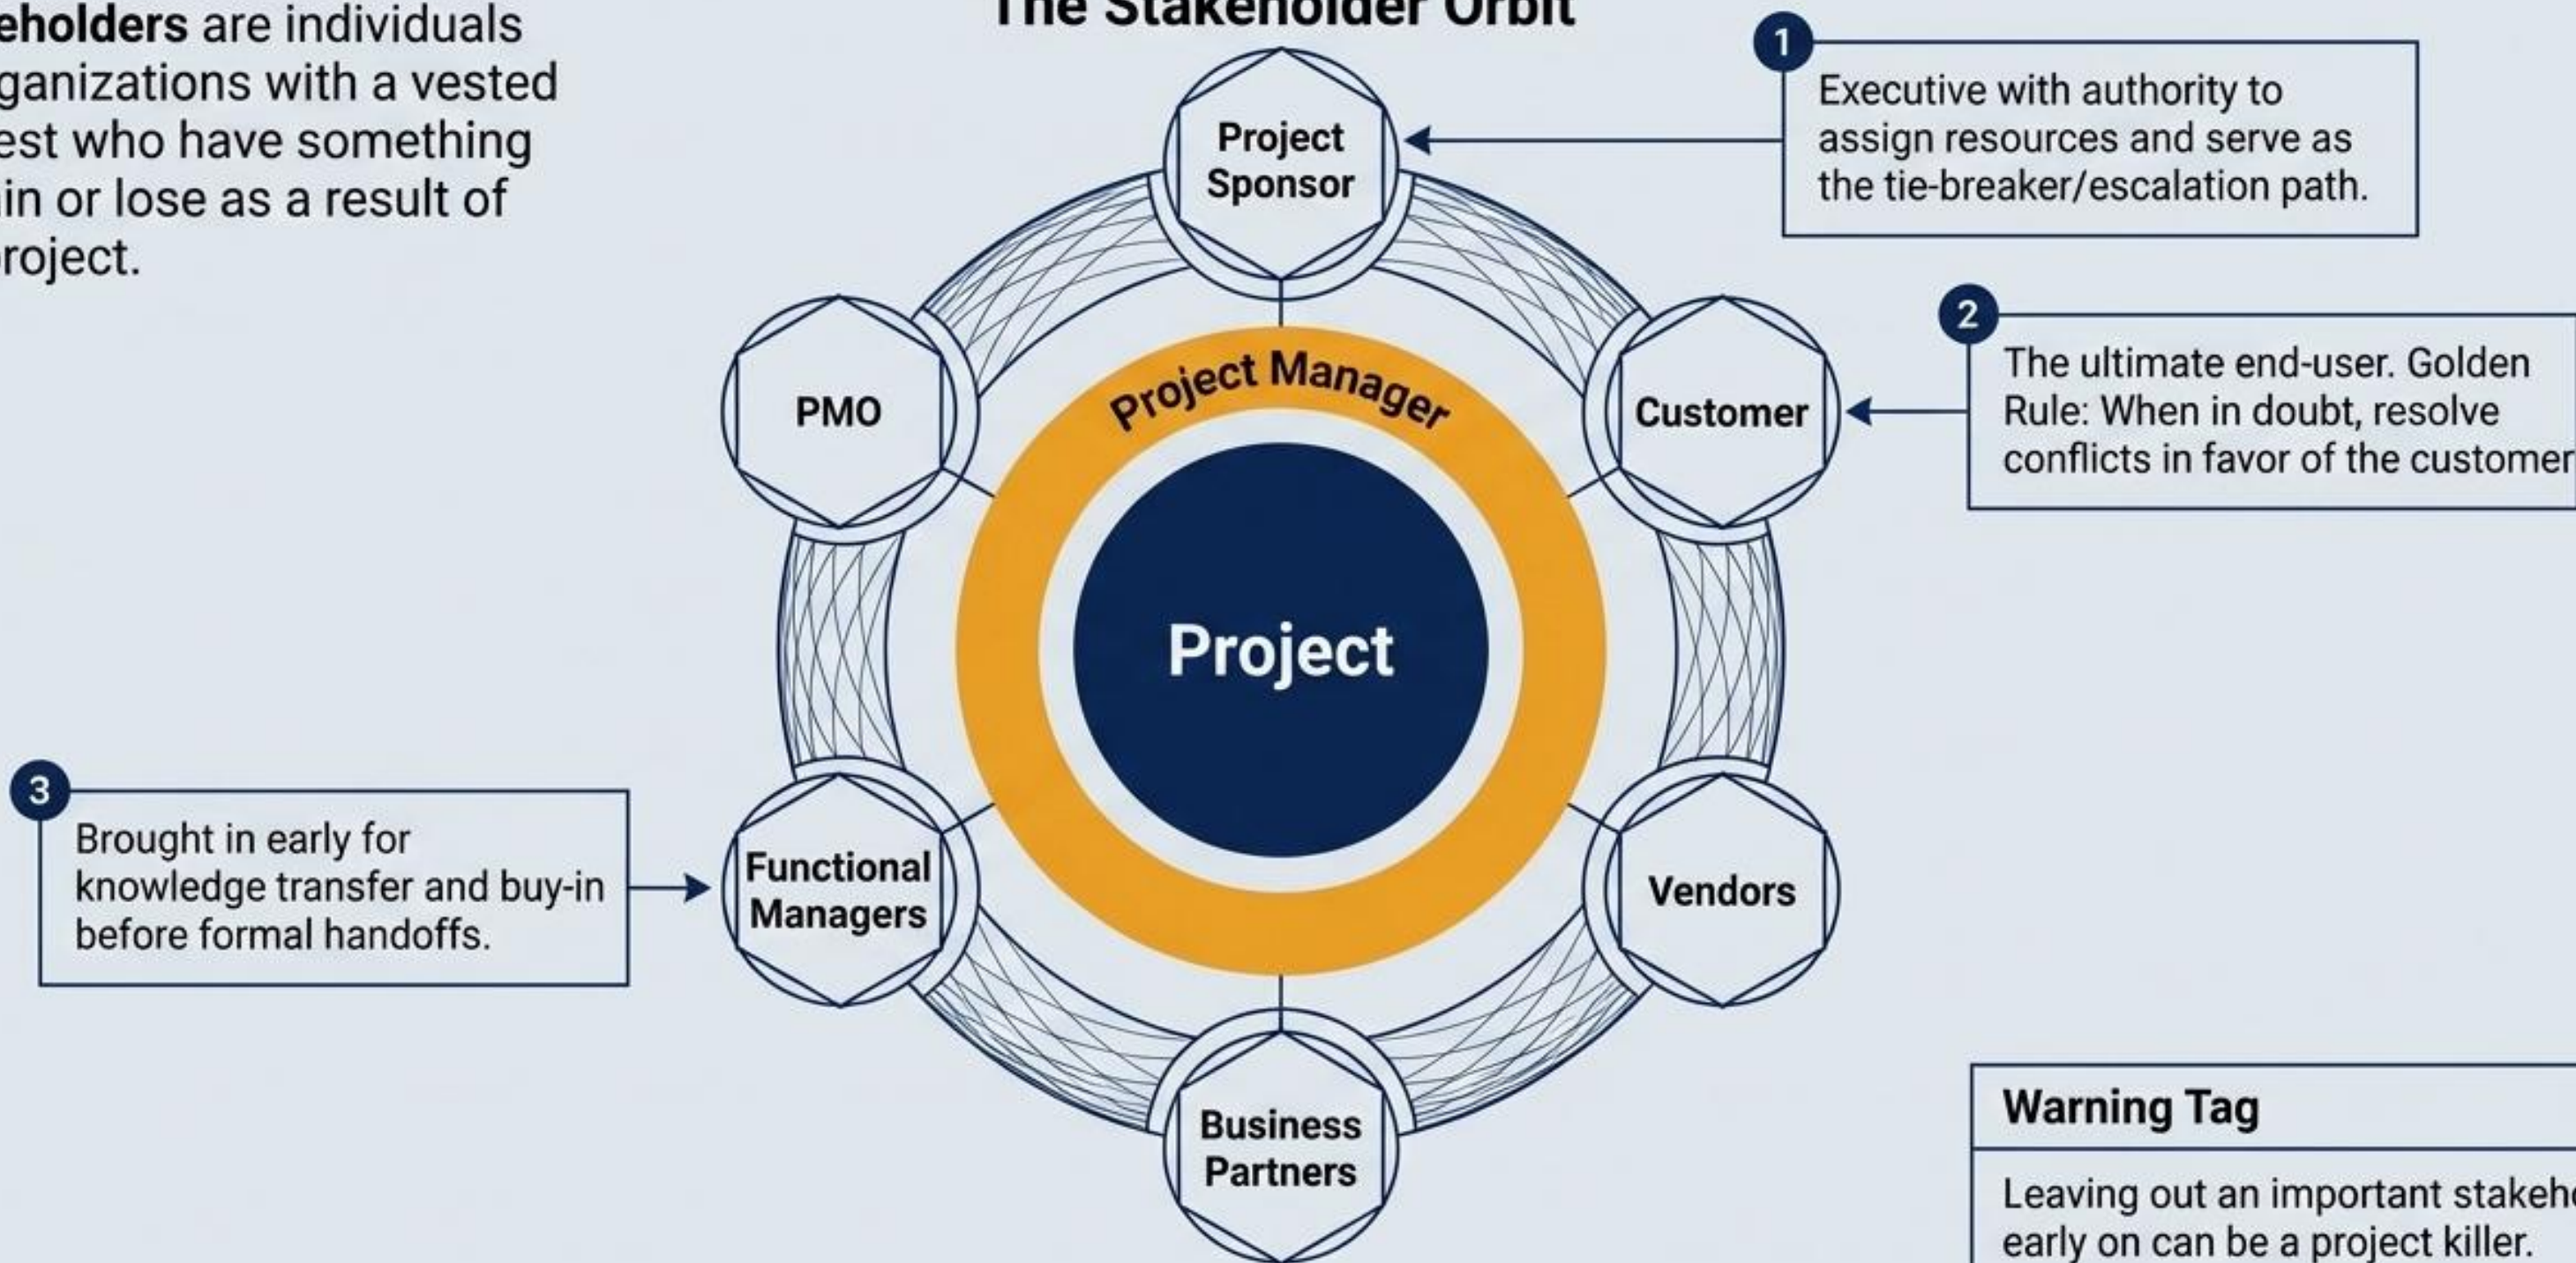

Defining Project Management

Project management replaces the haphazard “just start building” approach with careful planning, organizing, and monitoring.

Architectural Equation

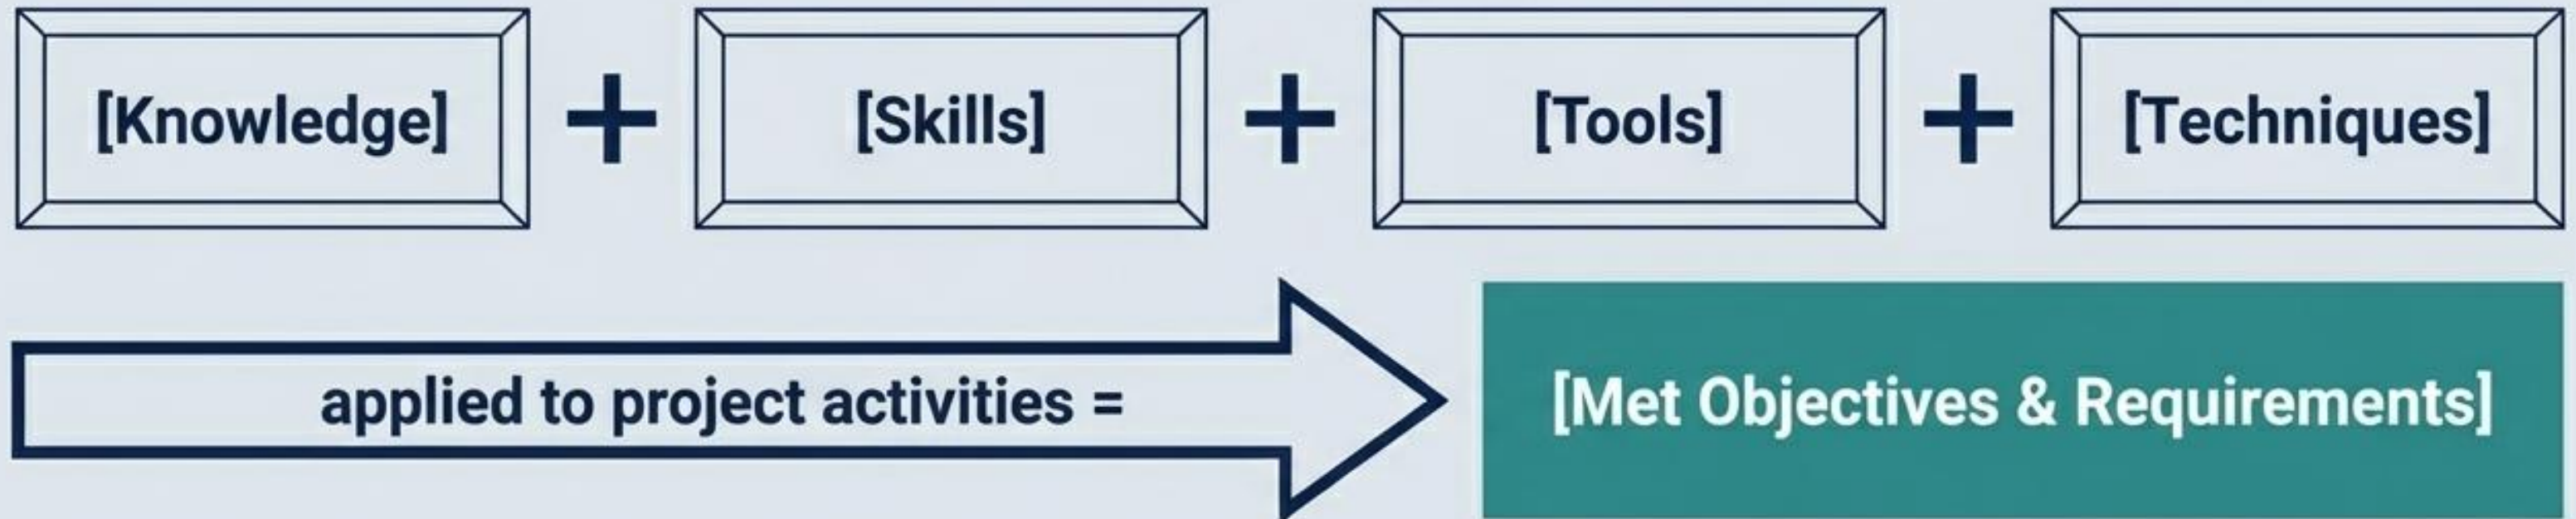

Warning Panel

The Colorado Law Case Study

The state of Colorado passed legislation requiring PMs on large state projects to be certified in best practices.

✓ **Result:** Increased probability of success, reduced negative risk, and more projects delivered on time/budget/scope.

The Alignment Hierarchy

Translating Strategic Goals into Execution



	Purpose	Focus
Portfolio	Aligns work to organizational strategic business objectives.	Optimizing efficiencies, costs, resources, and risks across all work. (Note: Projects within a portfolio are not necessarily related).
Program	Collects related projects managed in a coordinated fashion.	Managing project interdependencies to achieve collective benefits (e.g., an urban development program containing separate construction and marketing projects).
Project	Applies PM processes to create specific outputs.	Delivery of products, services, or results.

The Project Management Office (PMO)

A centralized organizational unit that oversees project and program management throughout the enterprise.



Control Center dashboard

1. Standardization

Establishing methodologies, templates, and the Organizational Project Management (OPM) framework to maintain a competitive edge.



2. Resource & Support

Managing resources, mentoring, coaching, and training project managers.




3. Auditing & Alignment

Archiving documentation, measuring performance against strategic objectives, and asking: 'Did it stay within budget/time/quality?'




The PMO Control Spectrum

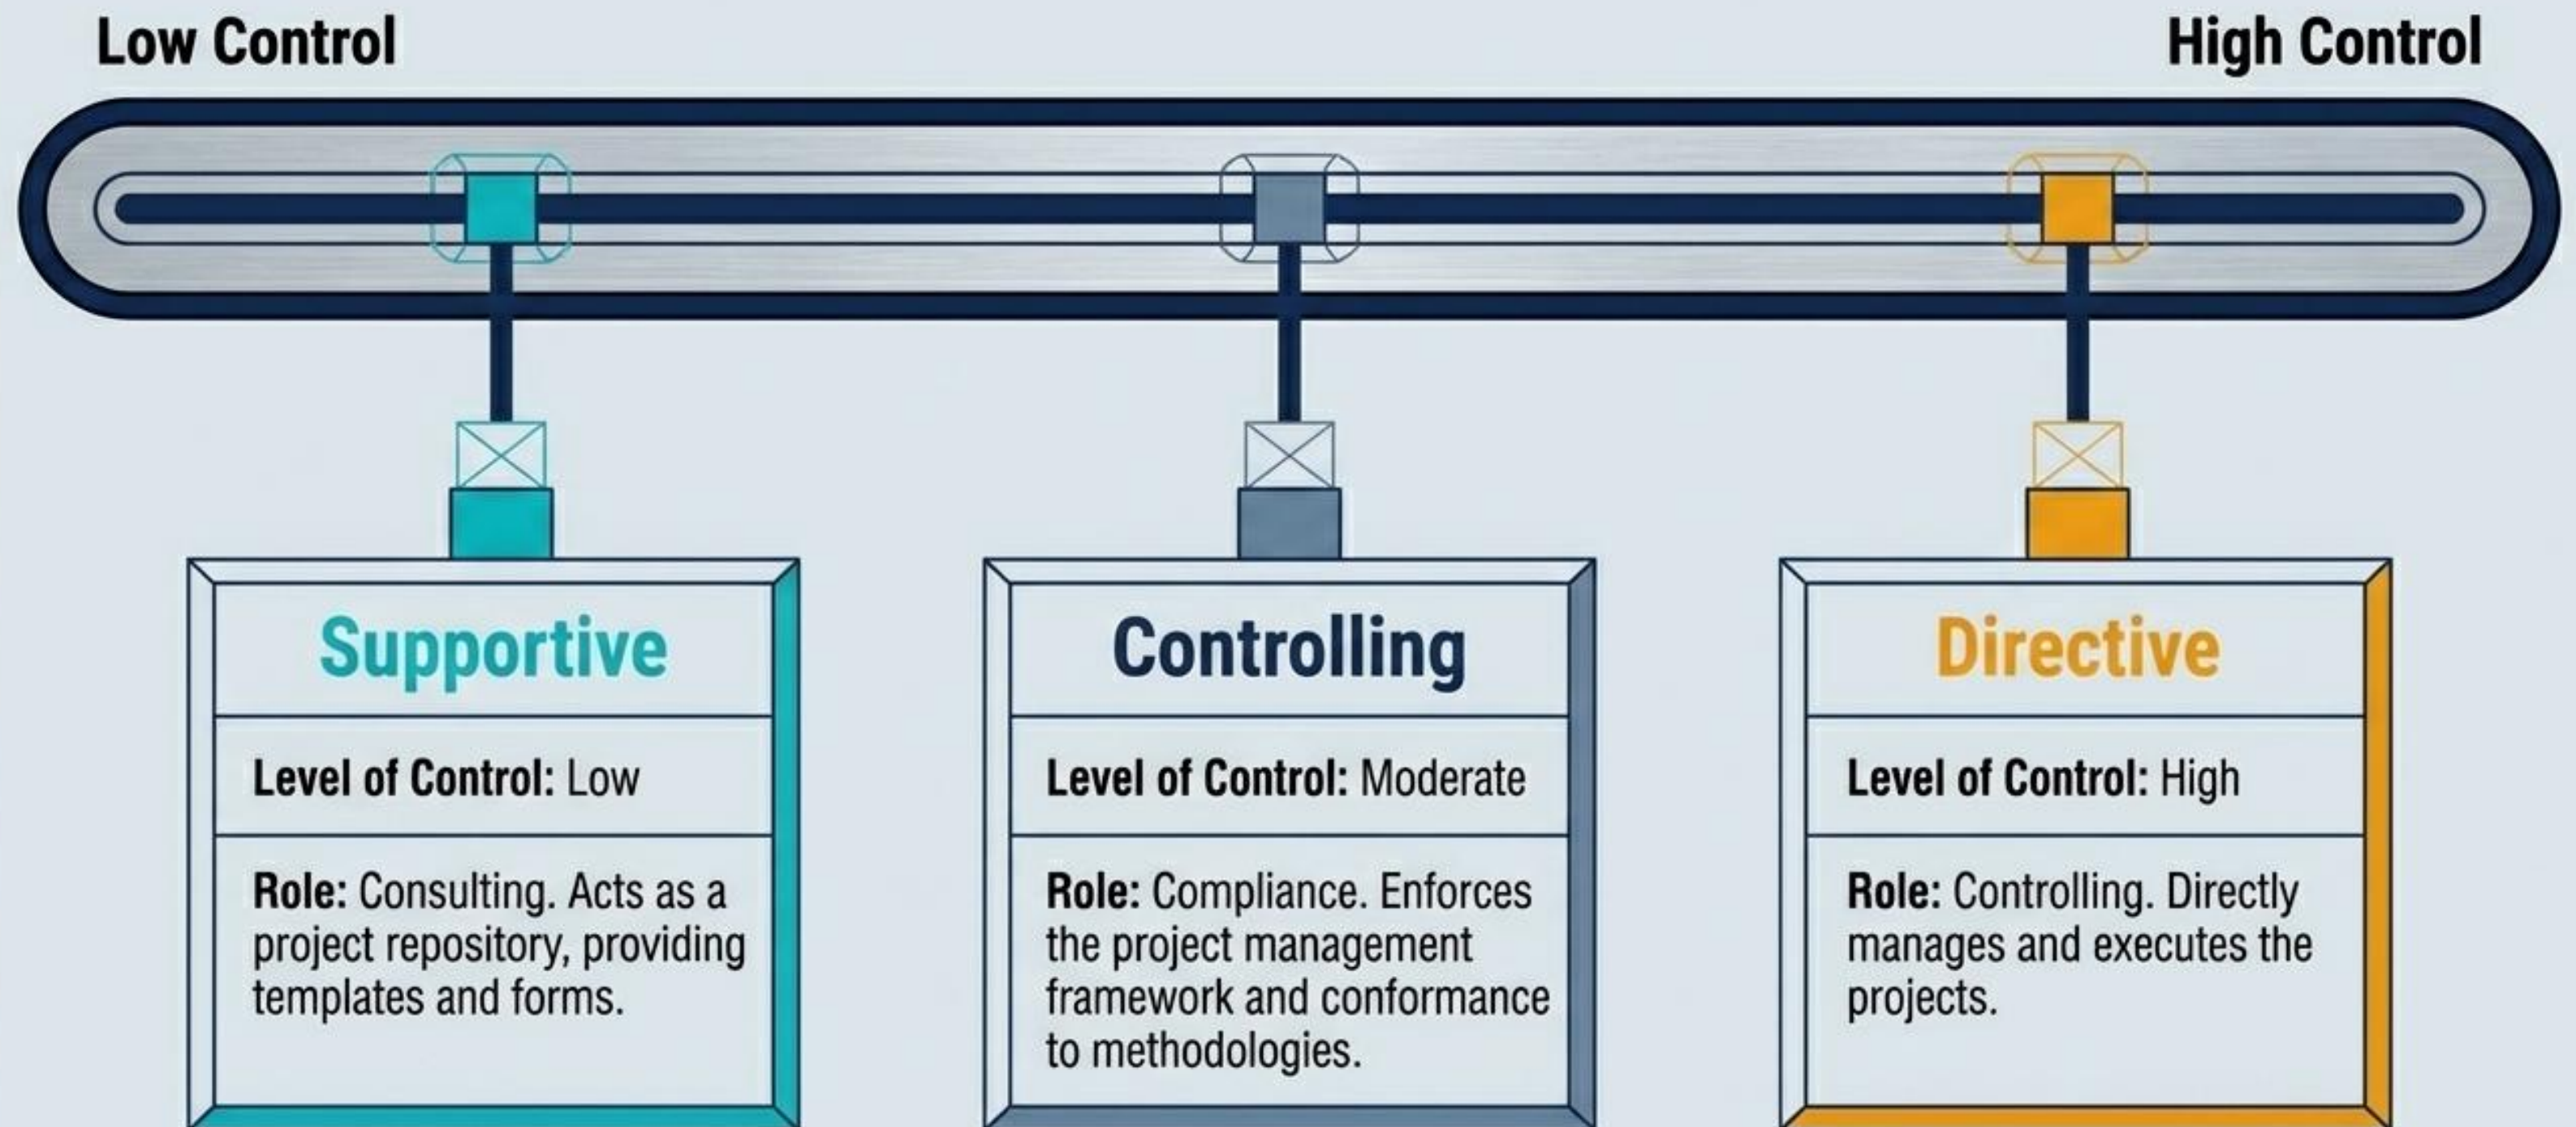

The Project Manager's Baseline

Technical expertise does not automatically translate to project management skill. PMs are generalists and problem-solvers requiring three core capabilities:

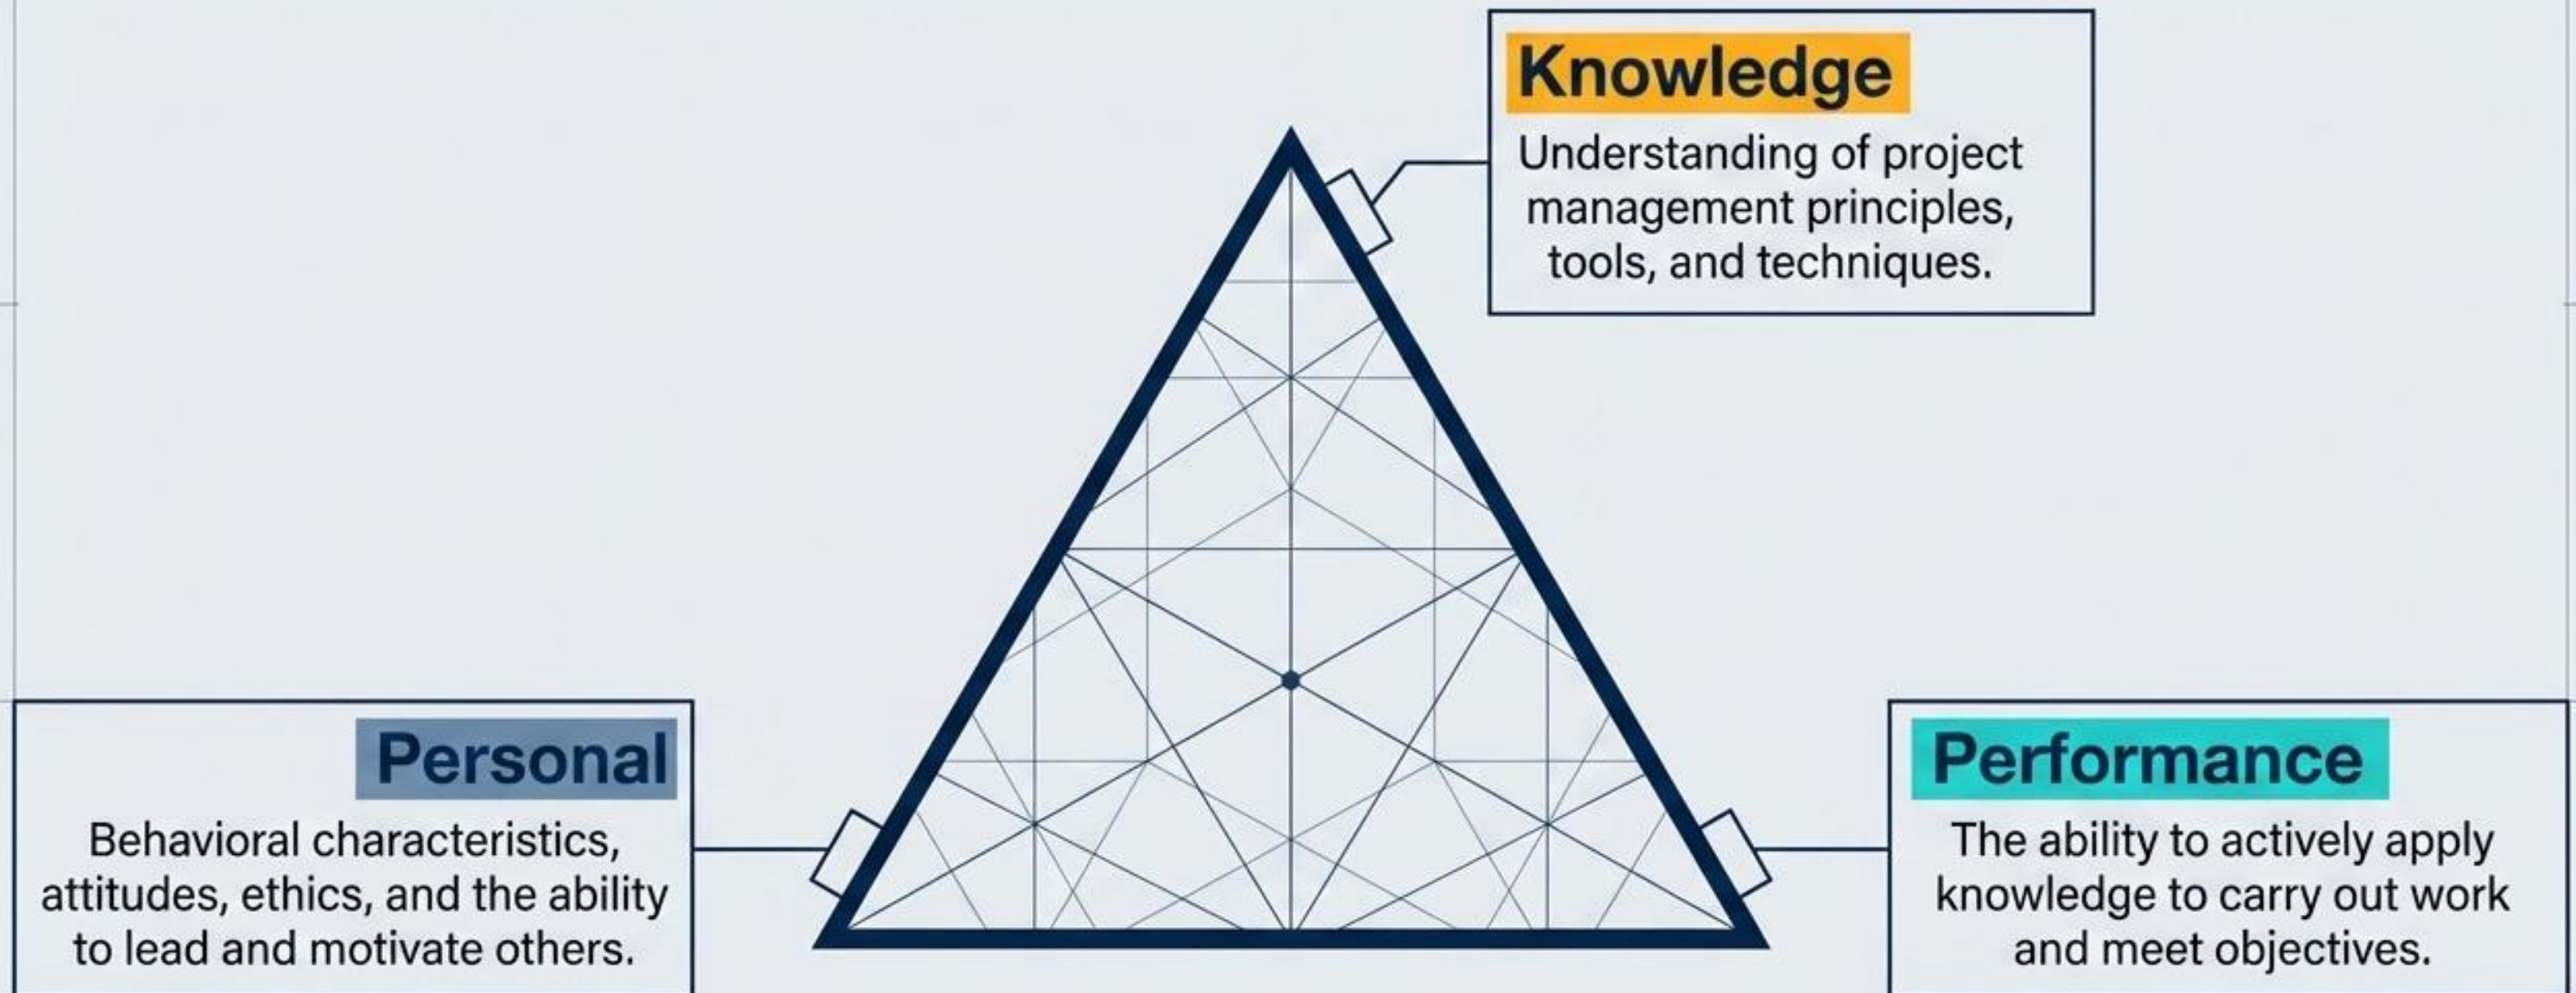


Interpersonal & General Management Skillsets

Communication:

The single most important characteristic.
Clear, explicit, complete.

Team Building:

Guiding diverse groups through development stages.

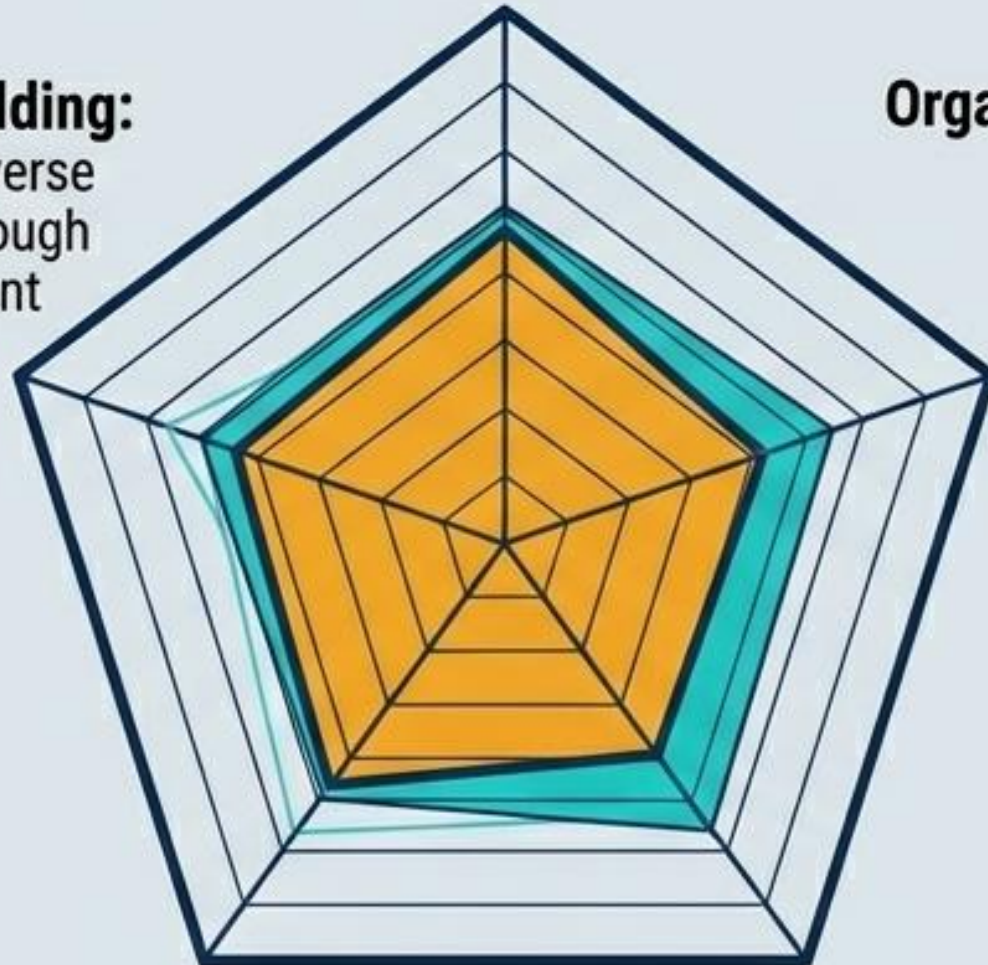

Organization & Planning:

Tracking documents, prioritizing tasks, managing time.

Negotiation & Influencing:

Gaining agreement and getting things done through structures.

Conflict Management:

Separating root causes from superficial symptoms.


The Duality of Command

Leadership:

Imparting vision, inspiring, and motivating.


Management

Focusing on results, requirements, and getting the job done.

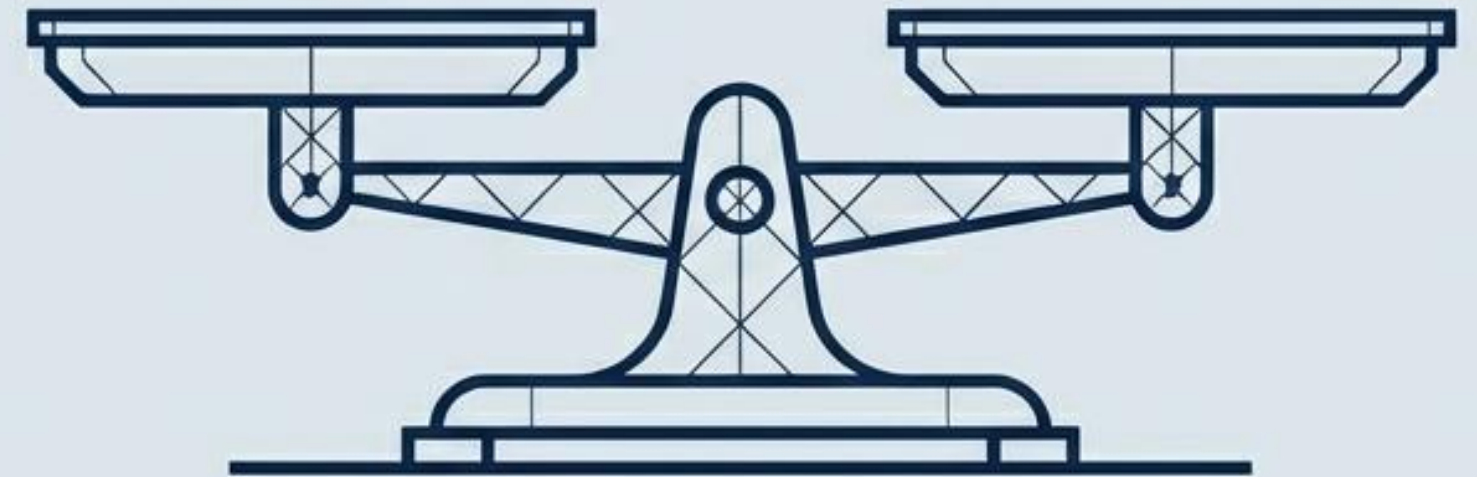

Note: A great PM knows exactly when to switch between the two.

Synthesis: The Value Creation Engine

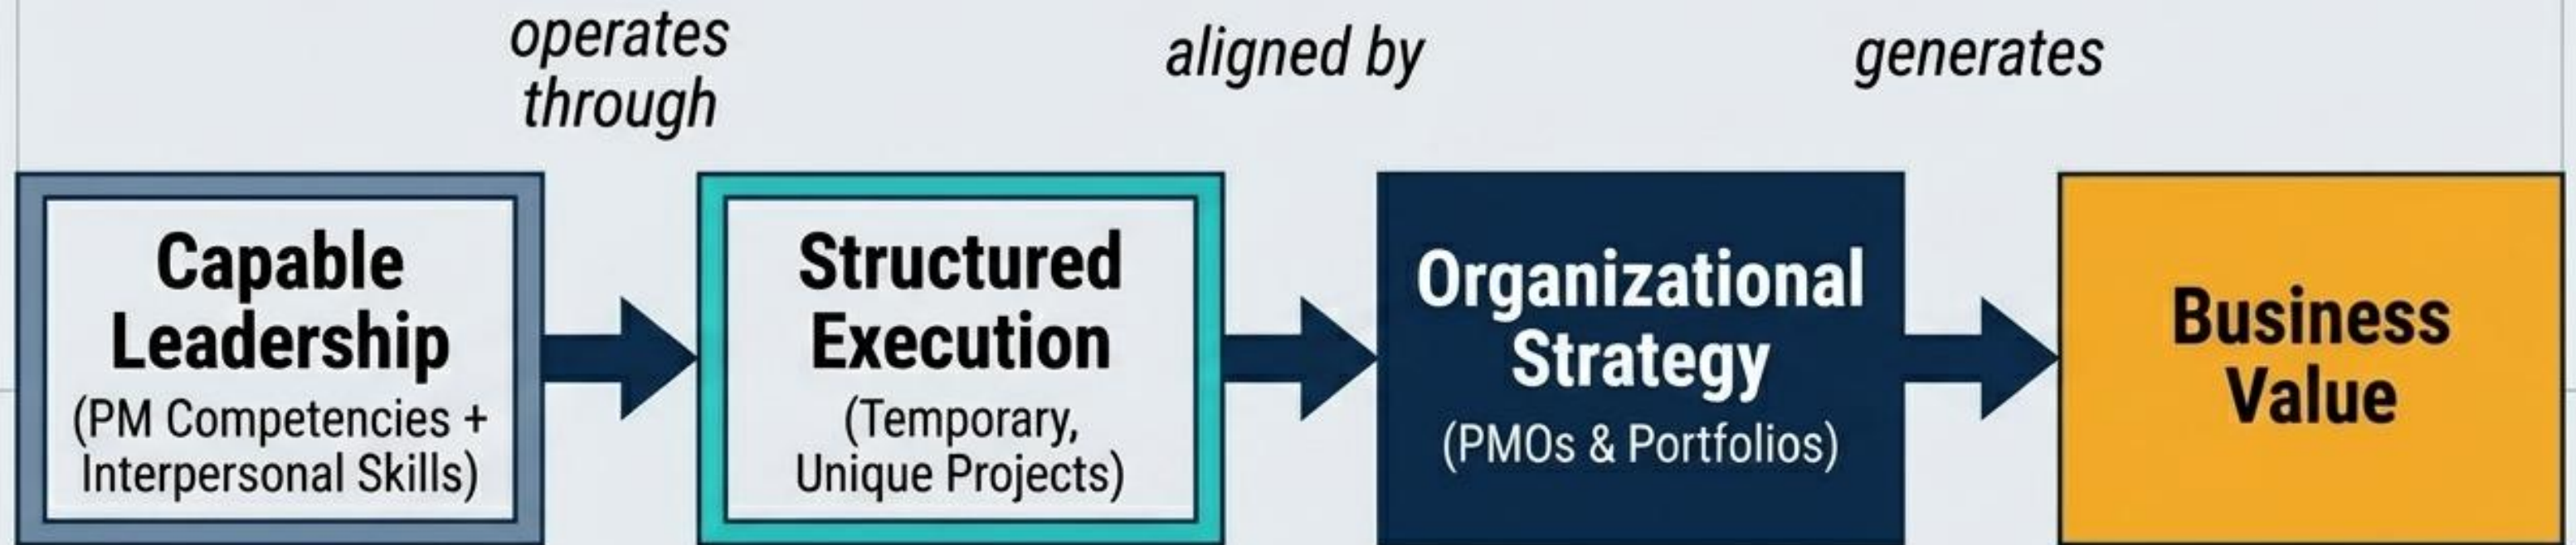

Concluding Takeaway: Project management is not merely administrative overhead. It is the primary engine through which an **organization transforms strategic vision into tangible and intangible business value.**
