



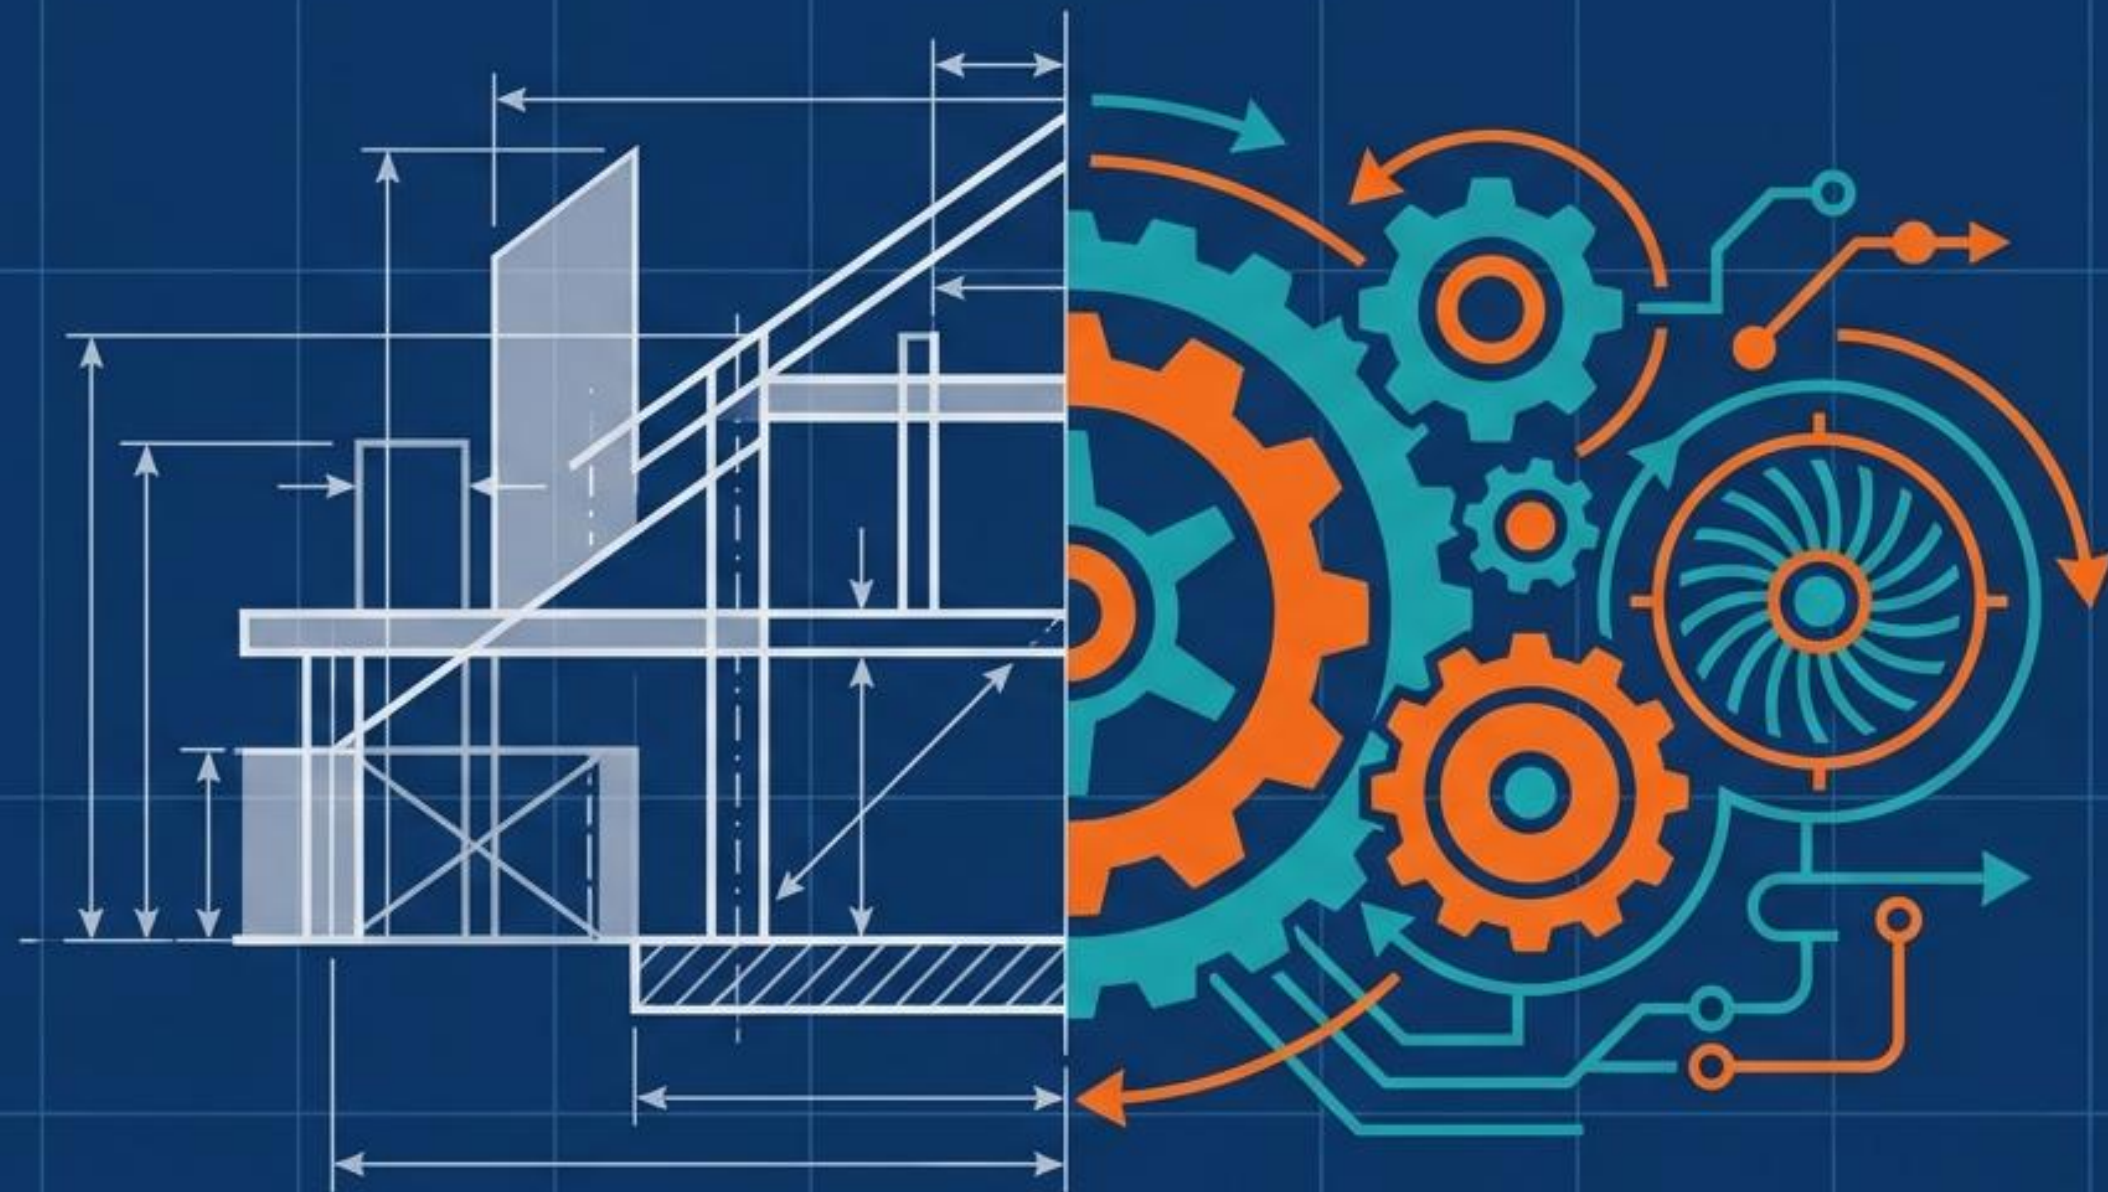

Certyfikat PMP: Project Lifecycle

dr Zbigniew Galar

Defining the boundary between projects and operations

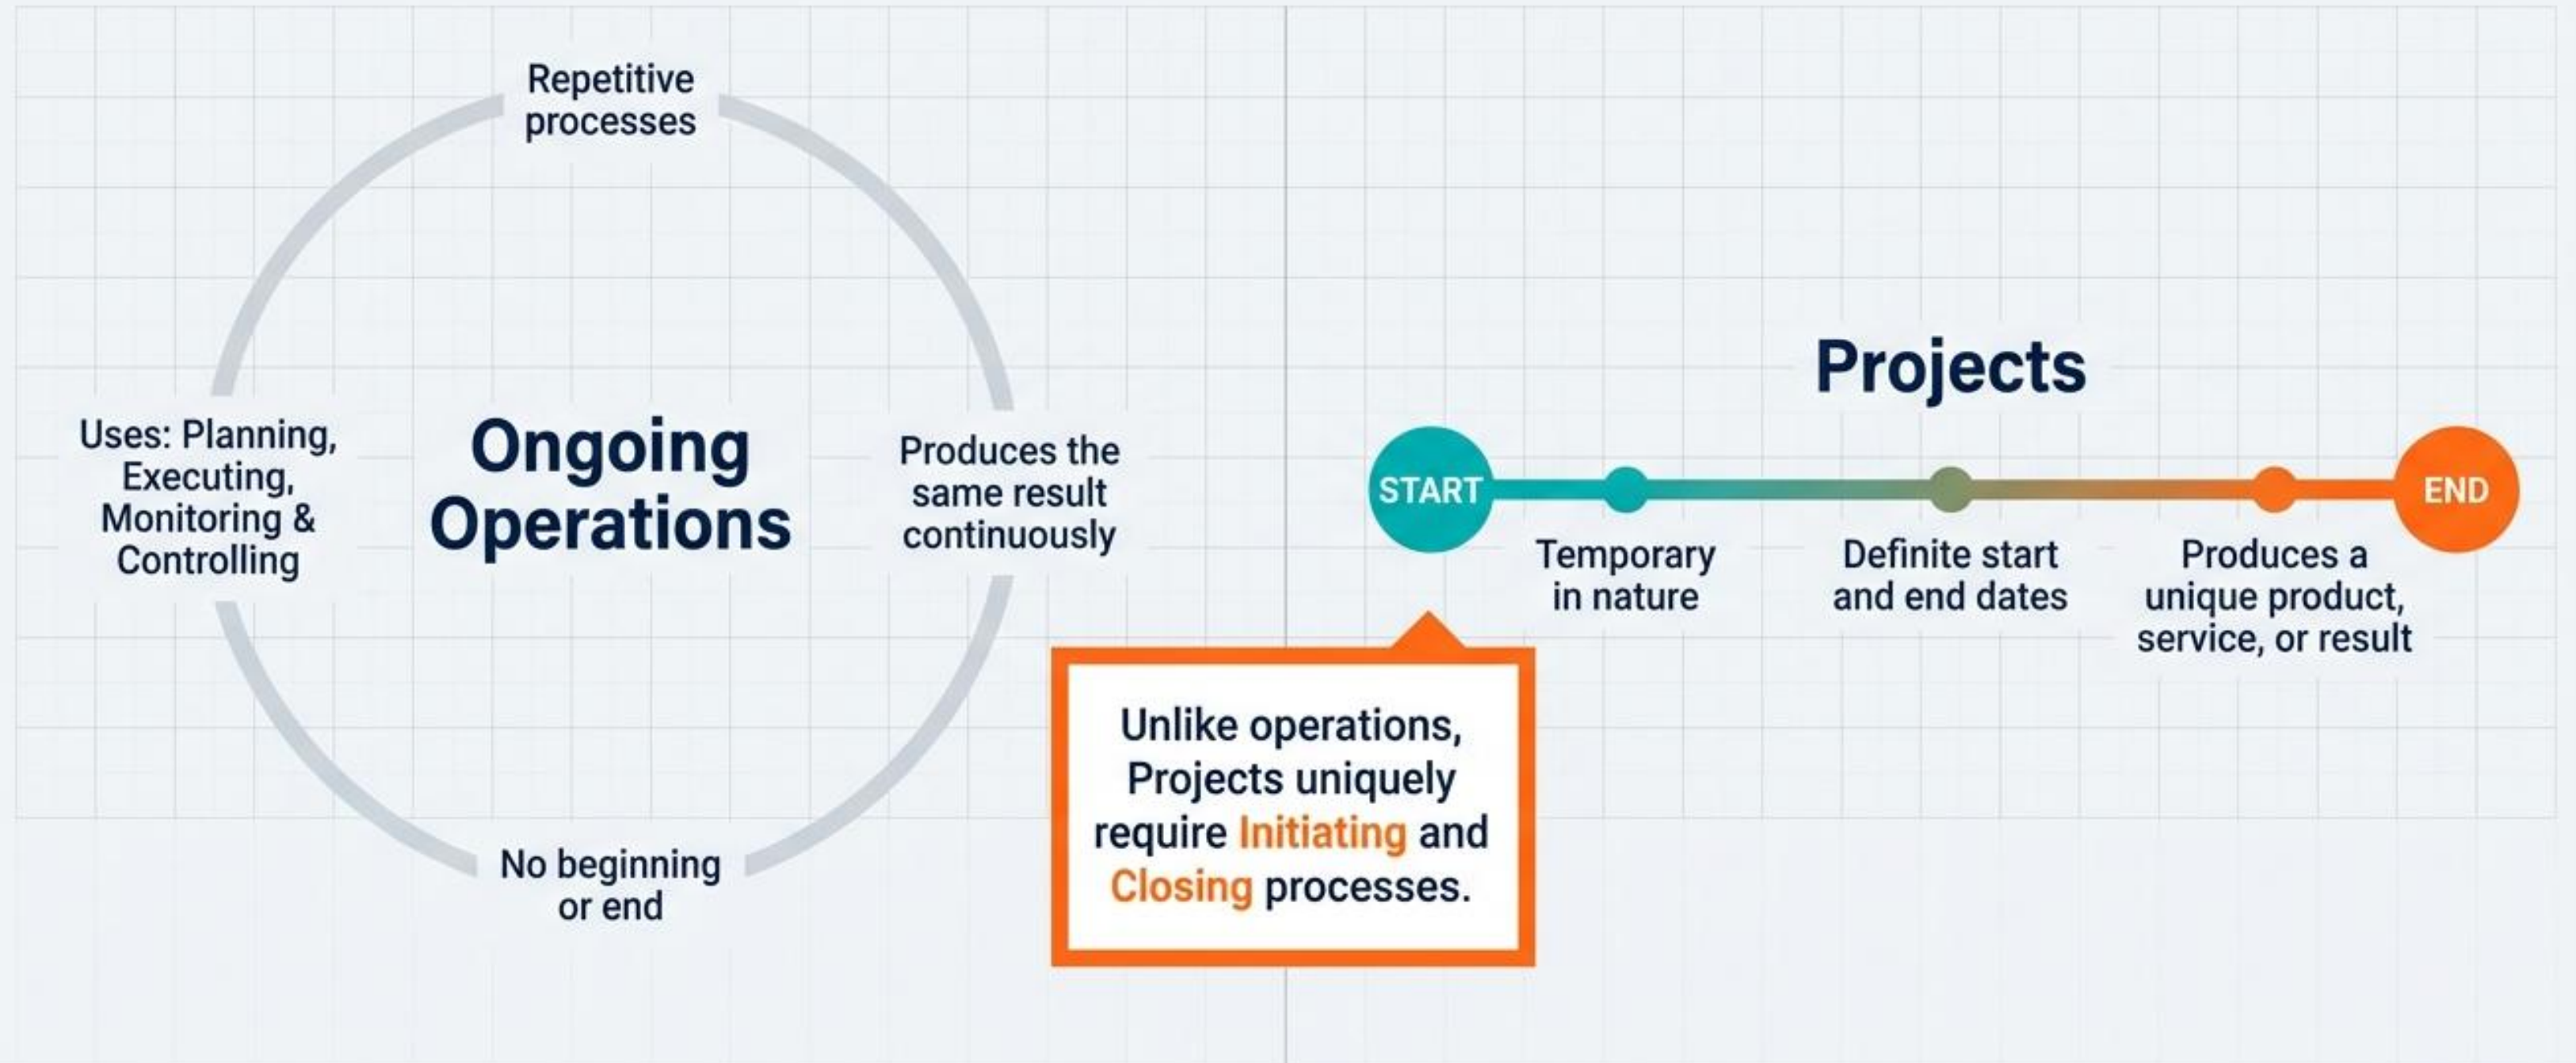


The structural blueprint: Life cycles and sequential phases

Macro Level

The Project Life Cycle

The collective progression of all phases from project approval to closeout.

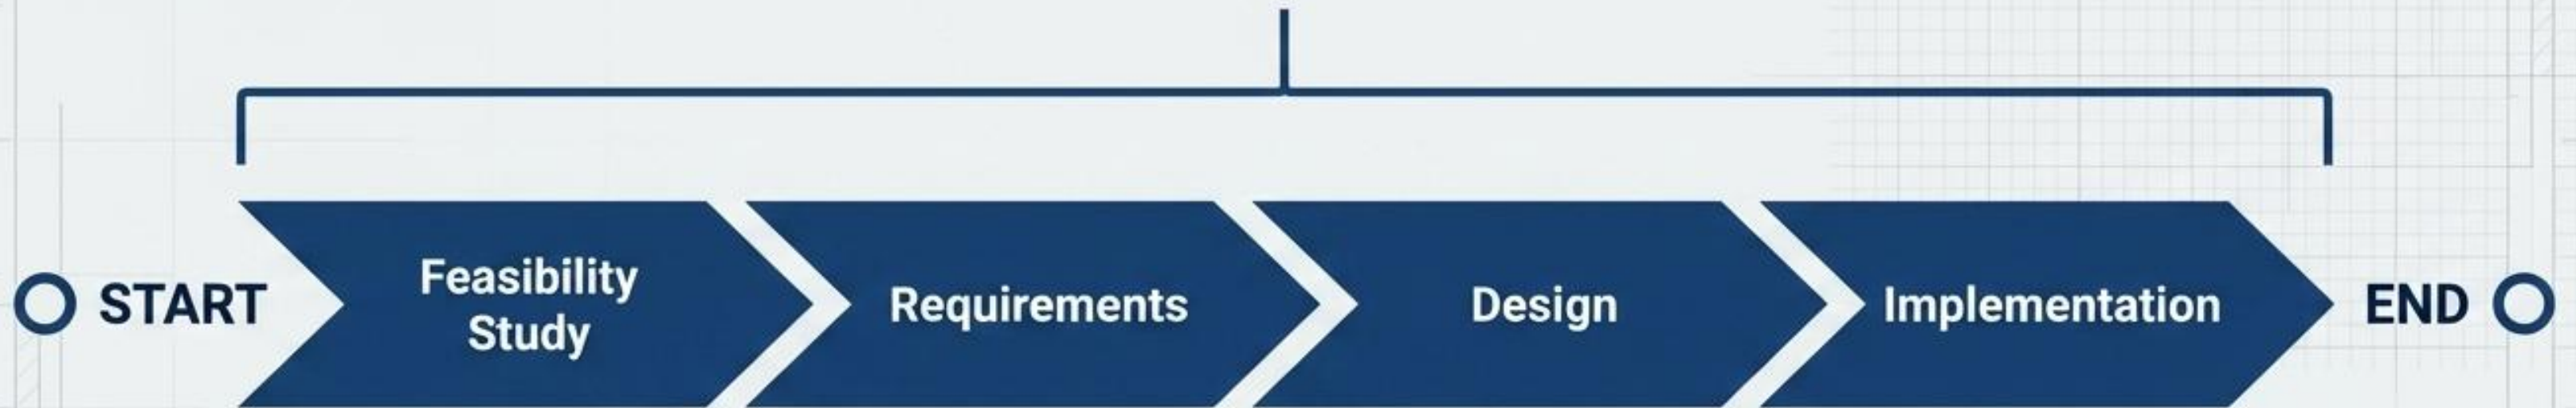

Micro Level

Phases


Segments of work for easier management and control.
Deliverables are typically unique to that phase.

Diagnostic matrix: Selecting the appropriate life cycle archetype

 Predictive (Fully Plan-Driven / Waterfall)	 Iterative and Incremental	 Adaptive (Agile / Change-Driven)
Strictly defined at the beginning.	Defined early but progressively elaborated.	Unclear upfront; evolves via stakeholder participation.
Highly monitored; requires formal acceptance and plan modifications.	Estimates refined continuously as the product clarifies.	Fixed time periods (2–4 weeks) and resources per iteration.
Distinct, non-repeating phases where schedules/budgets can be defined early.	Large, complex projects requiring incremental deliverables or known shifting objectives.	Changing environments requiring rapid, release-ready deliverables.

Phase relationships: The mechanics of schedule compression

Sequential Relationships



One phase must finish before the next can begin.

Overlapping Relationships (Fast Tracking)




Starting a later phase prior to completing and approving the prior phase.

Trade-off: Fast Tracking effectively **shortens** overall project duration, but inherently **increases project risk and potential rework**.



Handoffs and kill points: Navigating the phase gates

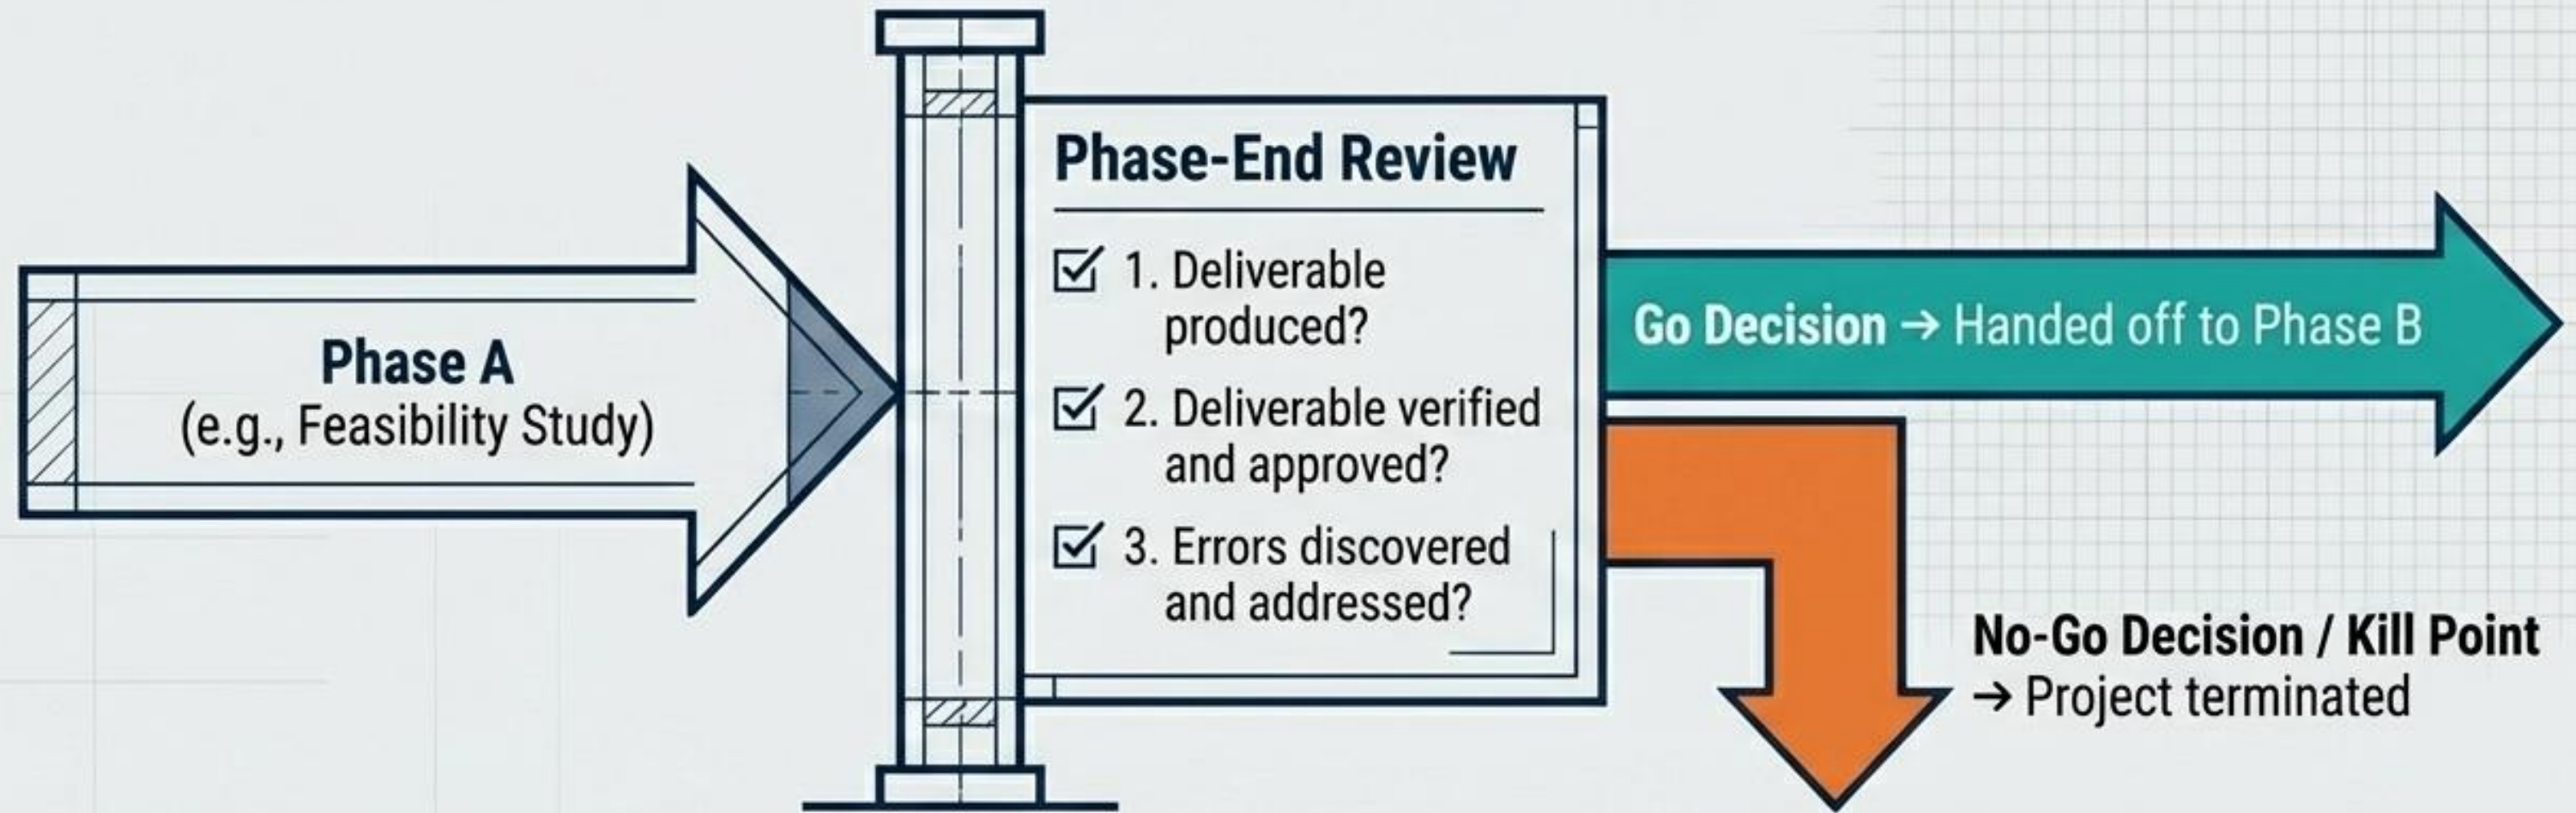

Terminology Note: PMBOK recognizes multiple terms for this checkpoint: **Phase Exits, Phase Gates, Phase Reviews, Milestones, Stage Gates, and Kill Points.**

The management engine: The 5 process groups

CRITICAL DISTINCTION: Do not confuse project phases (how the work is completed) with Process Groups (how the management is conducted).




Memory trick:
IPECC (Initiating, Planning, Executing, Controlling, Closing) sounds like syrup of ipecac.

The evolution of project dynamics




Process interactions: A dynamic, iterative system

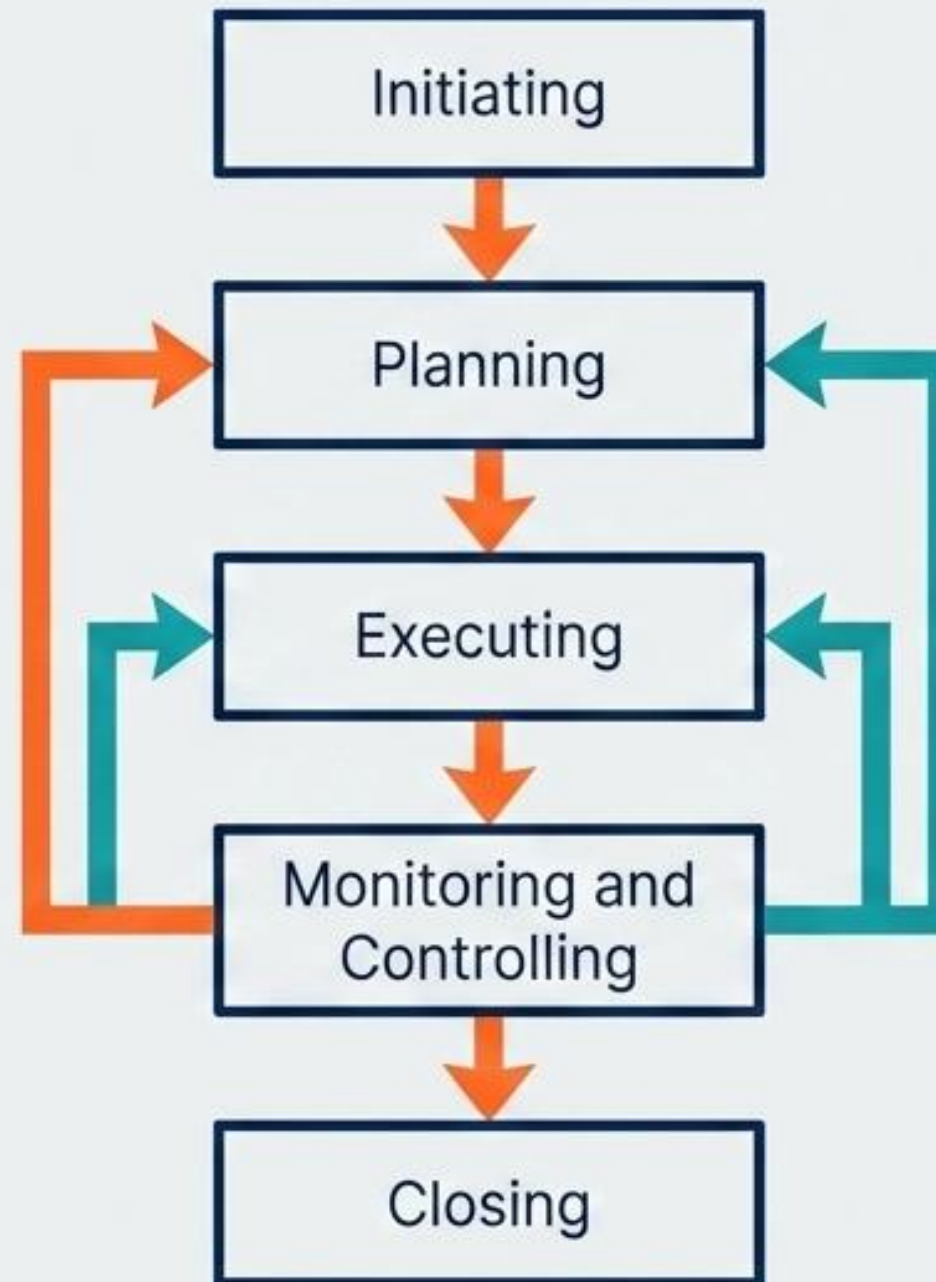


Process groups are not one-time, discrete elements. They overlap, interact, and are constantly revisited to refine the project plan as new information emerges.

The theoretical foundation: Plan-Do-Check-Act

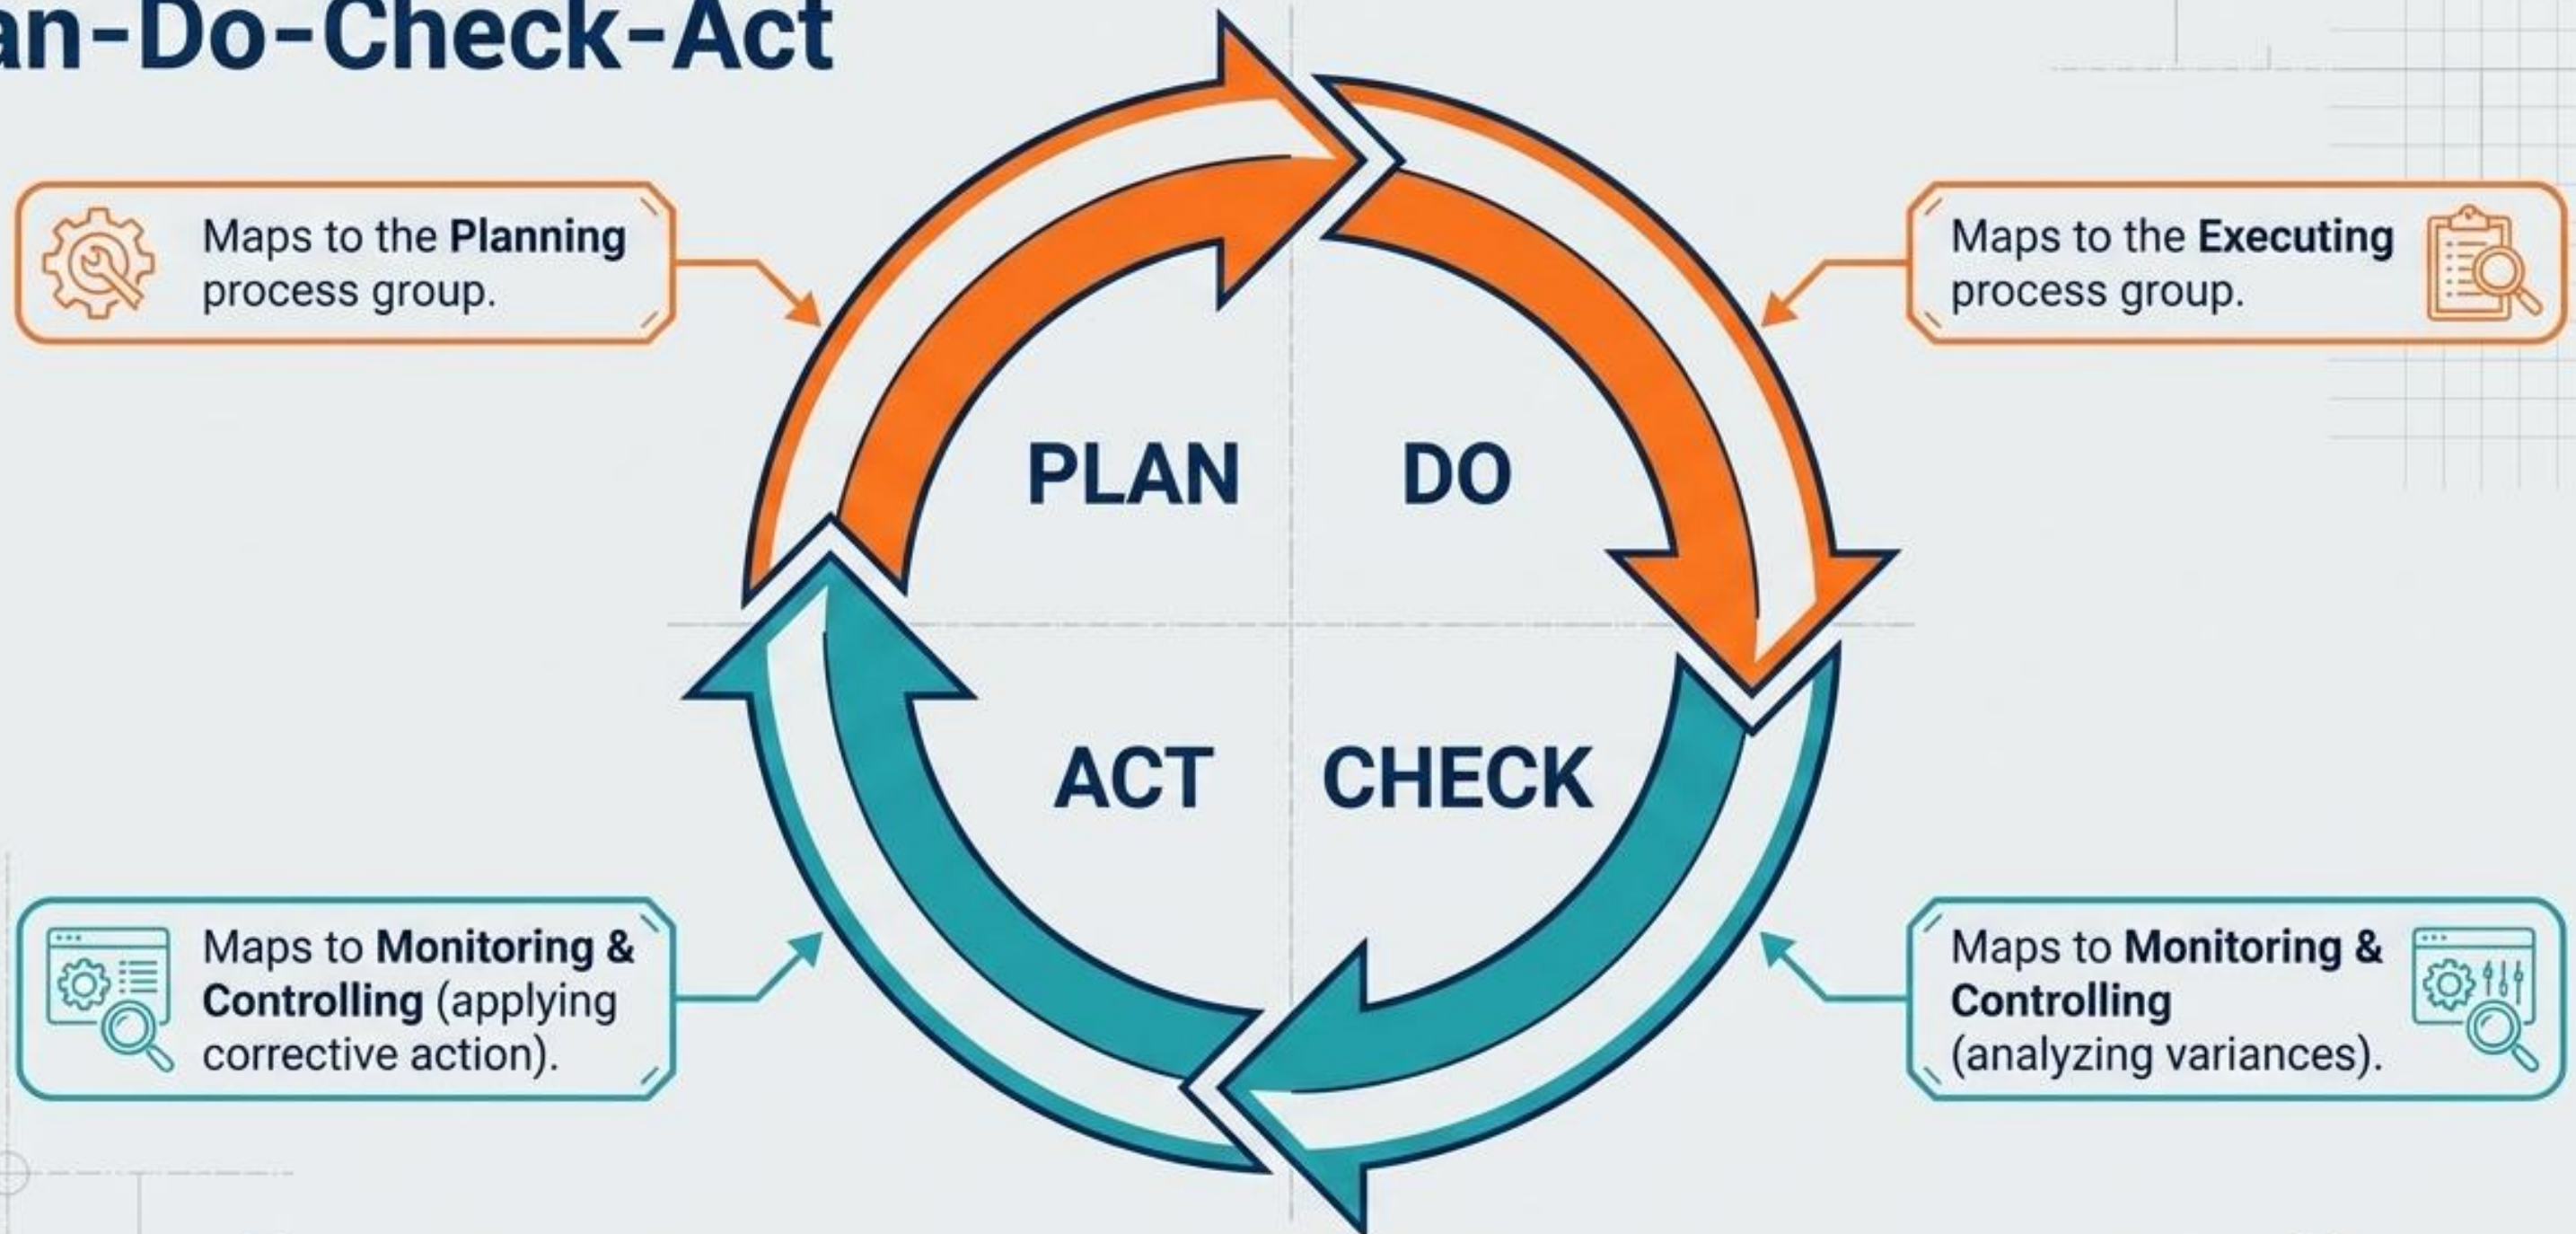

Core Message: The iterative nature of PMBOK process groups is driven by the results-oriented PDCA quality cycle. Outputs of one stage become inputs to the next.

System synthesis: Running the engine inside the blueprint

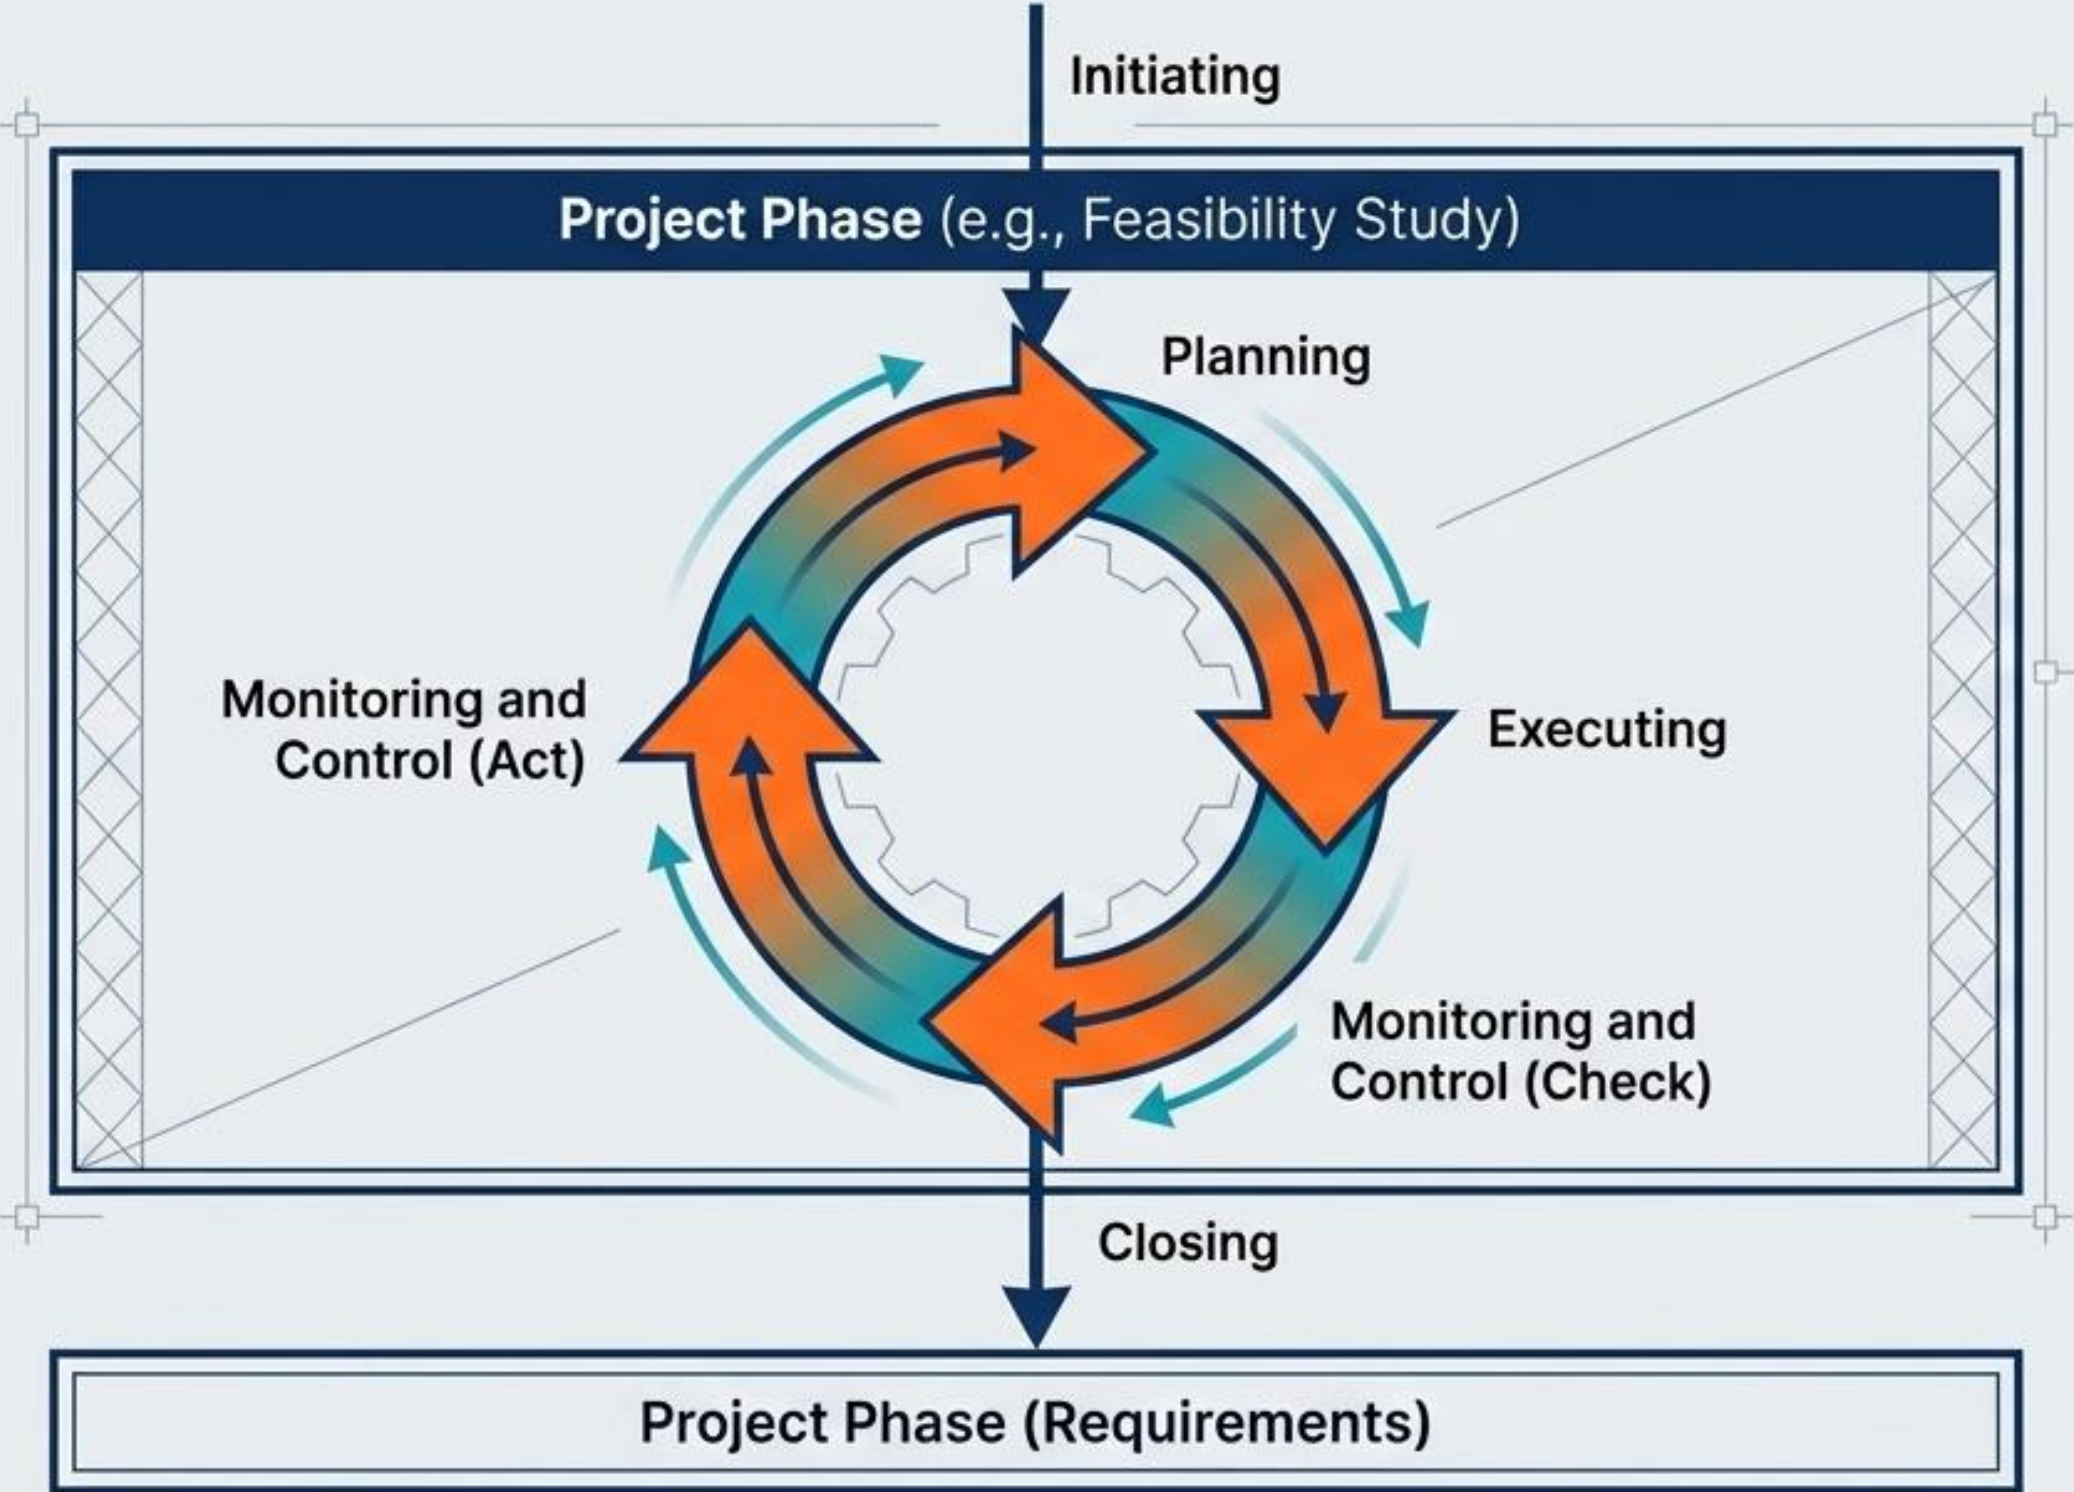


Synthesis Takeaway

The Grand Unification:

Project phases dictate what work is done sequentially. The 5 project management process groups iterate continuously within every single phase to drive that work forward.

The art of tailoring

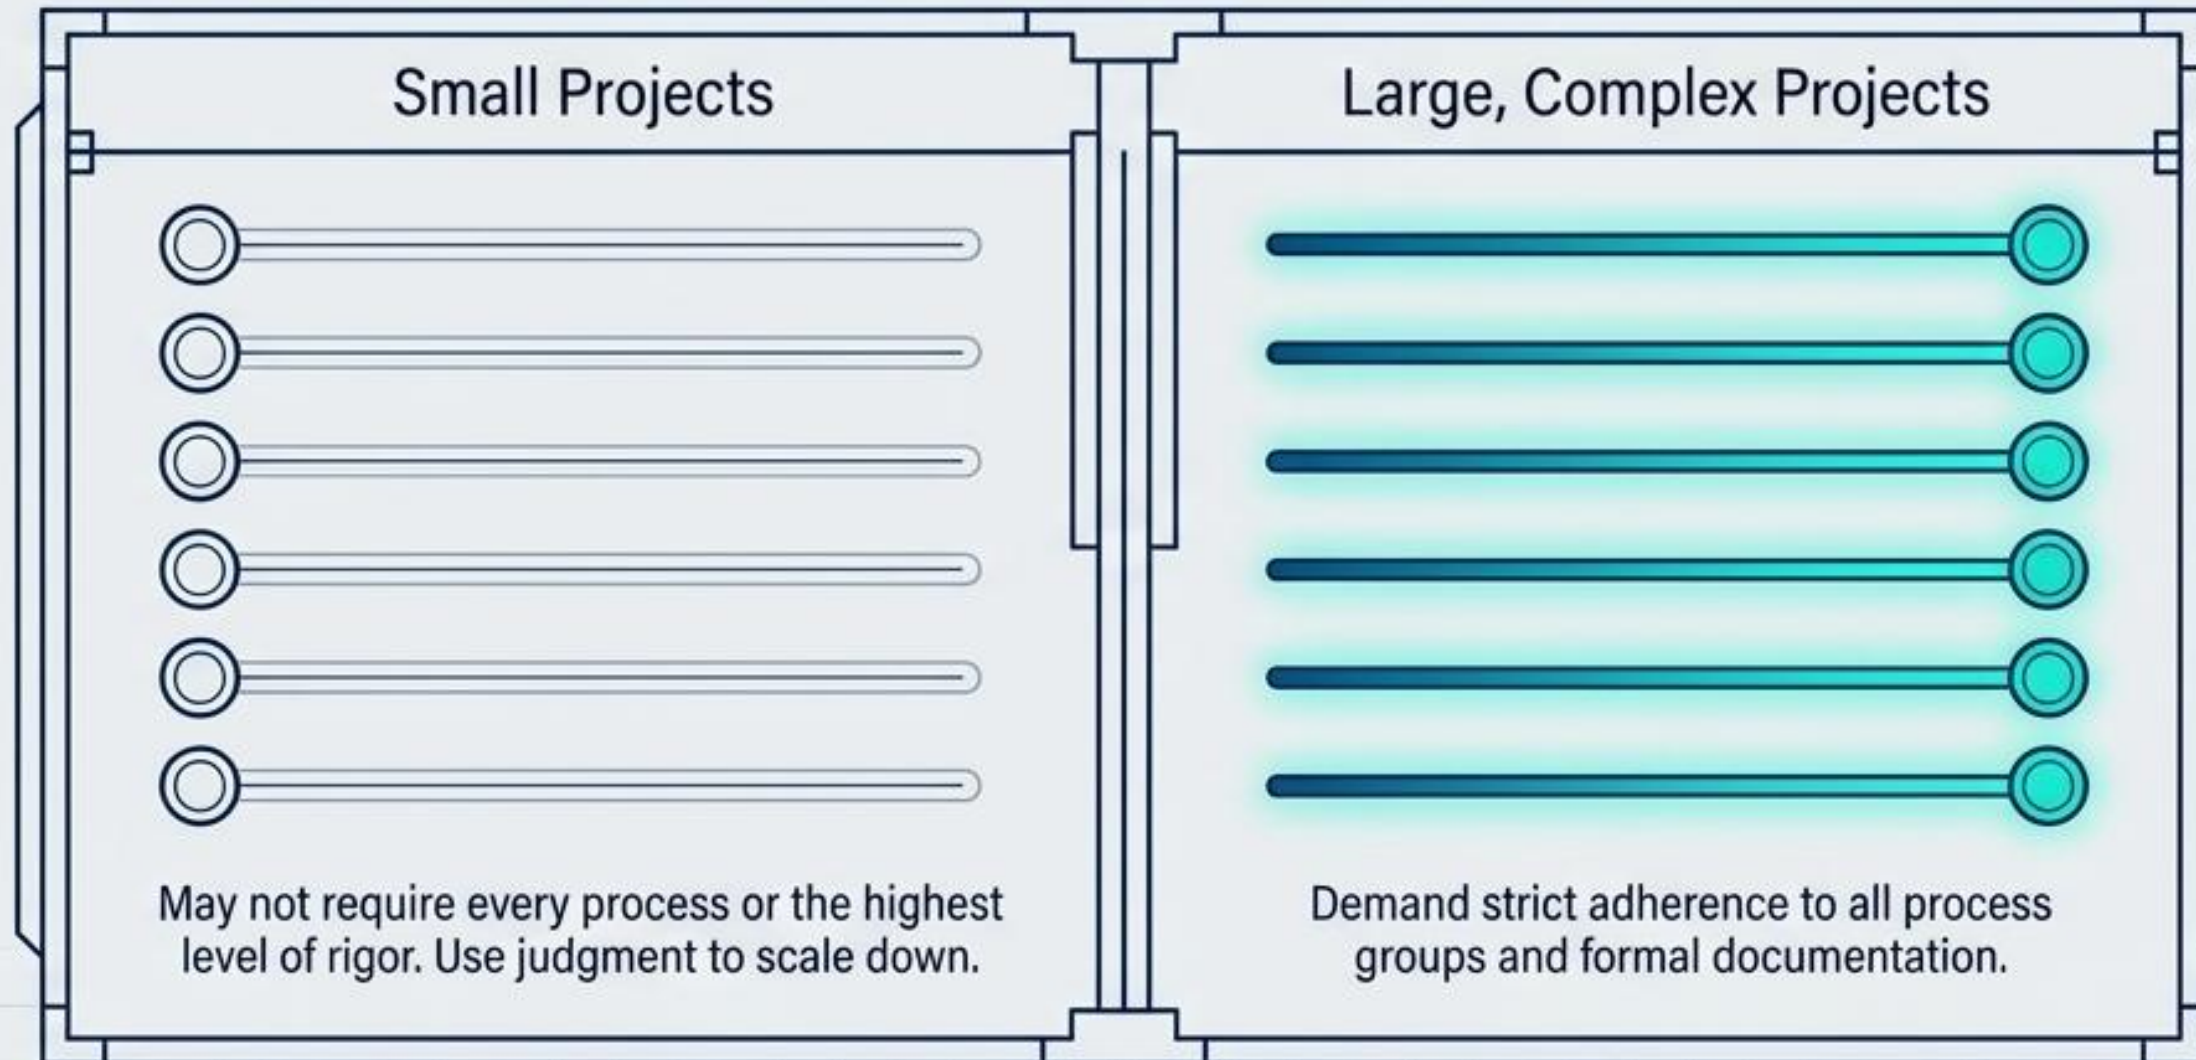

The PMBOK provides the engine and the blueprint, but the project manager and team are responsible for determining the specific processes appropriate for their unique reality. Tailoring is the bridge between theory and successful execution.
