




Certyfikat PMP: Project Environment			
dr Zbigniew Galar			

Mapping the Project Ecosystem

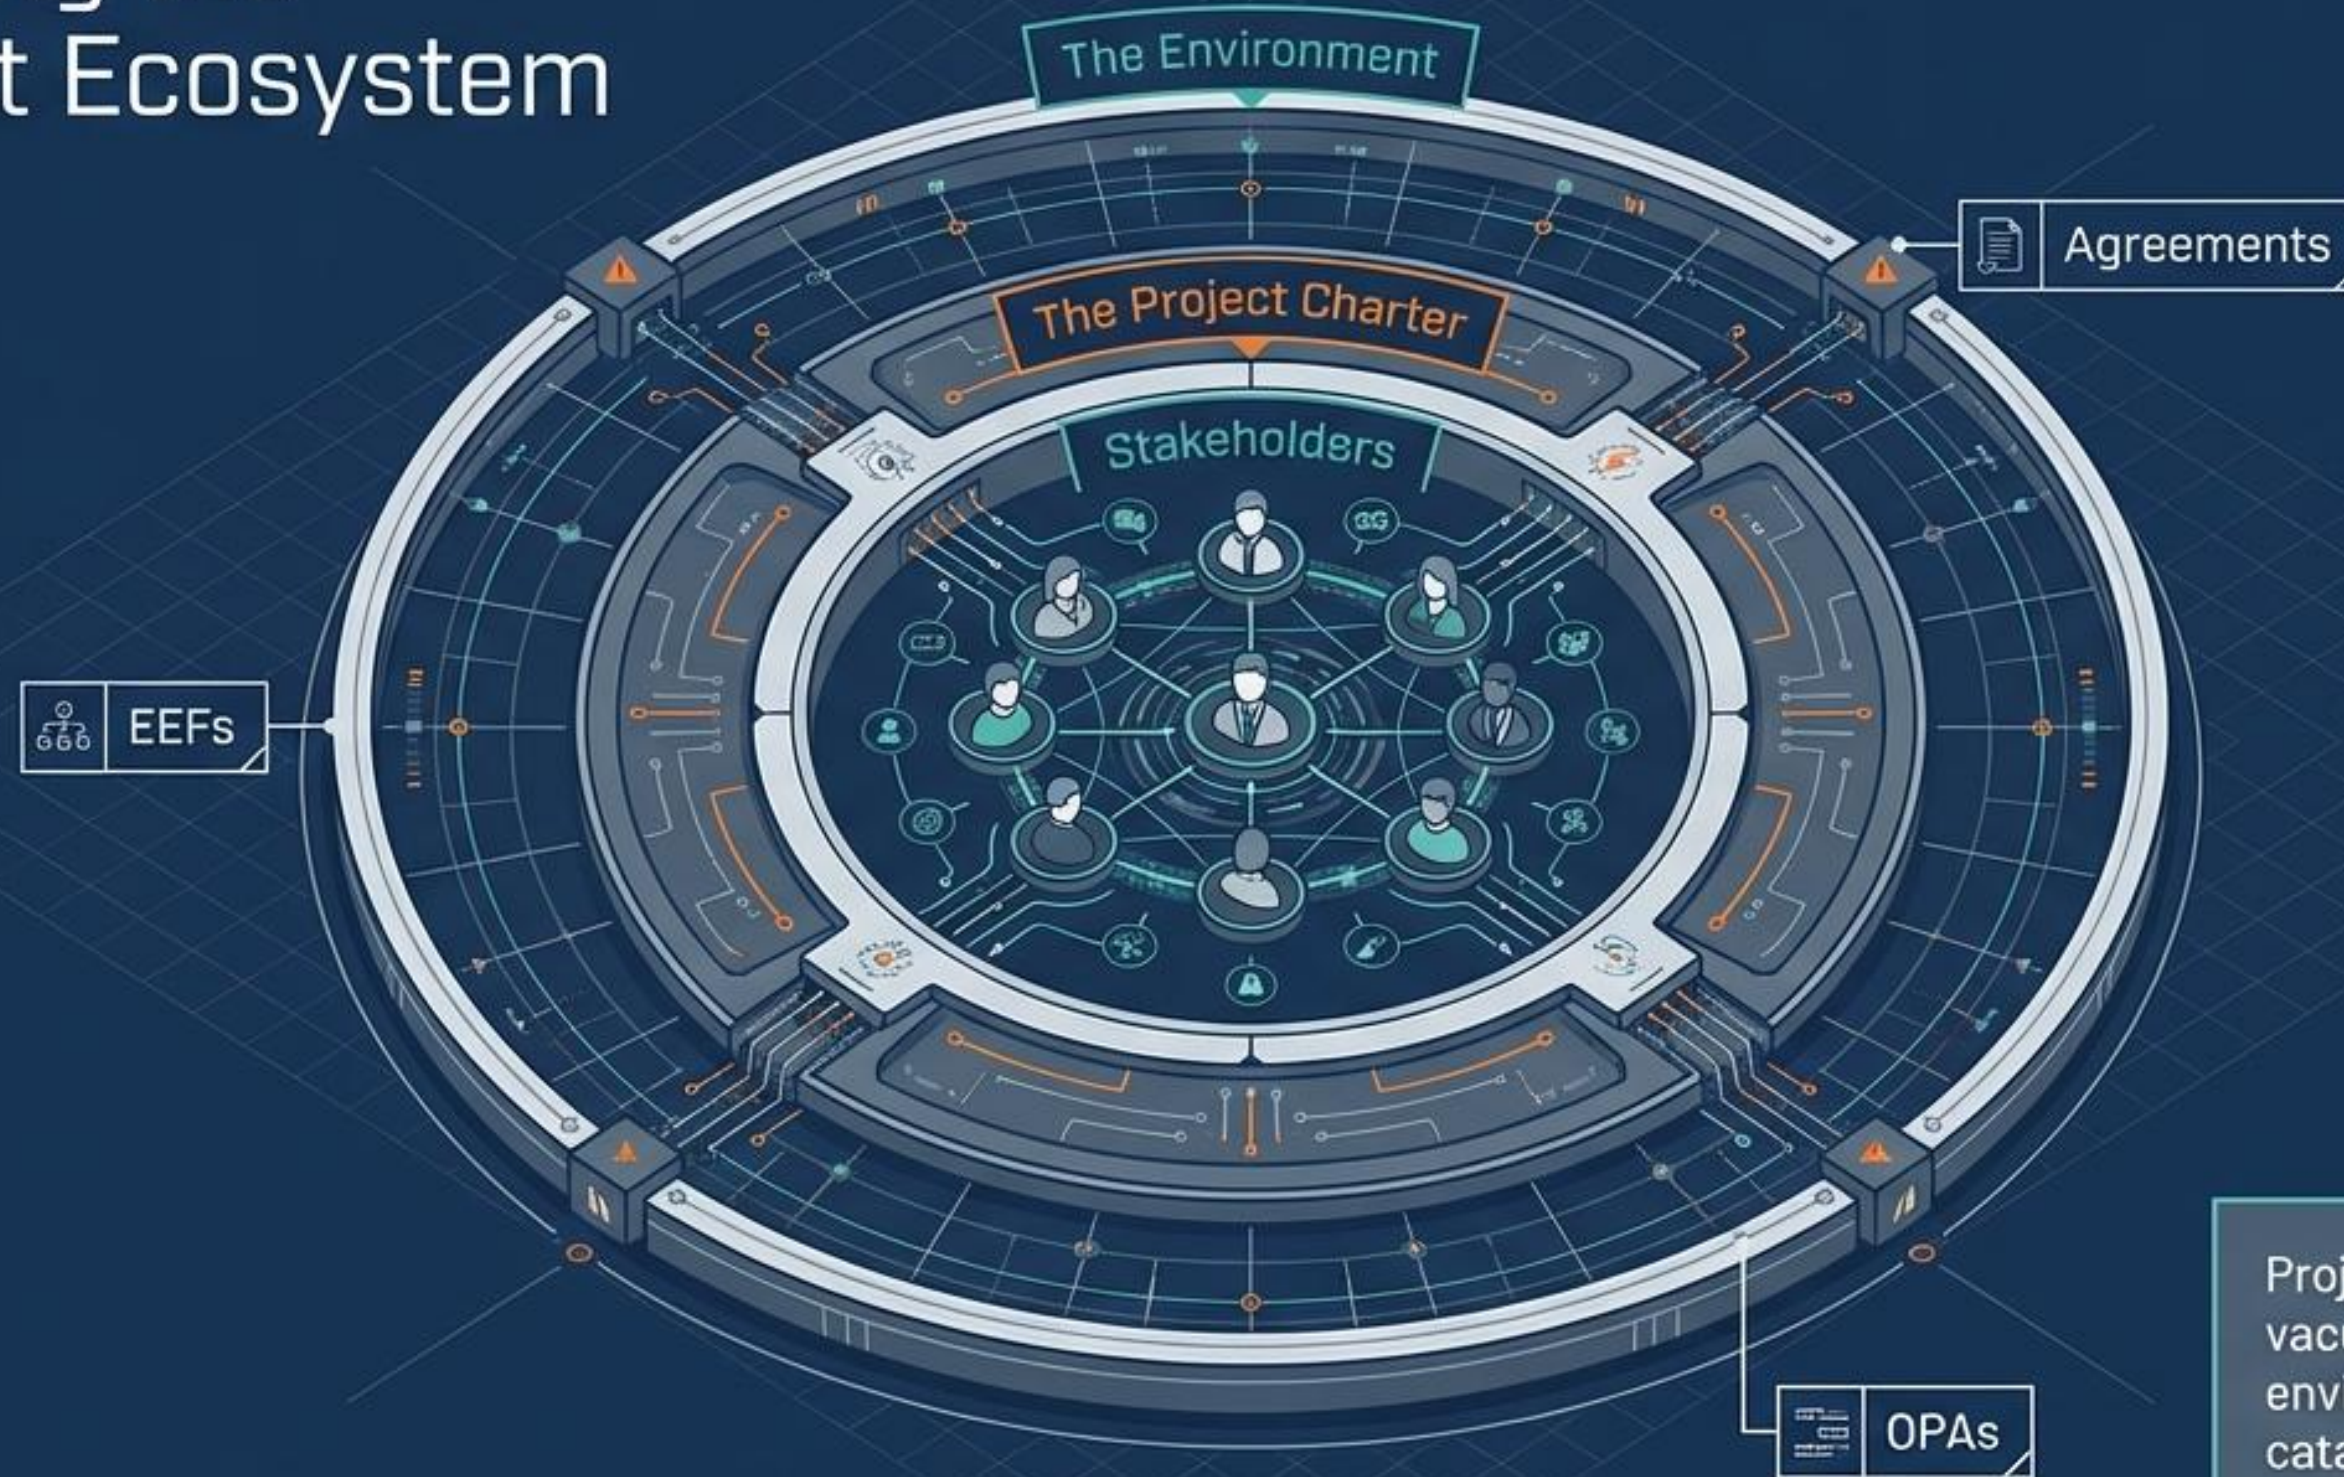

Projects do not begin in a vacuum. We inherit an environment, authorize a catalyst, and map the community.

The Formality Spectrum of Project Agreements




Agreements document the conditions, time frame, and work description before the project formally begins.


Navigating Enterprise Environmental Factors (EEFs)

Forces outside the project's control that influence, constrain, or direct project success.

Internal Terrain

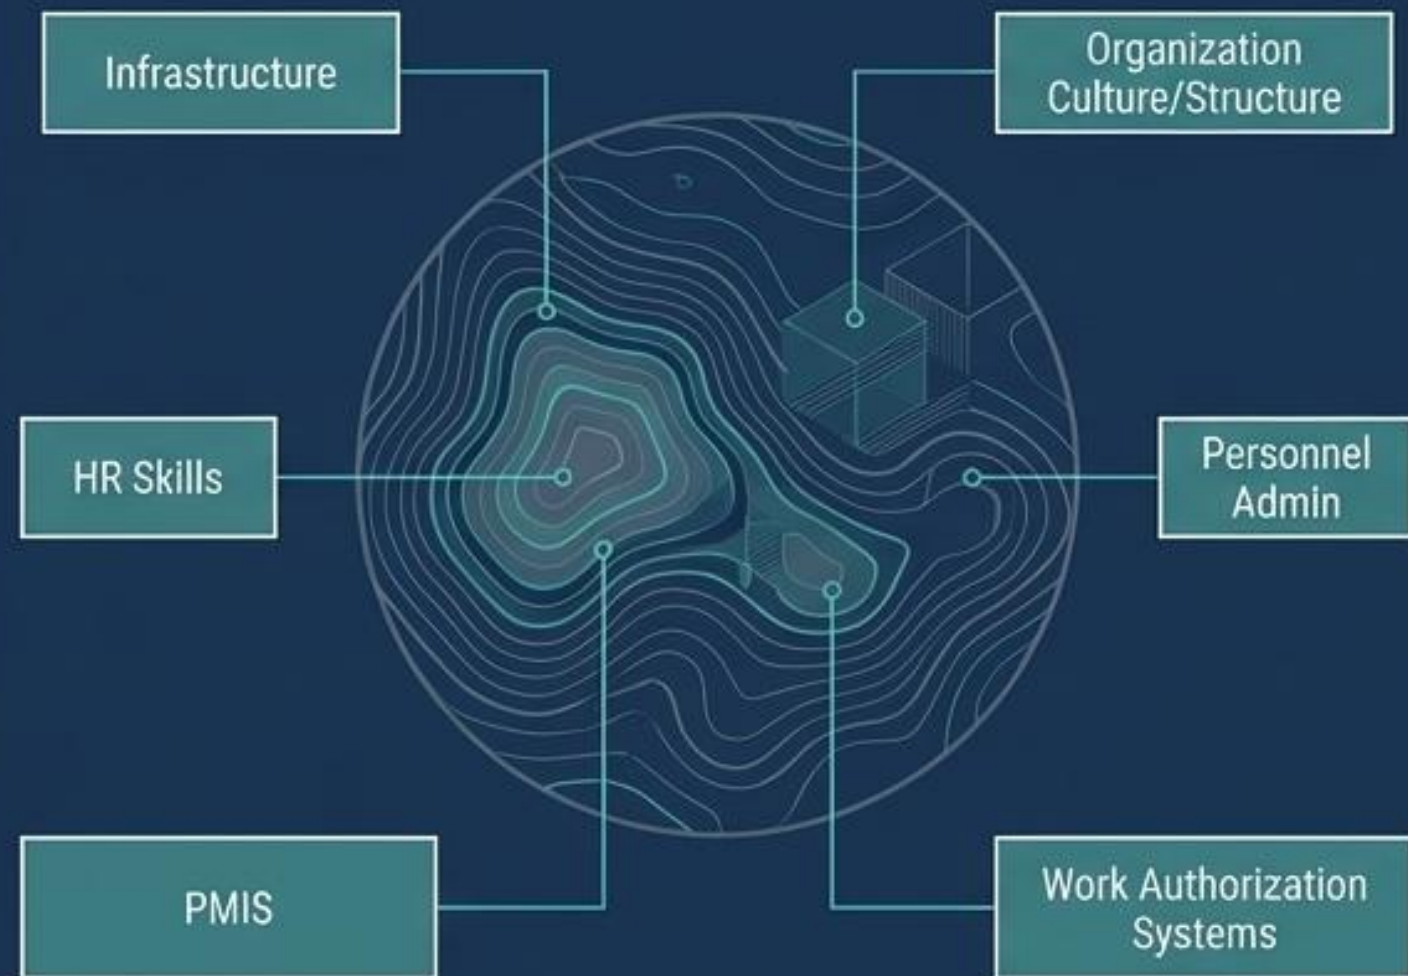

External Weather

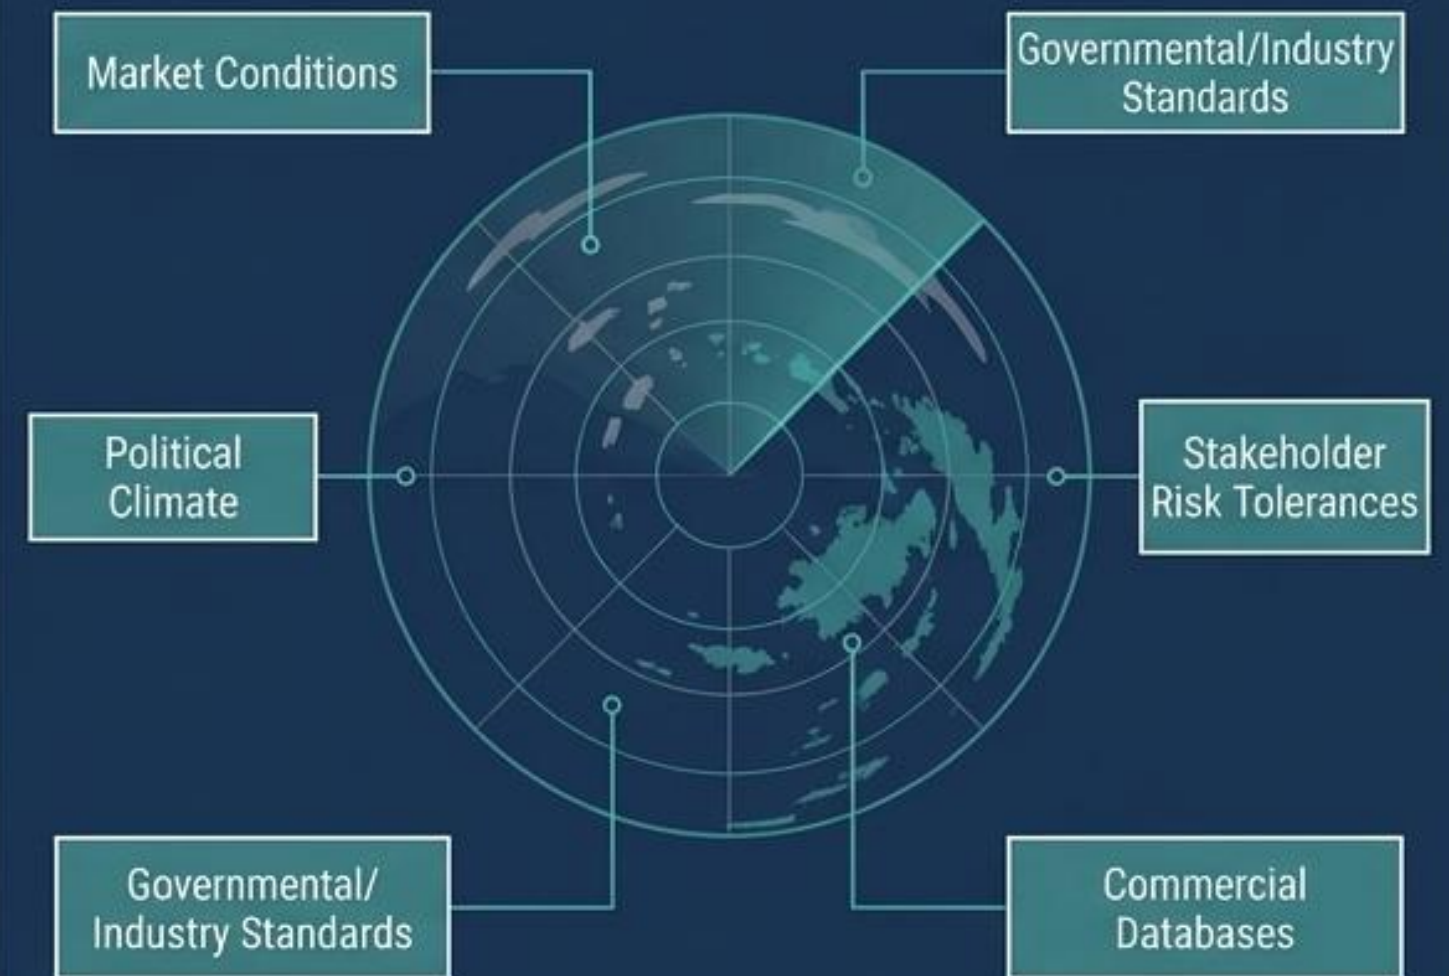

Leveraging Organizational Process Assets (OPAs)



Templates, safety policies, change/risk control procedures, financial controls


Historical information, lessons learned, process measurements, past budgets

Crucial for planning: Past project schedules and estimates prevent the repetition of historical mistakes.

Diagnostic Matrix: Distinguishing EEFs from OPAs

	Enterprise Environmental Factors (EEFs)	Organizational Process Assets (OPAs)
Nature	The rules you must play by (Restrictive)	The tools you play with (Empowering)
Origin	Internal or External environment	Internally generated by the organization
Project Impact	Limit options and shape risk	Accelerate planning and provide templates
Exam Rule of Thumb	Can I change it? No.	Can I use it? Yes.


The Charter Generation Funnel

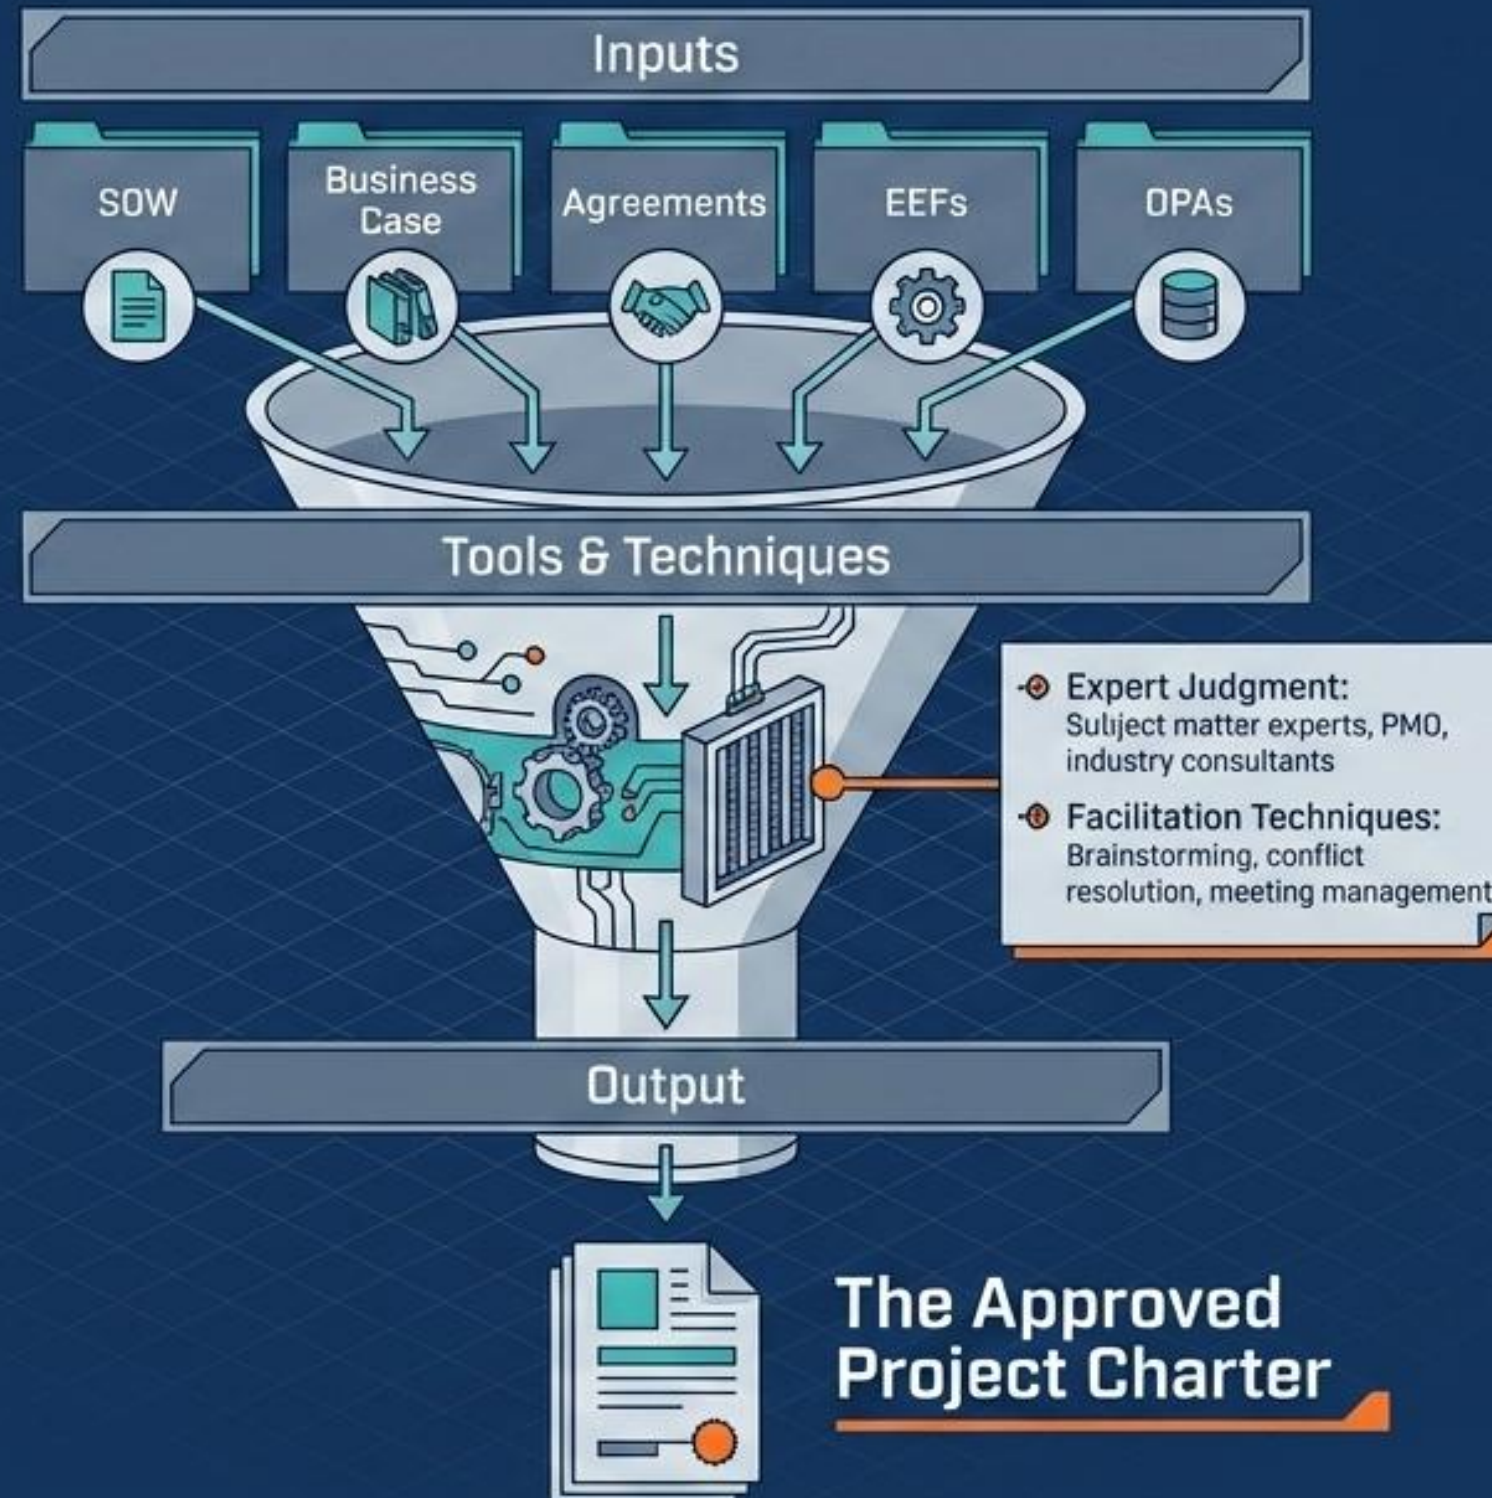

Anatomy of a Project Charter




The Triad of Project Authority

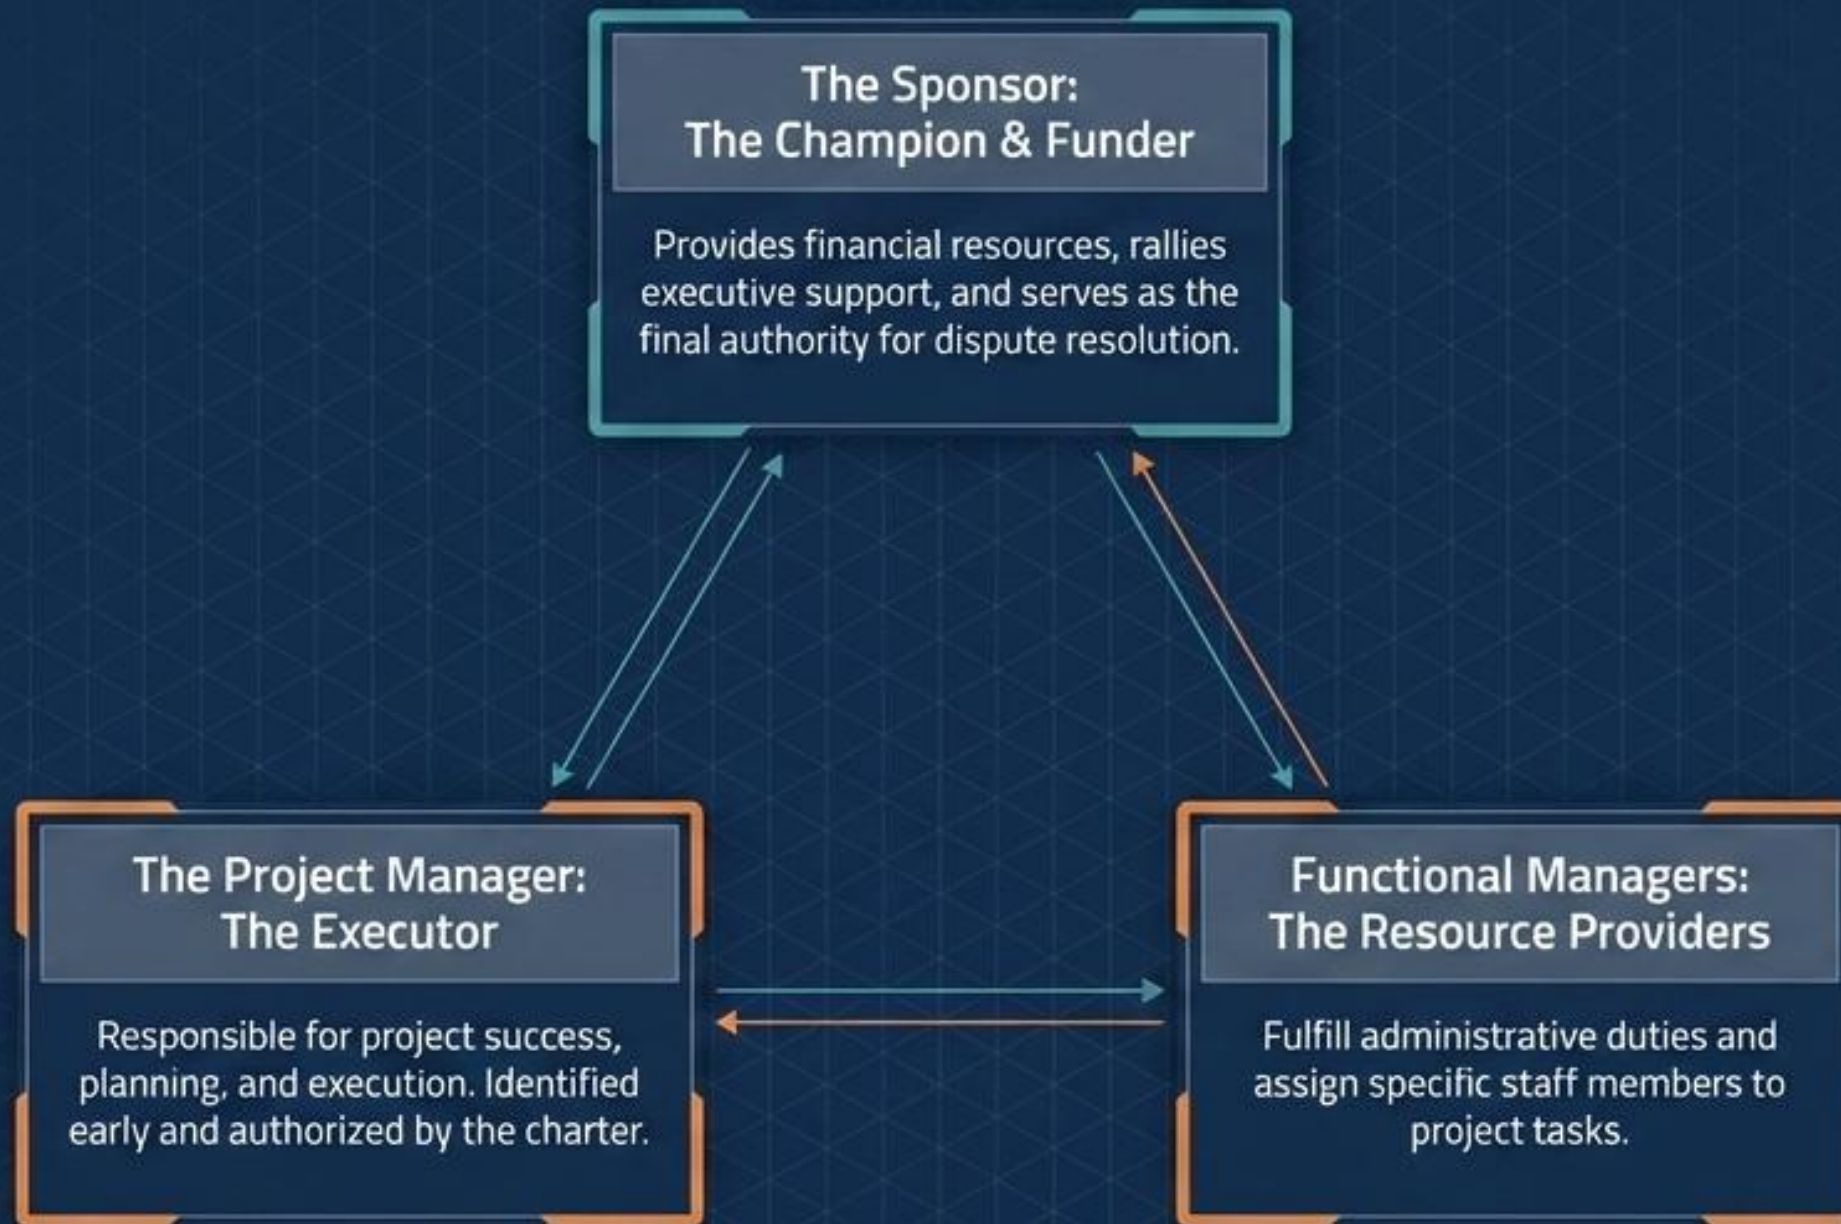

The Ignition Sequence: Formalizing the Charter



Phase 3: Iteration
The charter is a baseline, not a tombstone. It will evolve as the Planning processes uncover new details and issues.

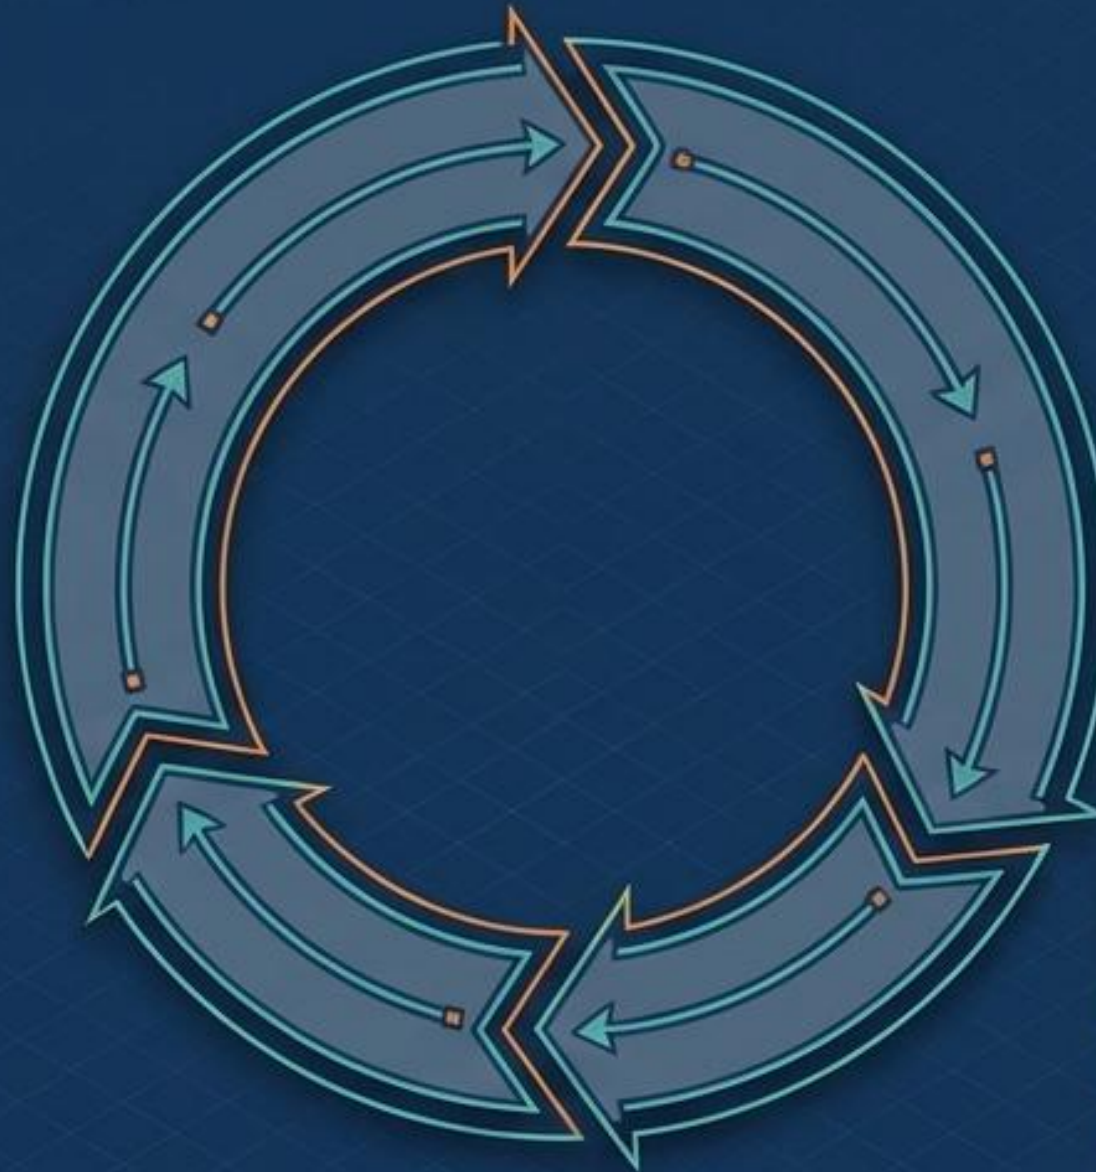

Phase 1: The Kickoff


Align key stakeholders and obtain formal sign-off. Signatures equal endorsement.



Phase 2: Authorization

The PM is officially granted the power to commit organizational resources.

Uncovering the Stakeholder Landscape

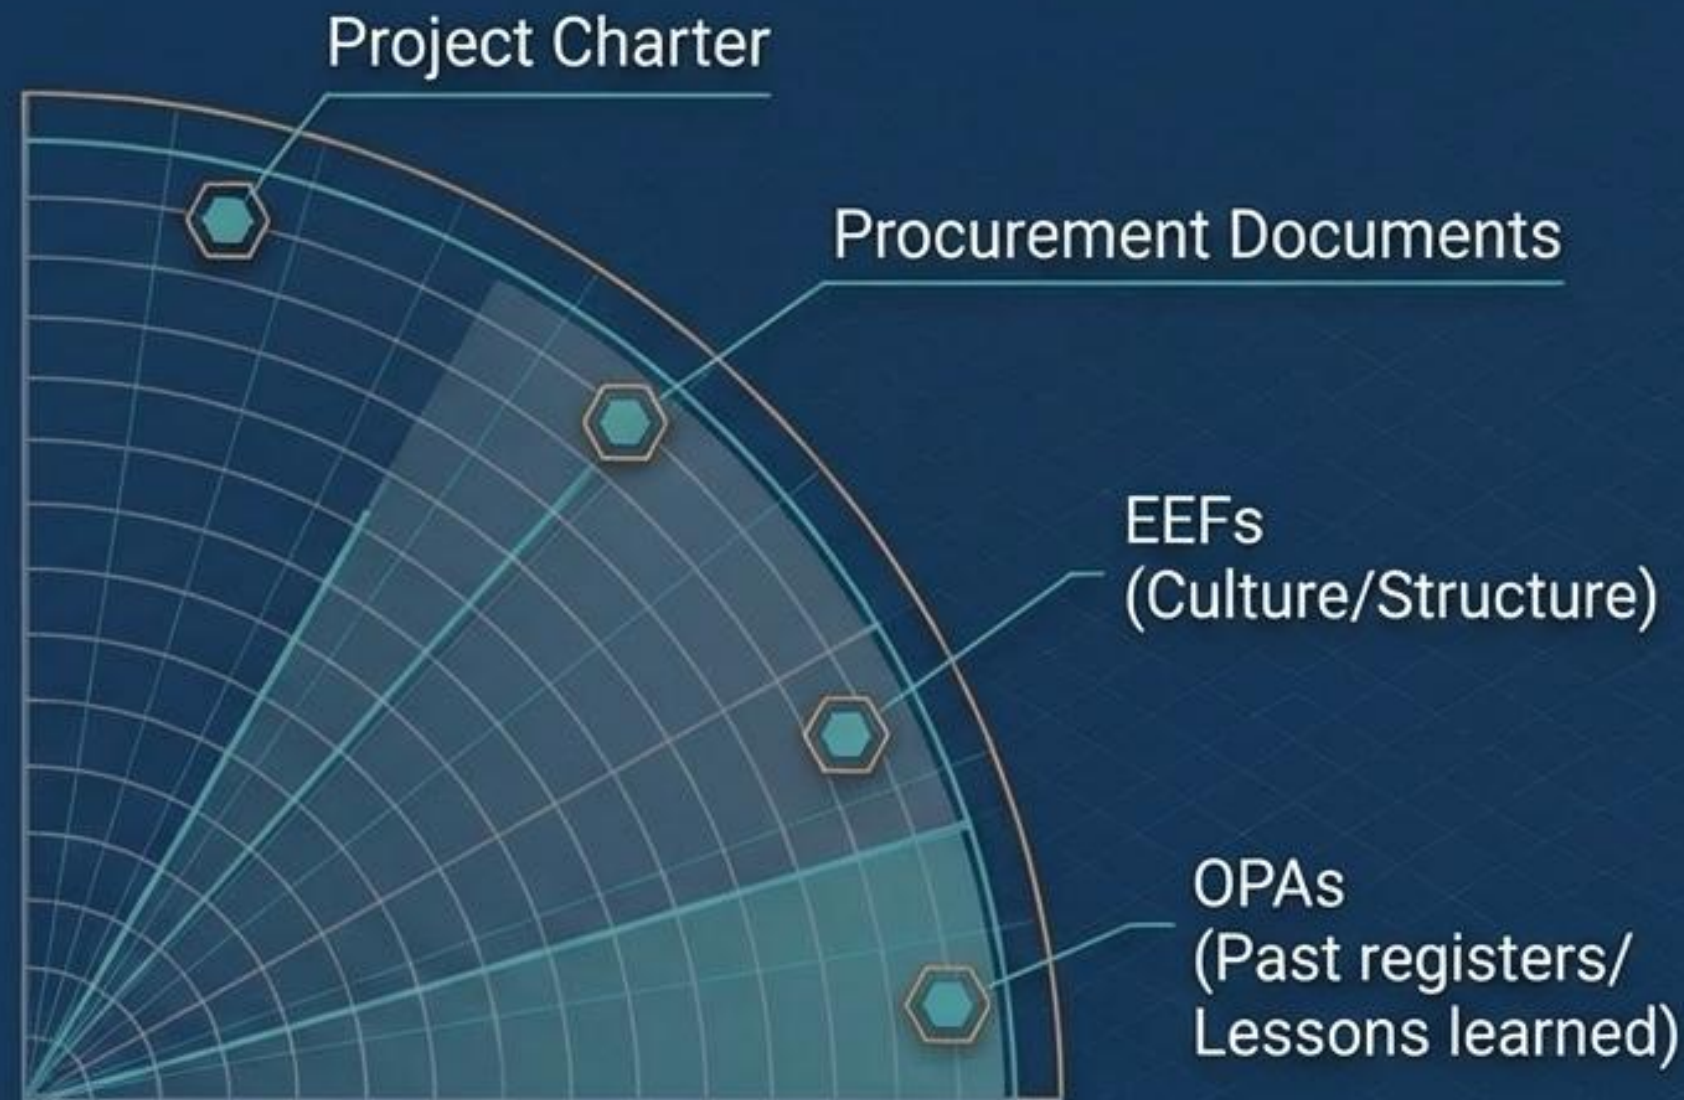

Identification must occur as early as possible.

Analysis is a 3-step process:

1. Identify
2. Analyze Impact
3. Assess Reaction

Critical Risk: Leaving out an important stakeholder during Initiation can spell disaster for the project deliverables.

Strategic Mapping: The Power/Interest Grid

The Power/Interest Grid



Alternative classification models include Power/Influence, Influence/Impact, and the Salience Model (Power, Urgency, Legitimacy).

The Stakeholder Register Blueprint

Name, Contact, Department, Project Role

Influence level, Key expectations, Critical phase of involvement

Secure Data

Identifying Info		Assessment Info		Classification	

Internal/External;
Supporter/Neutral/Resistor

Security Protocol: The register is often accessible to the team. Exercise extreme caution when documenting sensitive political strategies or resistance levels.

Synthesis: The Project Initiation Ecosystem

