



Certyfikat PMP: Project Scope Document

Author: dr Zbigniew Galar


Mastering the Planning Phase: PM Plan, Scope, and Requirements

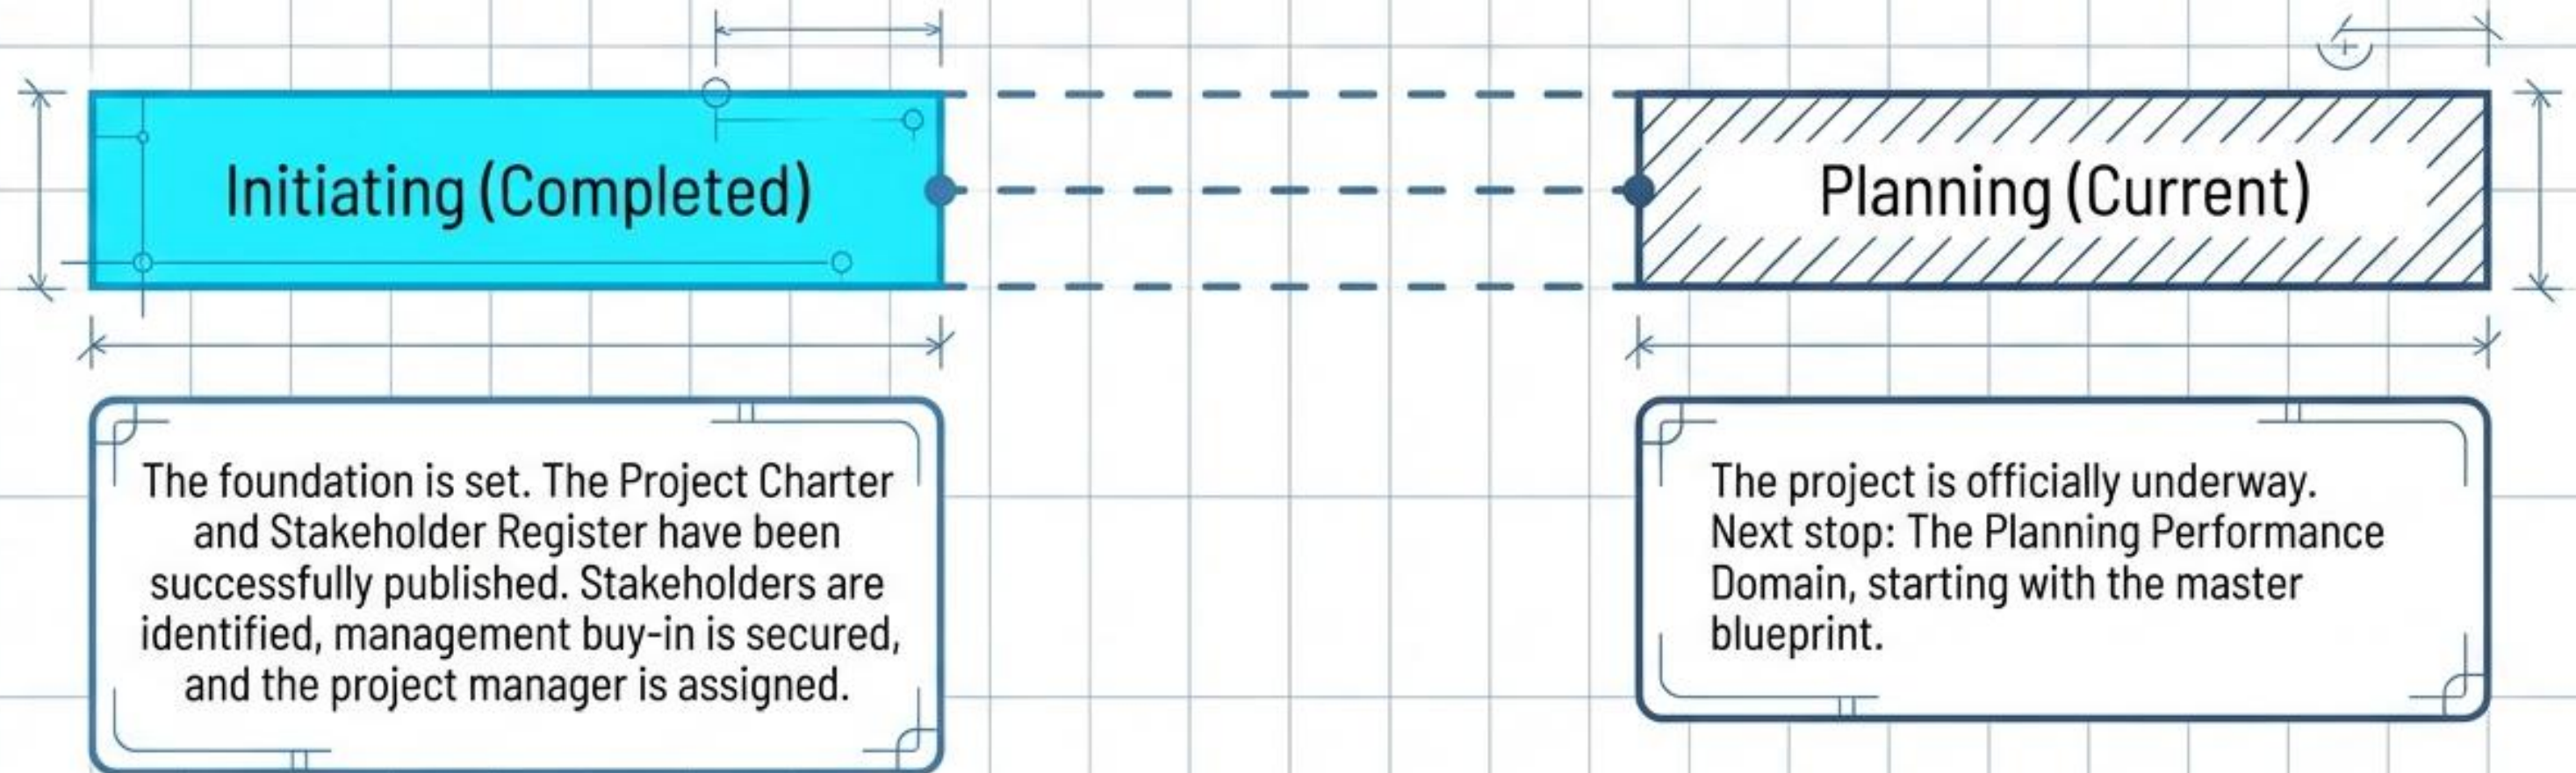

The Integration Engine: Develop Project Management Plan

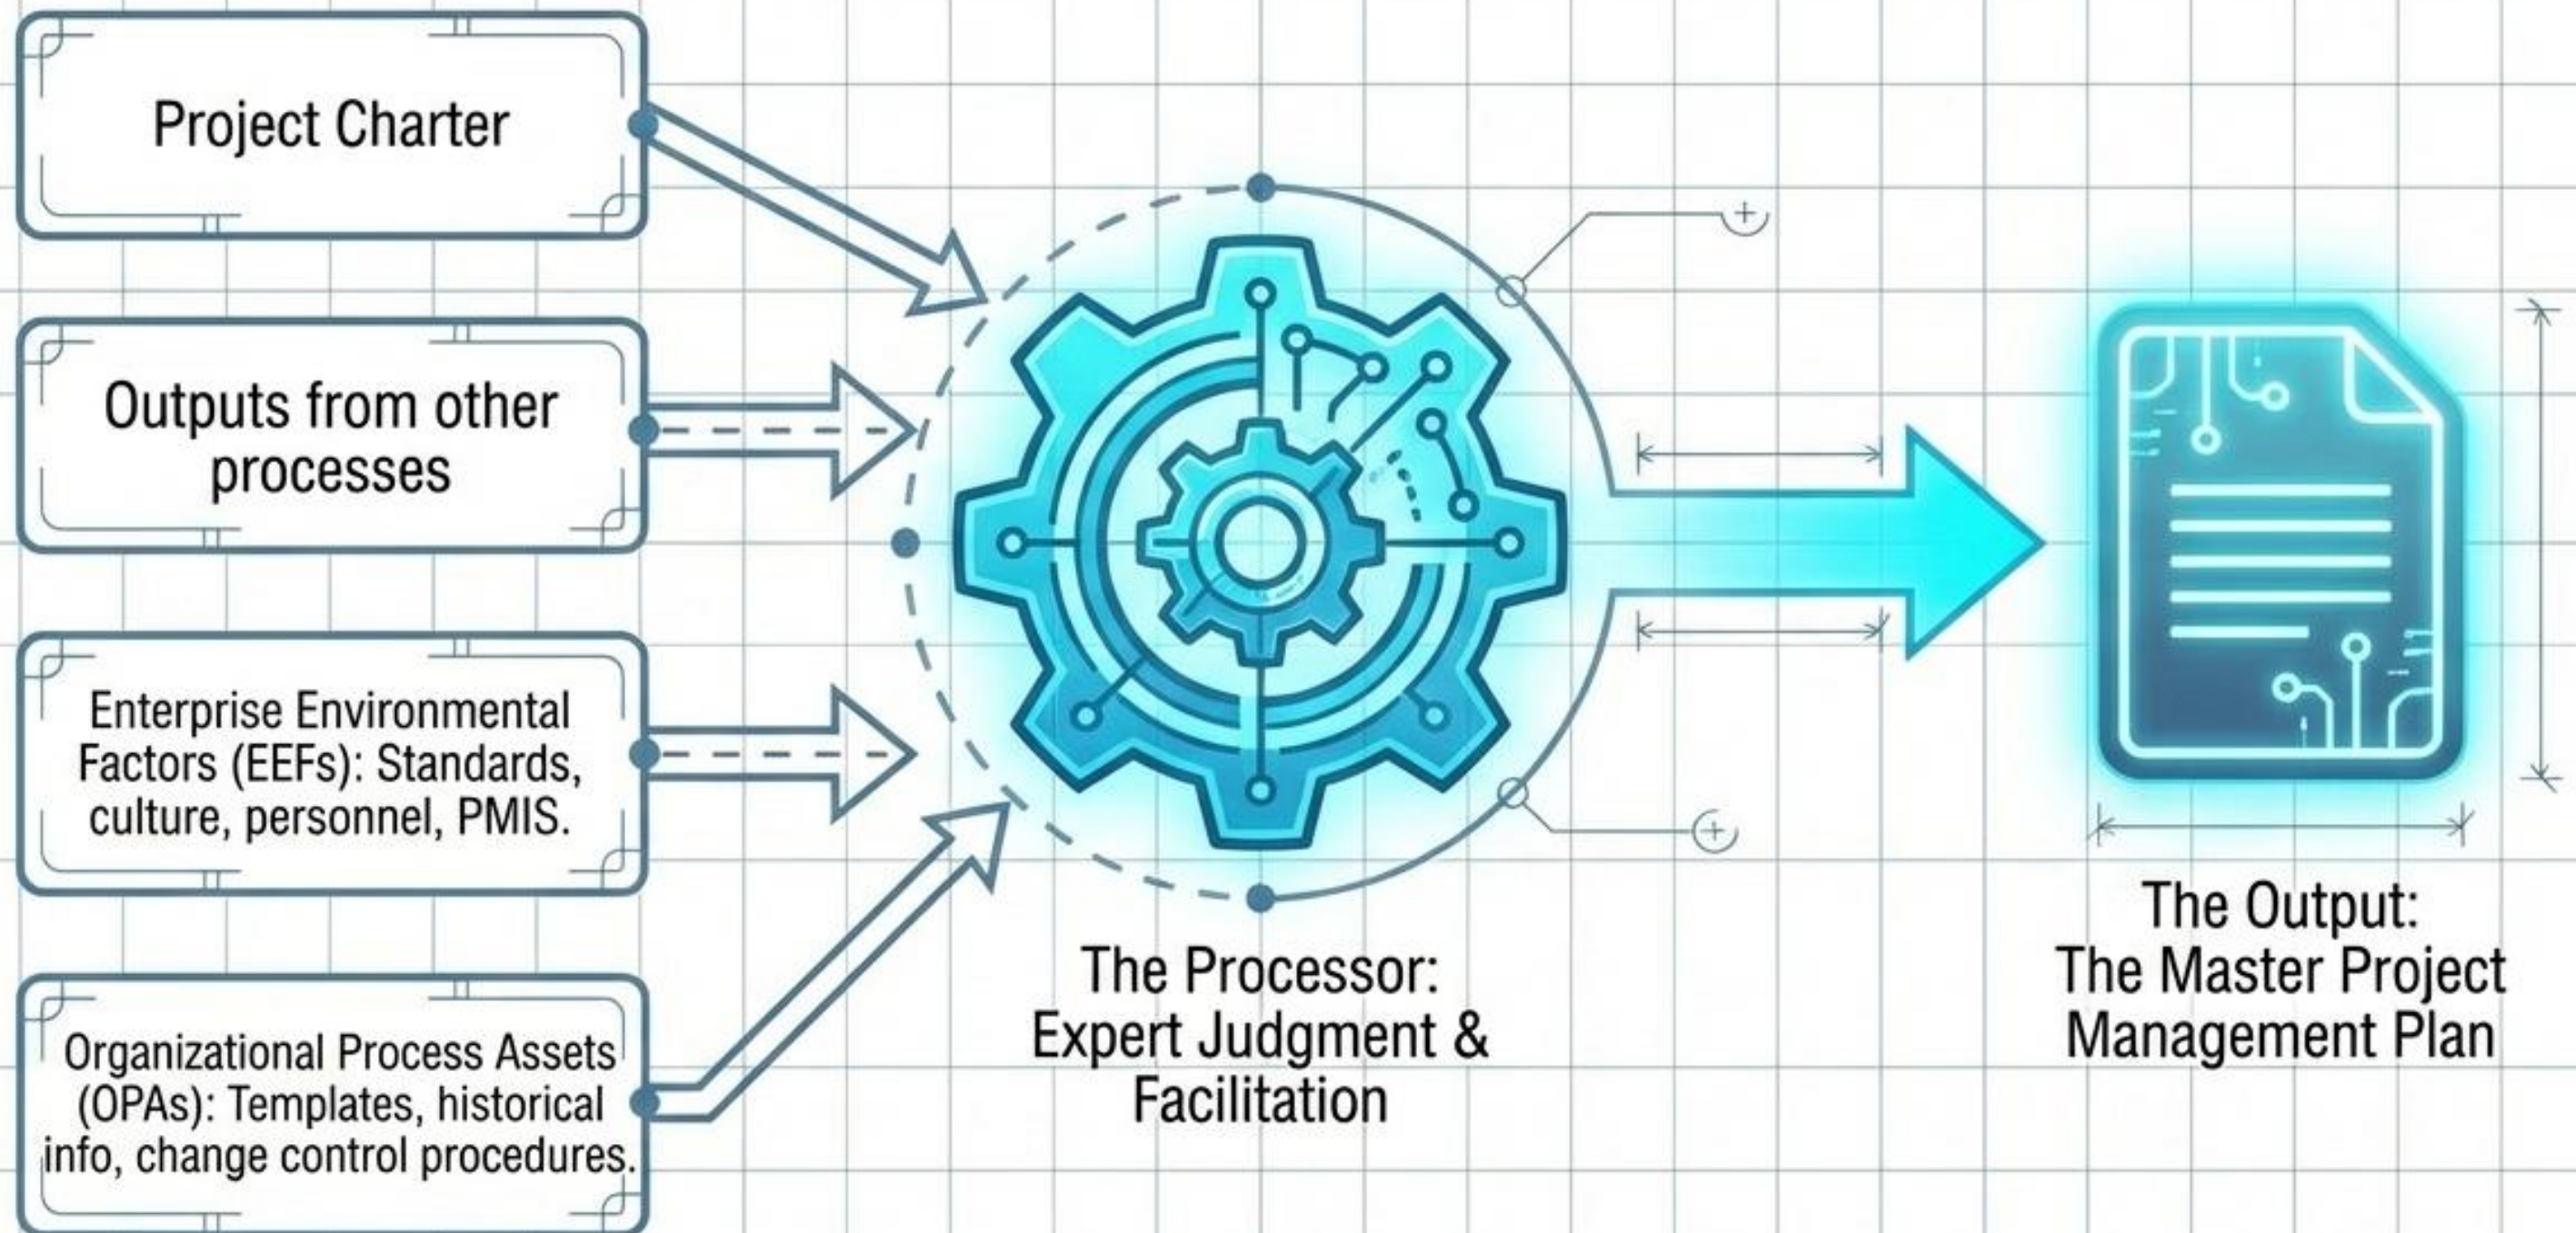


Anatomy of the Project Management Plan

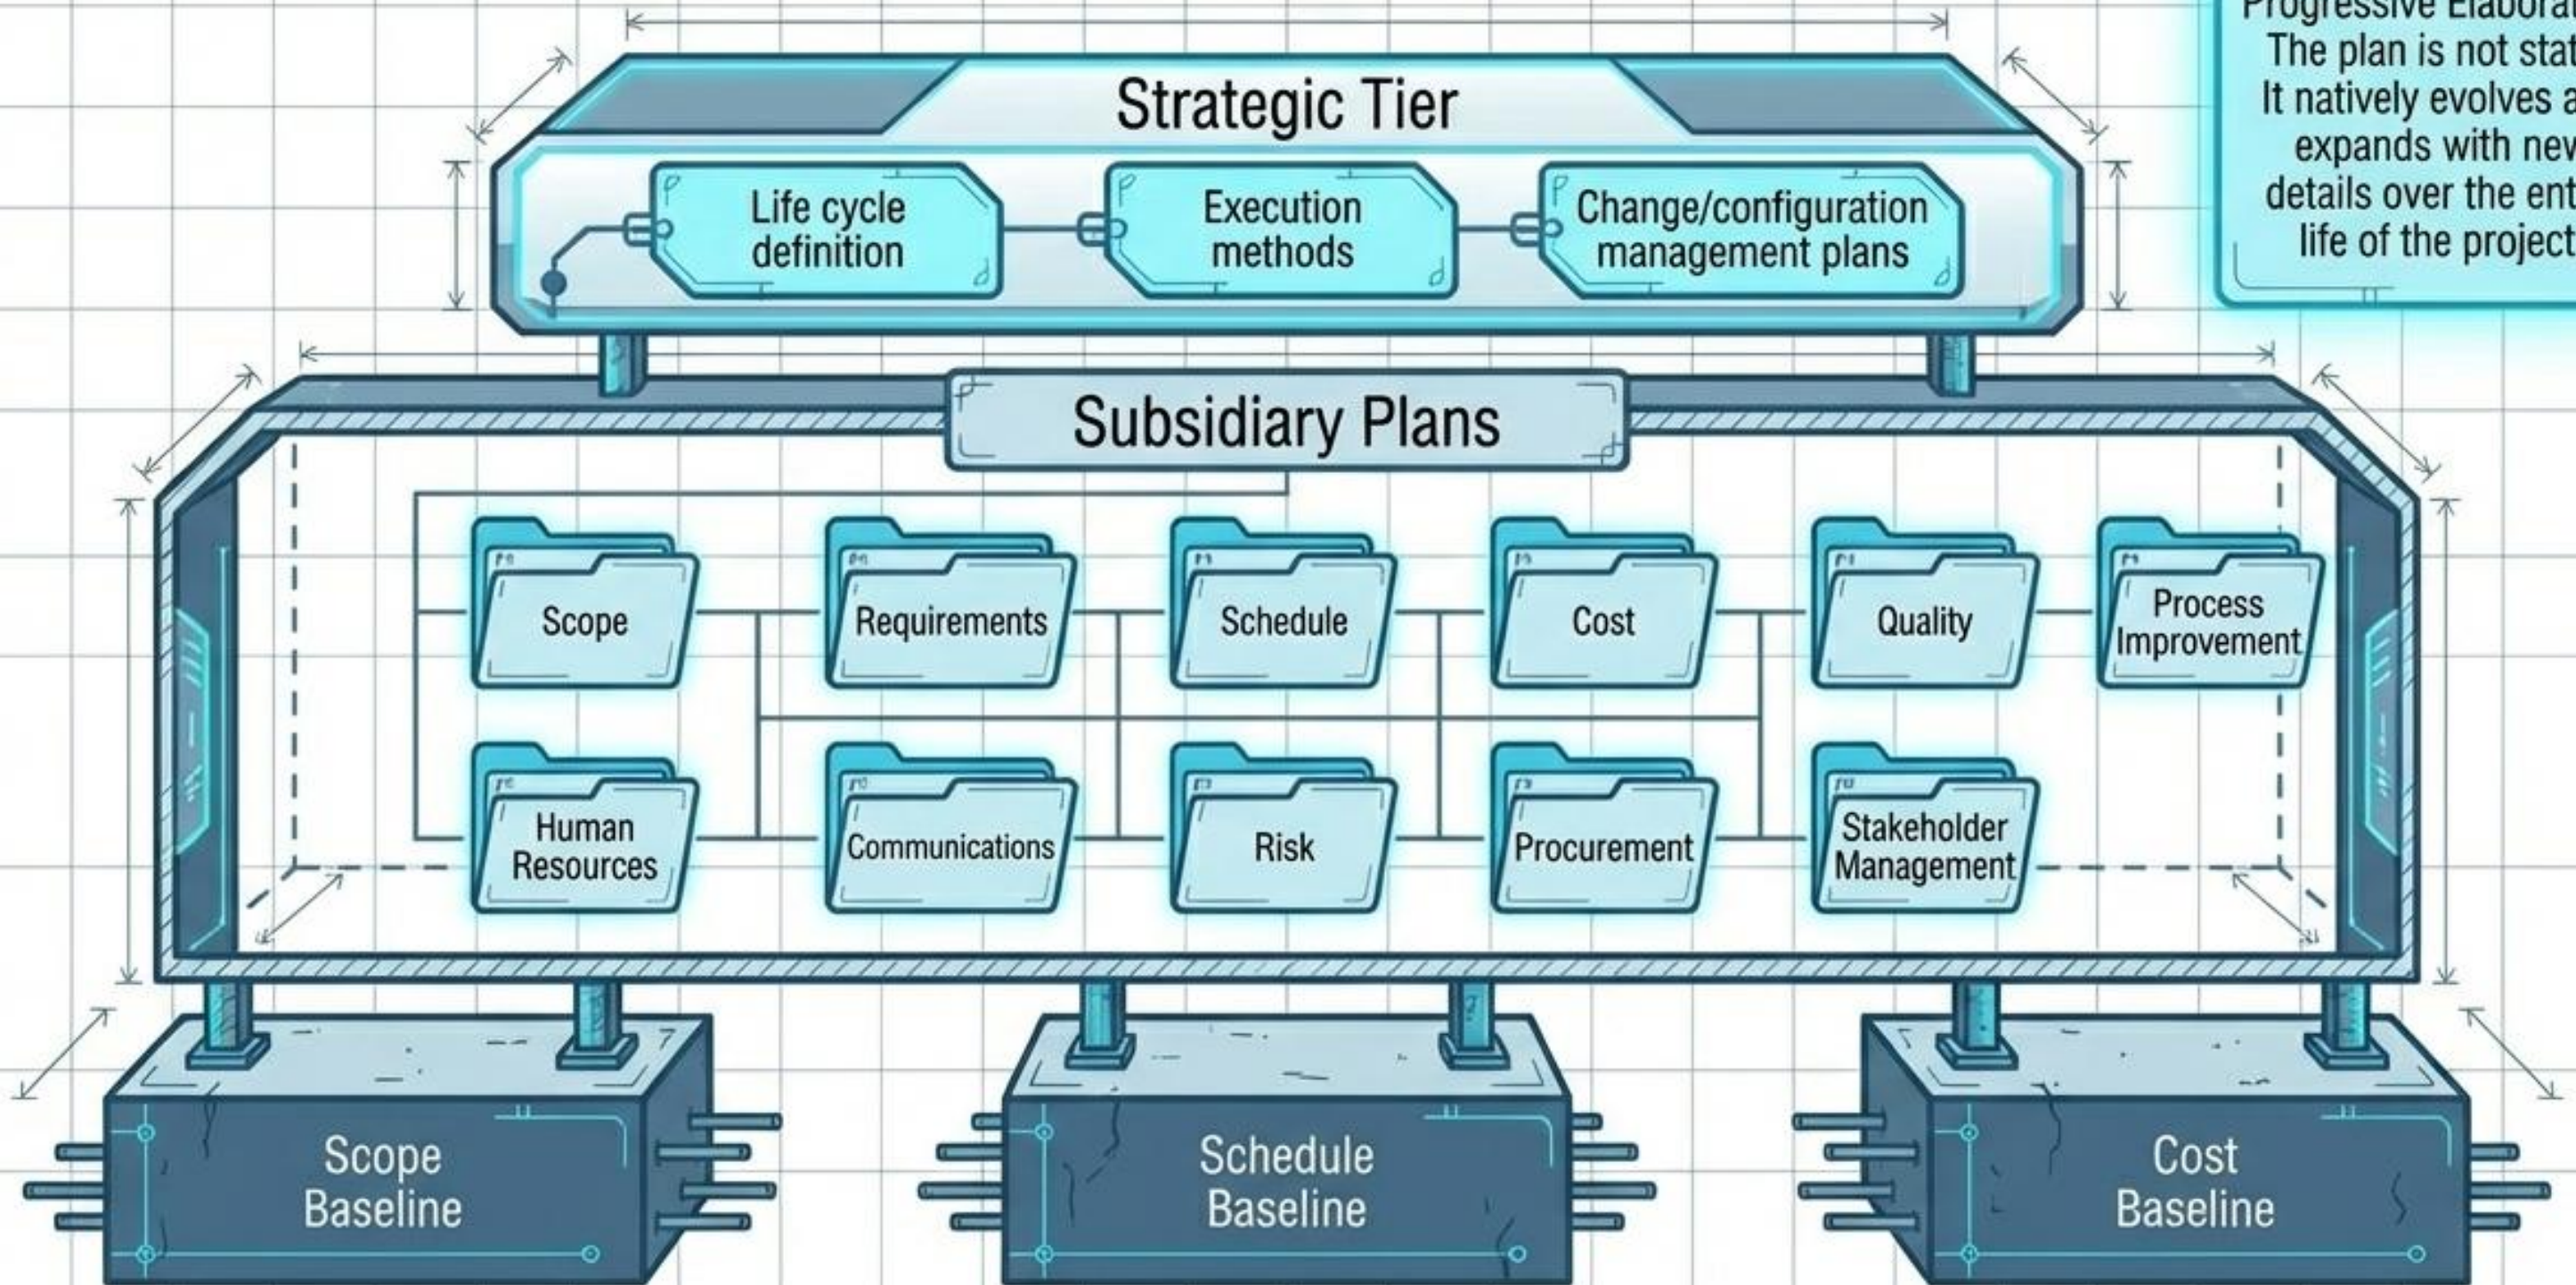

Key Insight

Progressive Elaboration:
The plan is not static. It natively evolves and expands with new details over the entire life of the project.

The PMIS & Configuration Management

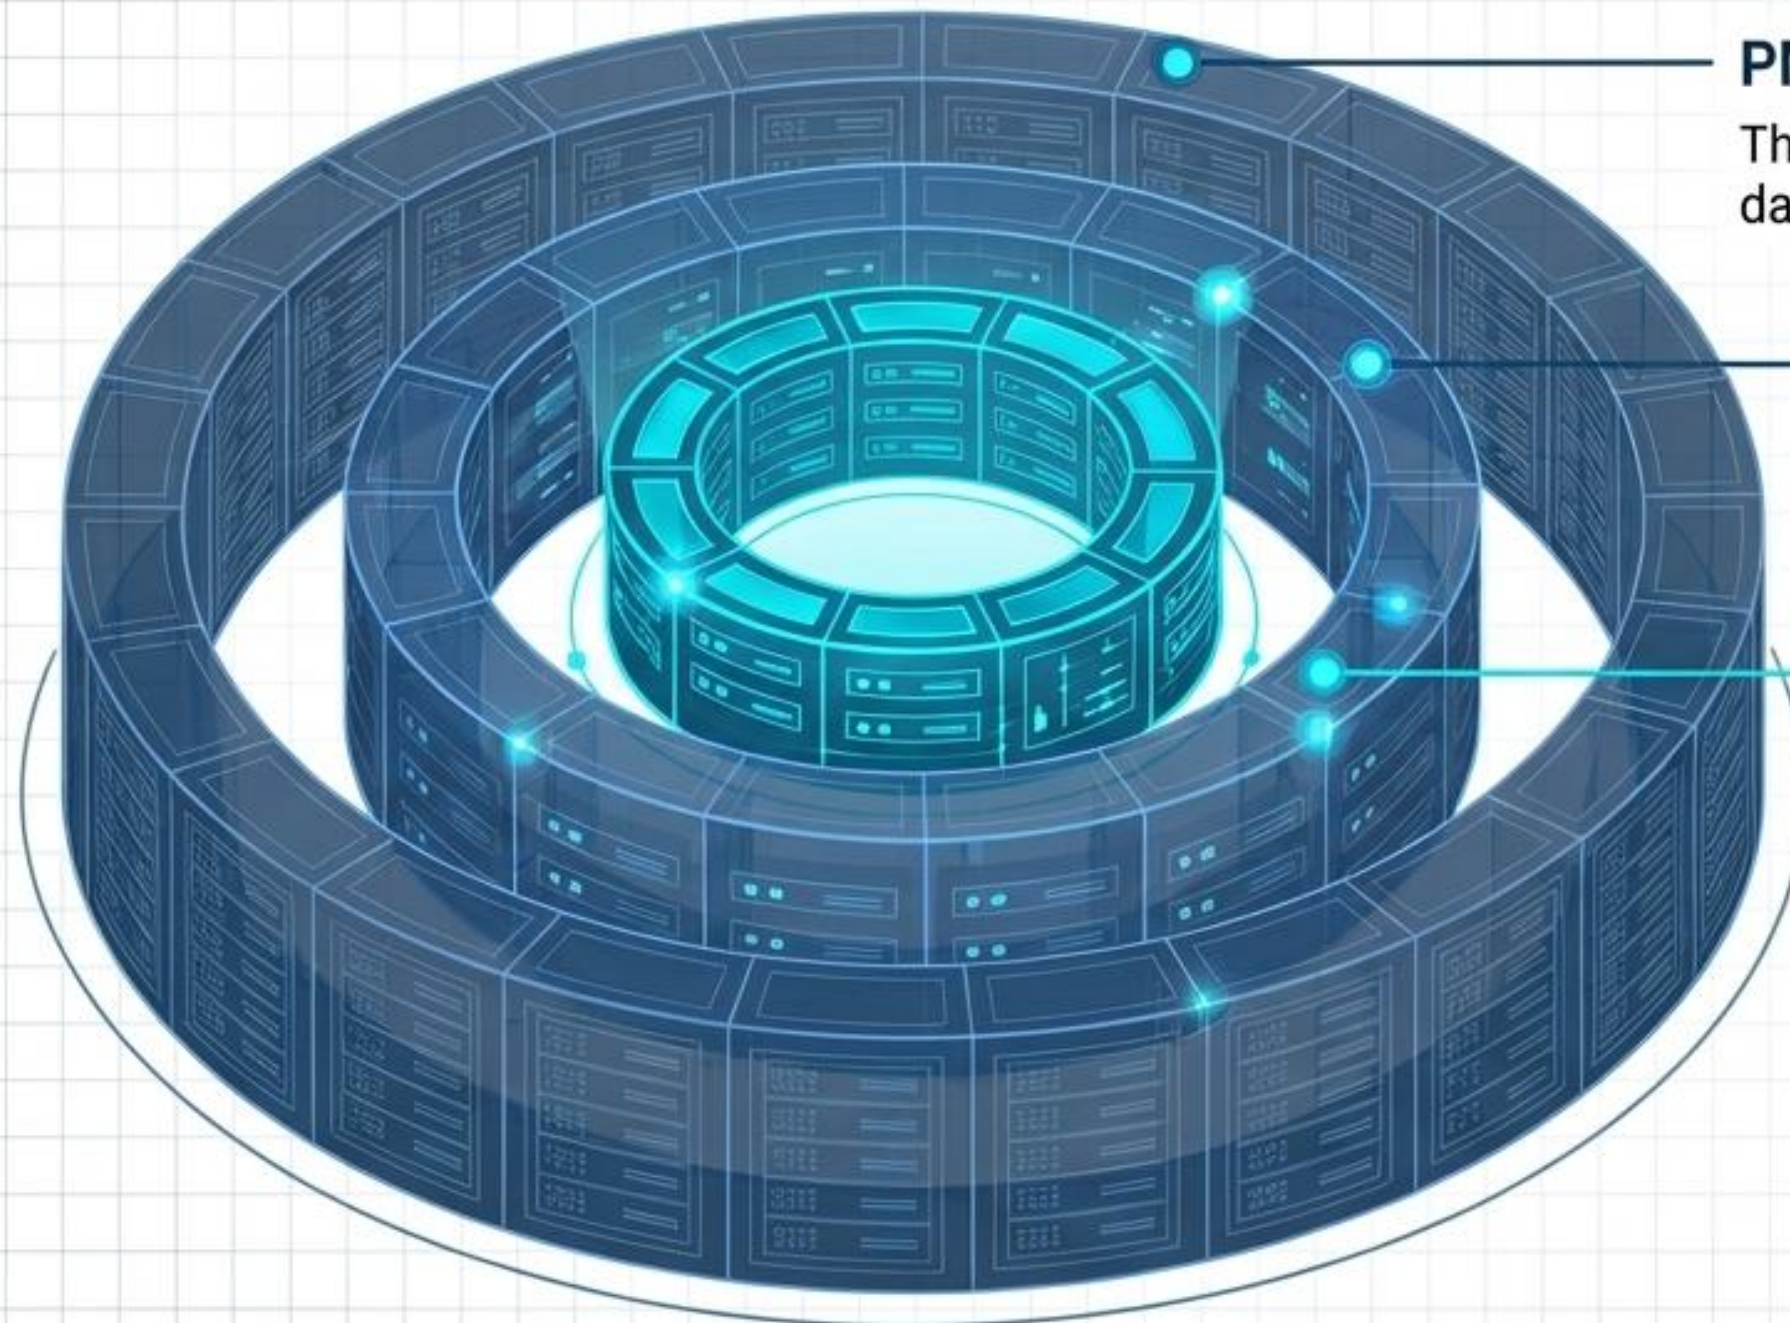

PMIS (Project Management Information System)

The overarching environment for automated/manual data collection, distribution, and document revision.

Configuration Management System

Contains official company policies, standards, and procedures.


Change Control System

The specific subsystem for evaluating and approving changes.



Exam Spotlight: Understand this exact hierarchy. The Change Control System is a subsystem of Configuration Management, which is completely nested within the PMIS.

Tailoring the Master Plan

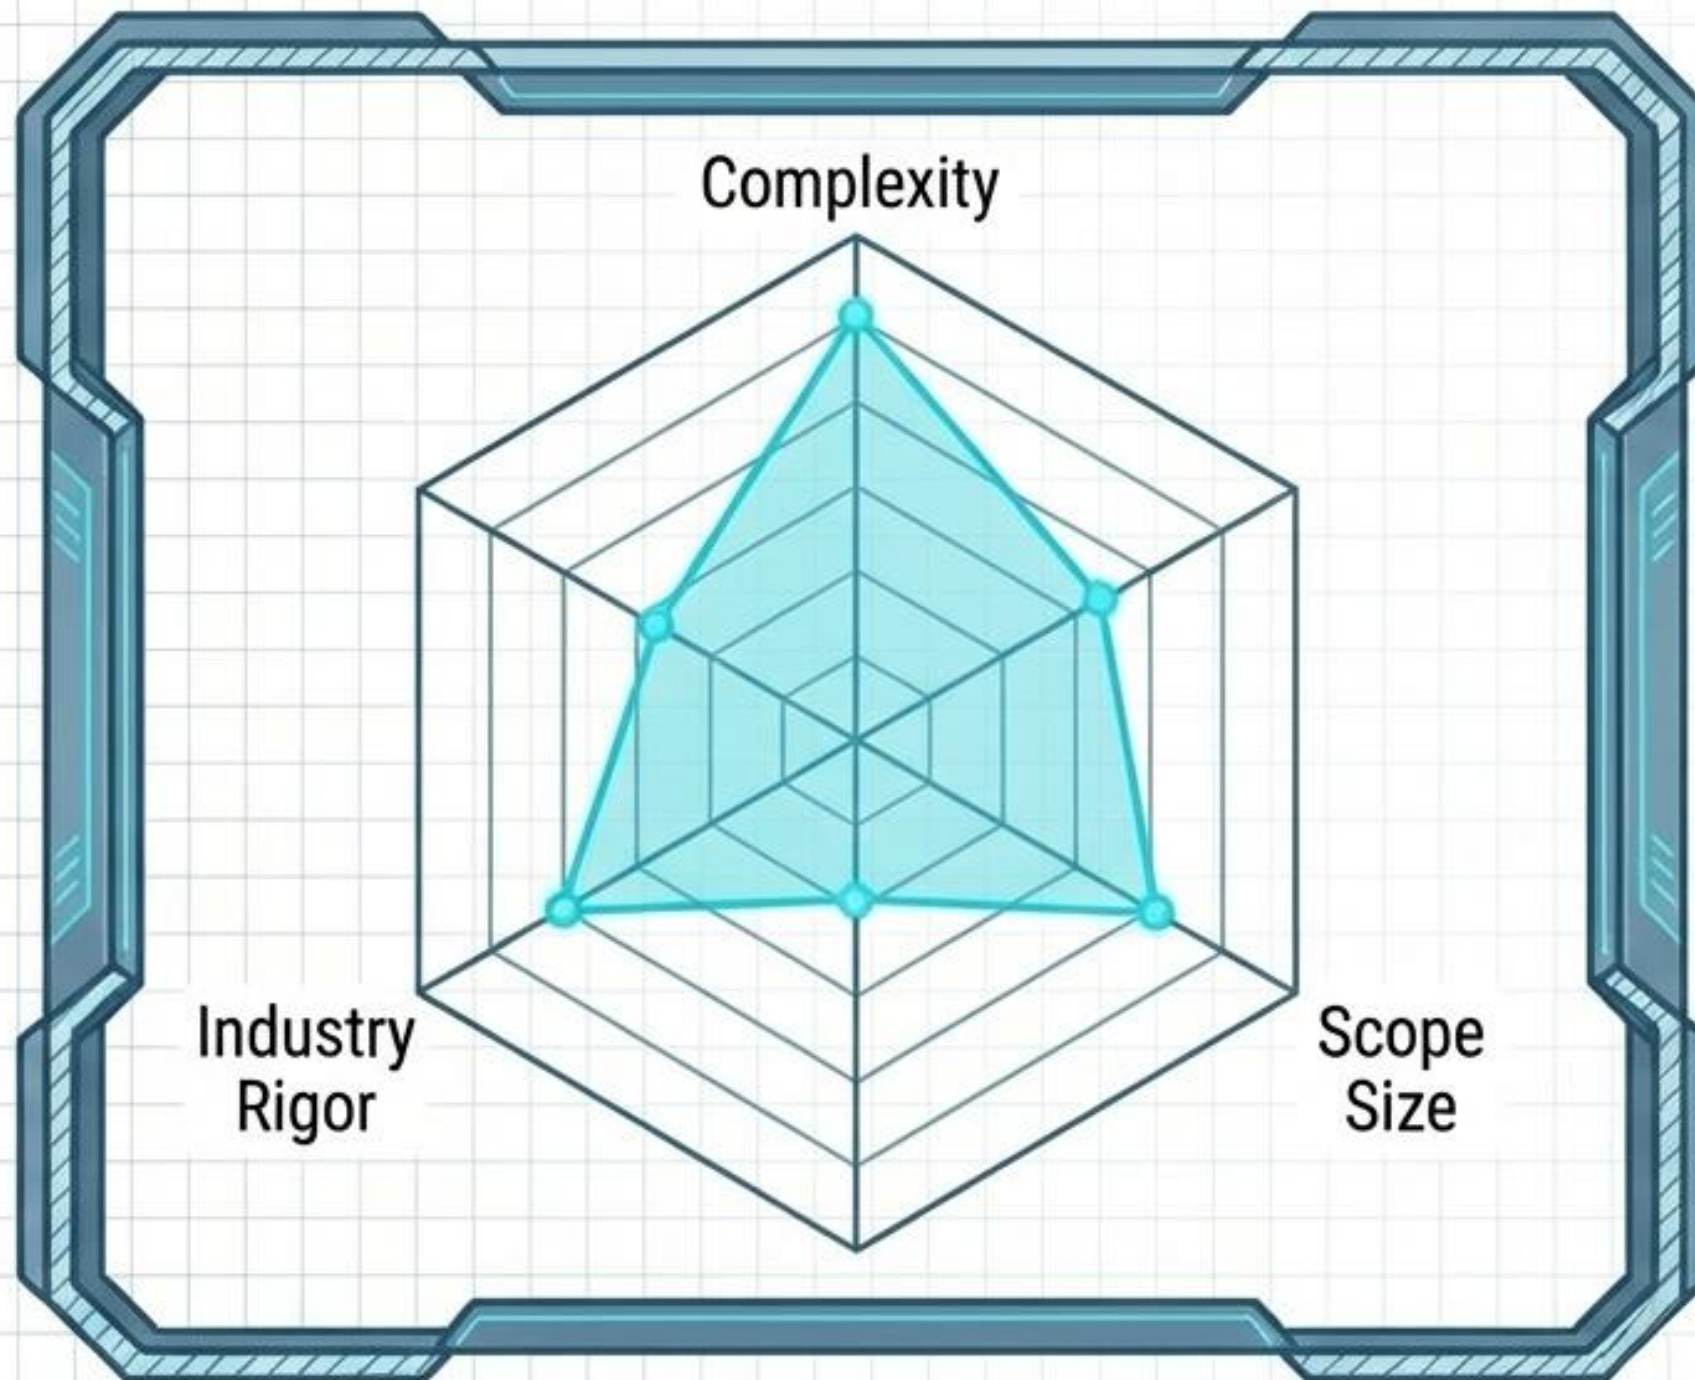


Tailoring the Master Plan:
The Project Management Plan is never one-size-fits-all.

The **specific processes** chosen depend heavily on the individual project's complexity, the overall scope, and organizational or industry standards.



Expert Judgment Tool: Used here to determine the exact level of configuration management and resource skills needed before locking in the plan.

Entering the Scope Knowledge Area

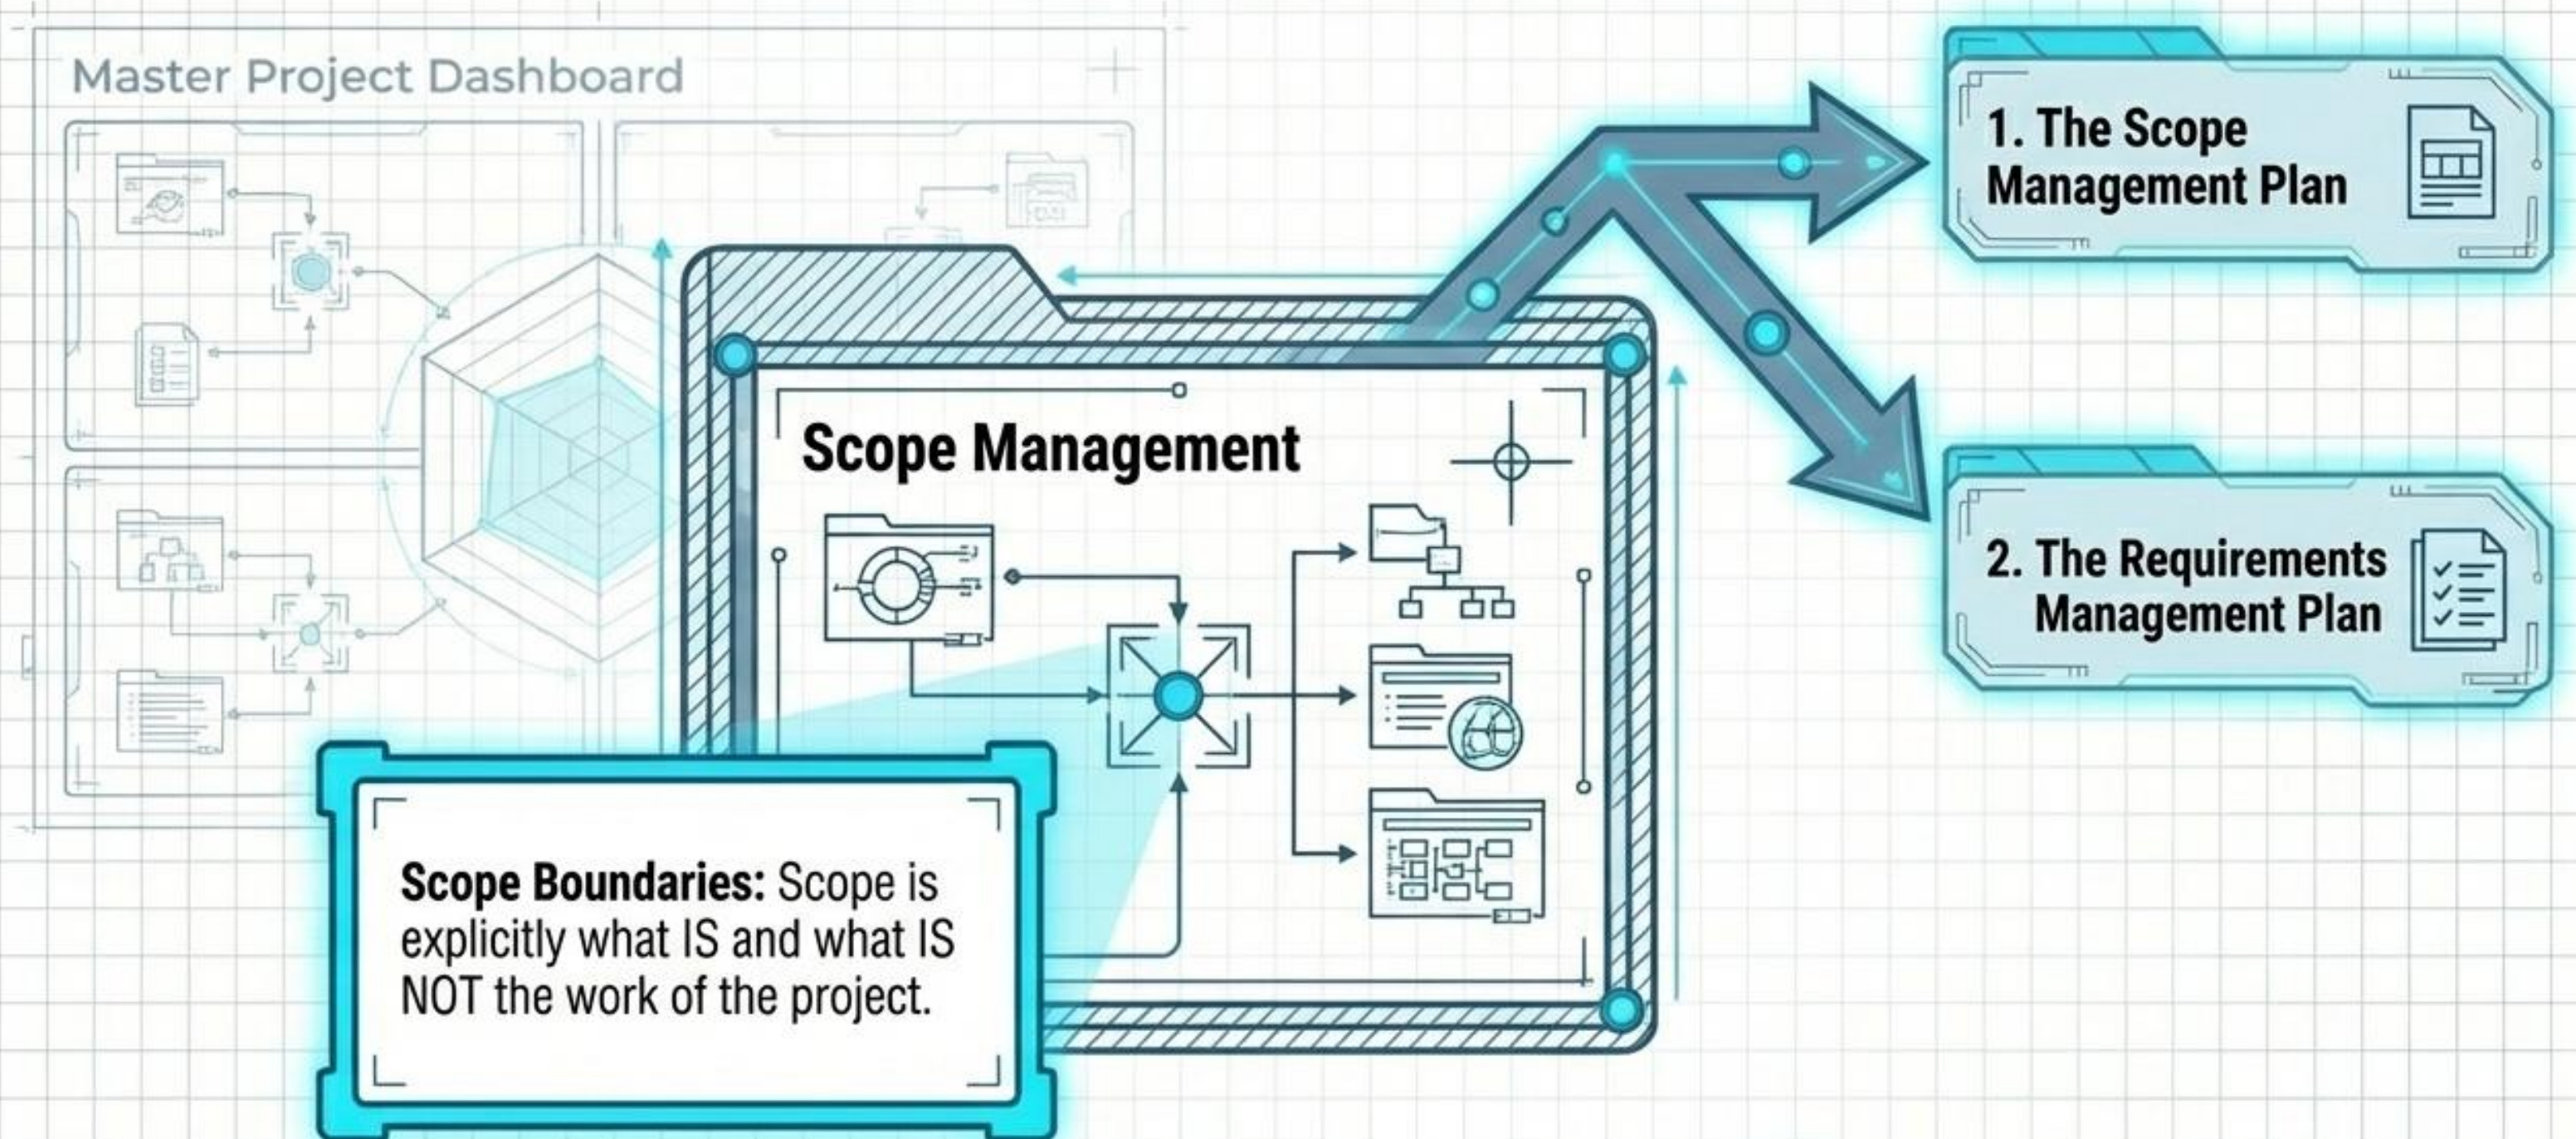

Comparison Matrix: Scope Plan vs. Requirements Plan

Scope Management Plan	Requirements Management Plan
Focus: The Deliverables .	Focus: The Stakeholder Needs .
Contents: Process for preparing the project scope statement, creating and maintaining the WBS, verifying deliverables for accuracy, and controlling scope change requests.	Contents: How requirements will be analyzed, documented, prioritized, traced, and tracked throughout the project. Includes the specific metrics used to trace product requirements.

Environmental & Organizational Influences on Scope

The Threat: EEFs



Personnel administration, informal culture, and “coffee-break scope creep.”

The Solution: OPAs & Planning



Historical data and formal policies strictly guiding the plan.



Real World Scenario

The Phil Reid Case: Phil is a gifted accident reconstructionist but lacks oral communication skills. A tailored Scope Management Plan requires clients to pre-define the output format and testimony requirements so Phil's organization can assign a supplementary communicator. Unmanaged environments lead to unmanaged scope!


Phase-to-Phase Relationships & Requirements

Sequential Relationship



Rule: Phase 1 strictly finishes before Phase 2 begins. All project requirements must be perfectly defined upfront before work commences.


Overlapping Relationship

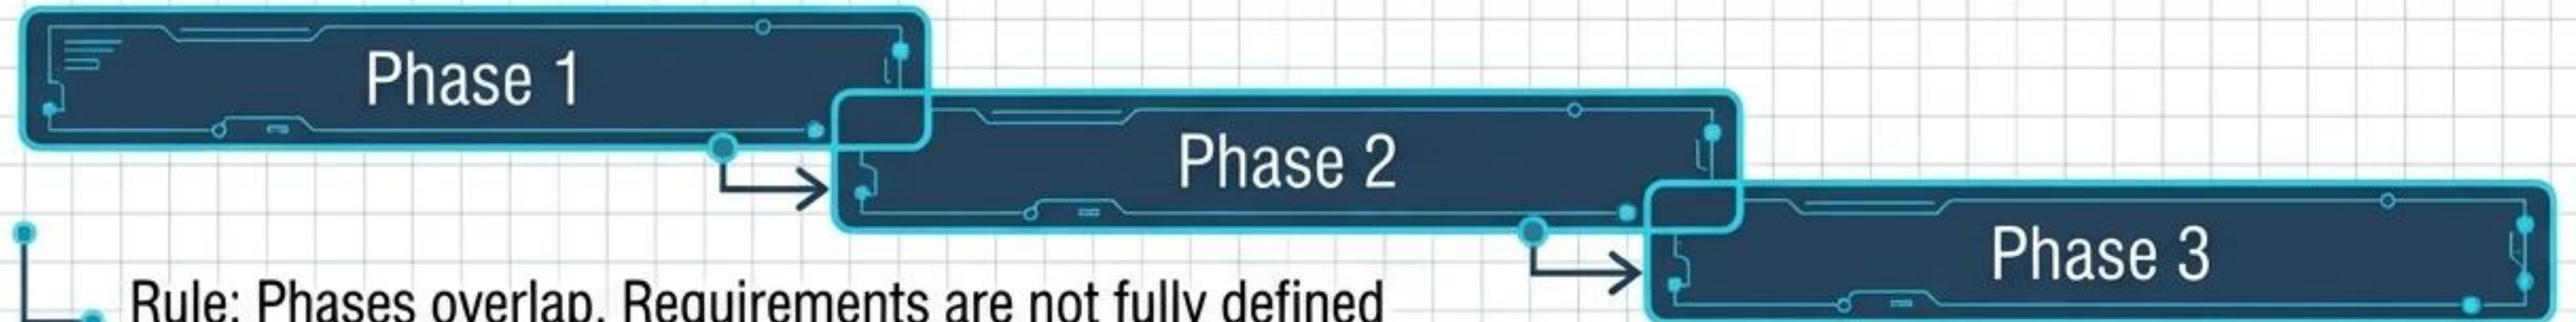

Rule: Phases overlap. Requirements are not fully defined before work begins and are progressively elaborated.

Key Takeaway: The chosen phase-to-phase relationship fundamentally dictates how requirements will be managed and must be explicitly documented in the Requirements Management Plan.

Collect Requirements: From Planning to Action

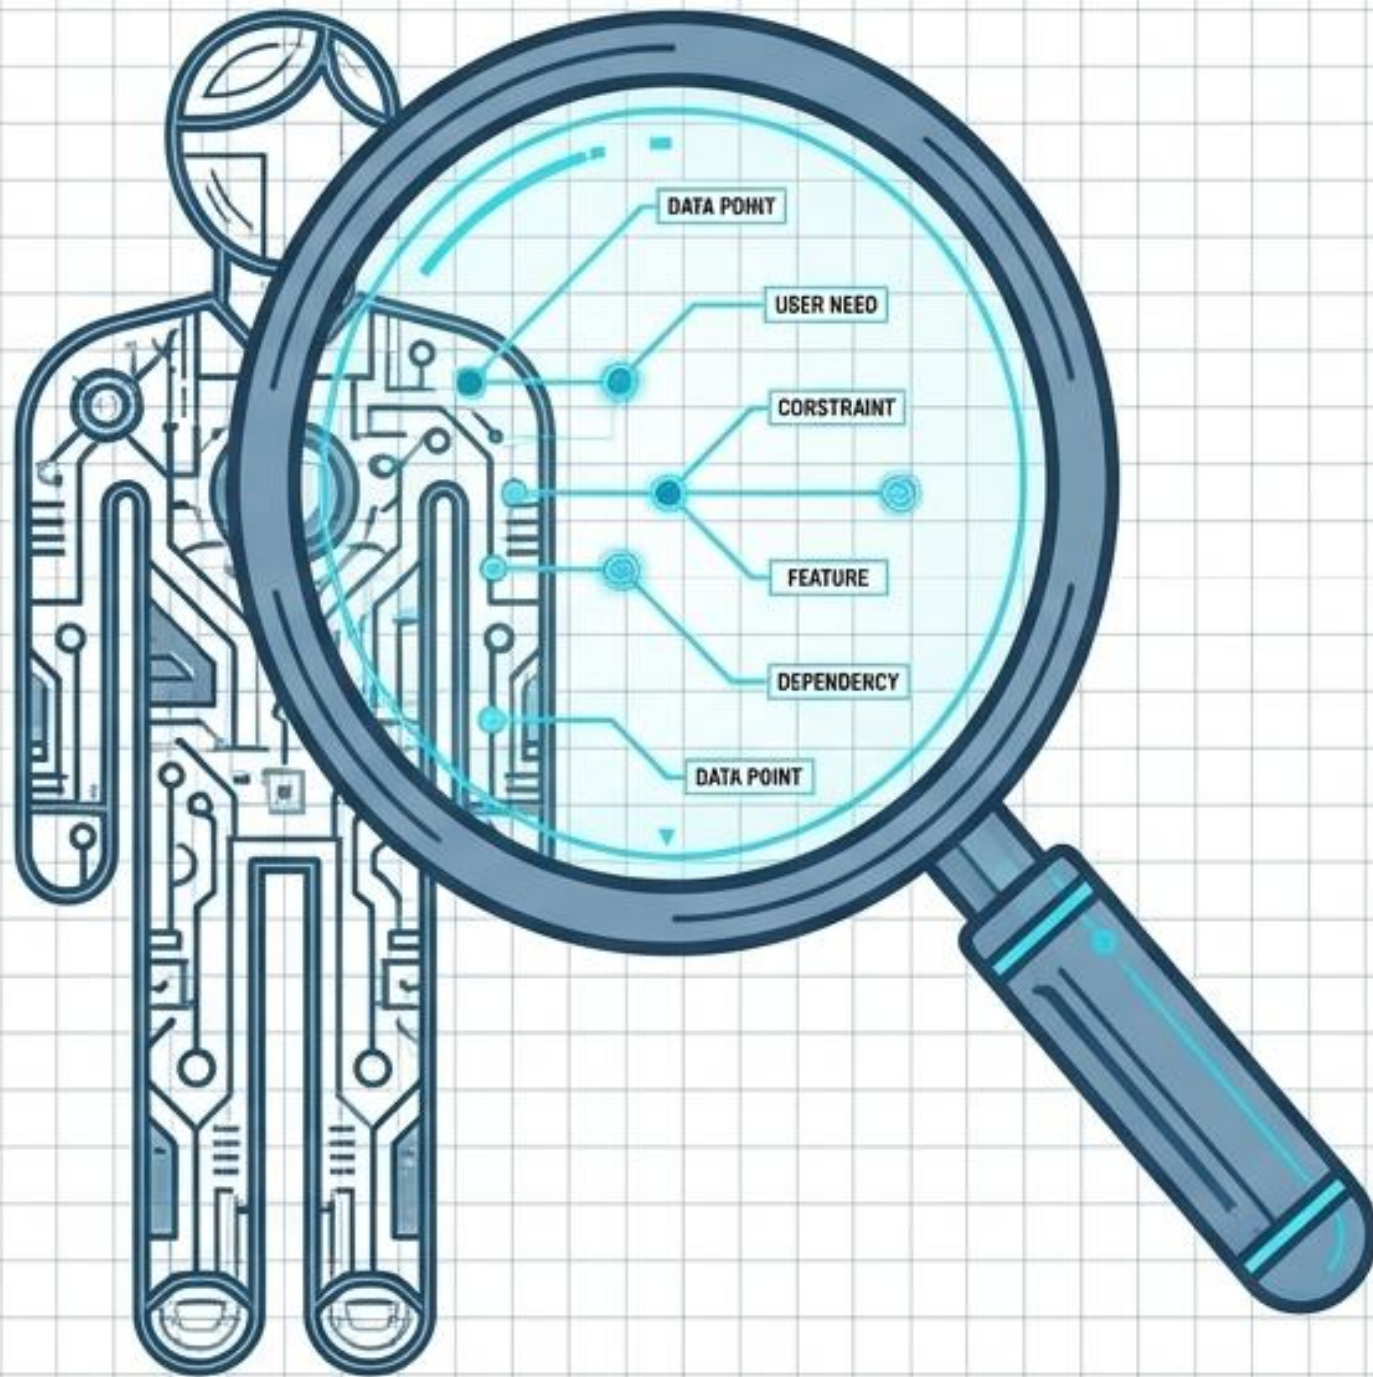


Shifting focus: From HOW we will manage to defining WHAT the deliverables will actually look like.

The Golden Rule of Requirements

- ☒ 1. Measurable
- ☒ 2. Traceable
- ☒ 3. Testable
- ☒ 4. Complete
- ☒ 5. Accepted by the sponsor/stakeholders

The Requirements Taxonomy

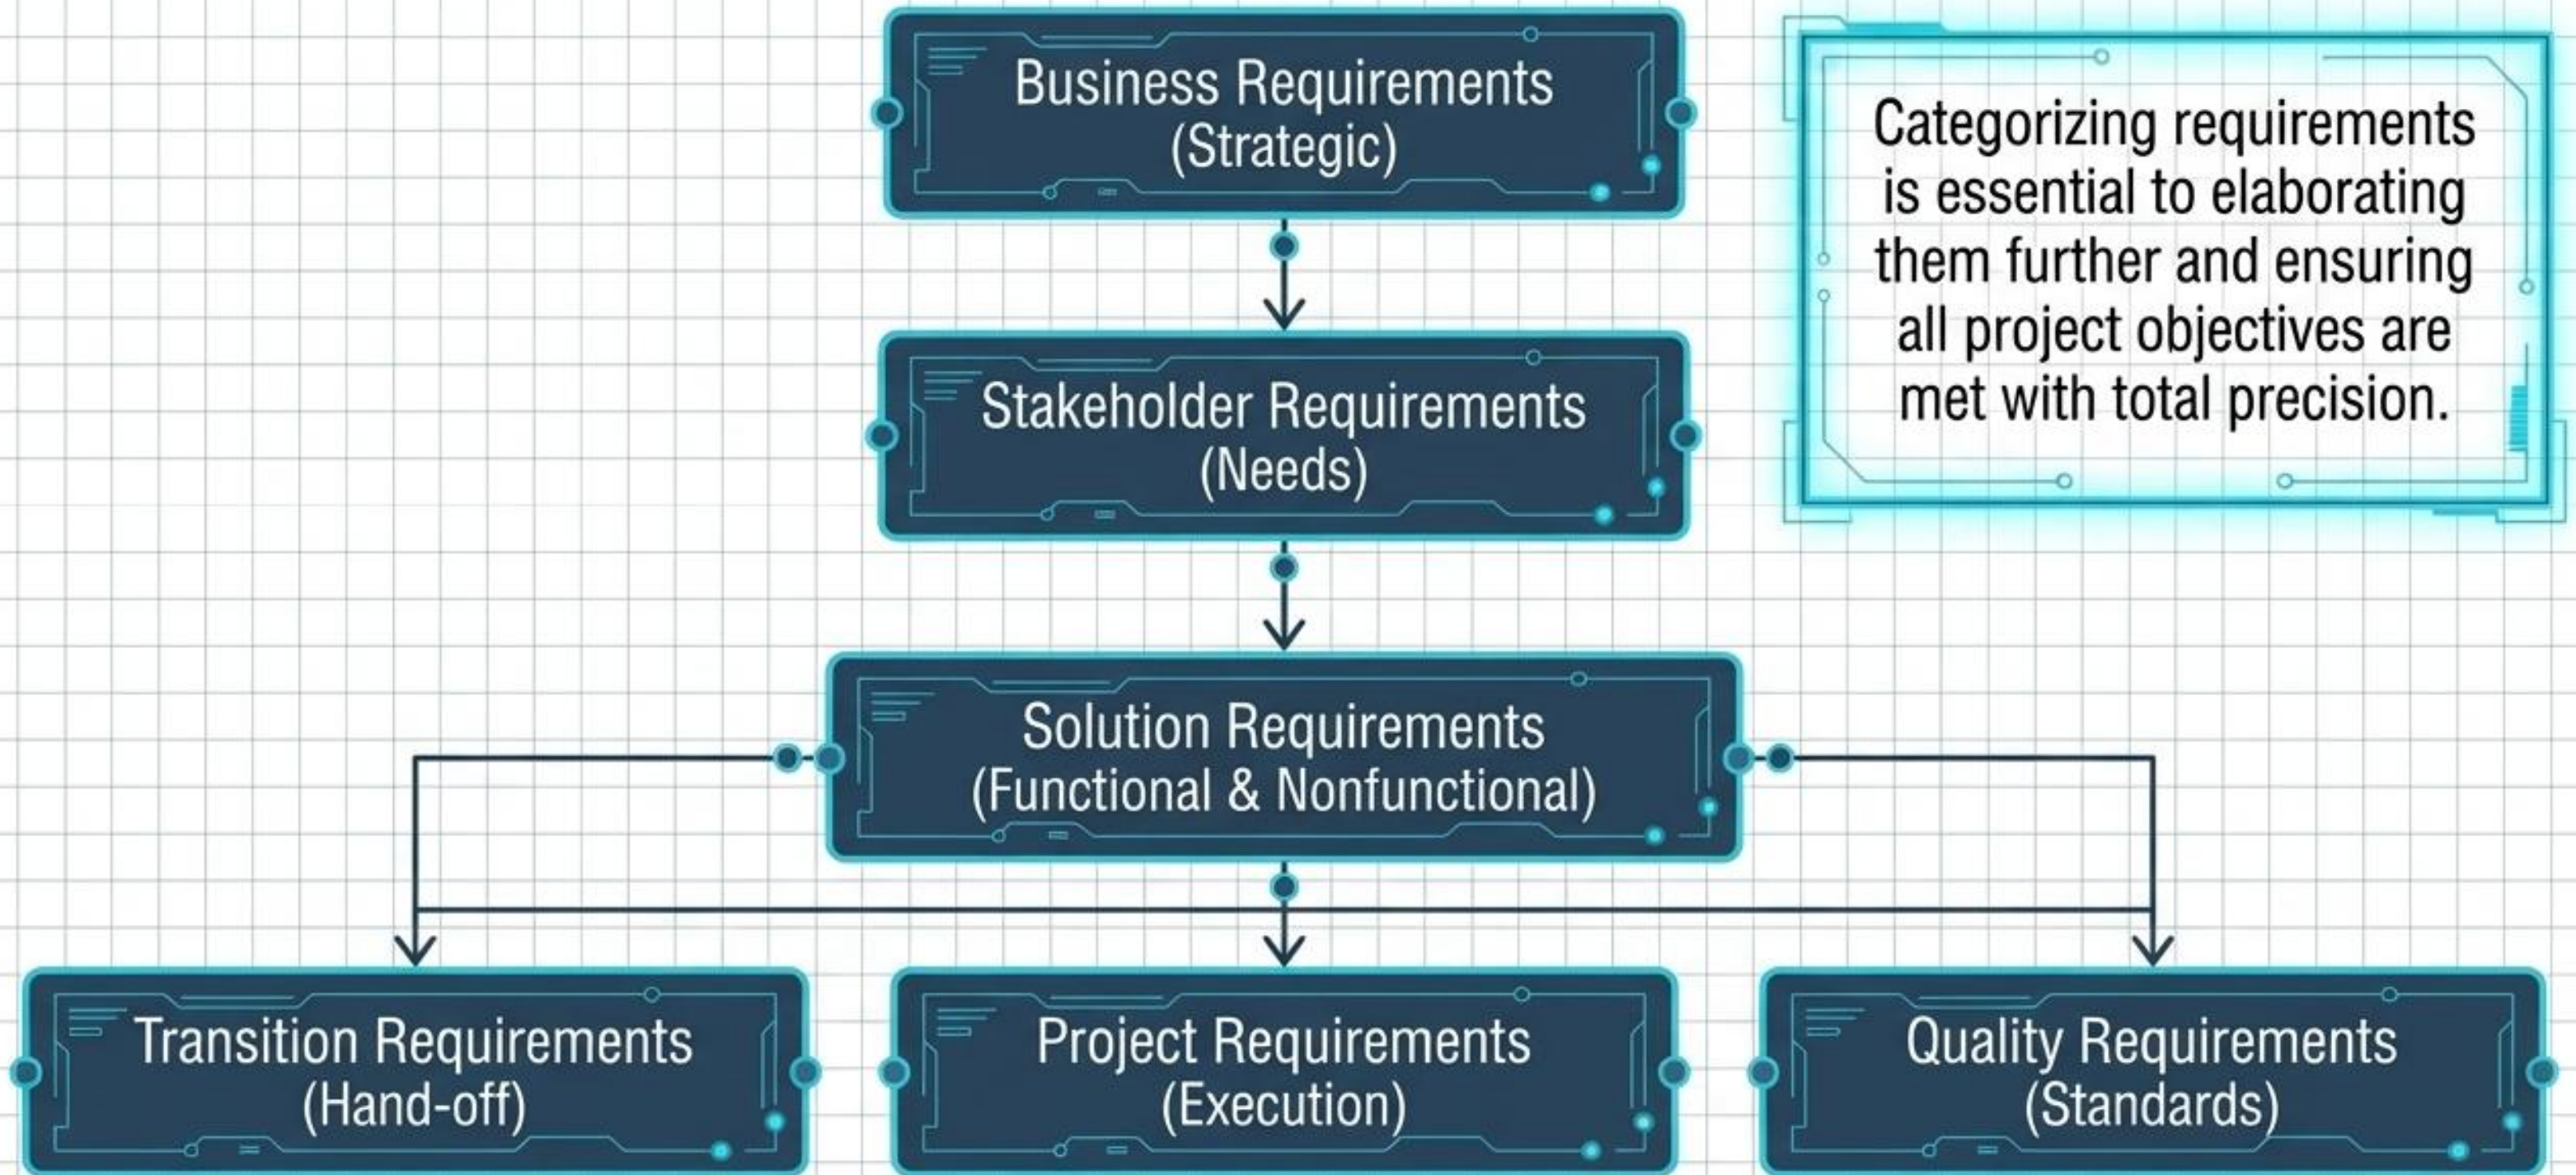


Tracing and Prioritization

Why We Trace


Ensures every captured requirement actively adds business value and links back to the project objectives.

Tracks requirements through the lifecycle using specific metrics and attributes.

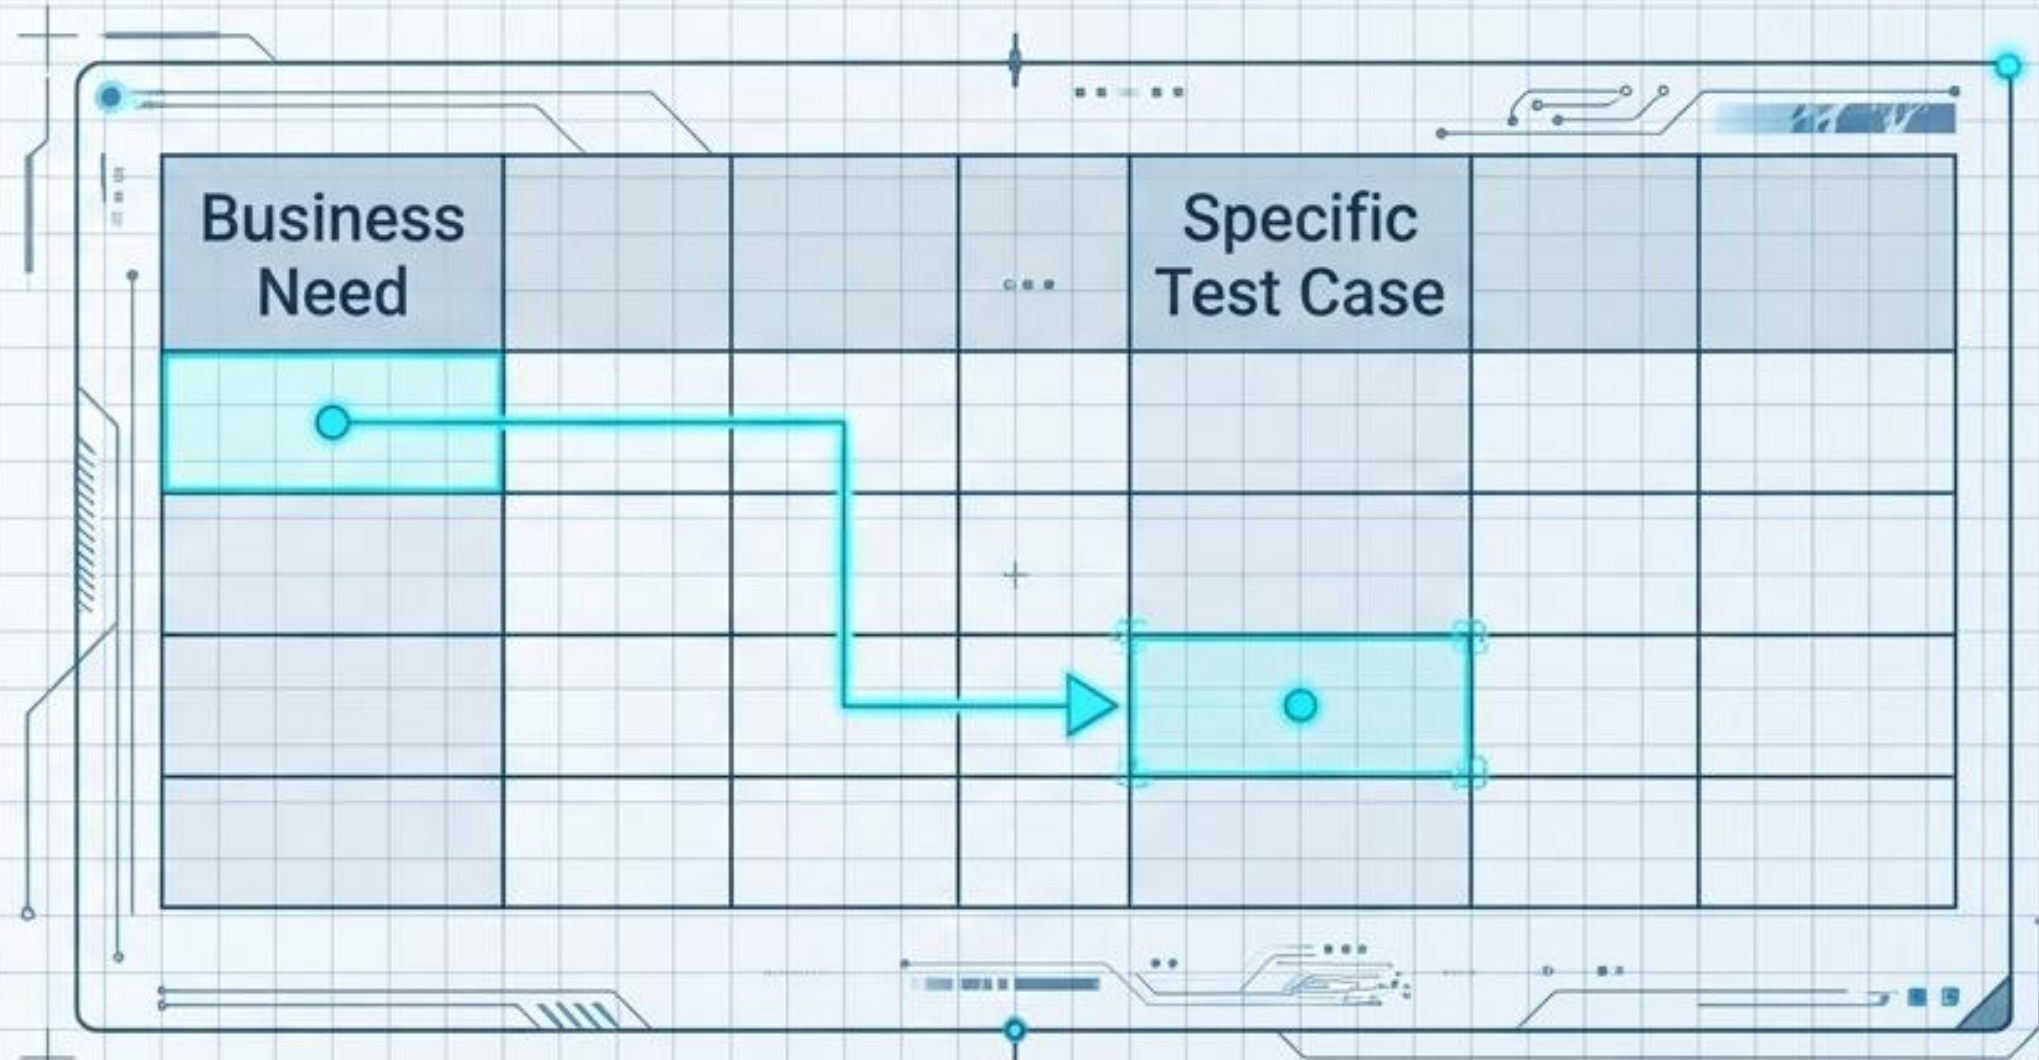

Critical Note: Not all gathered requirements make it into the final project! The subsequent Define Scope process will rigorously filter this list to determine the ultimate project deliverables.

Synthesis: The Scope Ecosystem

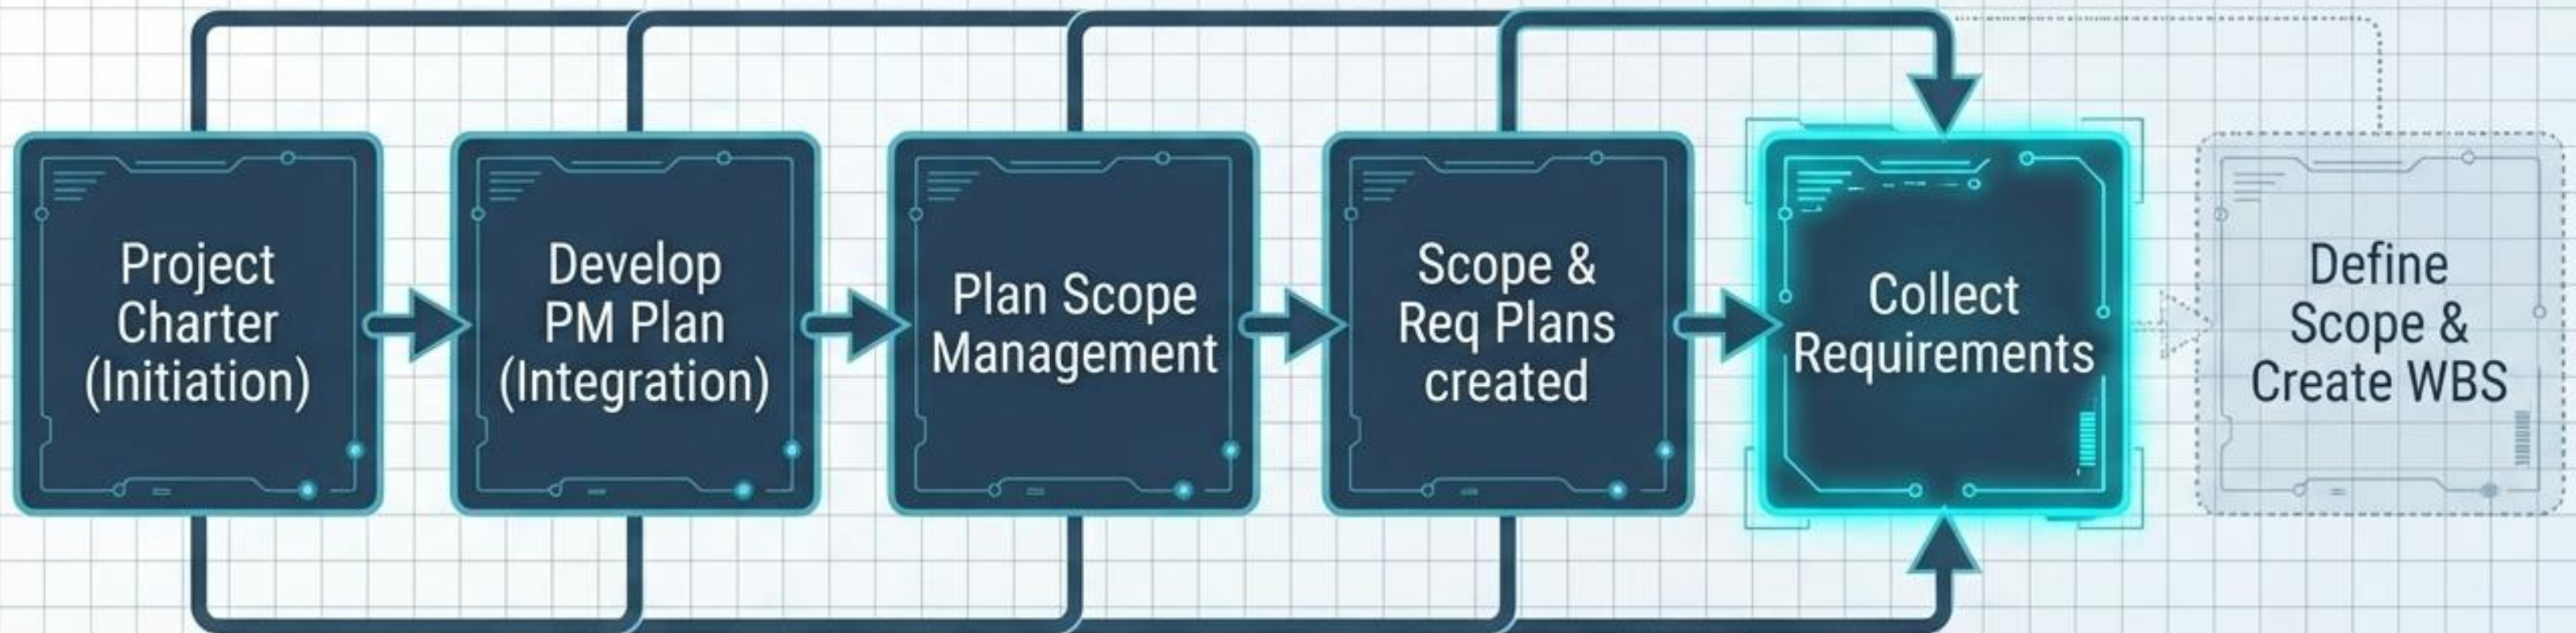

Data is progressively elaborated in an unbroken, logical chain—moving from high-level initiation down to granular, testable specifications.


The PMP Consultant's Cheat Sheet

Dashboard Summary



The Master Plan

- Integrates all subsidiary plans.
- Defines execution, monitoring, and closing.
- Progressively elaborated using Expert Judgment.



The Scope

- Defines rigid boundaries.
- Clarifies exactly what IS and IS NOT the work.
- Essential defense against scope creep.



The Requirements

- Quantifies stakeholder expectations.
- Spans from business needs to specific functional solutions.
- Must be strictly measurable, testable, and traceable.
