



Certyfikat PMP: Project Requirements Document

dr Zbigniew Galar

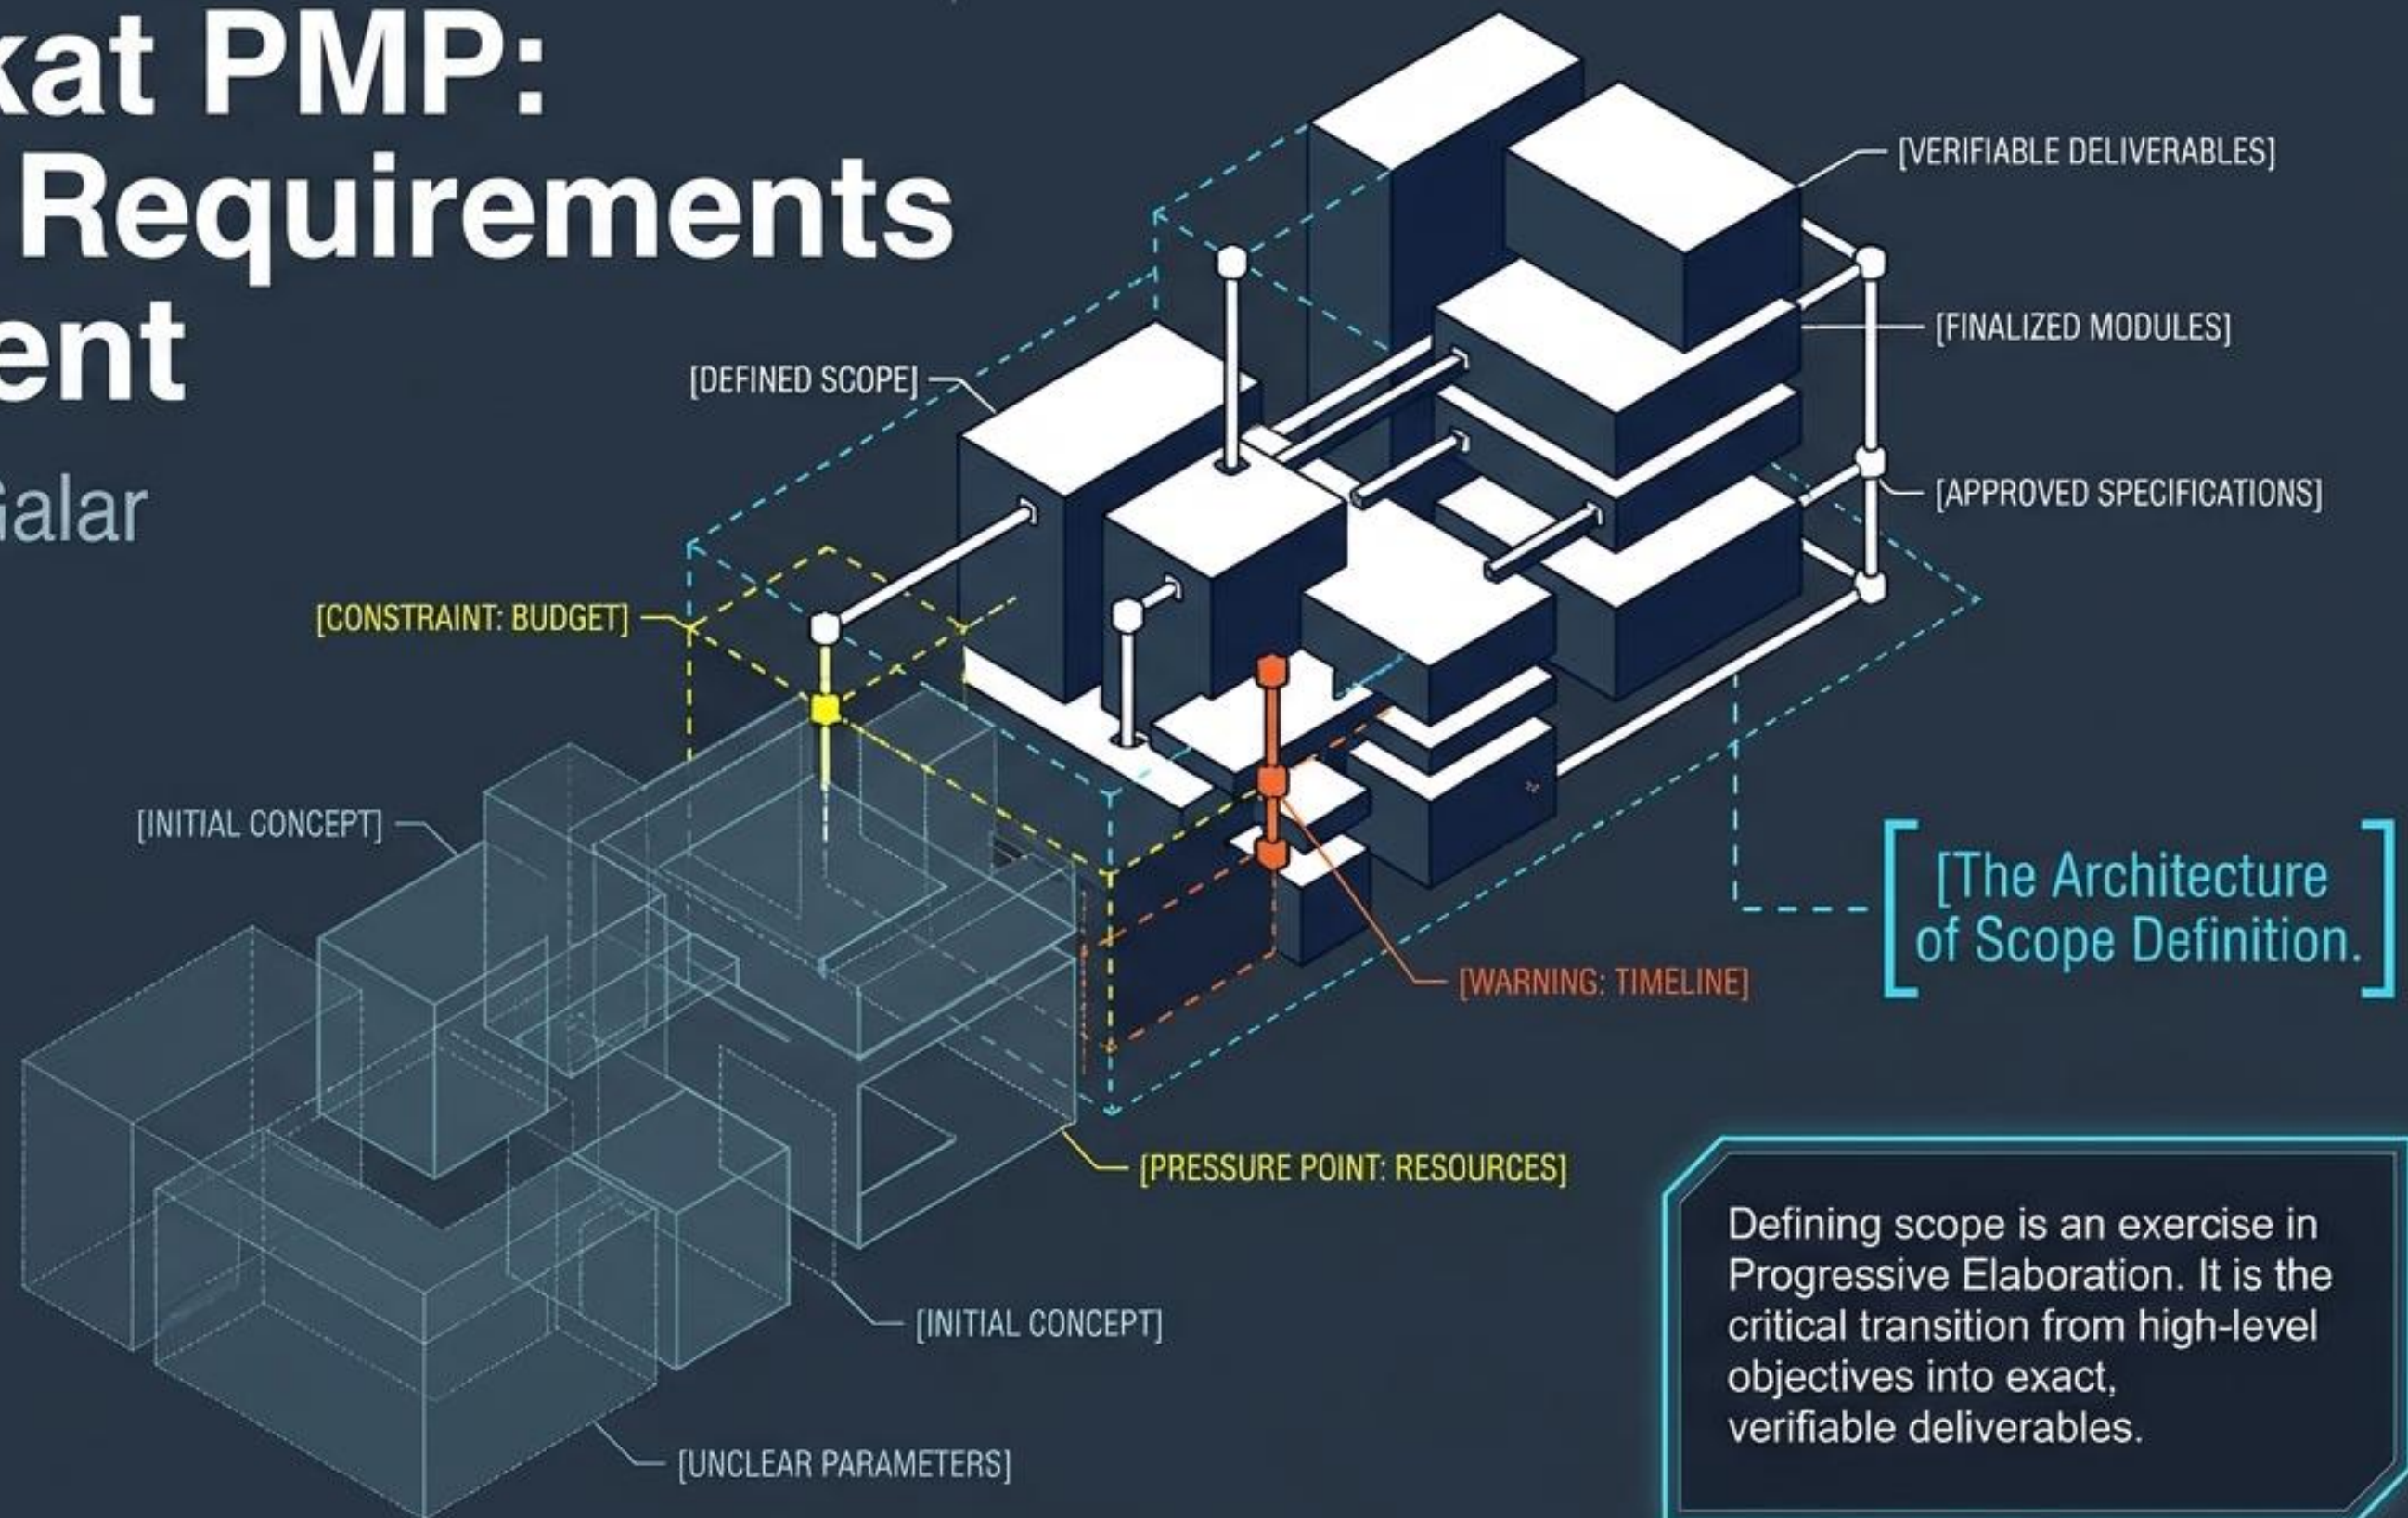

The Scope Definition Engine

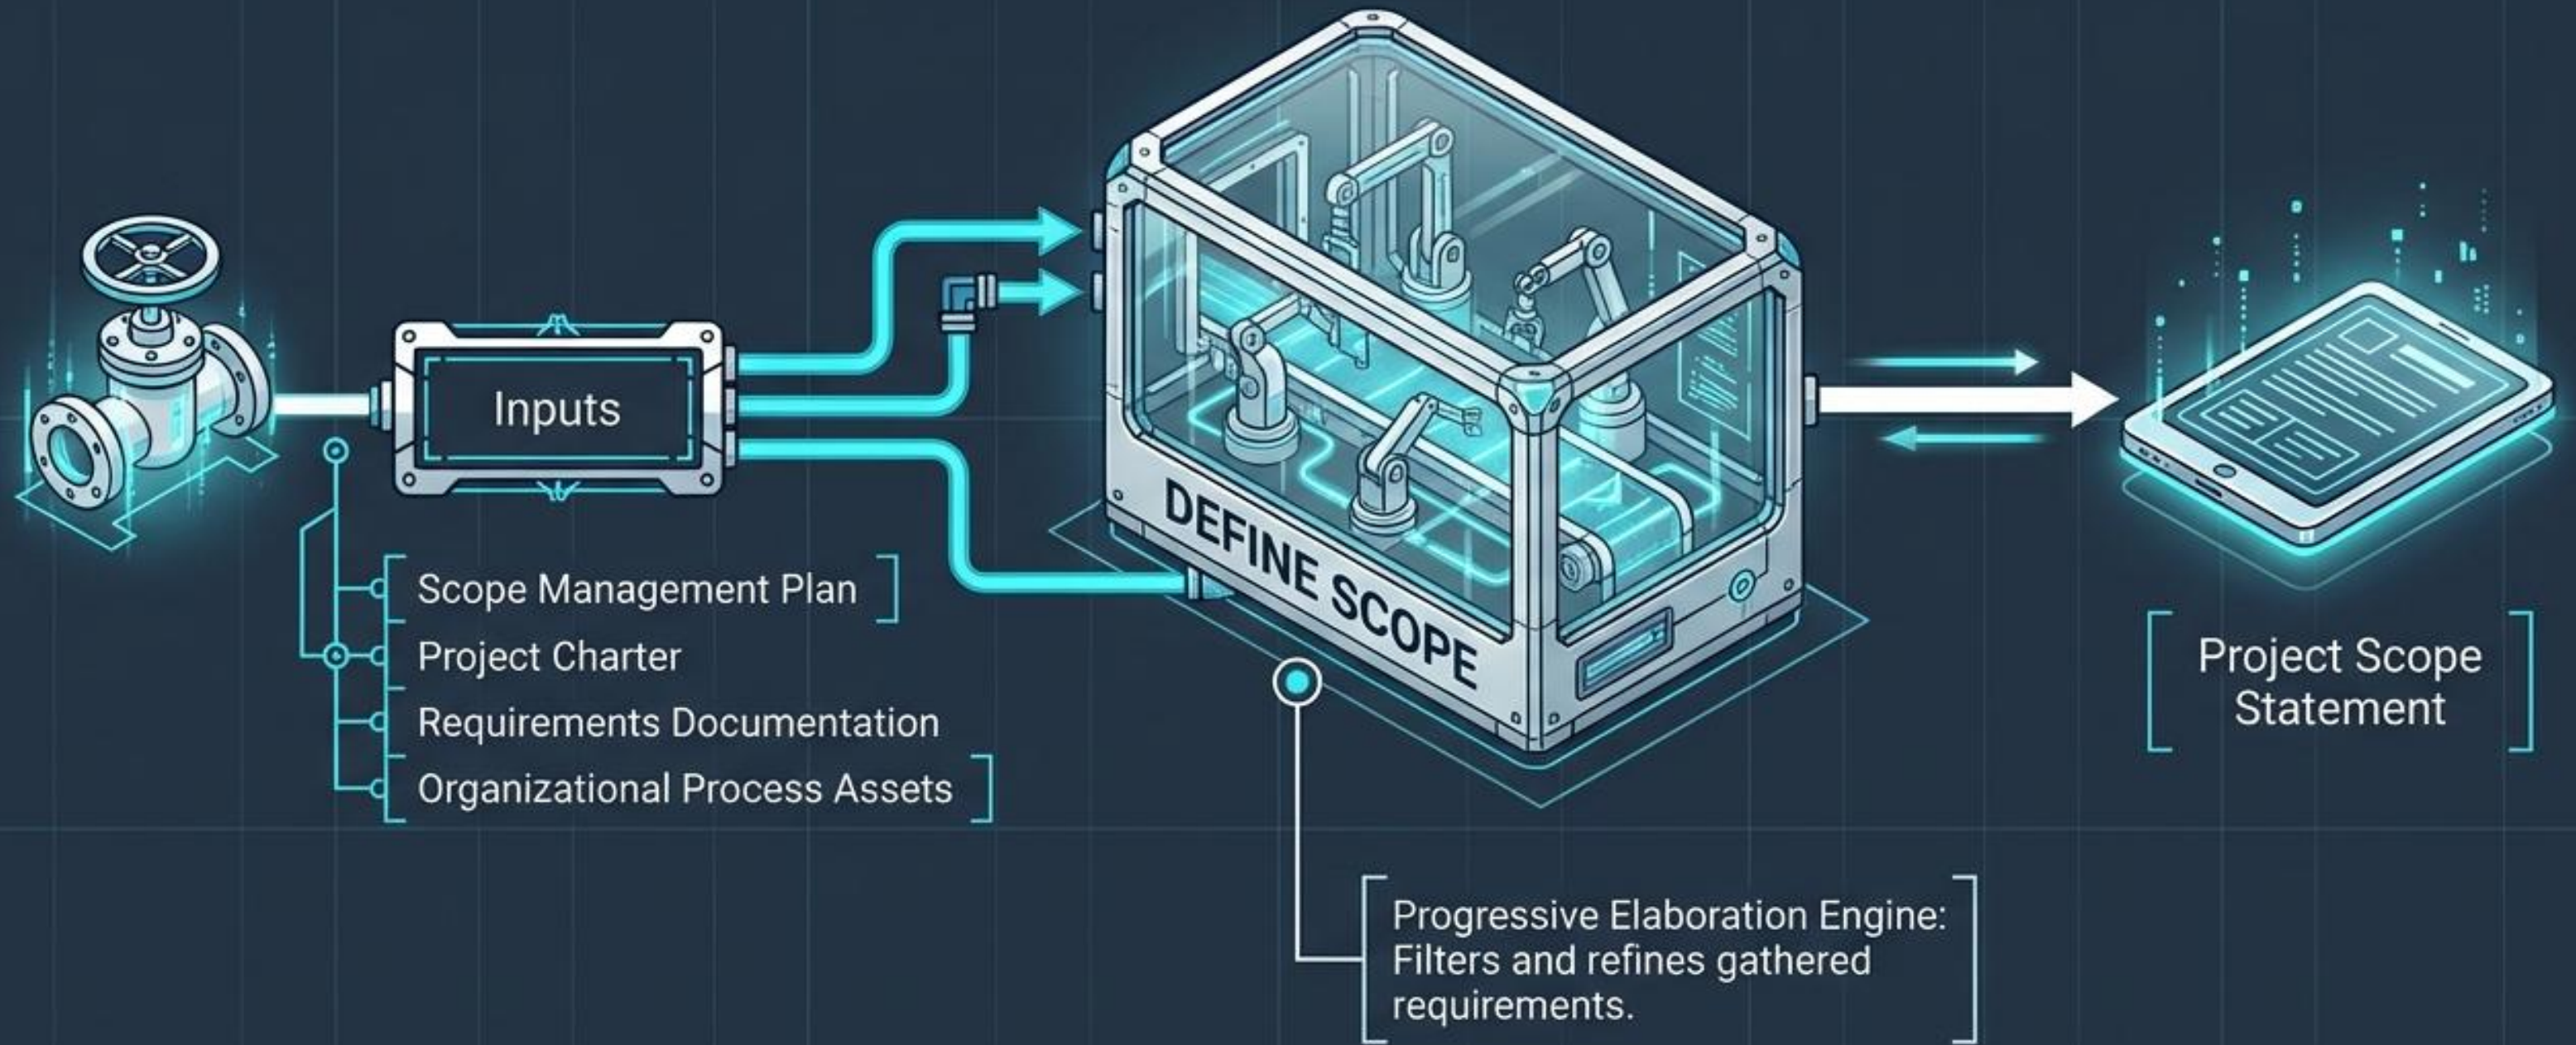

Clarifying the Twin Documents: Charter vs. Scope Statement



Tools of the Trade: Converting Inputs to Deliverables



Product Analysis

[Converting descriptions into deliverables via value analysis, product breakdown, or systems engineering. (Crucial when the end result is a tangible product).]



Alternatives Generation

[Discovering different methods to accomplish the work when constraints restrict the primary path.]



Expert Judgment

[Leveraging specialized knowledge to evaluate inputs.]



Facilitated Workshops

[Collaborative sessions to resolve conflicting requirements and reach stakeholder consensus.]

Cognitive Frameworks for Scope Definition


Lateral Thinking



Thinking outside the box. Separating scope components from their obvious presentation.


Example: If 8 people take a chocolate from a dish containing 8 chocolates, how does one remain? The last person took the dish.

Pairwise Comparisons

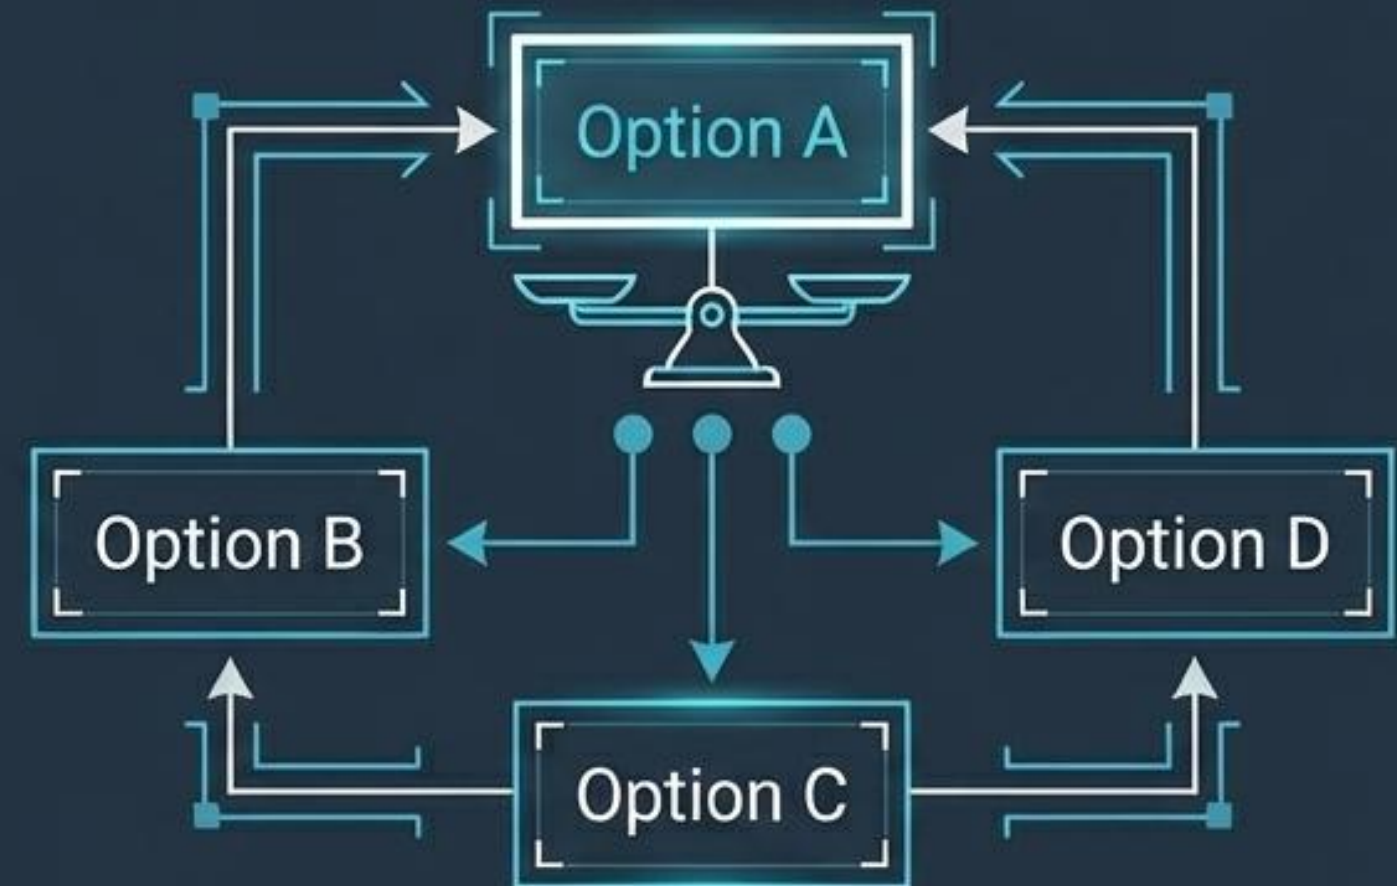


Using quantitative measures to compare any number of items directly against each other to determine the preferred option.

The Anatomy of the Project Scope Statement

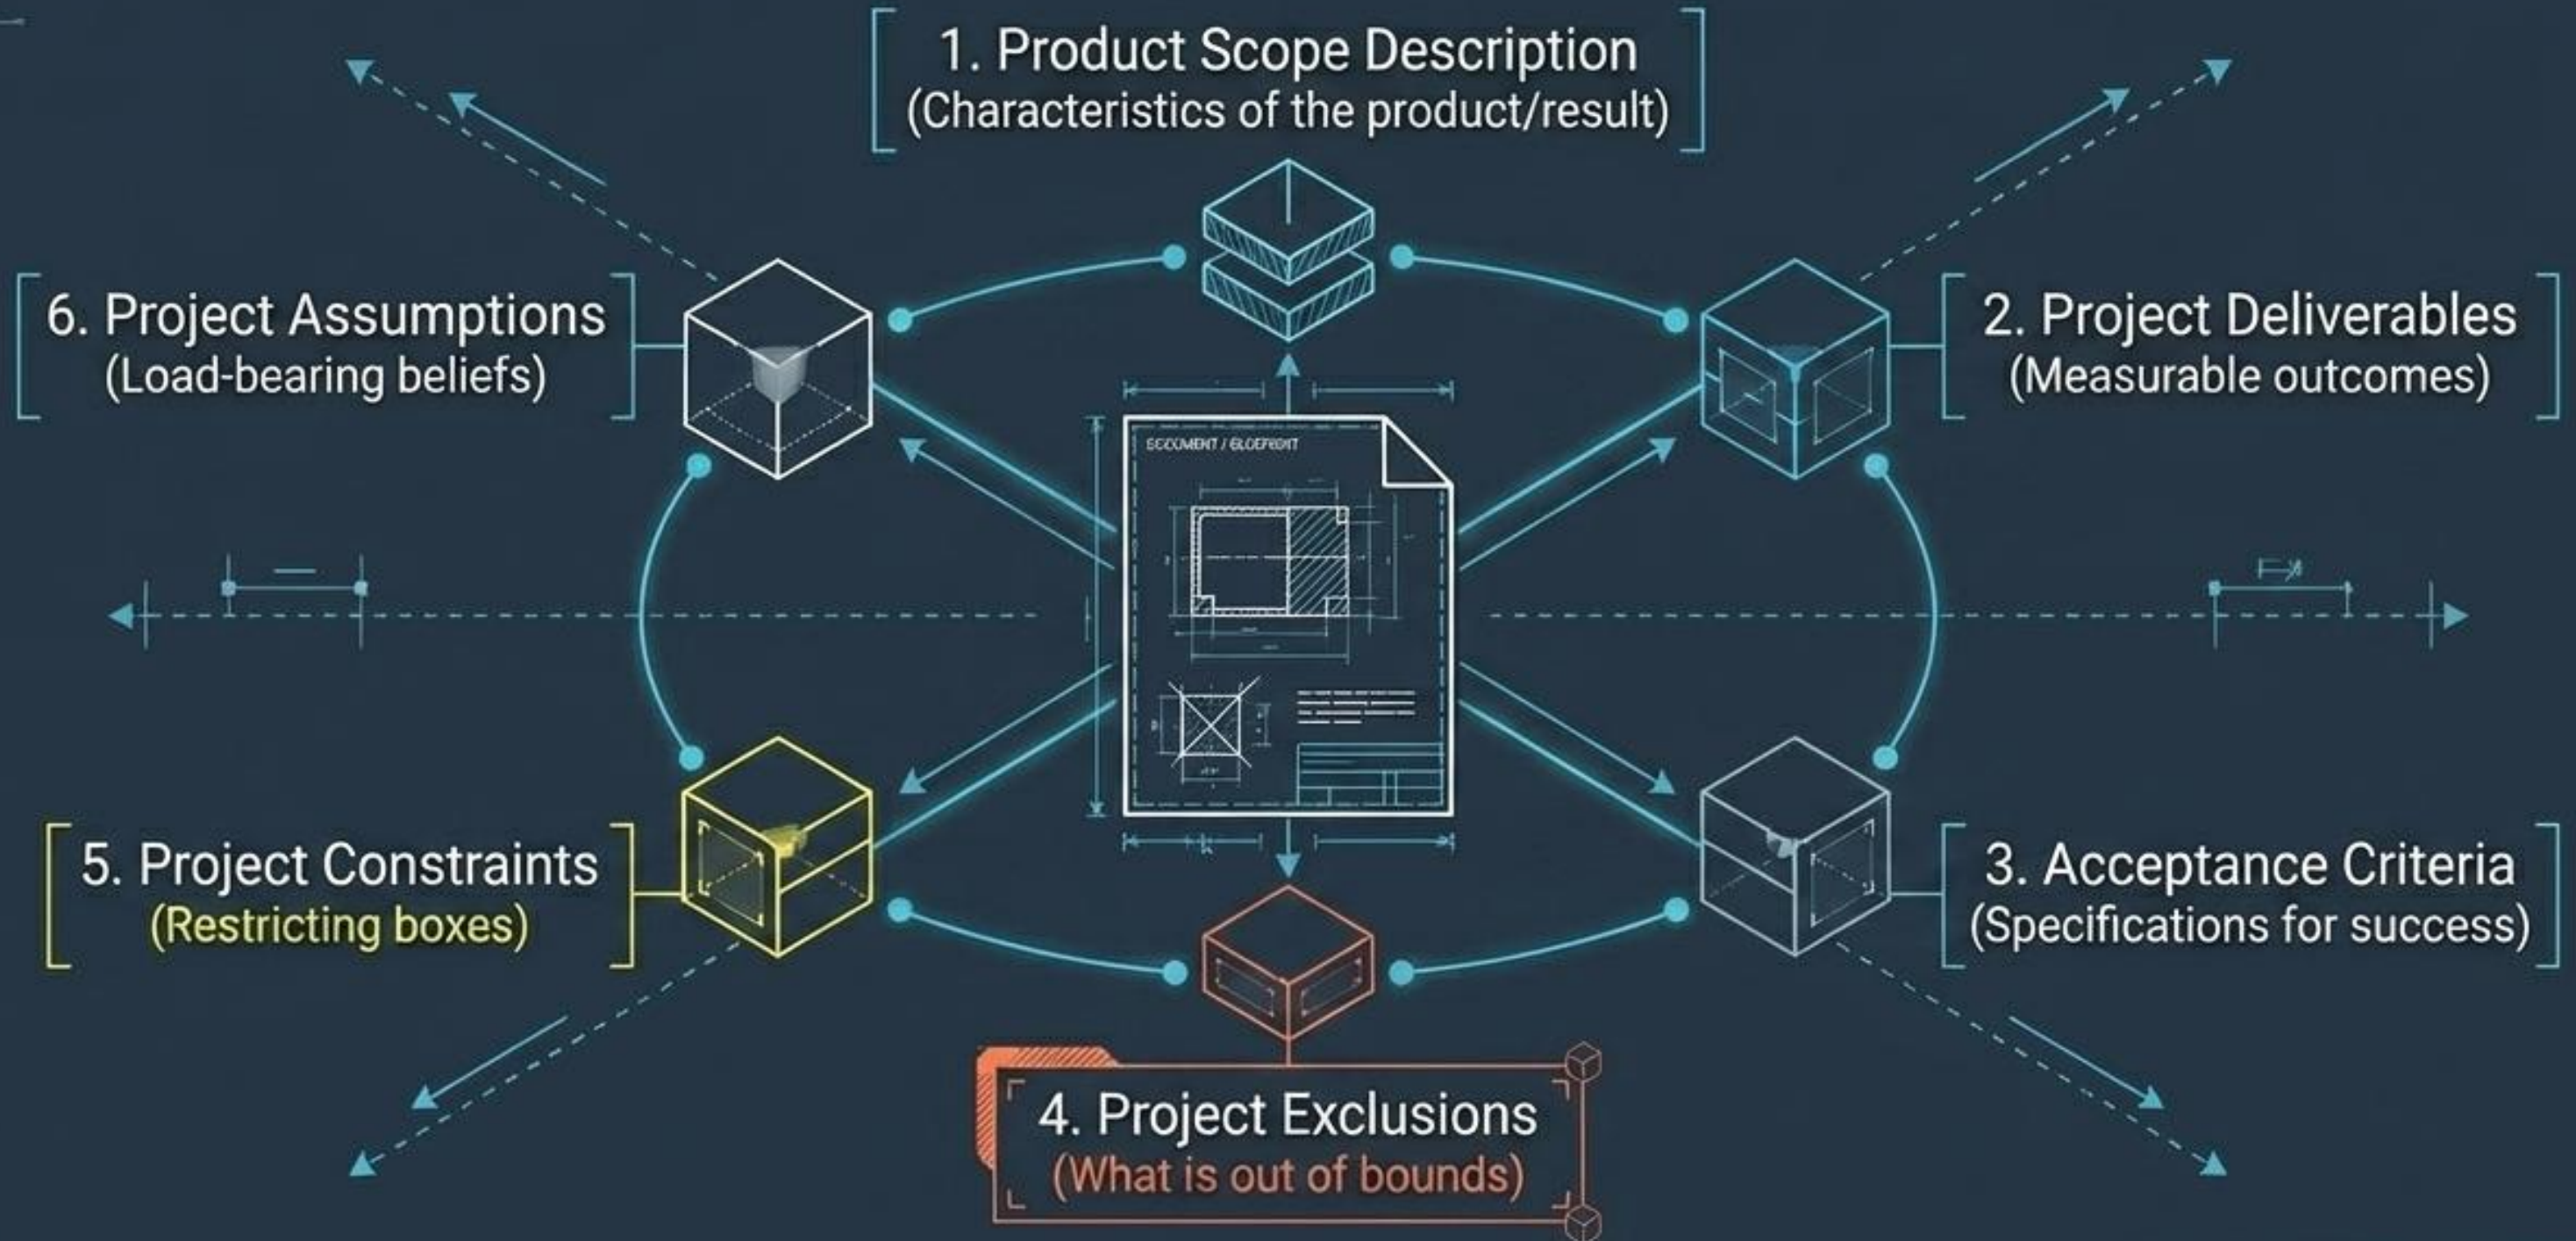

Defining the Tangible: Product Scope & Deliverables

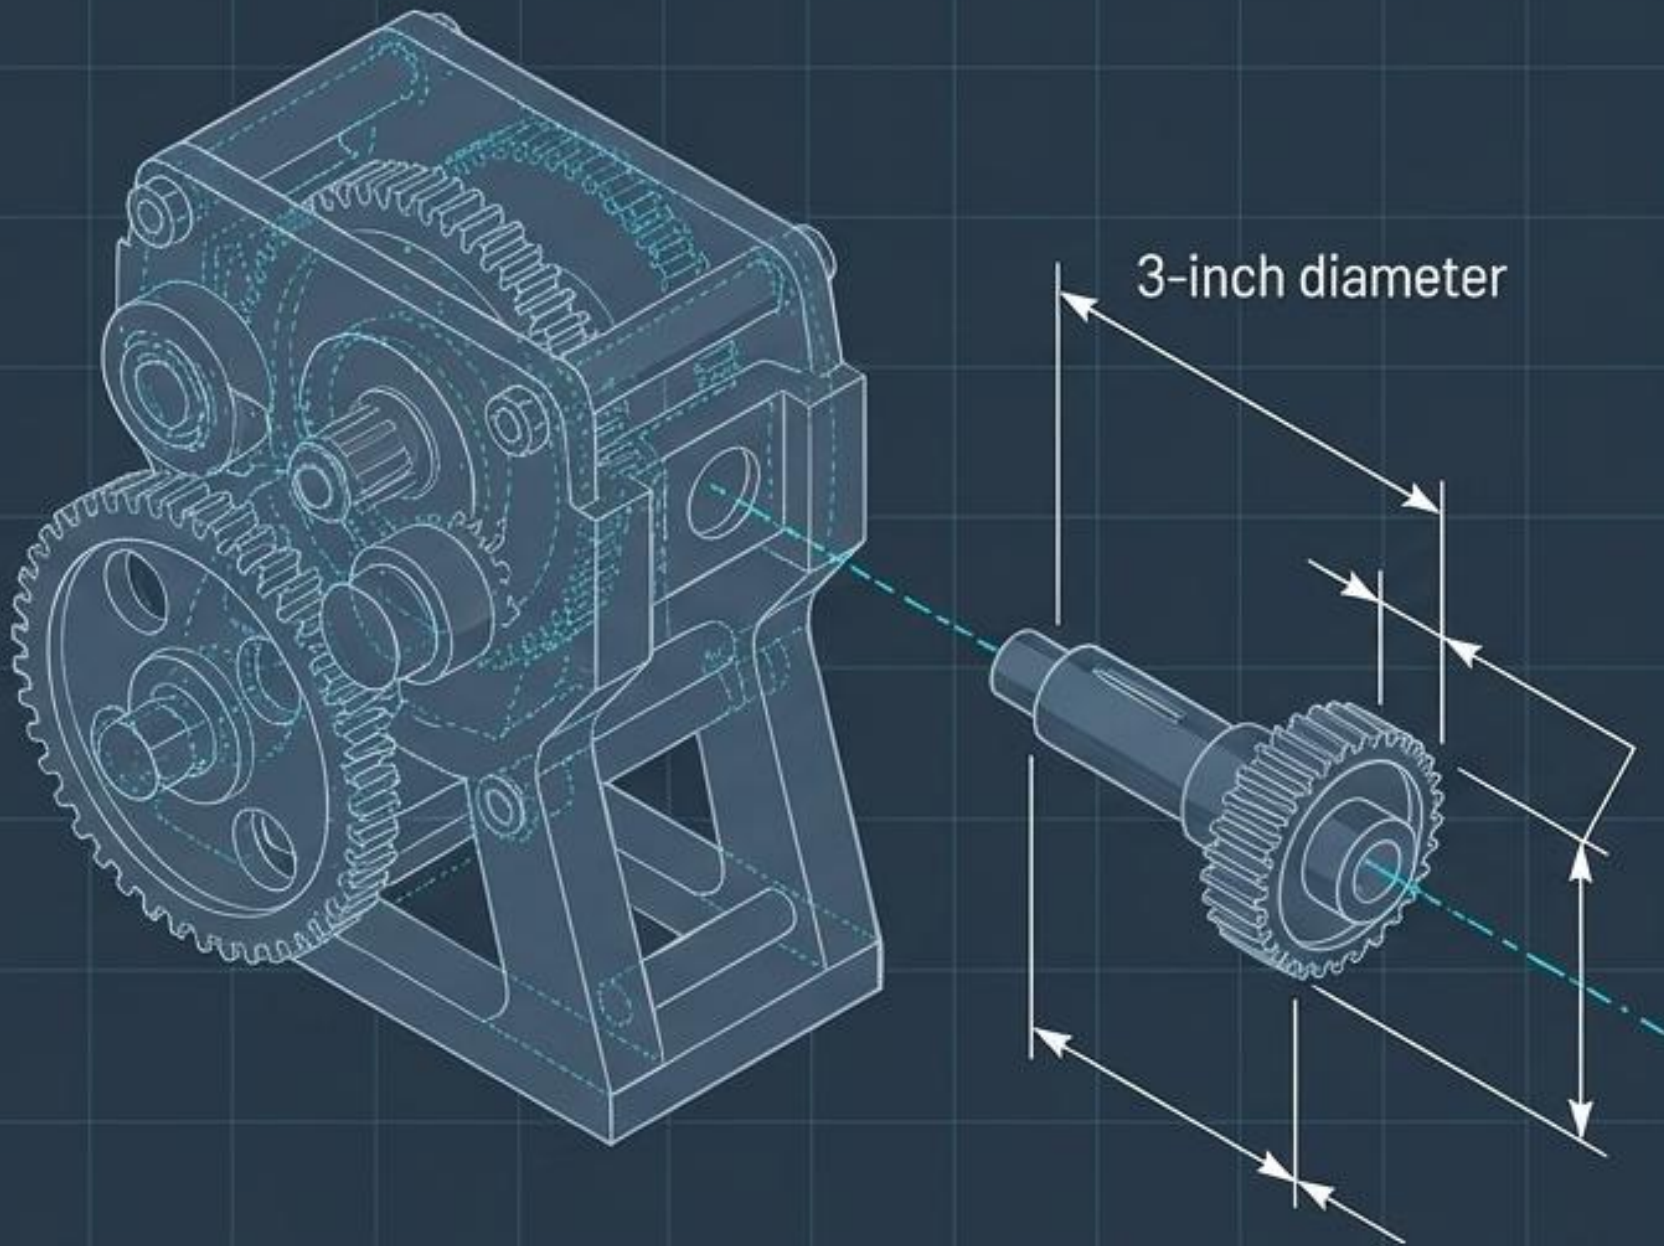

Product Scope

The specific characteristics of the product, service, or result. Completion is measured against these requirements.


Project Deliverables

Specific, verifiable, and measurable outcomes required to complete the project.

The Precision Rule

Deliverables must be exact. A requirement for 3-inch widgets communicated poorly might result in 2-inch widgets being manufactured—a career-limiting move that throws the entire project off schedule.

Establishing Boundaries: Acceptance & Exclusions

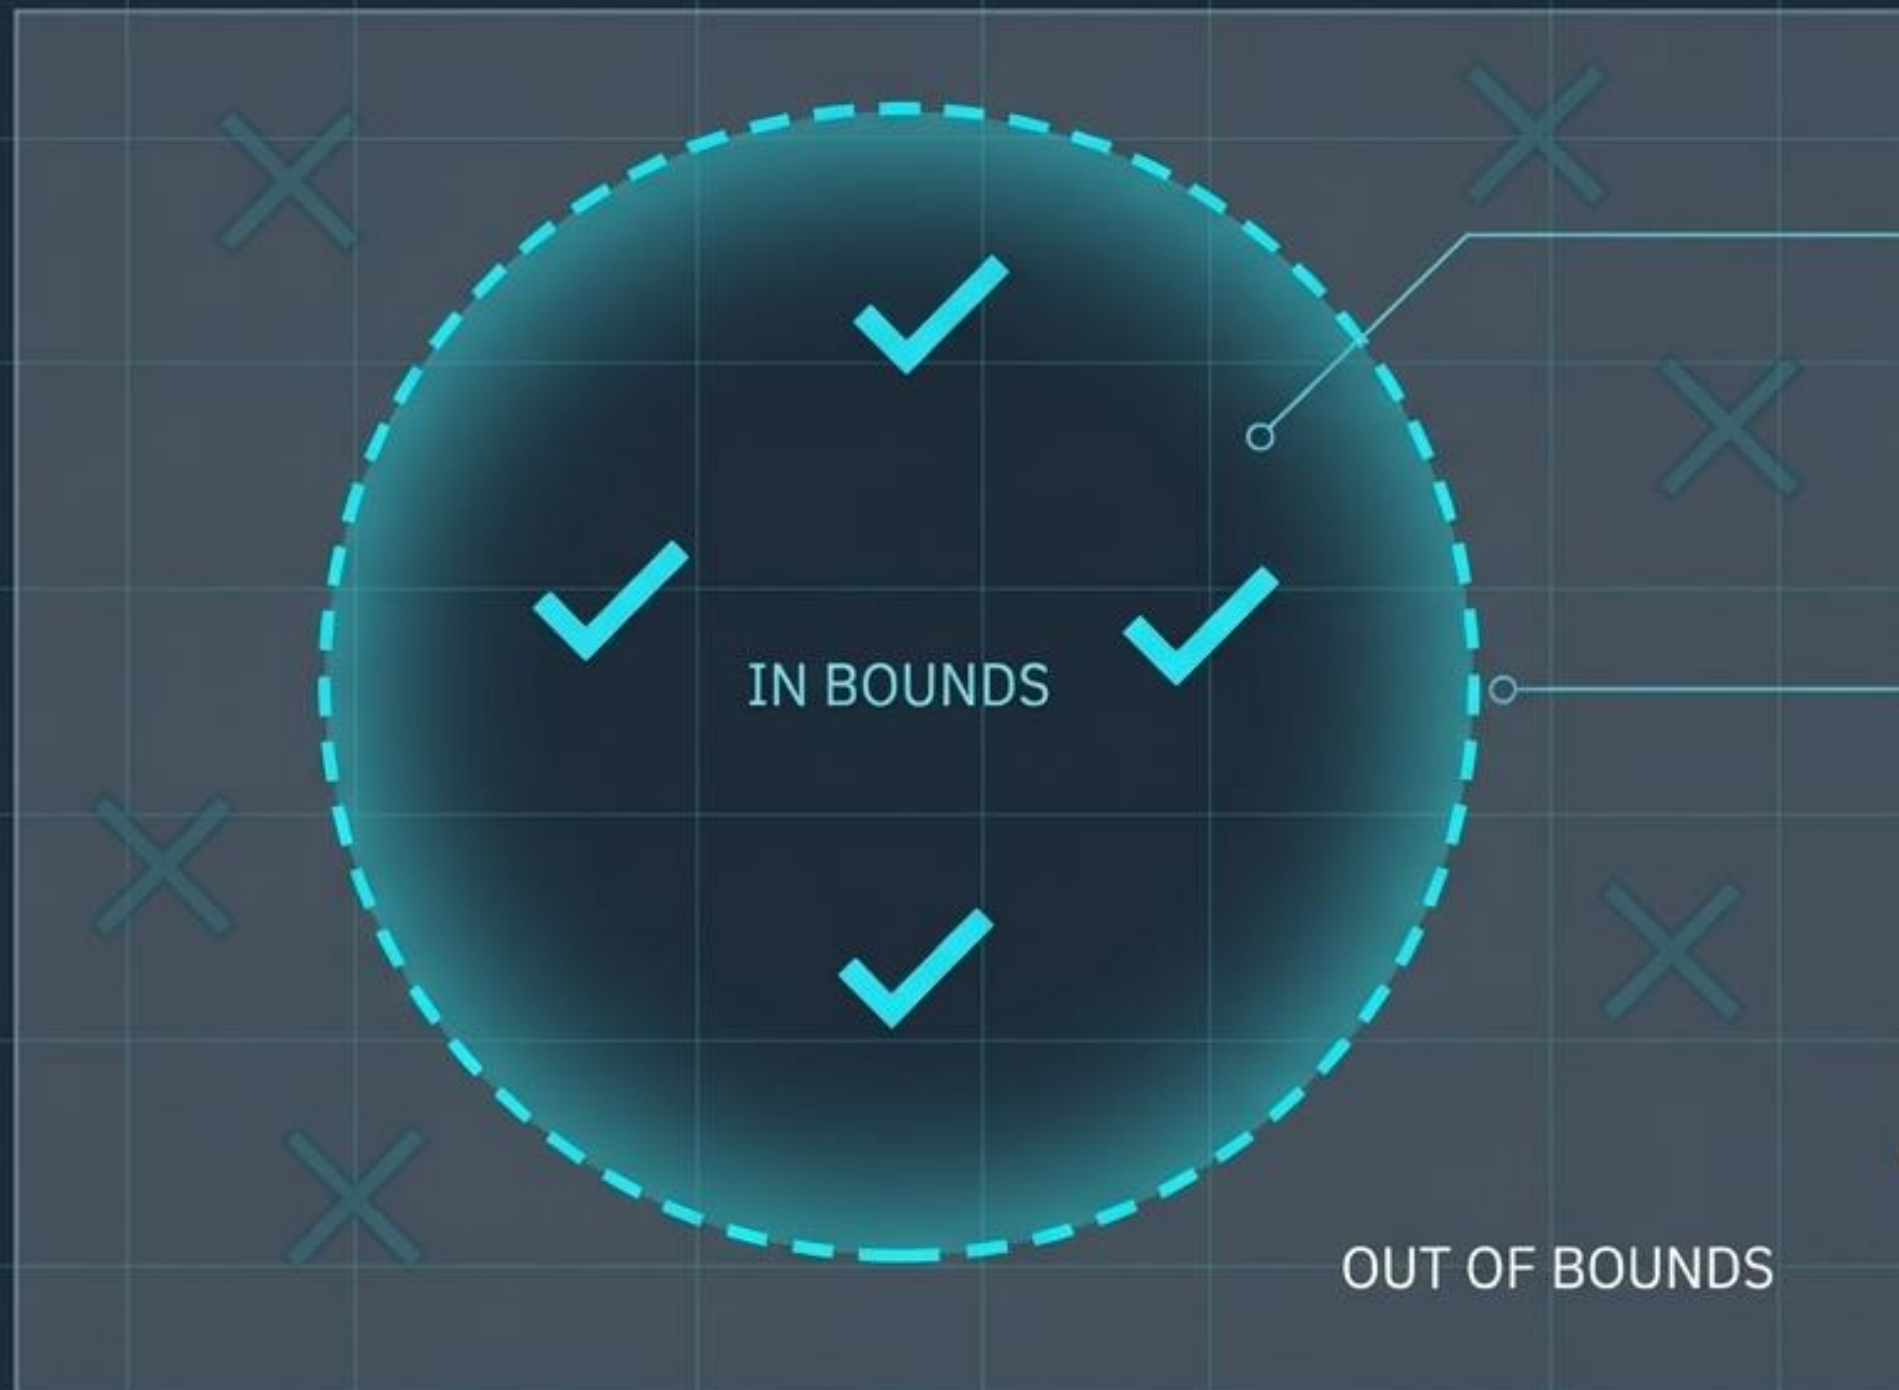

Acceptance Criteria

The exact process and specifications (fitness for use, quality criteria, performance metrics) used to determine if deliverables are satisfactory. How the stakeholder will officially indicate acceptance.


Project Exclusions

Explicitly documenting what is NOT included in the project work.

Strategic Value

Managing expectations and establishing immediate grounds to deny unauthorized scope creep.

Navigating the Box of Constraints

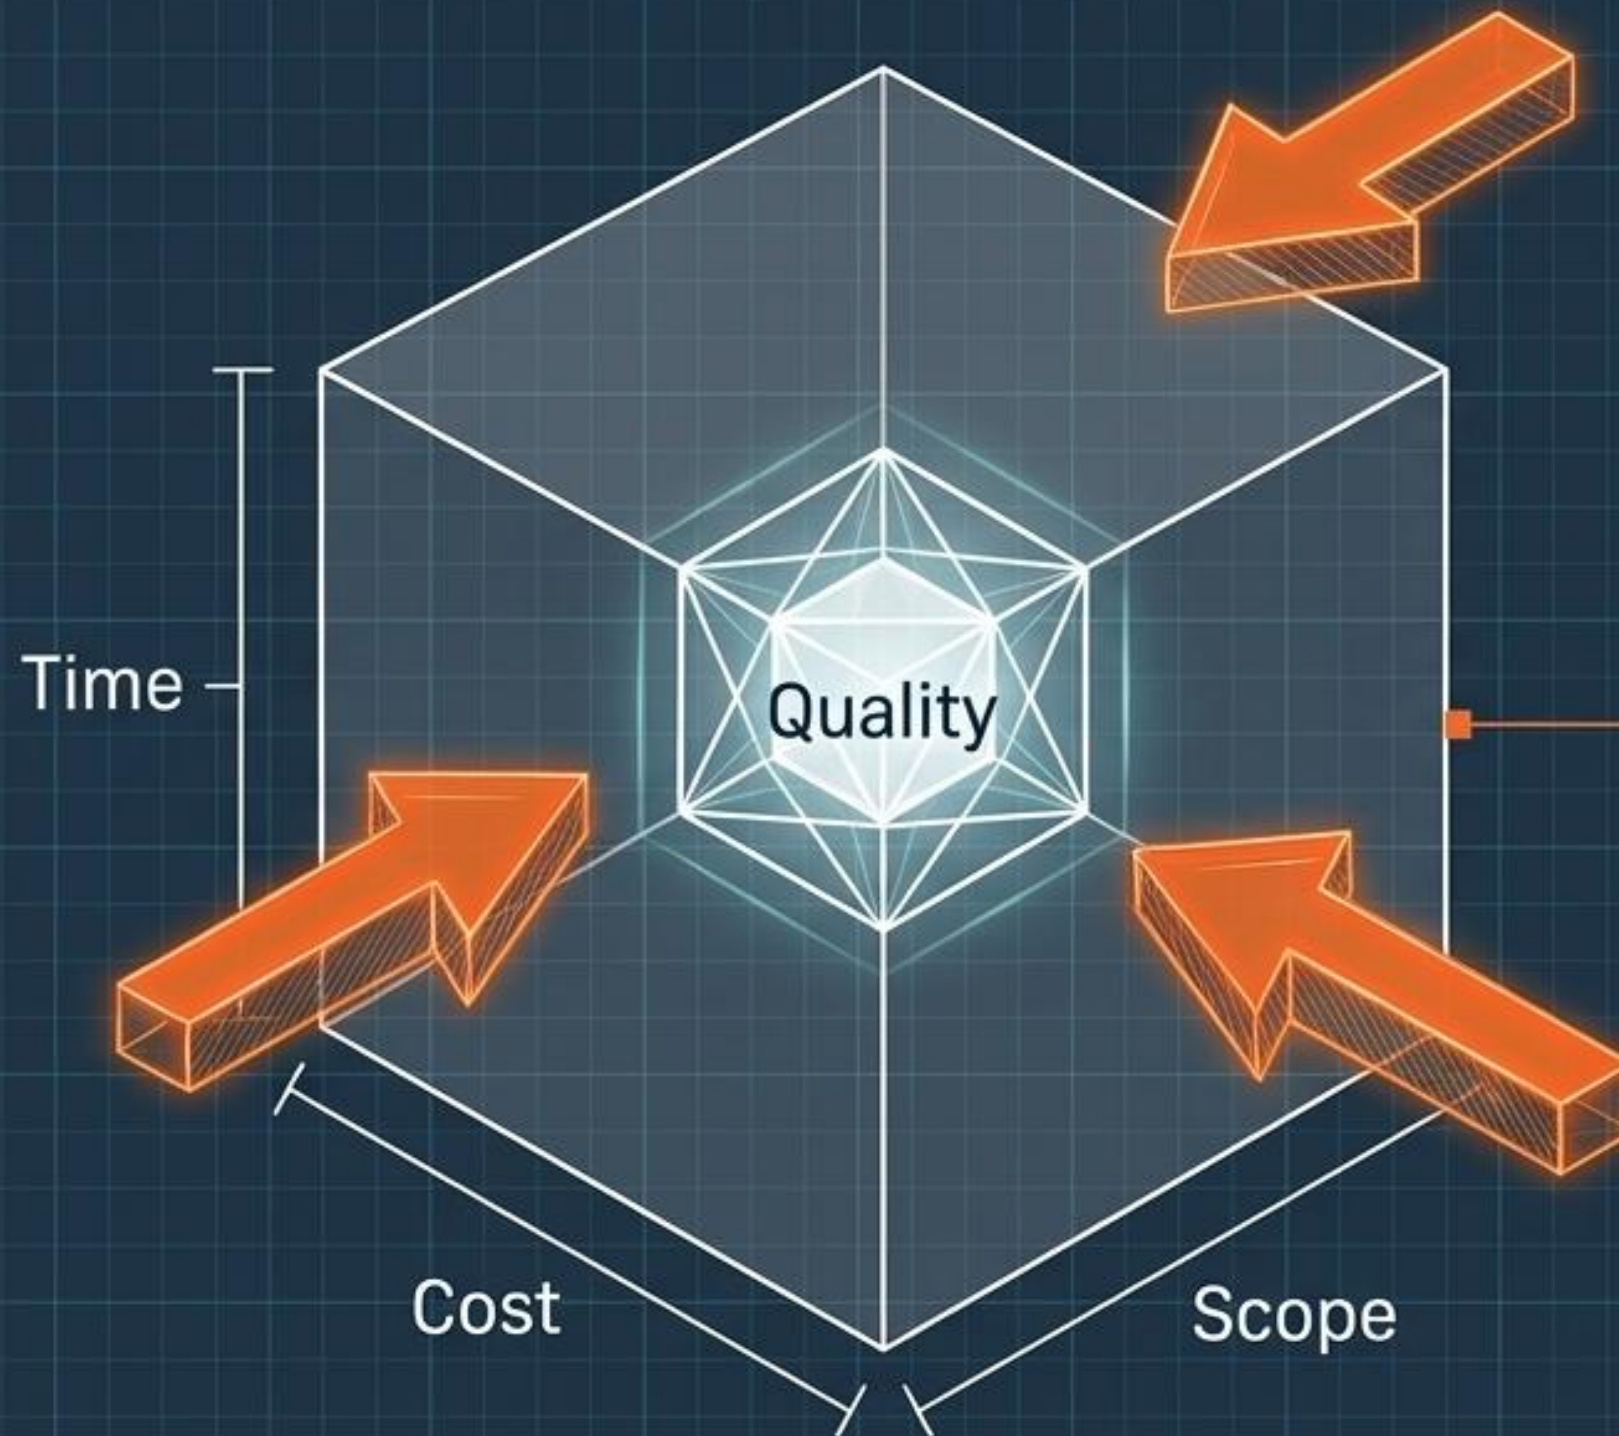

The Triple Constraint

Time, Cost, and Scope. Balancing these dictates the resulting Quality.
“I can give it to you fast or cheap, but not fast and cheap.”

External Pressures

[Resource Limitations]: Lack of skilled human capital or materials.
[Schedule/Technology]: Crane operator availability, untested new tech.
[Directive]: Management policies or cumbersome procurement processes.

Primary Constraint

Determine which constraint is paramount (e.g., rigid deadline vs. fixed budget) to guide future trade-offs.

Validating Load-Bearing Assumptions

The Definition


[Factors presumed to be true, real, or certain for planning purposes (e.g., material availability, vendor delivery times, key team member presence).]

The Rule

[Identify, document, and constantly refine assumptions. This is a continuous form of progressive elaboration.]

The Warning Callout

[When assumptions are incorrect or unrecorded, they become project killers. Always validate with vendors in writing.]

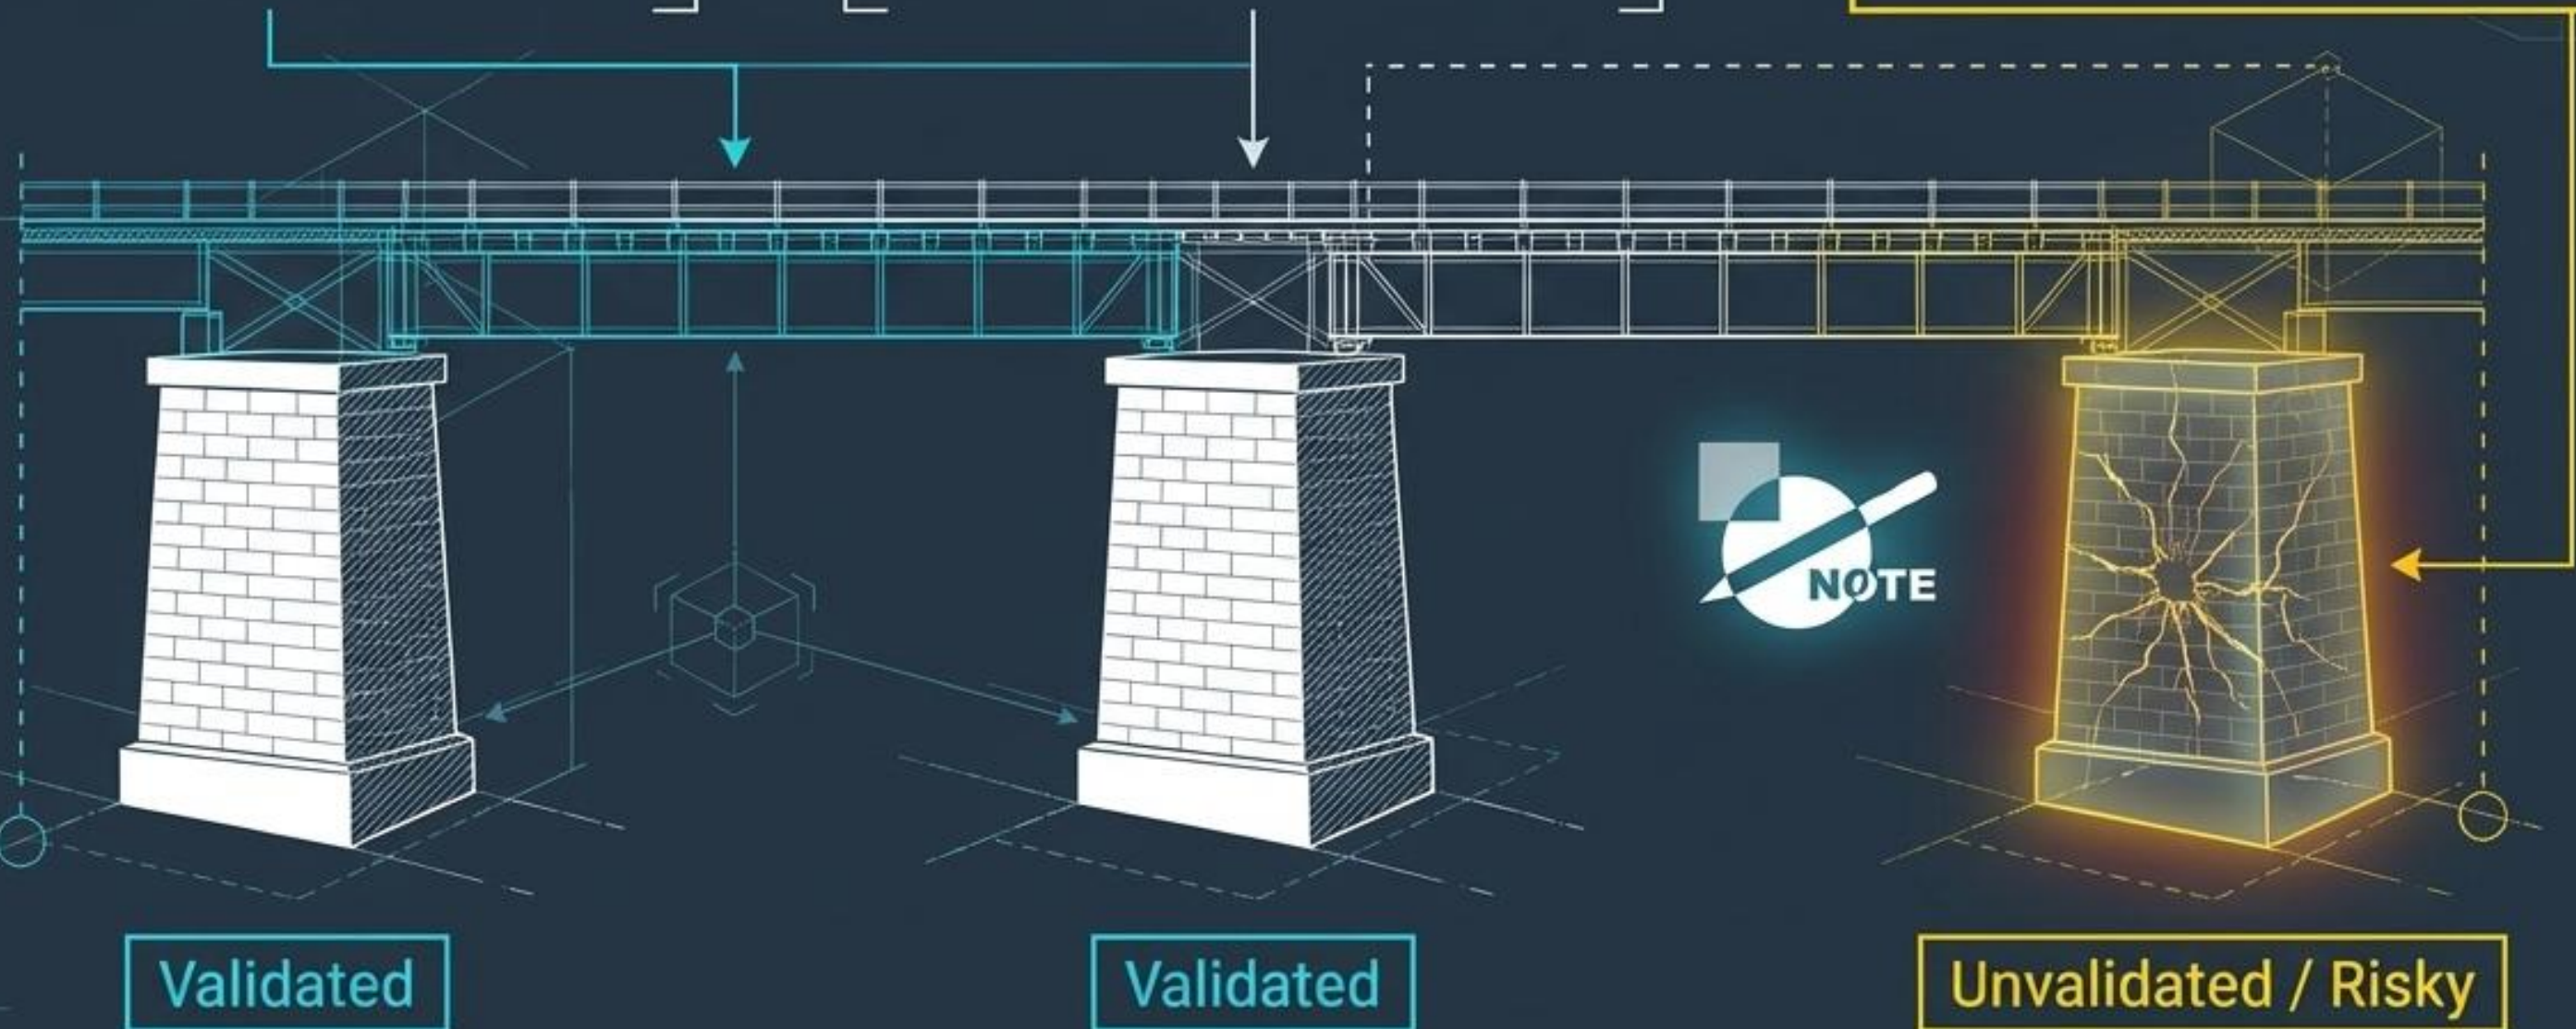

Case Application: Mountain Streams Services

• **Context Header:** CEO Maria Sanchez | April 12 Reception | 200 Guests | \$125/person Budget.

Deliverables

(The "What" / Nouns)

Location selection



Food and beverage menu



Invitations & Entertainment



Decorations (fountain pens)



Agenda



Requirements & Criteria

(The "How" / Conditions)

Must be in the downtown area



Open bar; plus-ones allowed (no children)




Agenda kept secret until reception




Decorations must feature company logo



Locking the Critical Baseline

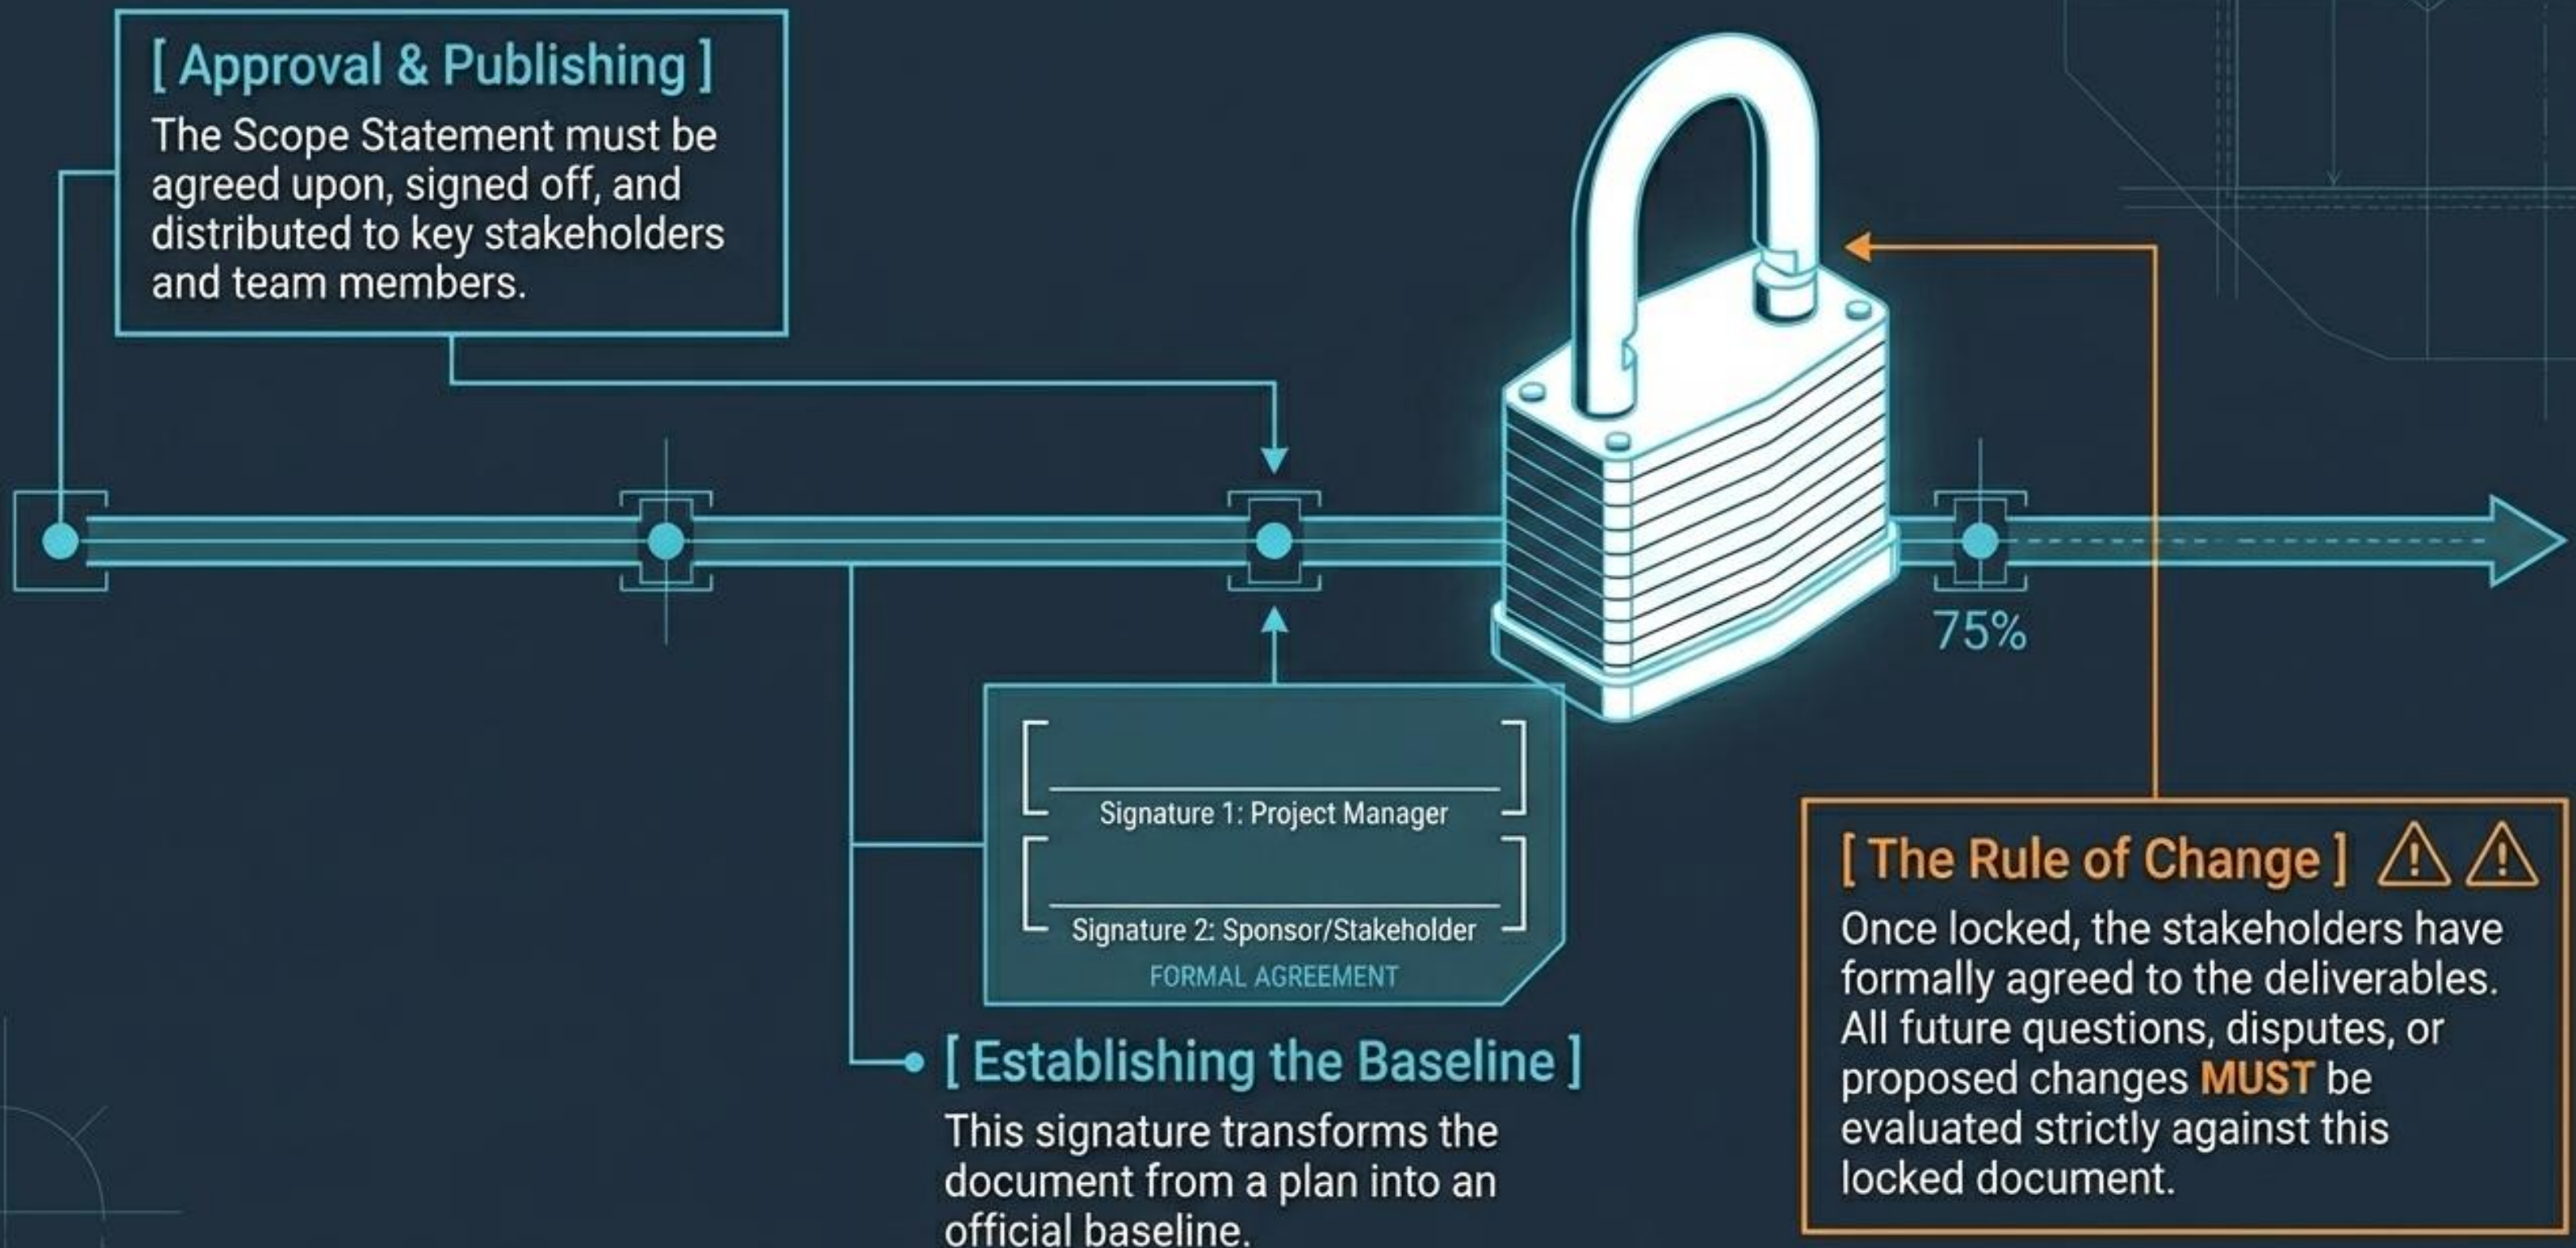

The Ripple Effect: Project Document Updates

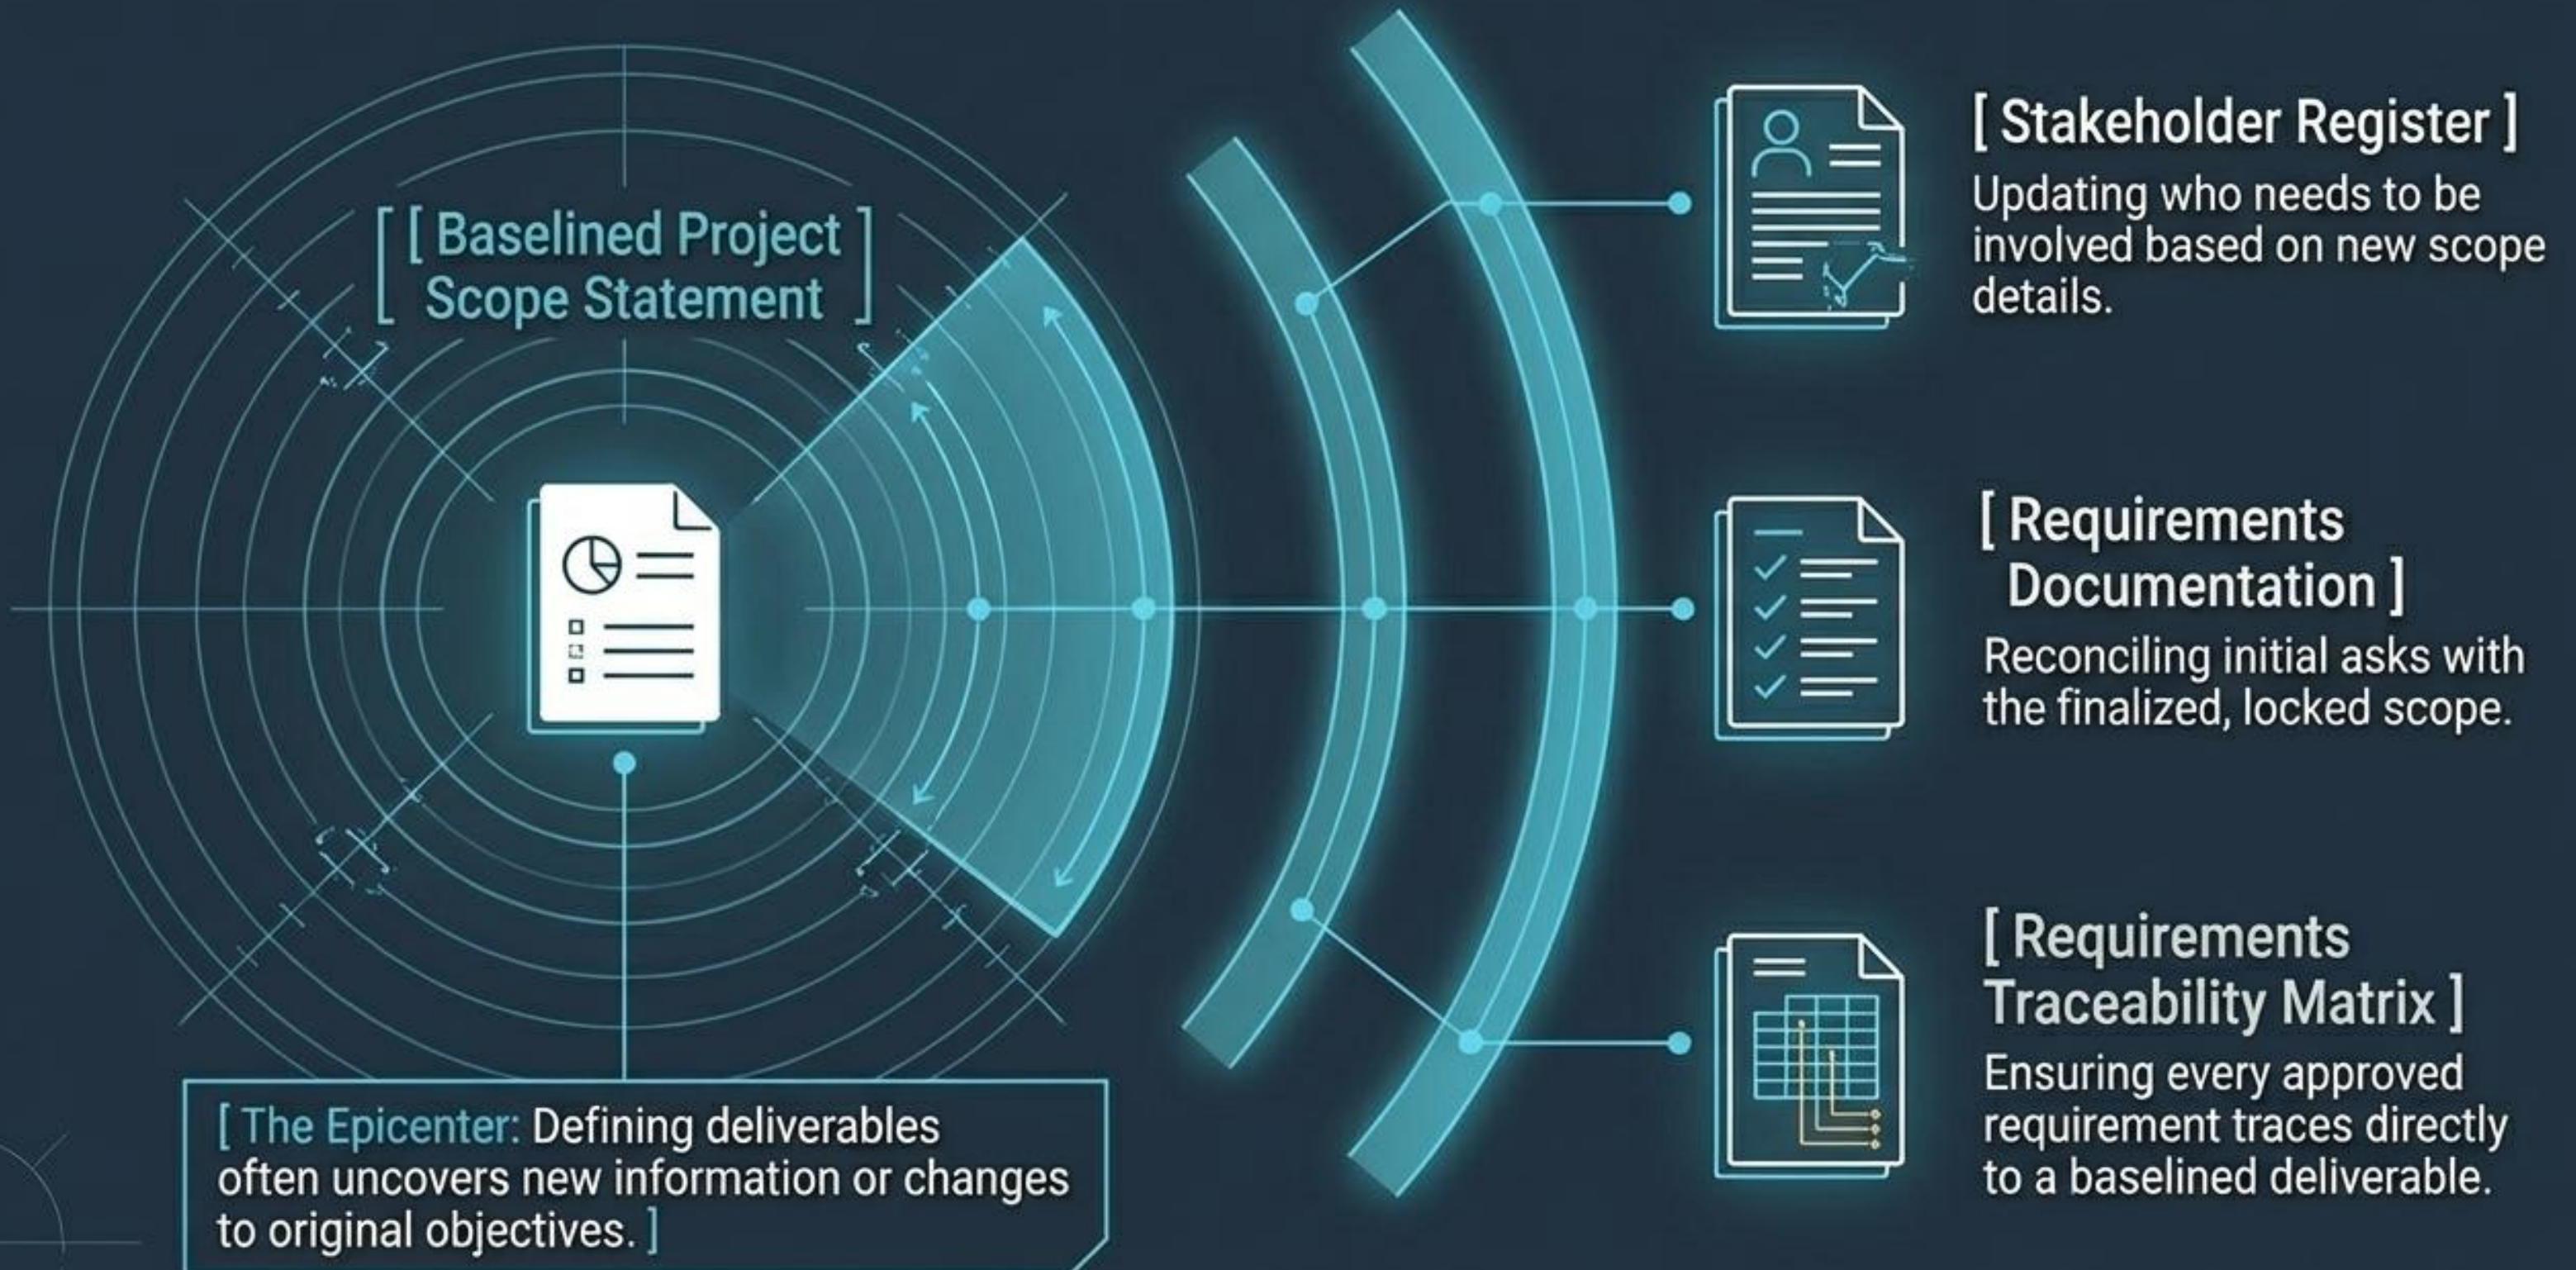


Next Steps: Bridging to the WBS

[Decomposing the Scope]

The finalized project scope statement is the direct foundation for the Create WBS process.

[The WBS (Work Breakdown Structure)]


A deliverable-oriented hierarchy that organizes the entire scope of work. It maps major deliverables into subdeliverables and work packages.

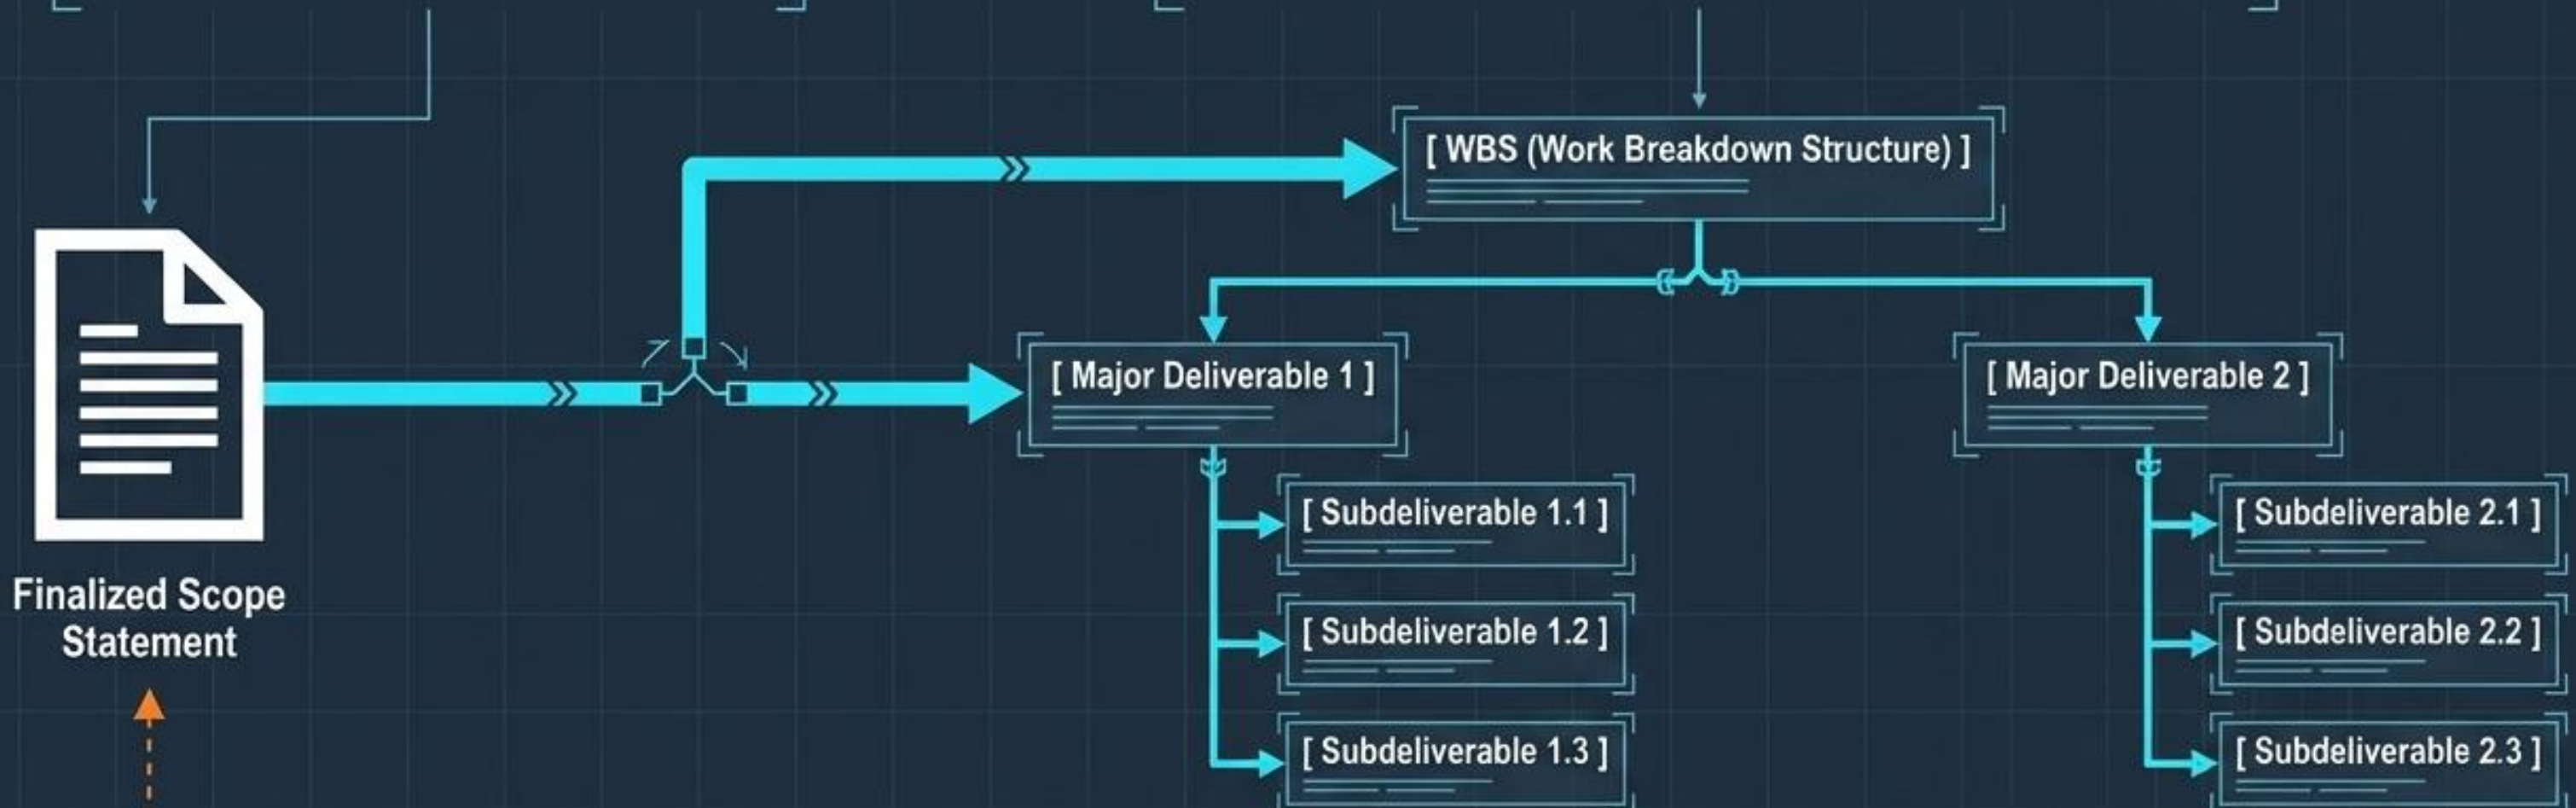

[The Rule]

The WBS must contain ONLY the work defined in the approved Scope Statement.

The Complete Scope Architecture

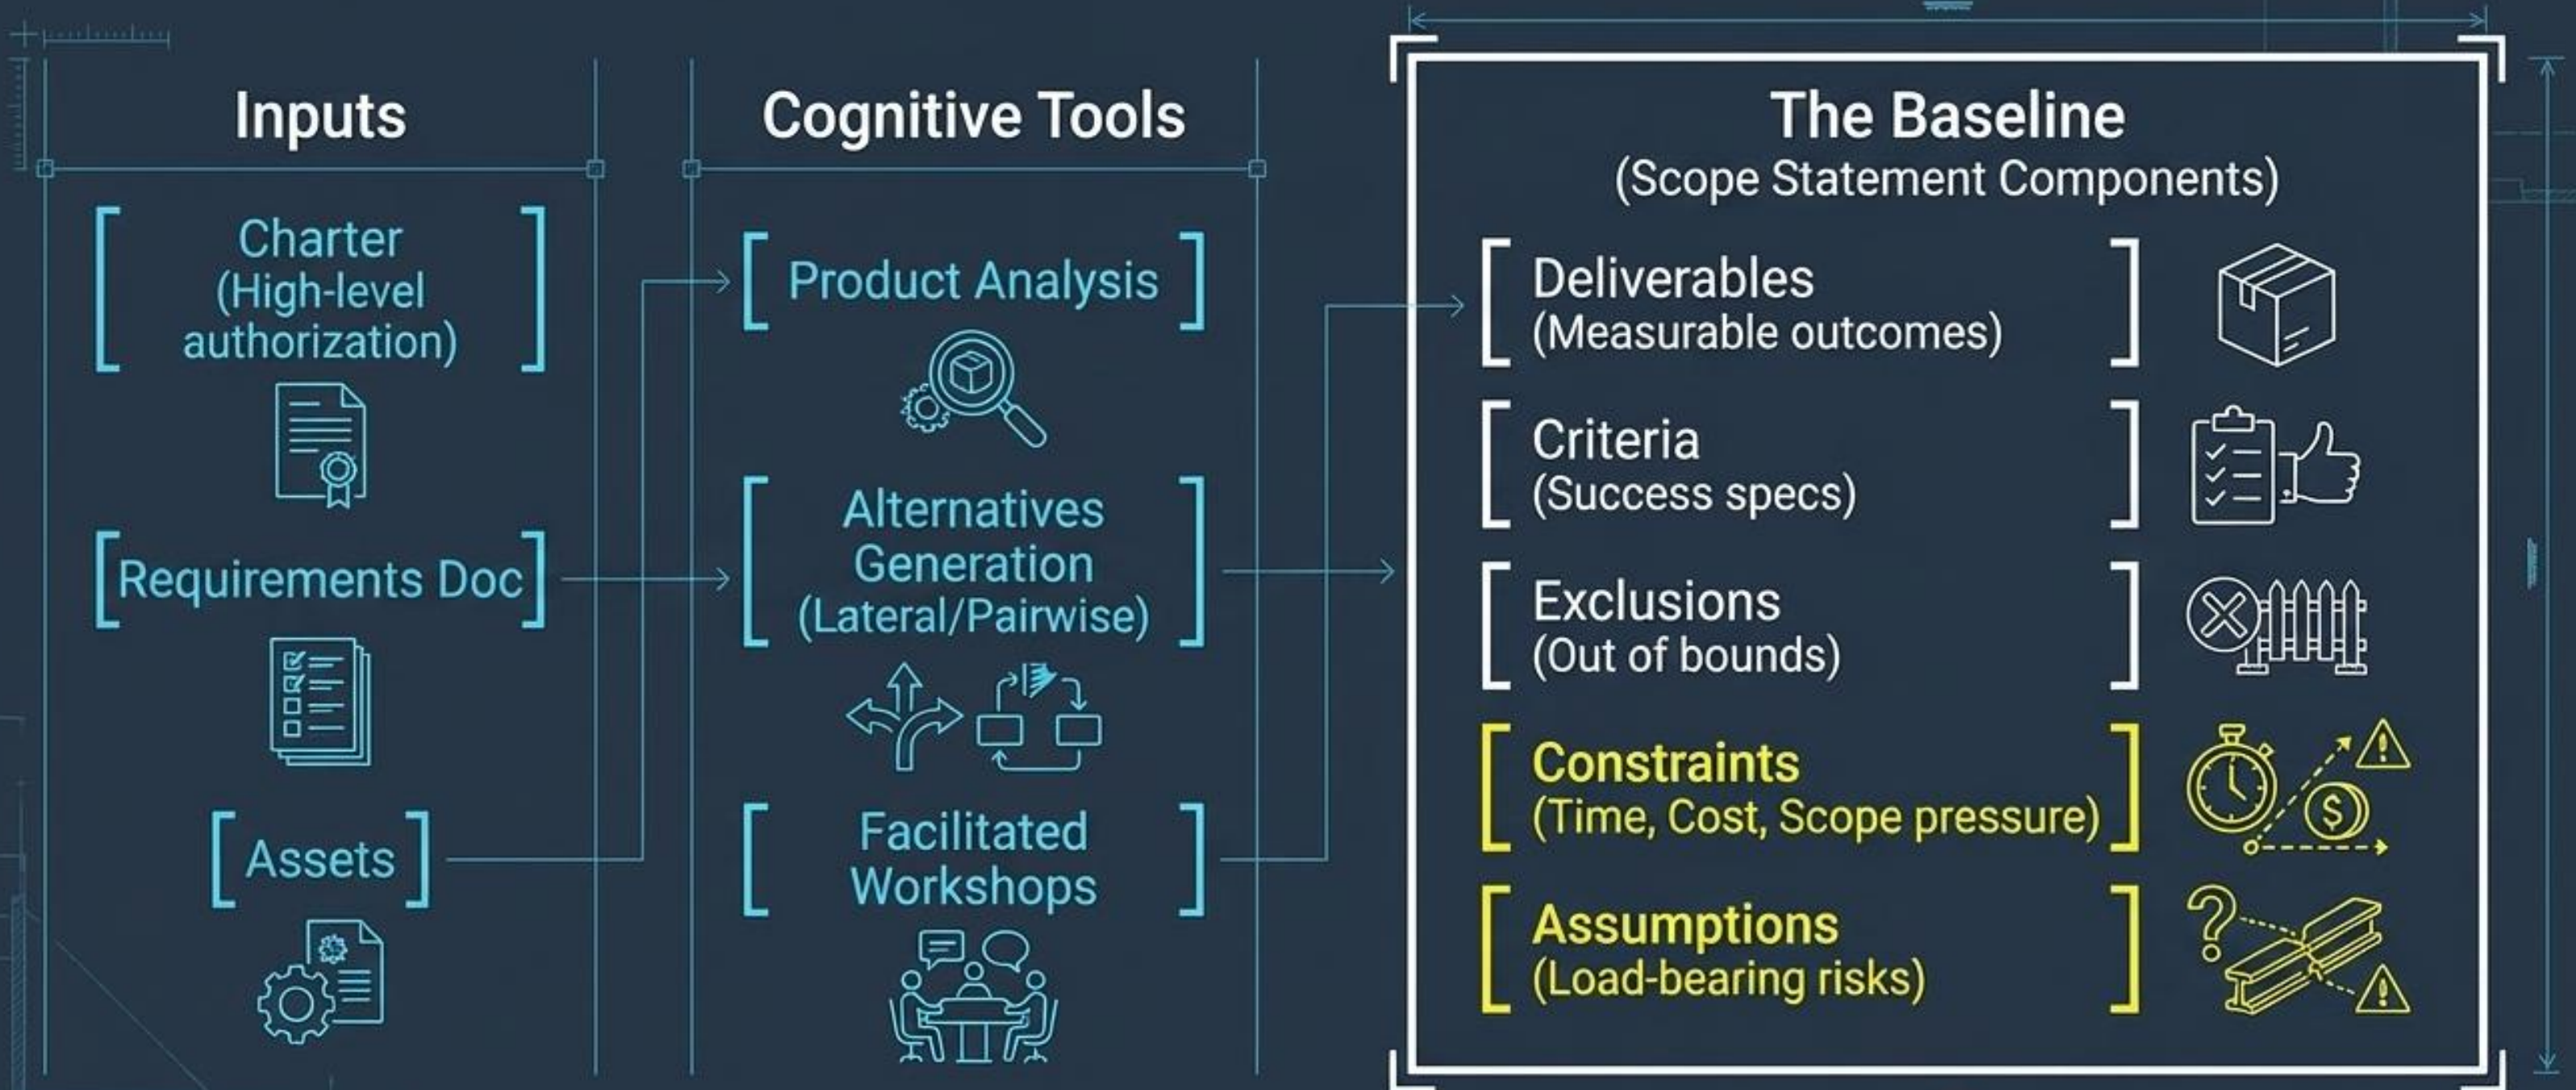

Progressive Elaboration → The baseline against which all execution is measured.
