

Certyfikat PMP: Human Resources Planning

Building the Project Ecosystem: From Procurement to Staffing Management


A visual study guide for PMP® Exam Preparation

Author: dr Zbigniew Galar


The Project Resource Ecosystem

Executing the project scope requires a hybrid approach. The resource ecosystem is built by answering one fundamental question: **Do we build this or buy this?**

Resource Ecosystem Map

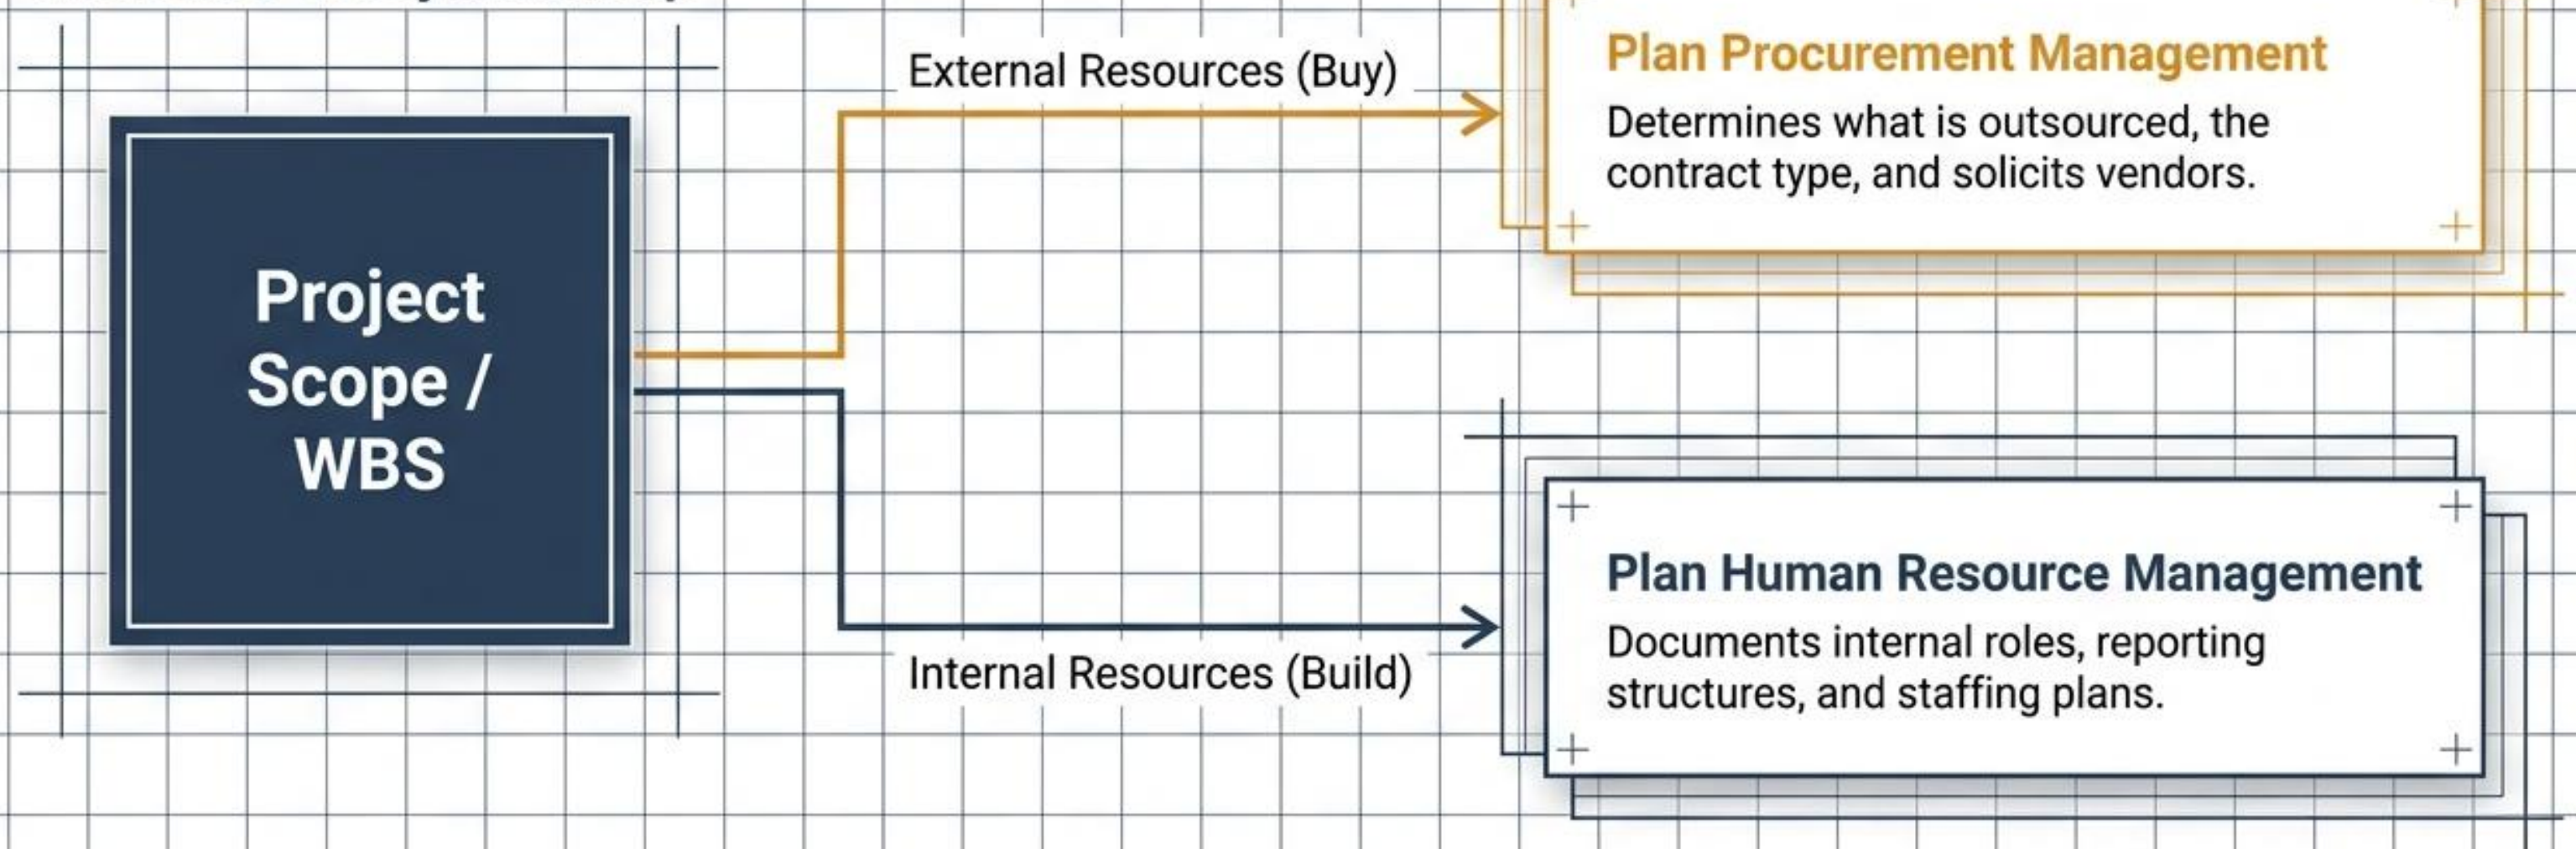

Translating Scope into Sourcing: The Make-or-Buy Decision

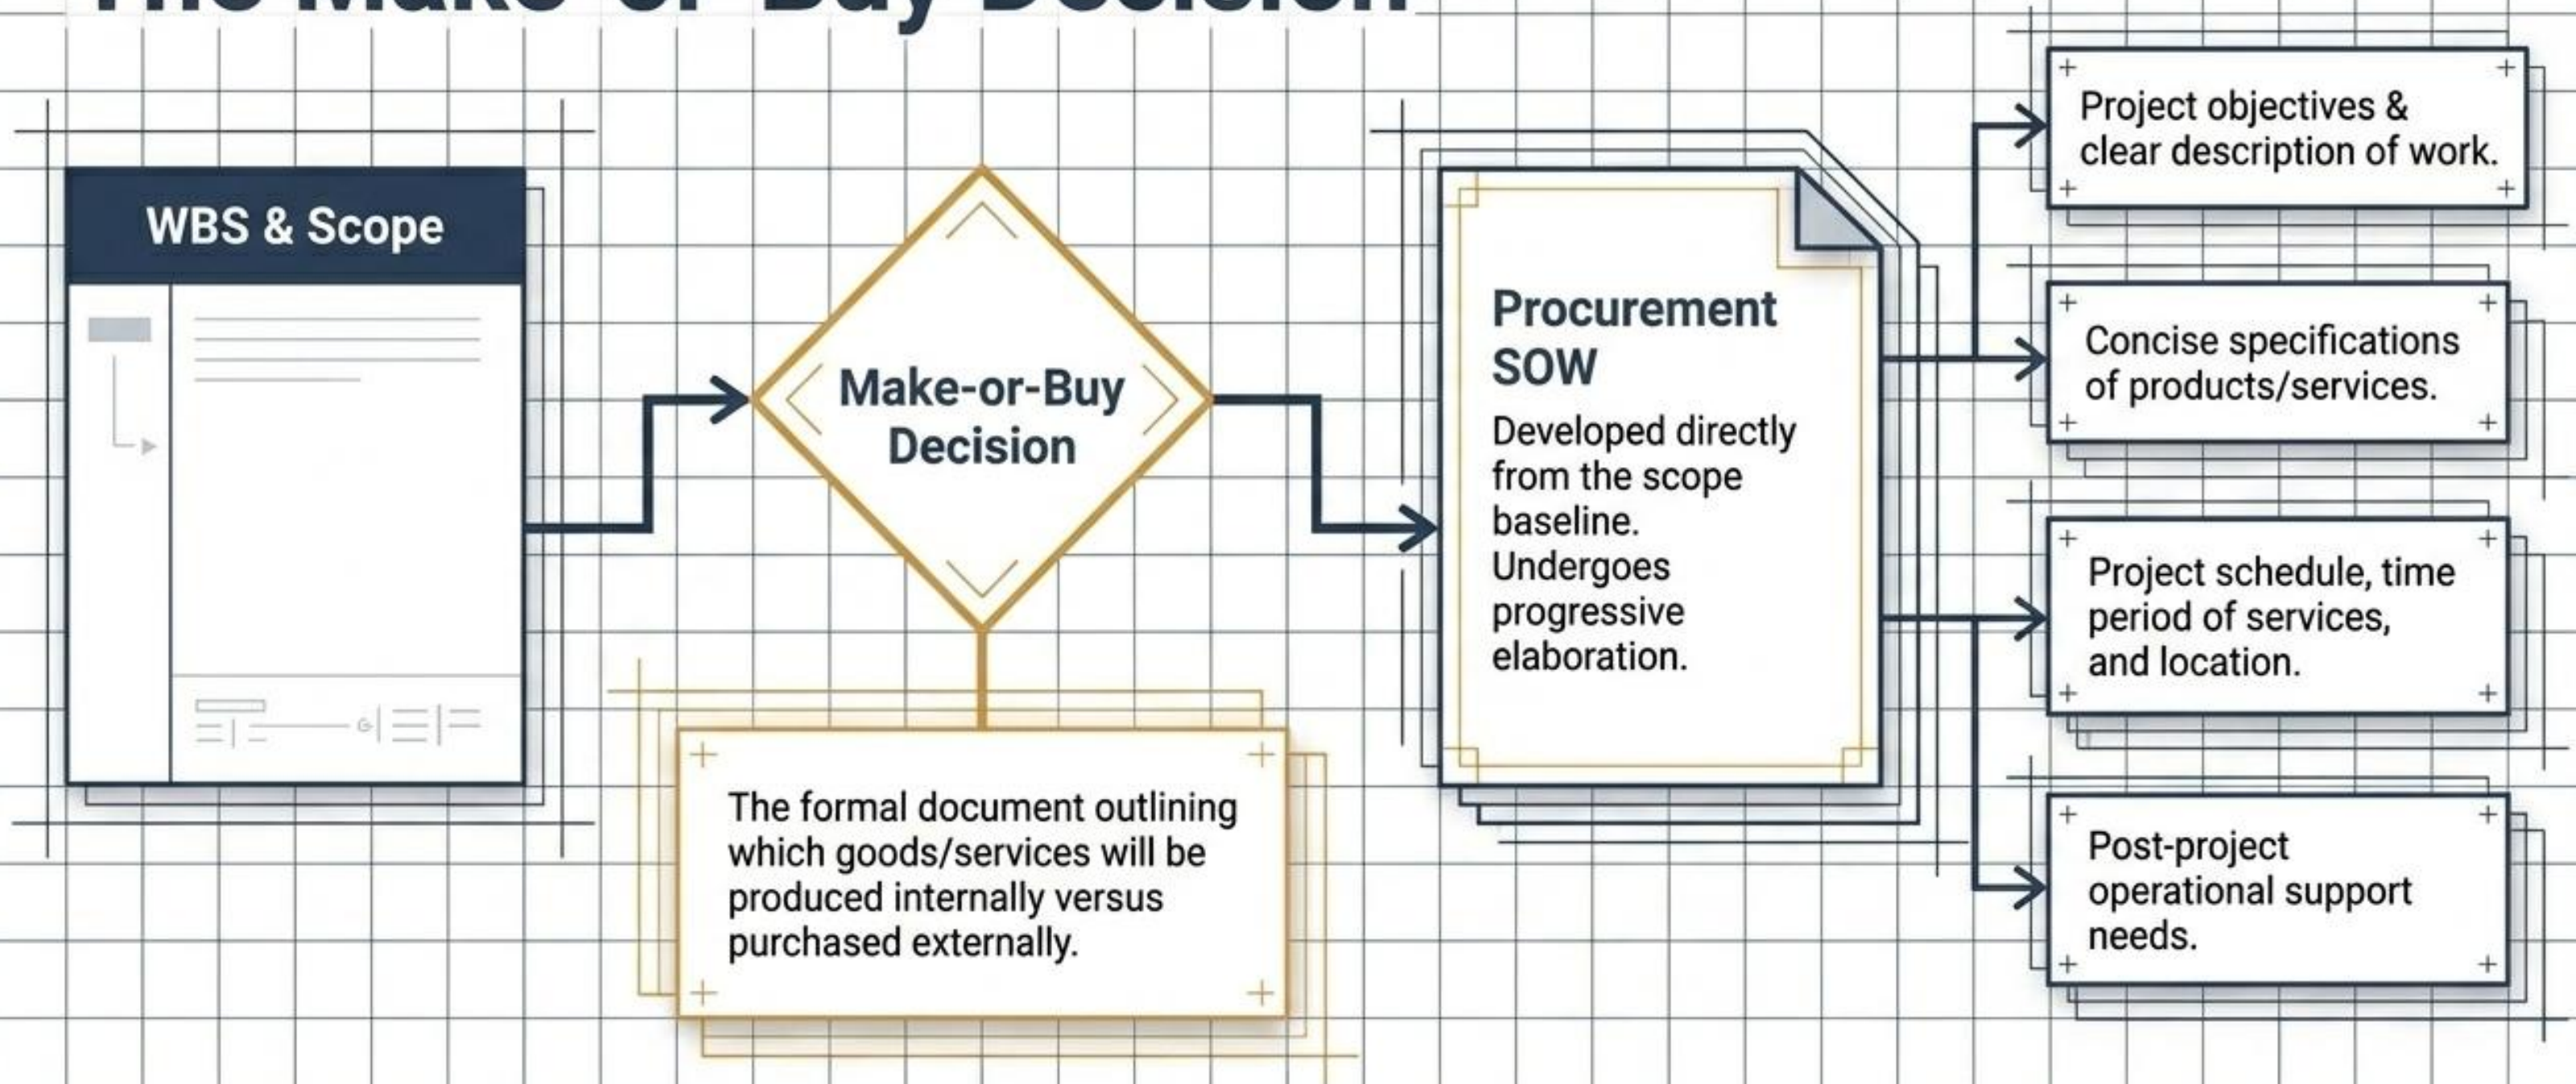

Sourcing Sellers: The Procurement Documents Matrix


Deciding Factor	Document Types	Use Case
Price is the Sole Factor	Invitation for Bid (IFB) / Request for Quotation (RFQ)	Seeking lowest cost for highly specified, standardized goods/services.
Holistic Solution is Required	Request for Proposal (RFP)	Seeking technical approaches, specific methodologies, or solving complex problems where price is secondary.



Require vendors to sign Non-Disclosure Agreements (NDAs) to protect proprietary information, marketing policies, or trade secrets during solicitation.


Defining Source Selection Criteria

Lowest purchase price is the sole criterion only when choosing among multiple highly qualified sellers. Otherwise, utilize a weighted scoring model.

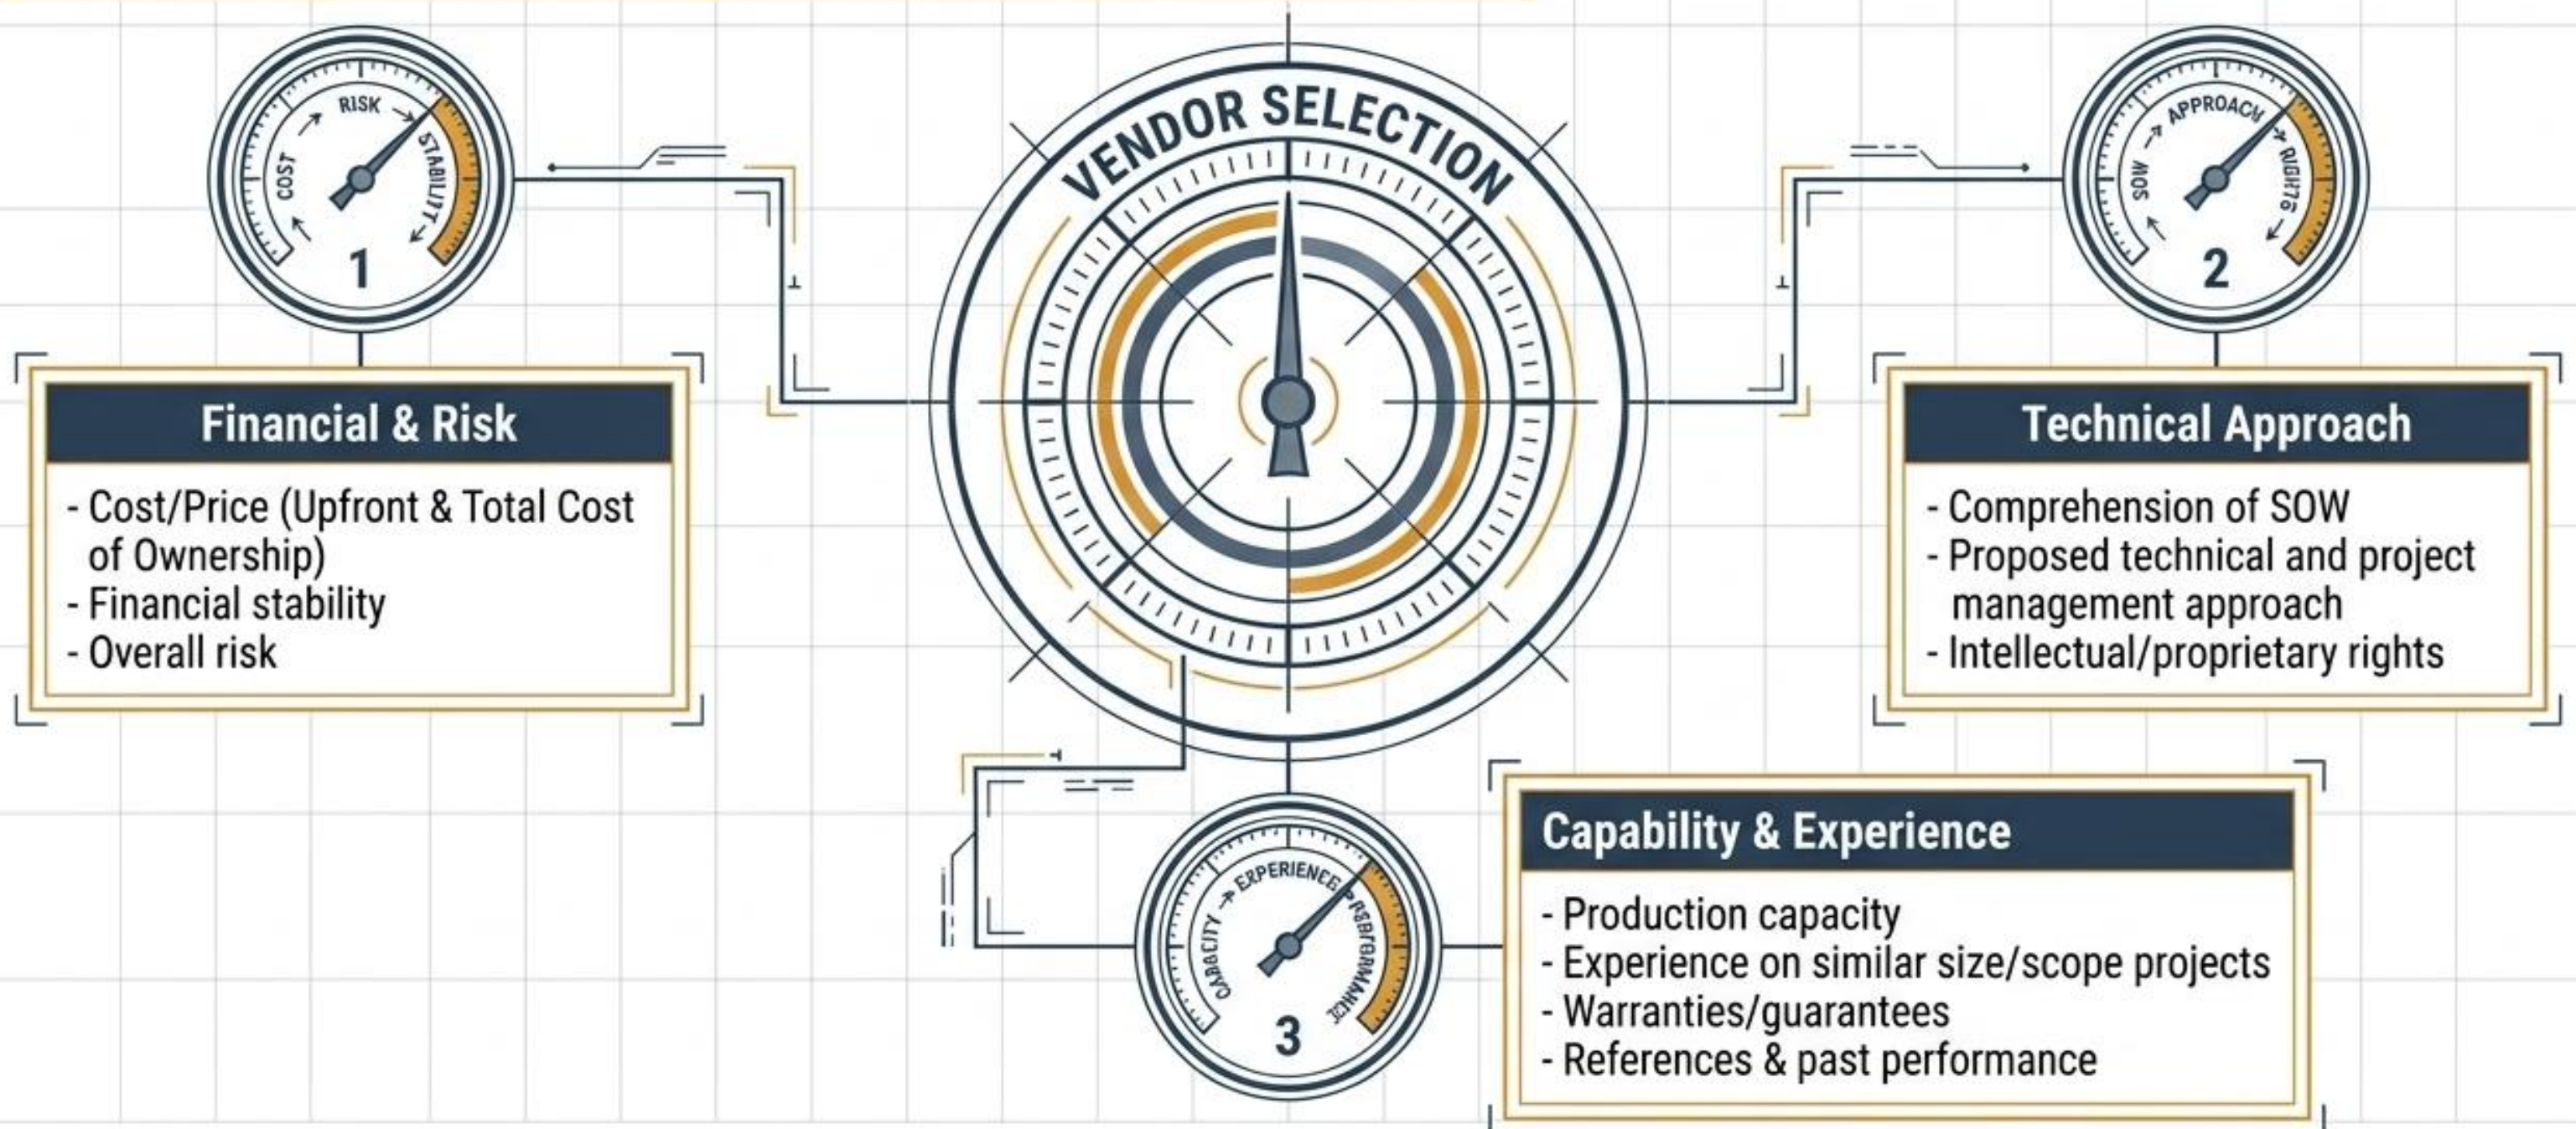


Shifting Focus: Plan Human Resource Management

Core Goal: Documenting roles, responsibilities, reporting relationships, and creating the staffing management plan for all individuals and groups involved in the project.

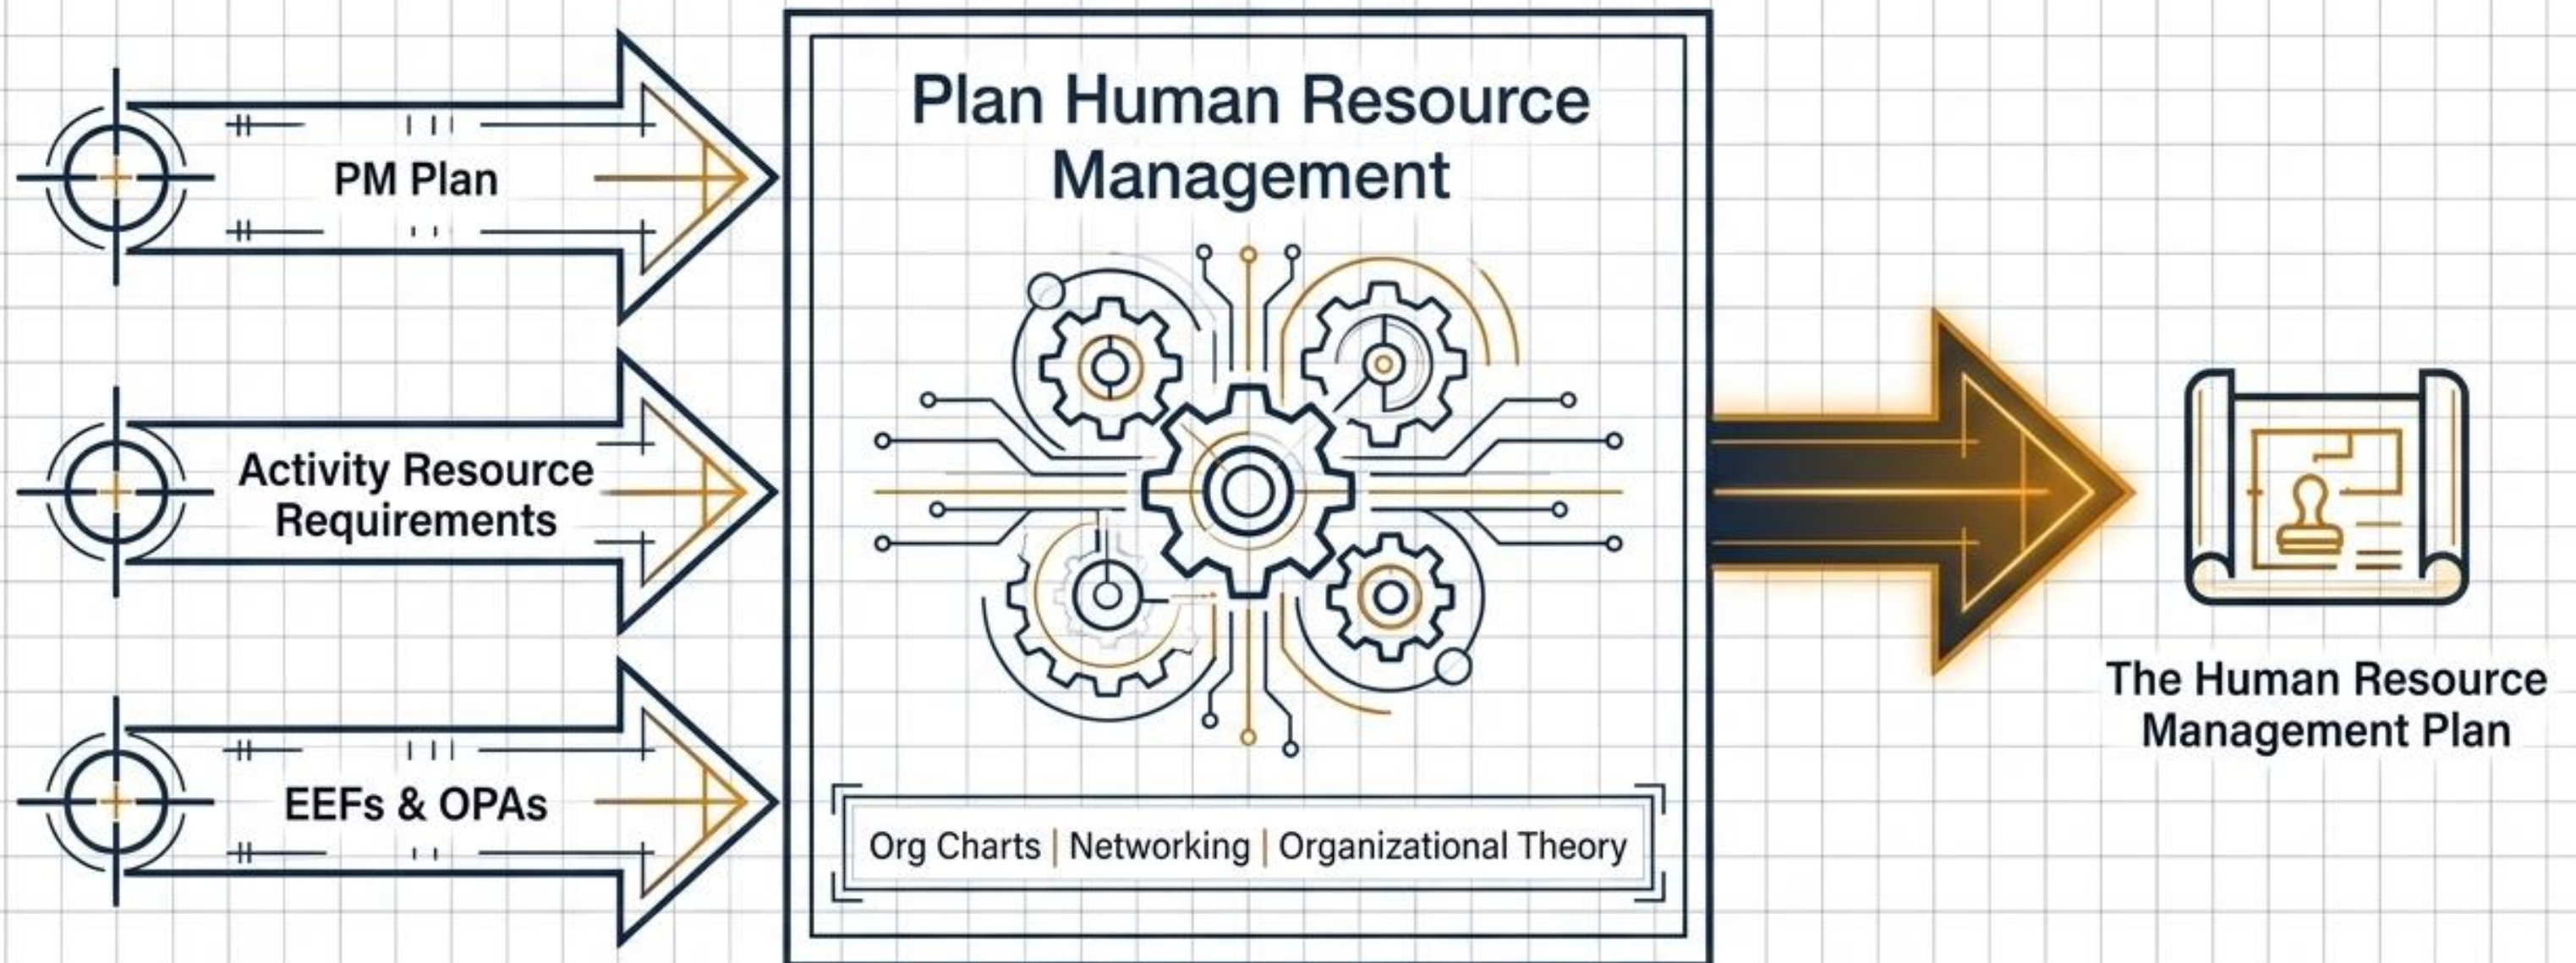


Navigating Enterprise Environmental Factors (EEFs)

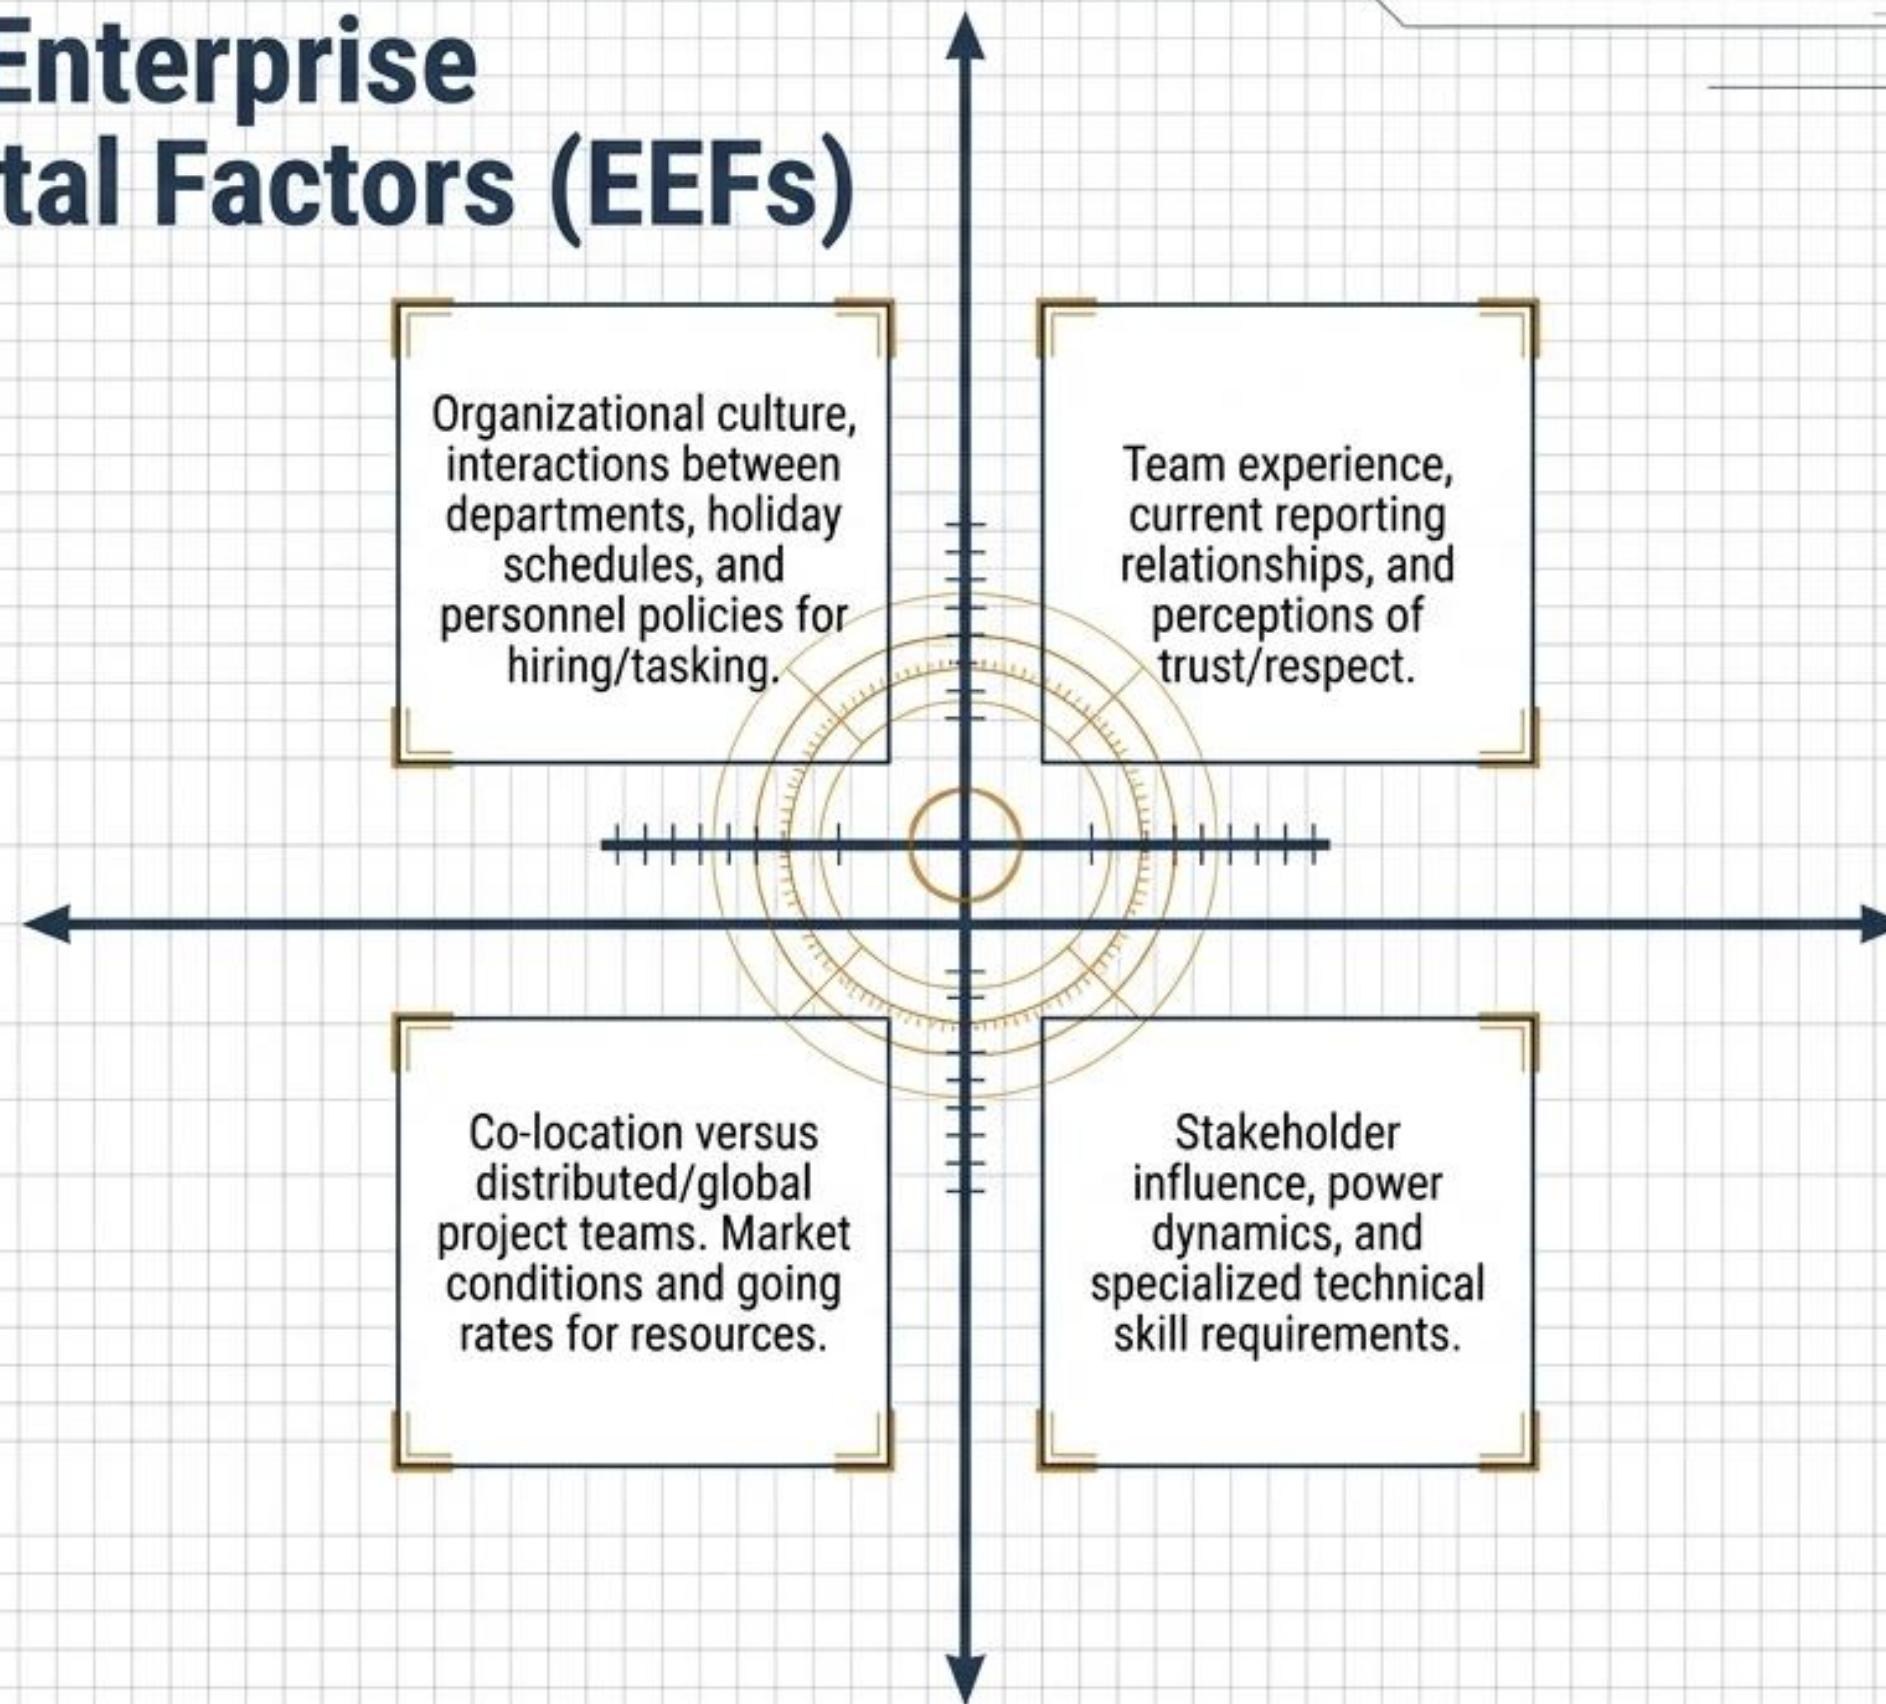

The Three Hard Constraints on HR Planning

HR Planning



Organizational Structures

The matrix power dynamic. Strong matrices grant PMs power; Functional structures grant almost none (requires sponsor support to mandate cooperation).



Collective Bargaining Agreements

Contractual obligations to unions and organized employee associations that dictate working conditions and reporting.




Economic Conditions

Severe limitations on the availability of funds for hiring staff, training, or traveling to locations.

Utilizing Organizational Process Assets (OPAs)

Leveraging historical assets ensures no key responsibilities are missed and drastically reduces planning time.

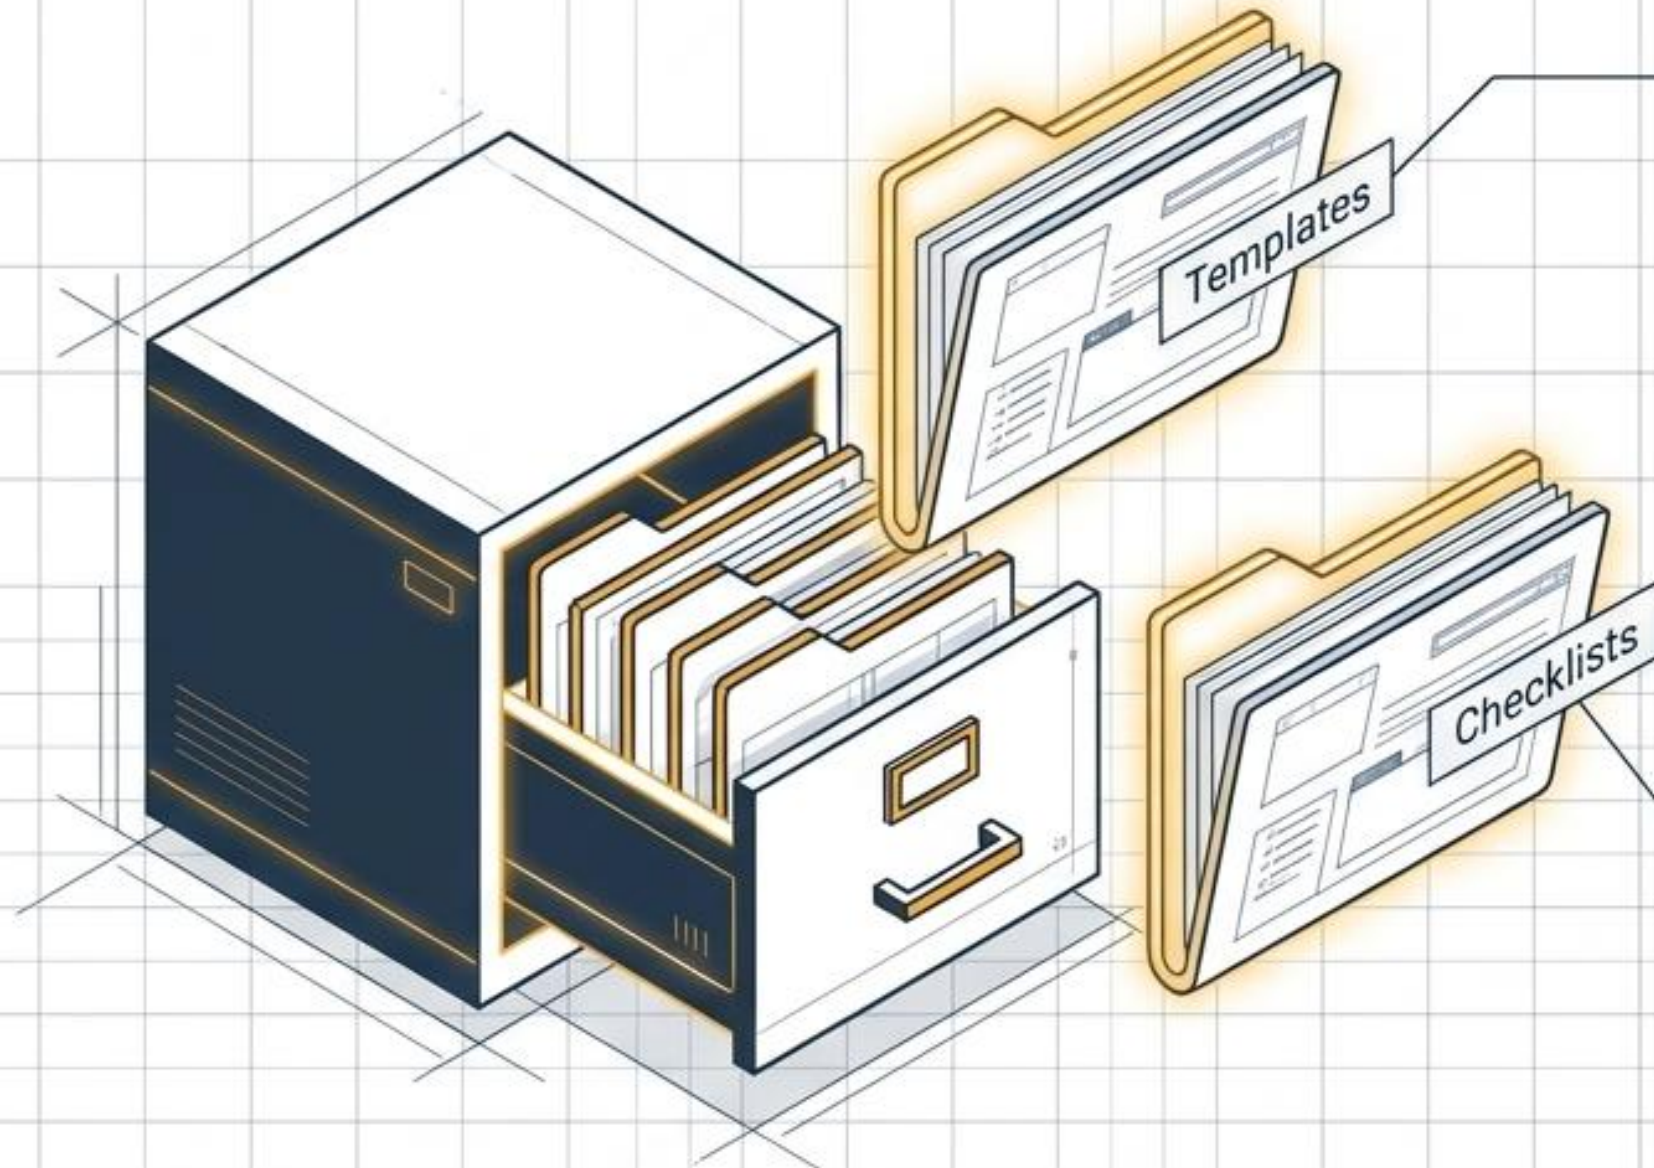


Asset Type 1: Templates

Standardized organizational charts, project descriptions, performance appraisals, and conflict management processes.

Asset Type 2: Checklists

Pre-flight verification for training requirements, skill competency levels, project roles, and safety issues.

Mapping the Team: Organization Chart Taxonomy

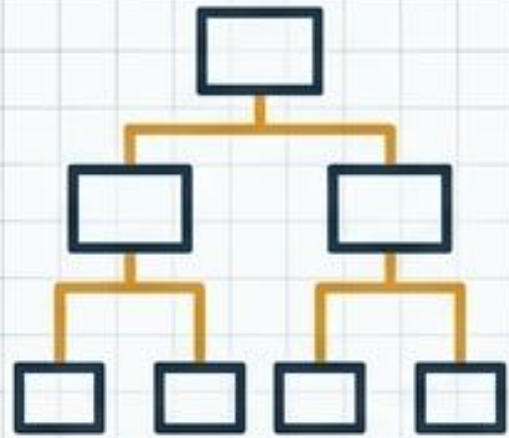

Hierarchical Charts

Top-down structures.

Includes Organizational Breakdown Structure (OBS) for departments/work departments/work units, and Resource Breakdown Structure (RBS) mapping project work to resource types (e.g., tracking average hourly salary for junior vs. senior programmers).



Matrix-Based Charts

Intersecting responsibility grids.

Relates the OBS to the WBS to ensure every work component has every work component has assigned ownership (e.g., RAM/RACI).



Text-Oriented Formats

Detailed role-responsibility-authority forms or position descriptions for complex roles requiring significant detail.

Deep Dive: The RACI Matrix (RAM)

The **Responsibility Assignment Matrix** connects the WBS deliverables to the OBS personnel.

A (Accountable): The ultimate owner who approves/signs off.
Critical Rule: Only one 'A' per task! (e.g., Rae ensures the design is approved).

R (Responsible): Performs the actual work (e.g., Olga designs the software).

	Olga	Rae	Jantira	Nirmit
Design	R	A	C	C
Test	I	R	C	A
Implement	C	I	R	A


C (Consult): Provides input to decisions.

*R = Responsible, A = Accountable, C = Consult, I = Inform

I (Inform): Kept in the loop on decisions/results.


Output Part 1: Defining Roles & Responsibilities

Every defined position in the HR Management Plan must comprehensively document four elements:

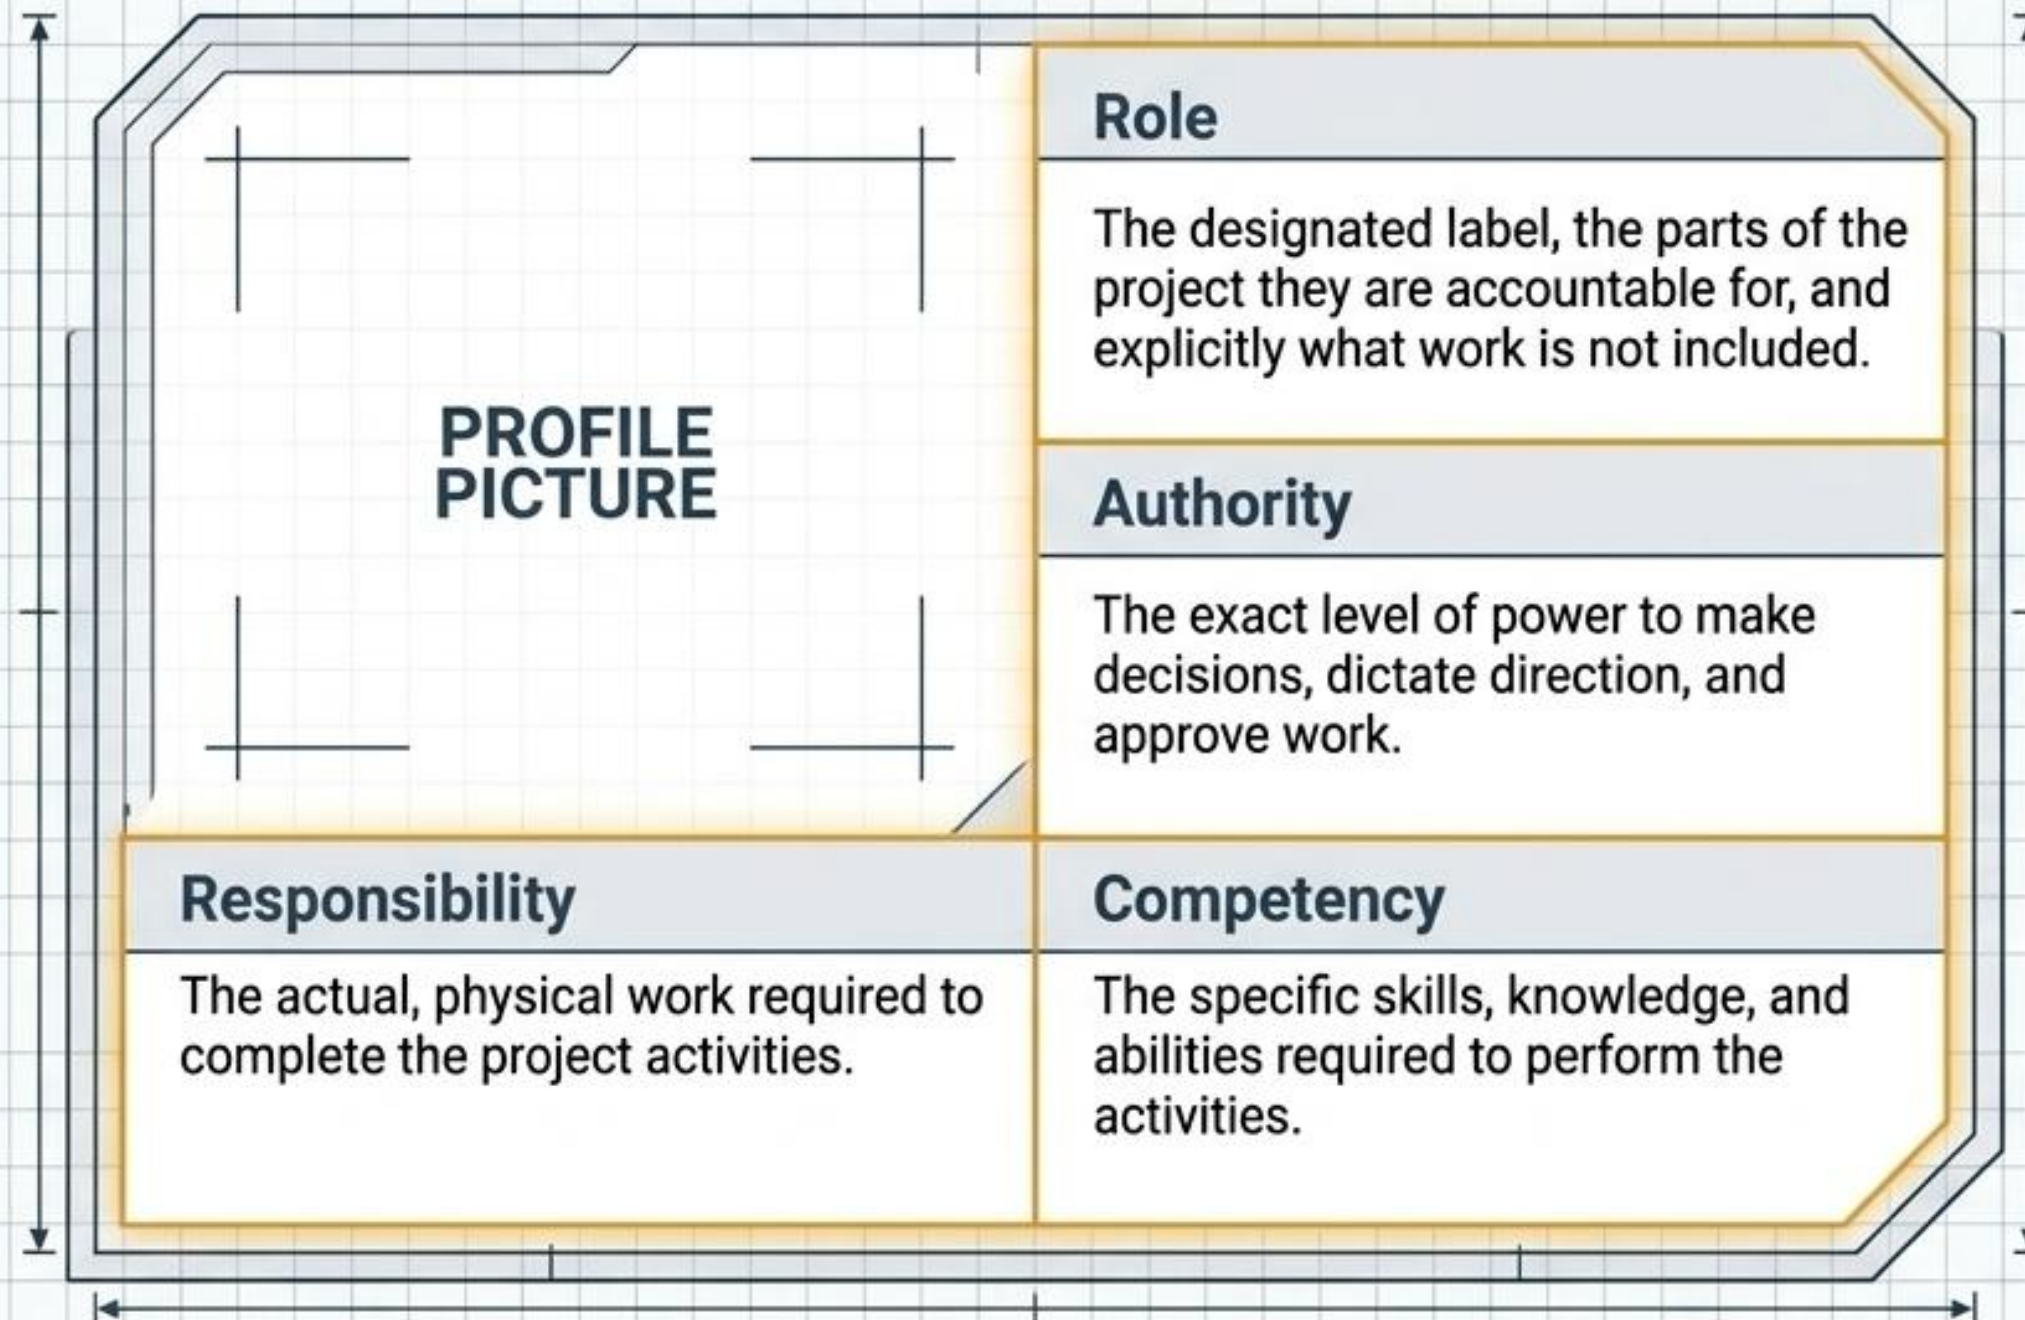

Output Part 2: The Staffing Management Plan

Lifecycle Timeline

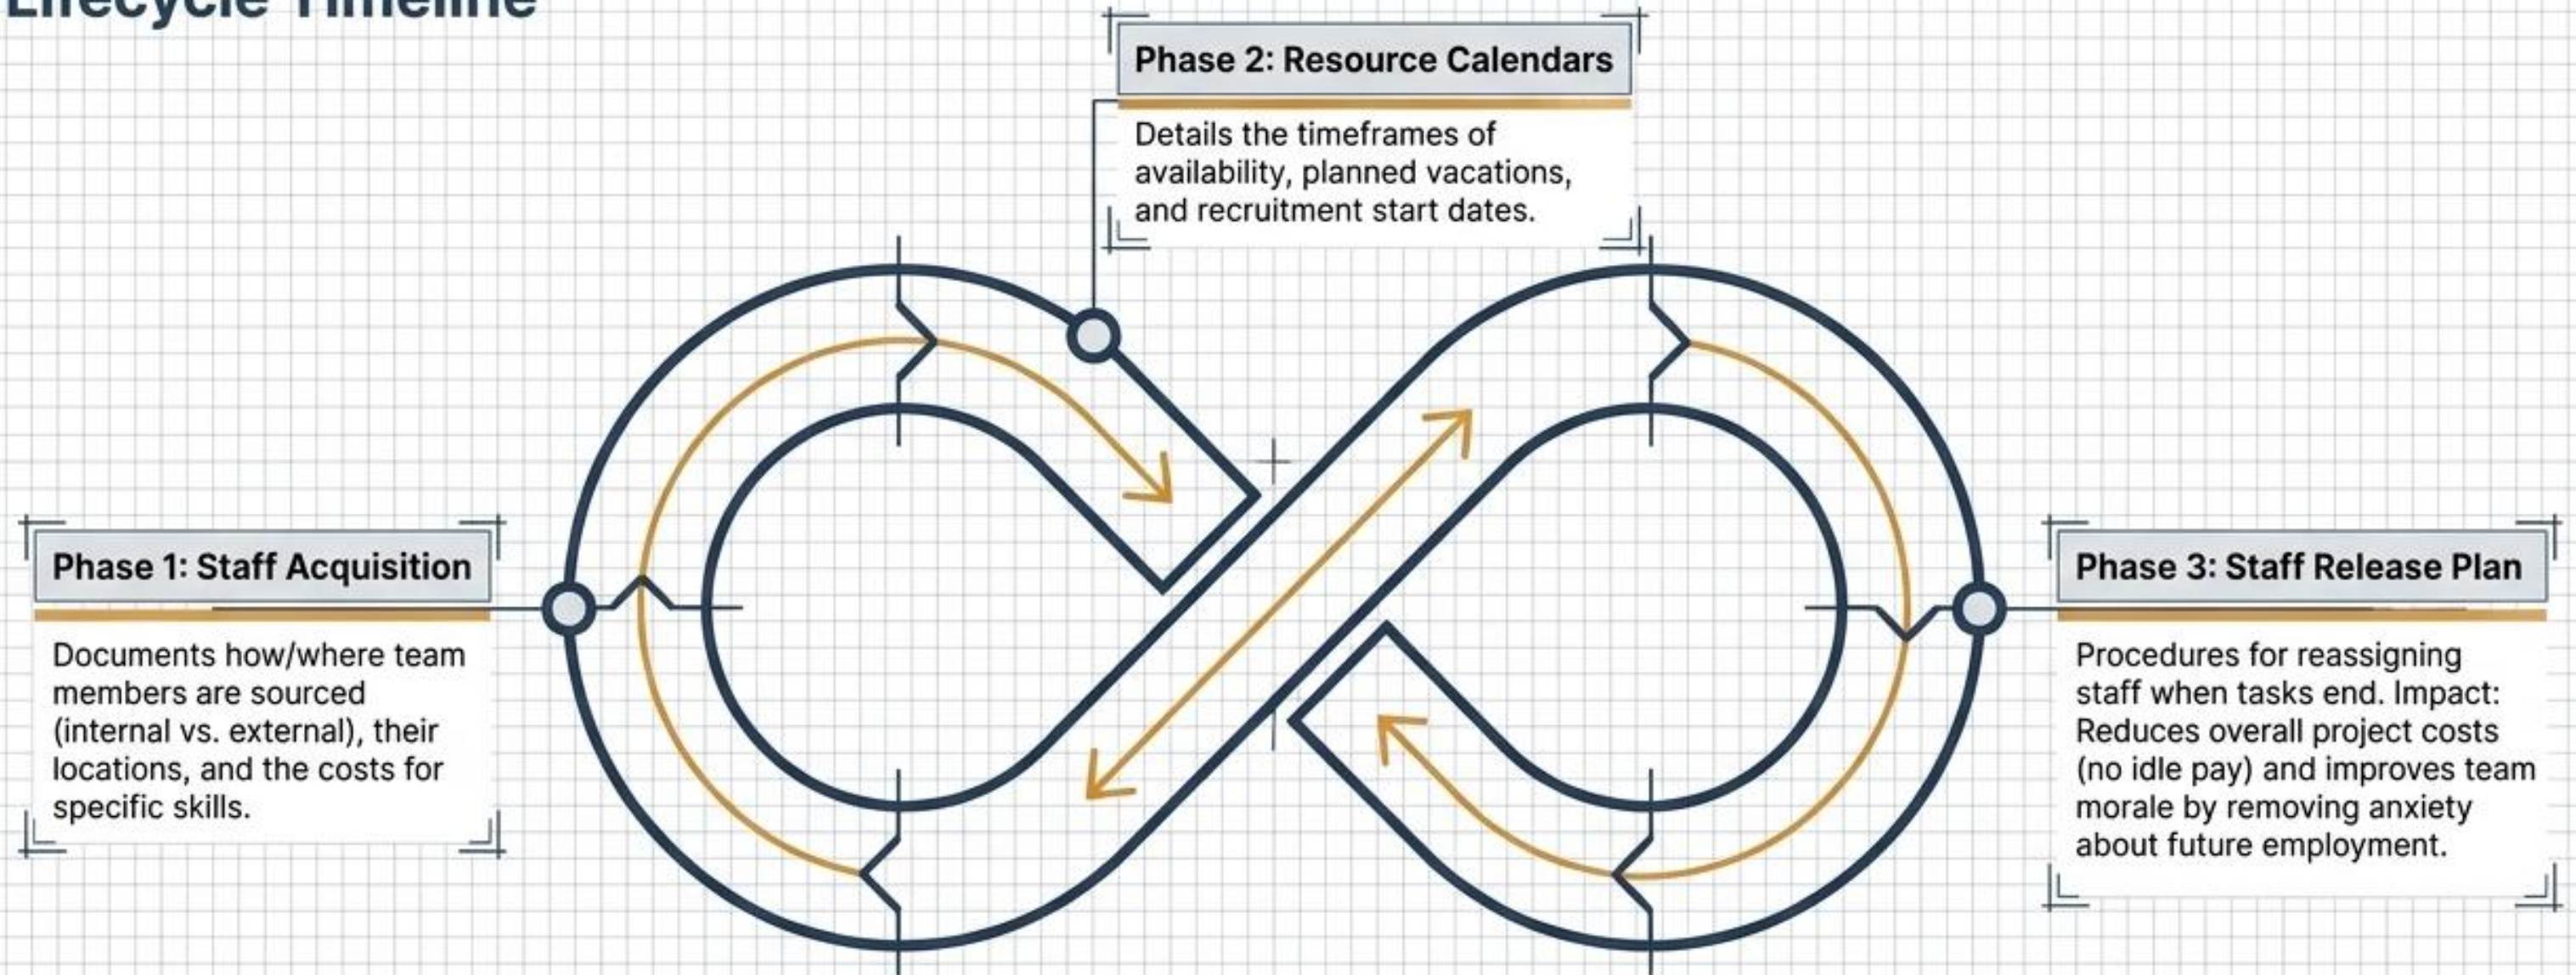

Visualizing Time & Demand: Resource Histograms

Context: A critical component of Resource Calendars within the Staffing Management Plan.

Function: Maps project timeline (horizontal axis) against required staff hours (vertical axis).

Strategic Value: Makes it immediately obvious when peak staffing is required, highlights resource overallocation, and aids in precise budget forecasting and schedule control.

