



Certyfikat PMP: Project Team

Author: dr Zbigniew Galar

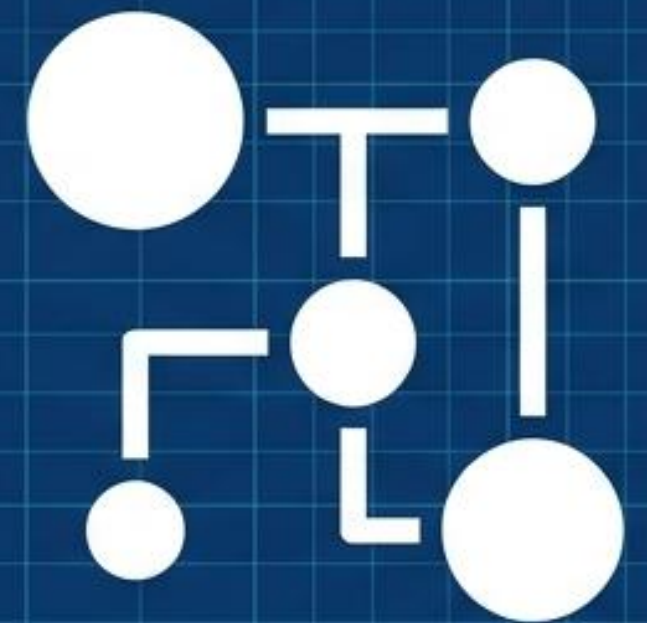

THE REALITY: EXECUTING PROCESS GROUP

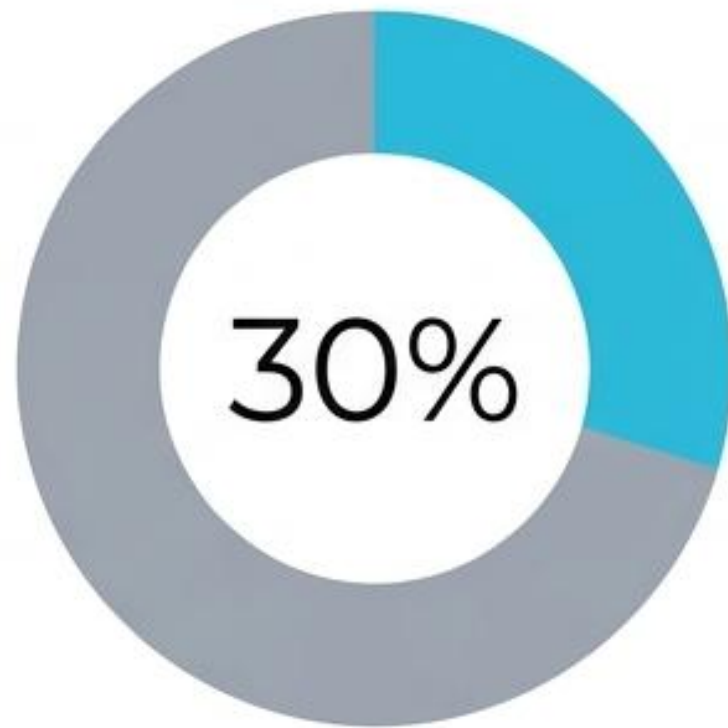

Executing Process Group

Accounts for 30% of PMP Exam Questions.

Majority of Project Budget Expended



Majority of Project Time Expended



THE METAPHOR: WHERE THE RUBBER MEETS THE ROAD




Where the Rubber Meets the Road

- The Executing phase is about putting plans into action.
- The Project Manager is an orchestra conductor: signaling instruments to begin, monitoring the tempo, and orchestrating resources.
- Primary Challenge: Schedule Conflicts.

Process 1: Direct and Manage Project Work

The central action process: carrying out the project management plan, committing resources, and producing the product.

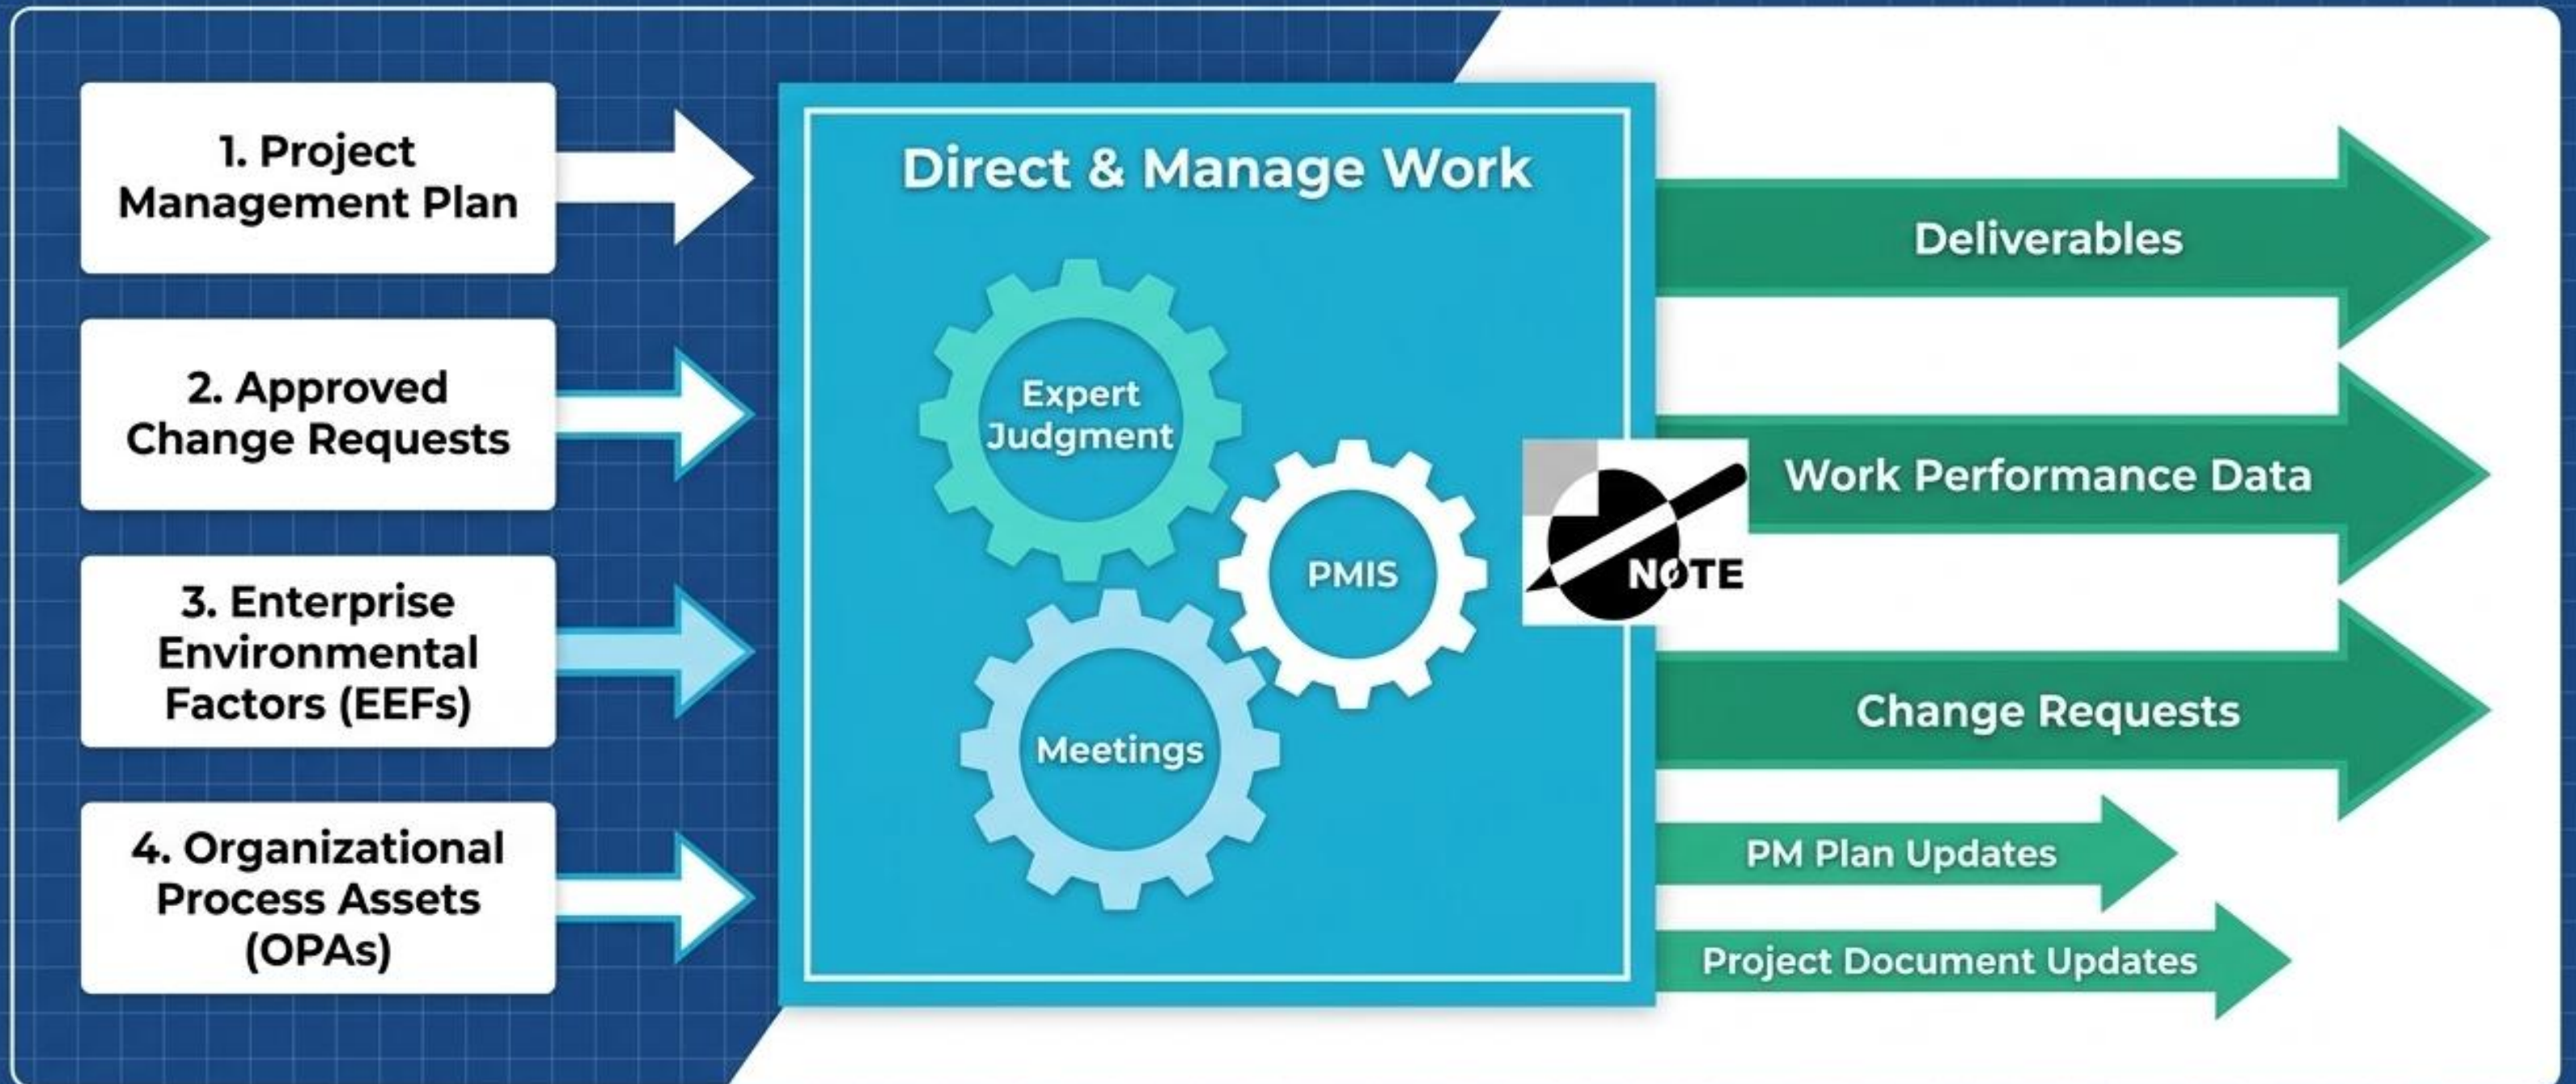

The Pulse of the Project: Work Performance Data


Observing, gathering, and recording activity status.

Schedule & Progress



- Schedule status and progress
- Activity start and end dates
- Percent of overall work complete
- Completion estimates for started activities

Cost & Resources

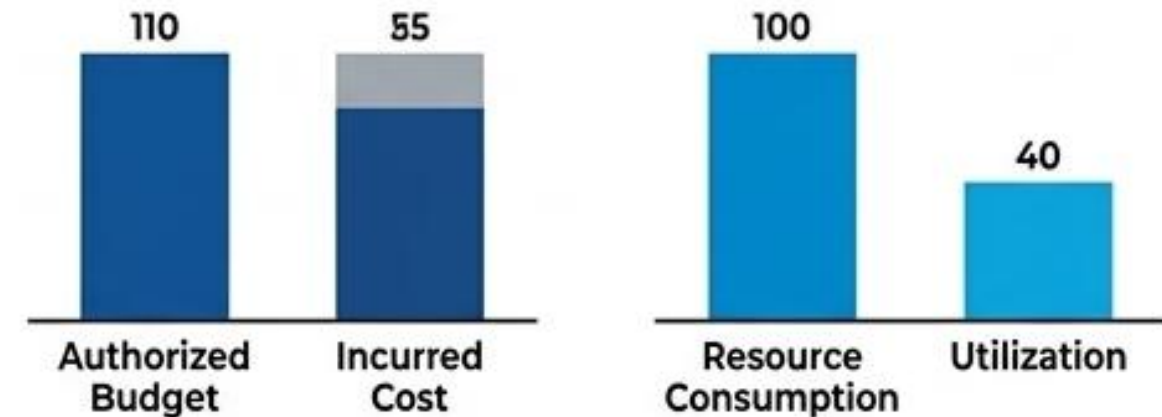

- Status of costs (authorized vs. incurred)
- Resource consumption and utilization



Quality & Deliverables

- Status of deliverable completion
- Adherence to quality standards



Friction & Learning

- Number of change requests generated
- Lessons learned captured

Navigating Friction: Change Requests Matrix

Corrective Actions	Preventive Actions	Defect Repairs	Updates
Trigger: Misalignment with PM Plan.	Trigger: Identified Risk.	Trigger: Quality Failure.	Trigger: Evolving Reality.
Time Orientation: Future-focused.	Time Orientation: Future-focused.	Time Orientation: Past-focused (fixing what is broken).	Time Orientation: Present-focused.
Goal: Realign anticipated future outcomes with the baseline.	Goal: Reduce potential negative impacts of risk events (e.g., contingency plans).	Goal: Correct non-conforming components. (Note: Validated Defect Repair = reinspection of the fix).	Goal: Modify project documents (scope, budget, schedule) to capture new realities.

Process 2: Acquire Project Team

Core Constraint: The Project Manager often lacks direct authority over resource selection due to matrix structures or collective bargaining.

Inputs - Raw Materials



1. Human Resource Management Plan (Roles, Staffing Plan)



2. Enterprise Environmental Factors



3. Organizational Process Assets

Manufacturing Funnel

Acquire Project Team

- * Preassignment
- * Negotiation
- * Acquisition
- * Virtual Teams
- * Multi-criteria Decision Analysis



Outputs - Finished Goods


Project Staff Assignments

Resource Calendars

PM Plan Updates

The Resource Environment: EEFs vs. OPAs

Enterprise Environmental Factors (EEFs)

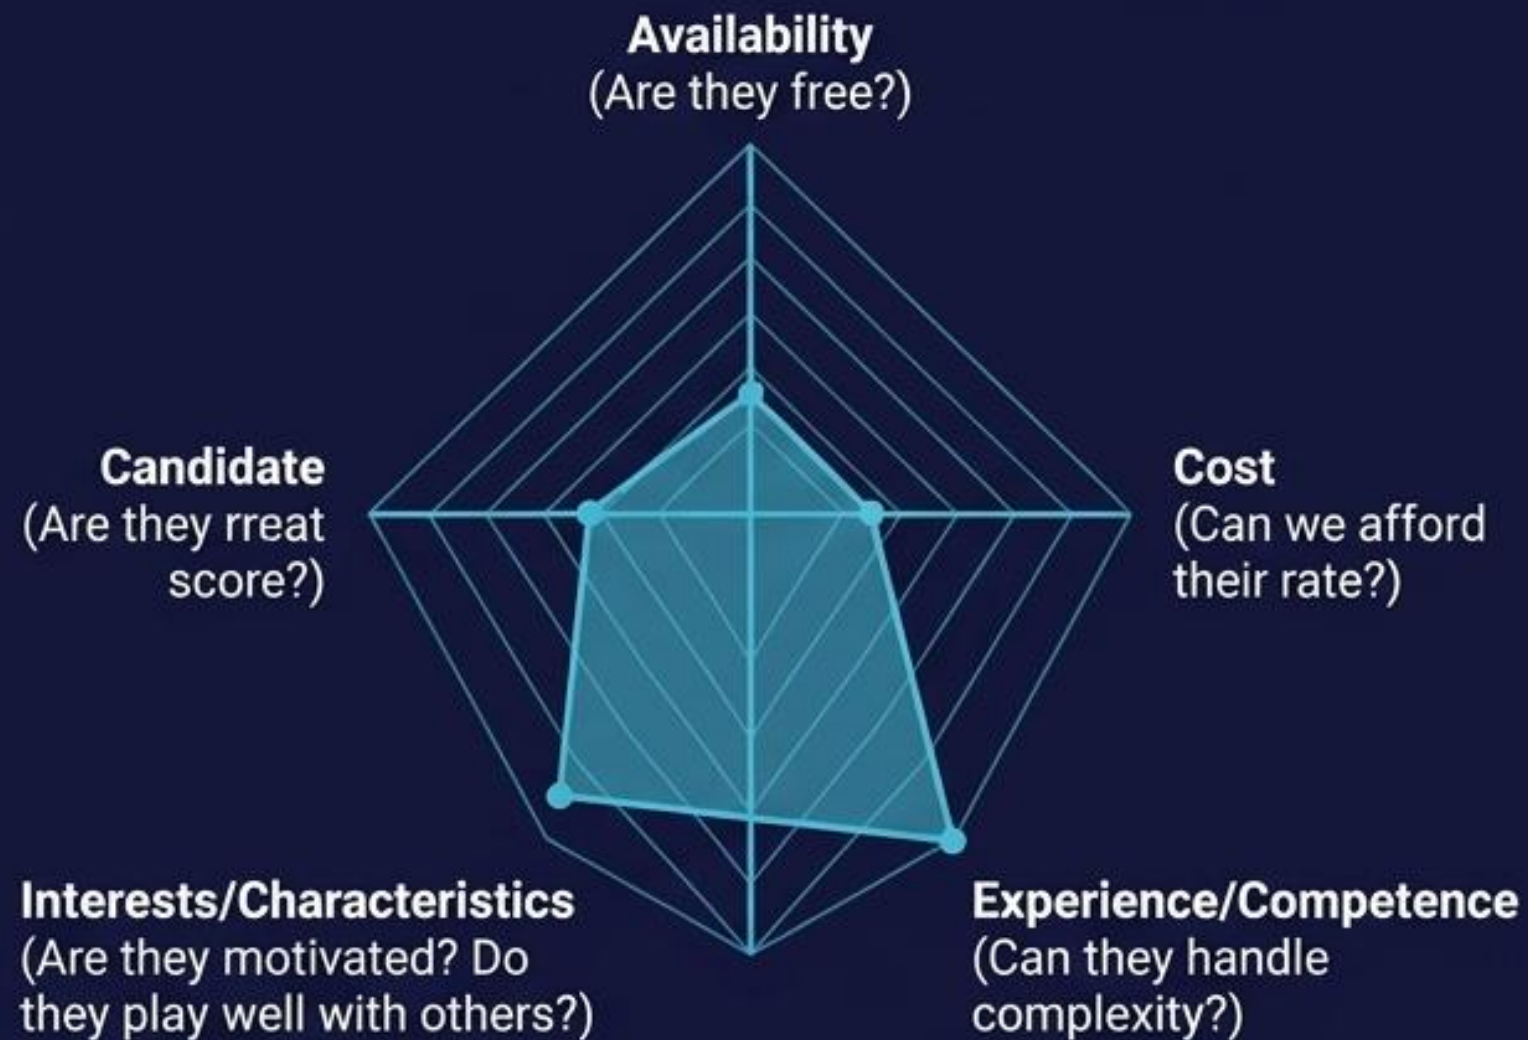

Organizational Process Assets (OPAs)

OPAs dictate the rules of engagement. Standard recruitment practices, organizational policies, and procedures act as hard constraints when acquiring staff.



The Acquisition Toolkit

Preassignment

Promised Resources

Staff guaranteed in the project charter or bid proposal.

Multi-criteria Decision Analysis

Analytical Scoring

Ranking candidates based on experience, education, and skills.

Virtual Teams

Distributed Action

Utilizing remote talent regardless of geography or mobility.

Negotiation

Internal Bartering

Securing staff from functional managers. Must balance availability with actual competency.


Acquisition

External Action

Hiring outside contractors or employees when internal competencies are lacking.

The Virtual Team Framework

Structural Benefits



- Bypasses geographic limitations.
- Accommodates different shifts and working hours.
- Includes individuals with mobility limitations.



Management Protocols



- Requires strict communication protocols and clear decision-making processes.
- Crucial PM Duty: The PM must actively recognize and give credit for remote performance, as distributed team members cannot visually observe each other's efforts.


Outputs of Acquisition

Project Staff Assignments



The final team directory.
Assigning specific names to the roles identified in RAM charts and organizational charts.

Resource Calendars

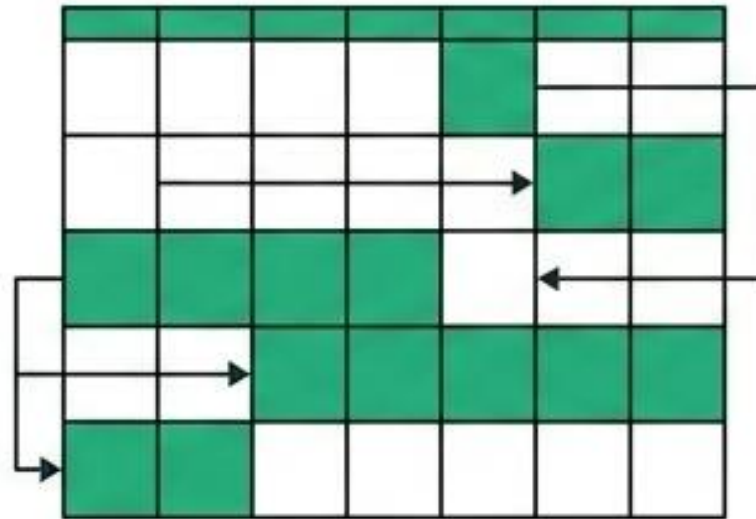

Documents exact time periods team members are available.
Highlight: The 'Composite Resource Calendar' aggregates availability, capabilities, and skills across all potential resources.

PM Plan Updates



Updating the HR and Staffing Management plans to reflect actual assigned personnel and any changes due to promotions or departures.

The Project Manager's Dual Engine

