


CERTYFIKAT PMP: PROCUREMENT CONTROLLING

dr Zbigniew Galar



THE INFORMATION PROCESSING ENGINE




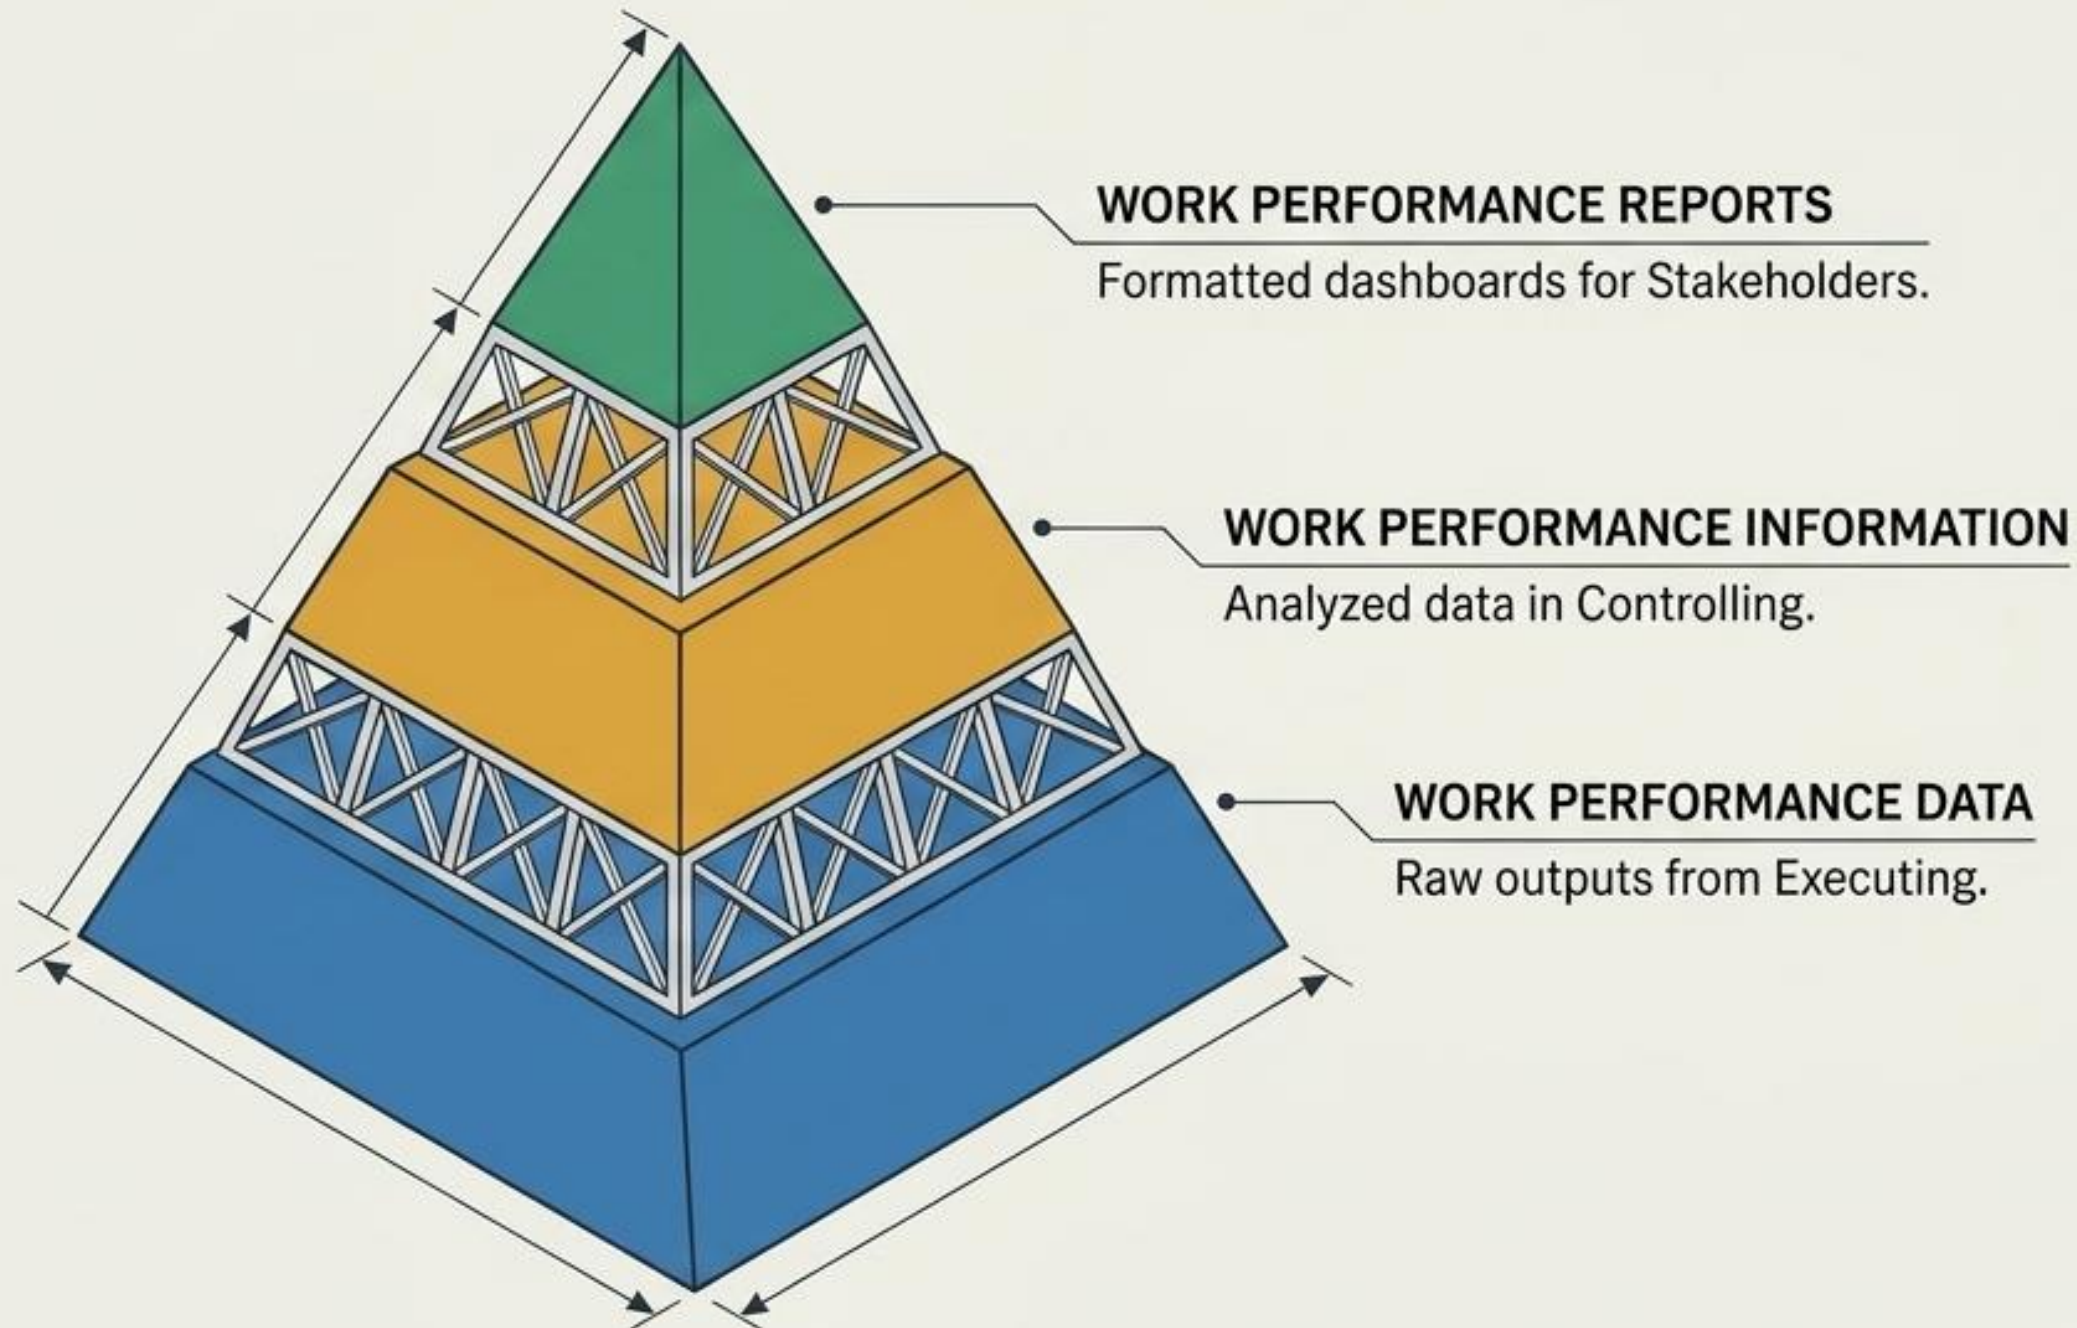


EXAM SPOTLIGHT

Work performance reports are the primary output of Monitor and Control Project Work.

They create awareness of issues, drive decisions, and determine necessary actions.

WORK PERFORMANCE REPORTS: THE DIAGNOSTIC DASHBOARD

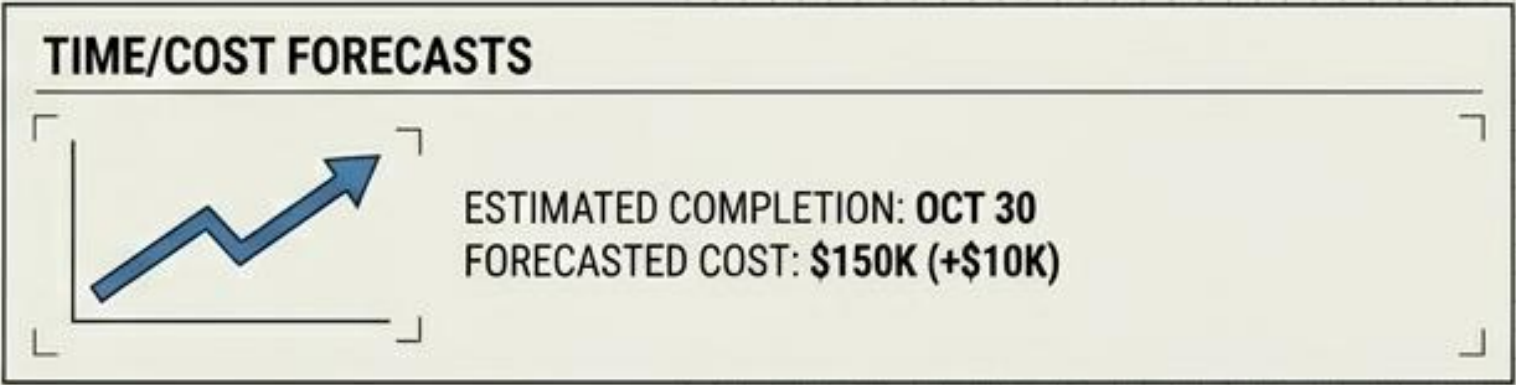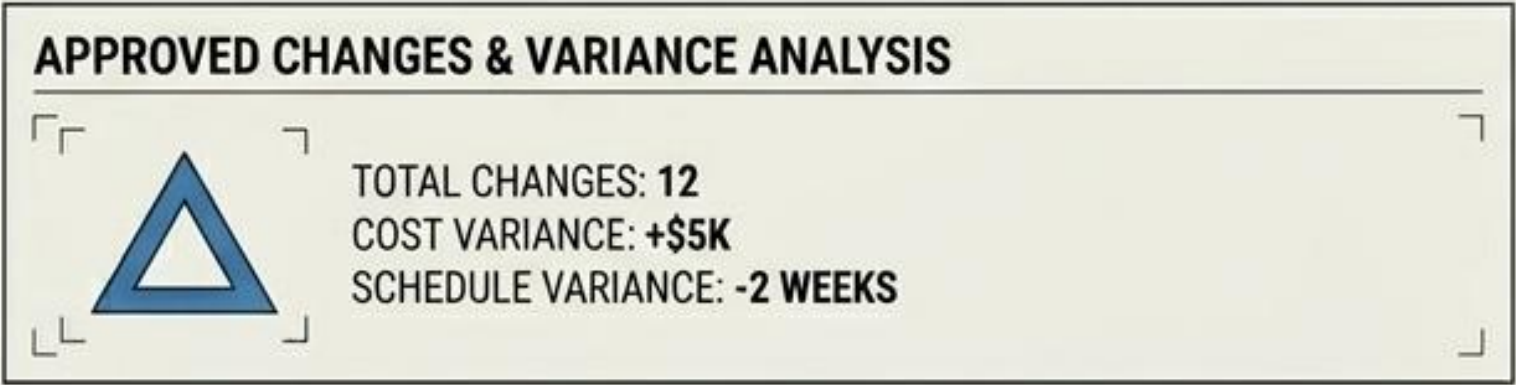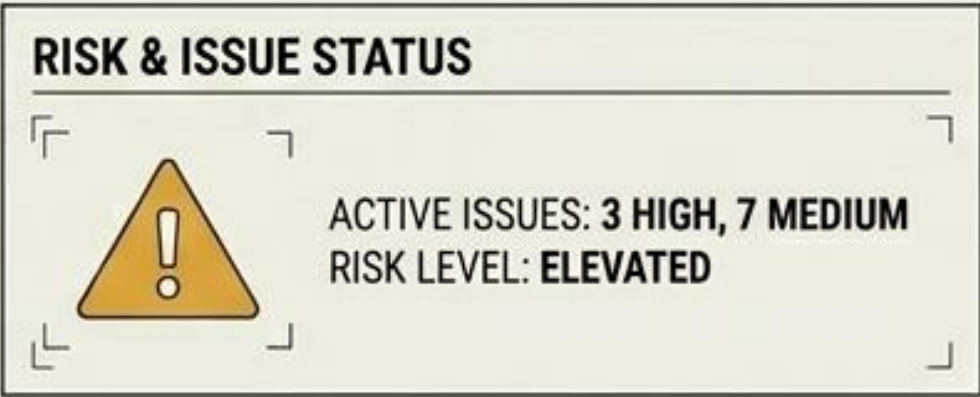


THE CHANGE REQUEST MATRIX




CORRECTIVE ACTIONS

Brings the work of the project into alignment with expected future performance.




PREVENTIVE ACTIONS

Implemented to help reduce the probability of negative project risks.




DEFECT REPAIRS

Corrects or replaces components that are substandard or malfunctioning.




SUB-SYSTEM ACTIVATION: CONTROLLING PROCUREMENTS

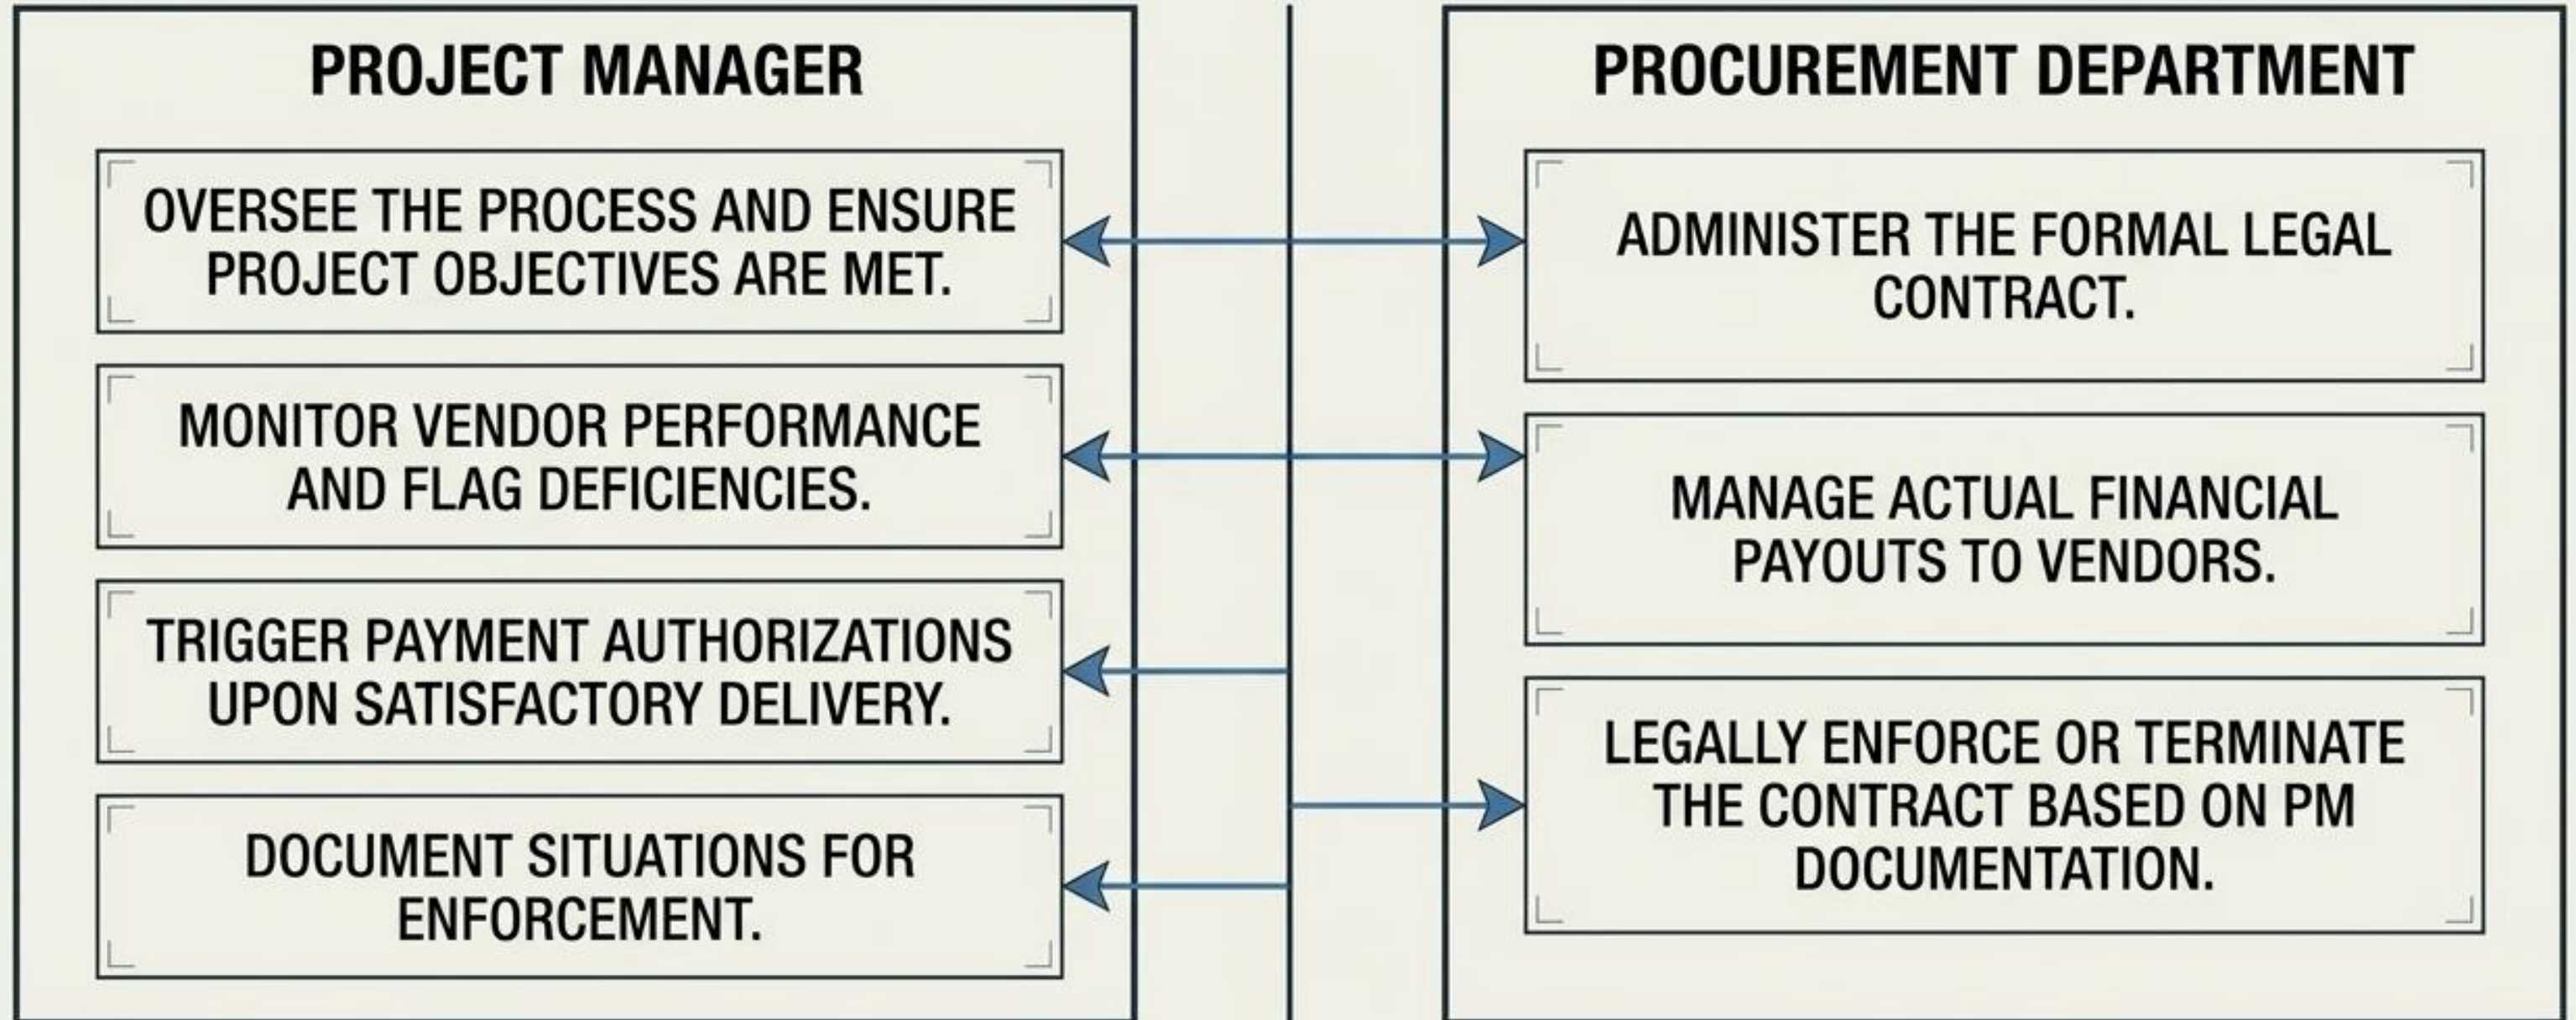

EXAM CONCEPT: BUYERS AND SELLERS ARE EQUALLY RESPONSIBLE FOR MONITORING THE CONTRACT. EACH HAS A VESTED INTEREST IN ENSURING CONTRACTUAL OBLIGATIONS ARE MET.


THE INTERFACE MULTIPLIER: MANAGING VENDOR ECOSYSTEMS

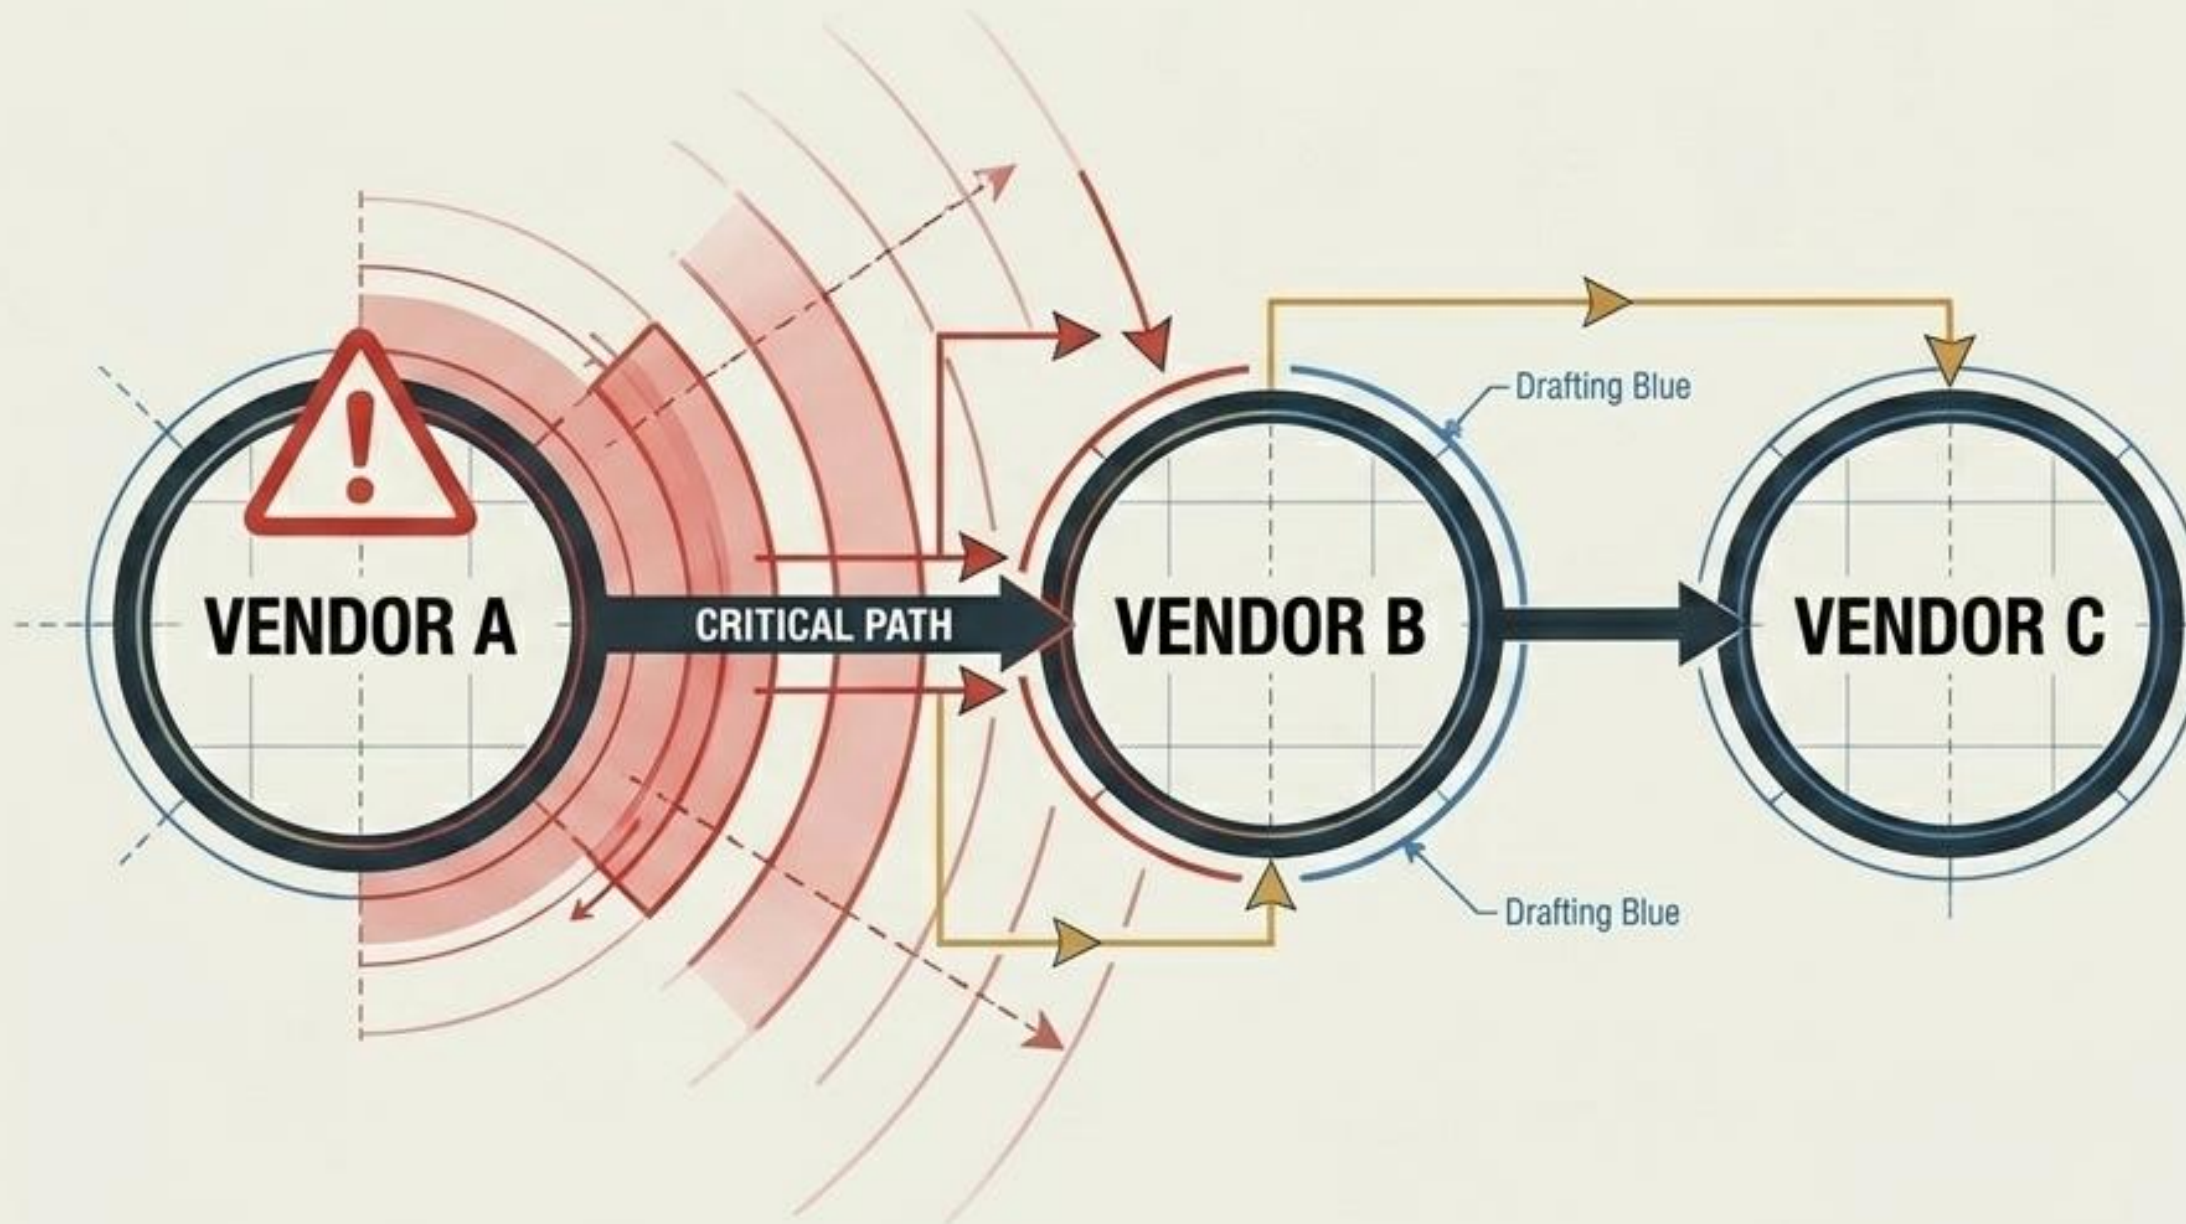

When multiple vendors provide goods and services, the PM must coordinate the interfaces among them.

The team must be aware of all agreements to avoid inadvertently violating contract terms.

SYSTEM ARCHITECTURE: PROCUREMENT ITTO BLUEPRINT

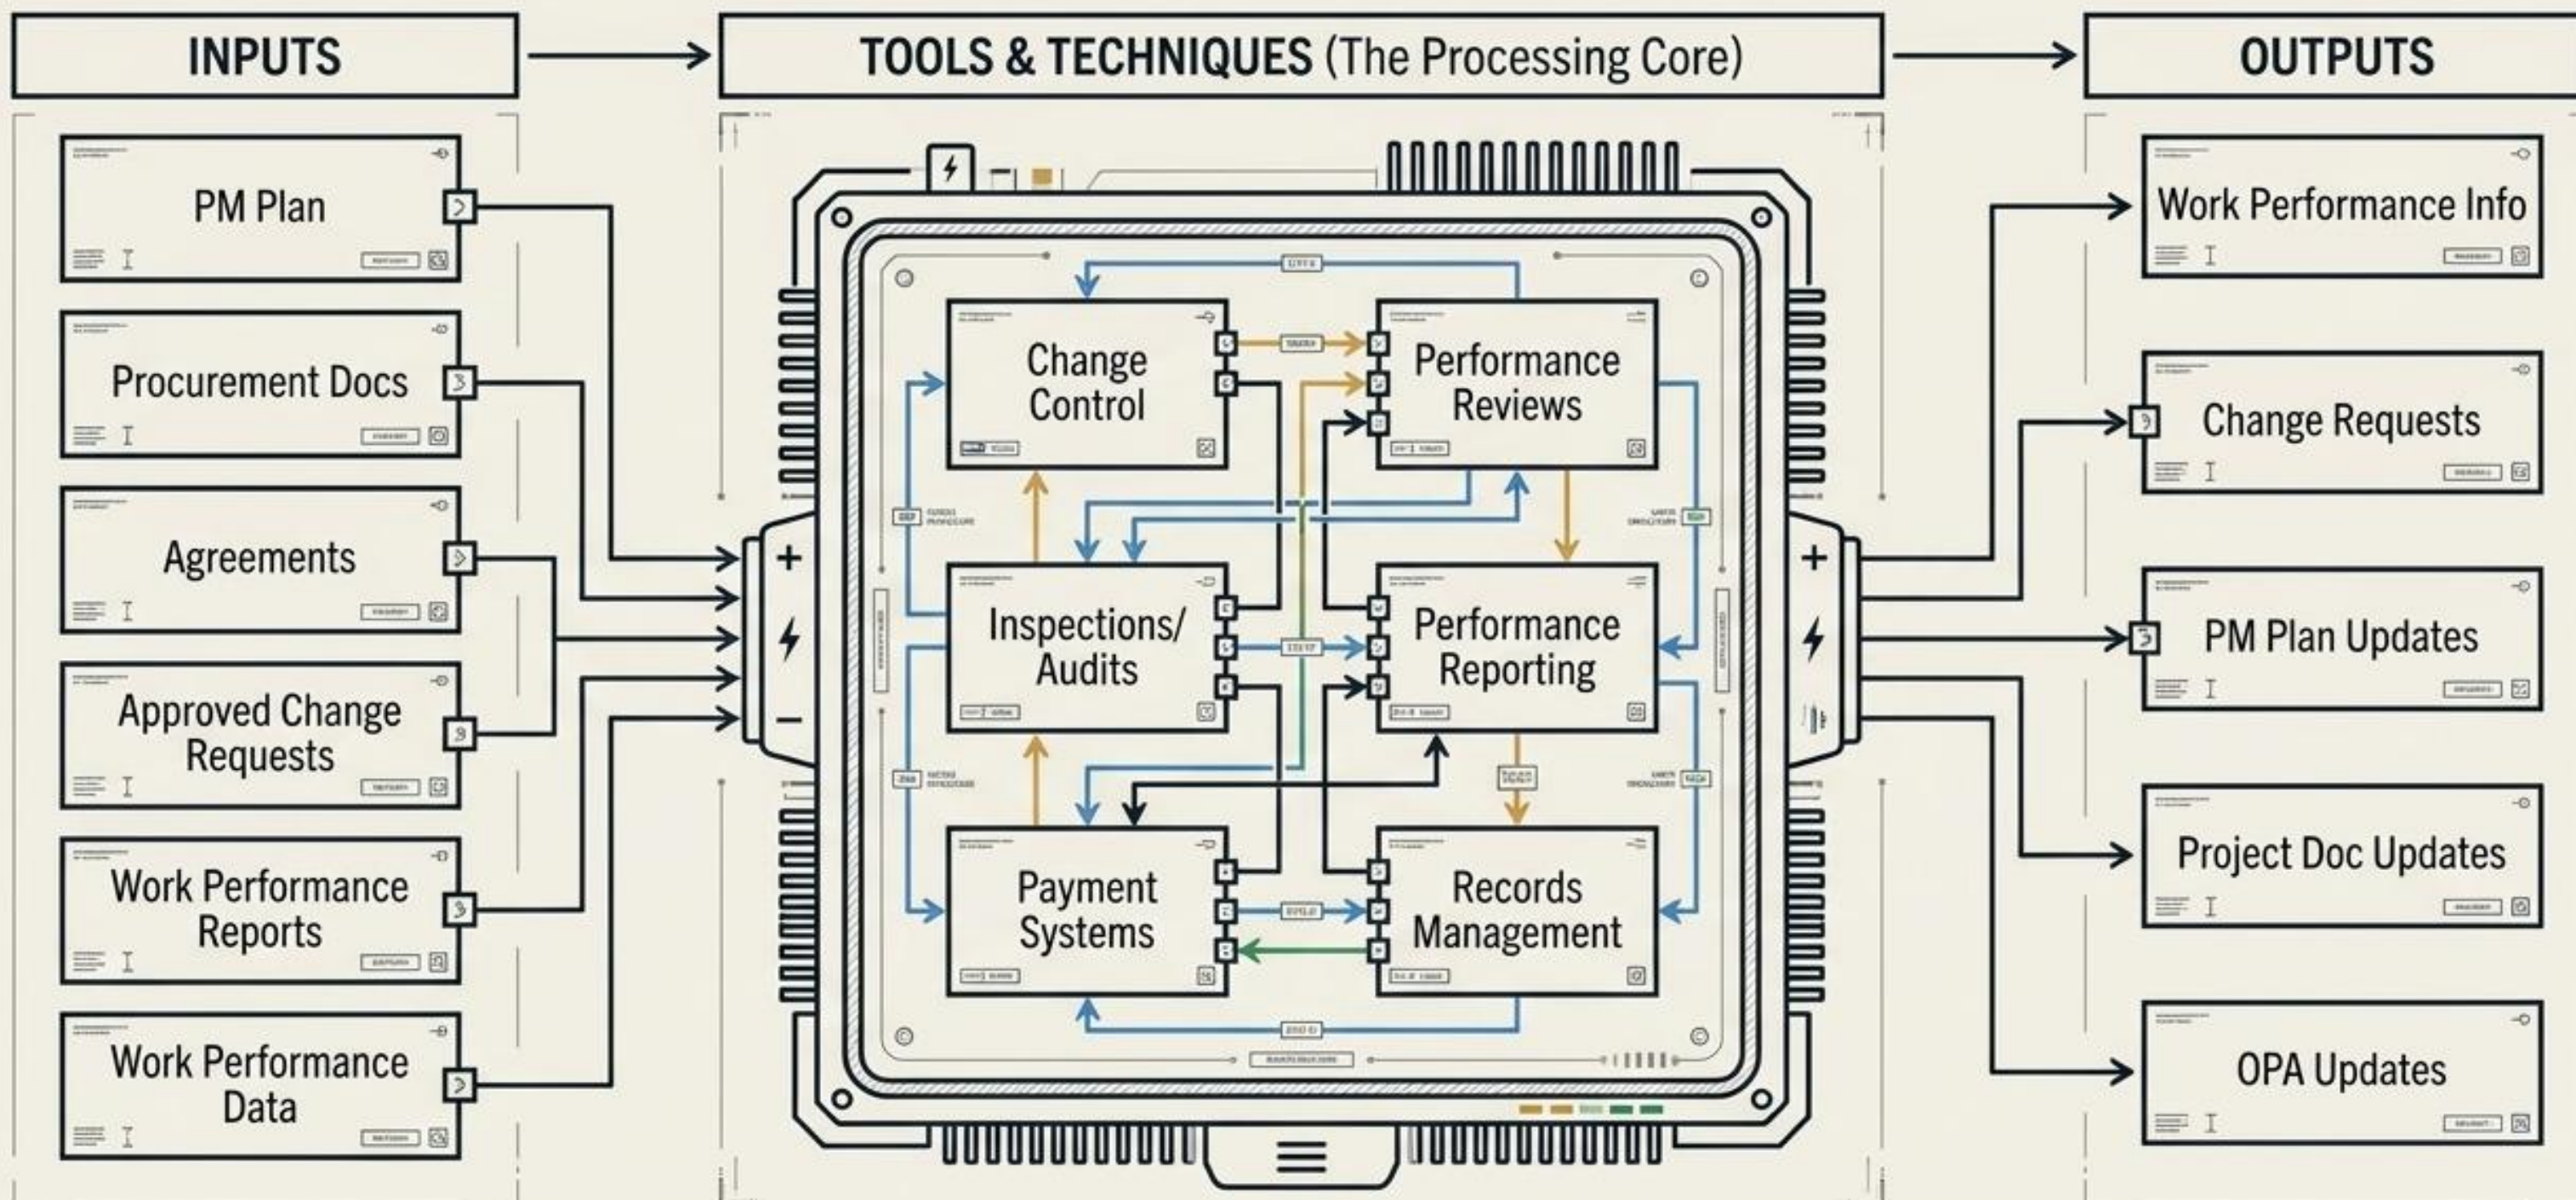

INPUT FEED: EVALUATING VENDOR BASELINE DATA

WORK PERFORMANCE DATA



Sourced directly from
Direct and Manage
Project Work.

WORK PERFORMANCE REPORTS




Technical documentation
developed by the seller,
paired with Seller Invoicing
and necessary supporting
documentation.

WORK PERFORMANCE INFORMATION



Analyzed details regarding
deliverables completion
status, physical,
physical quality, and exact
costs incurred to date.

THE CONTRACT TERMINATION TRIAD

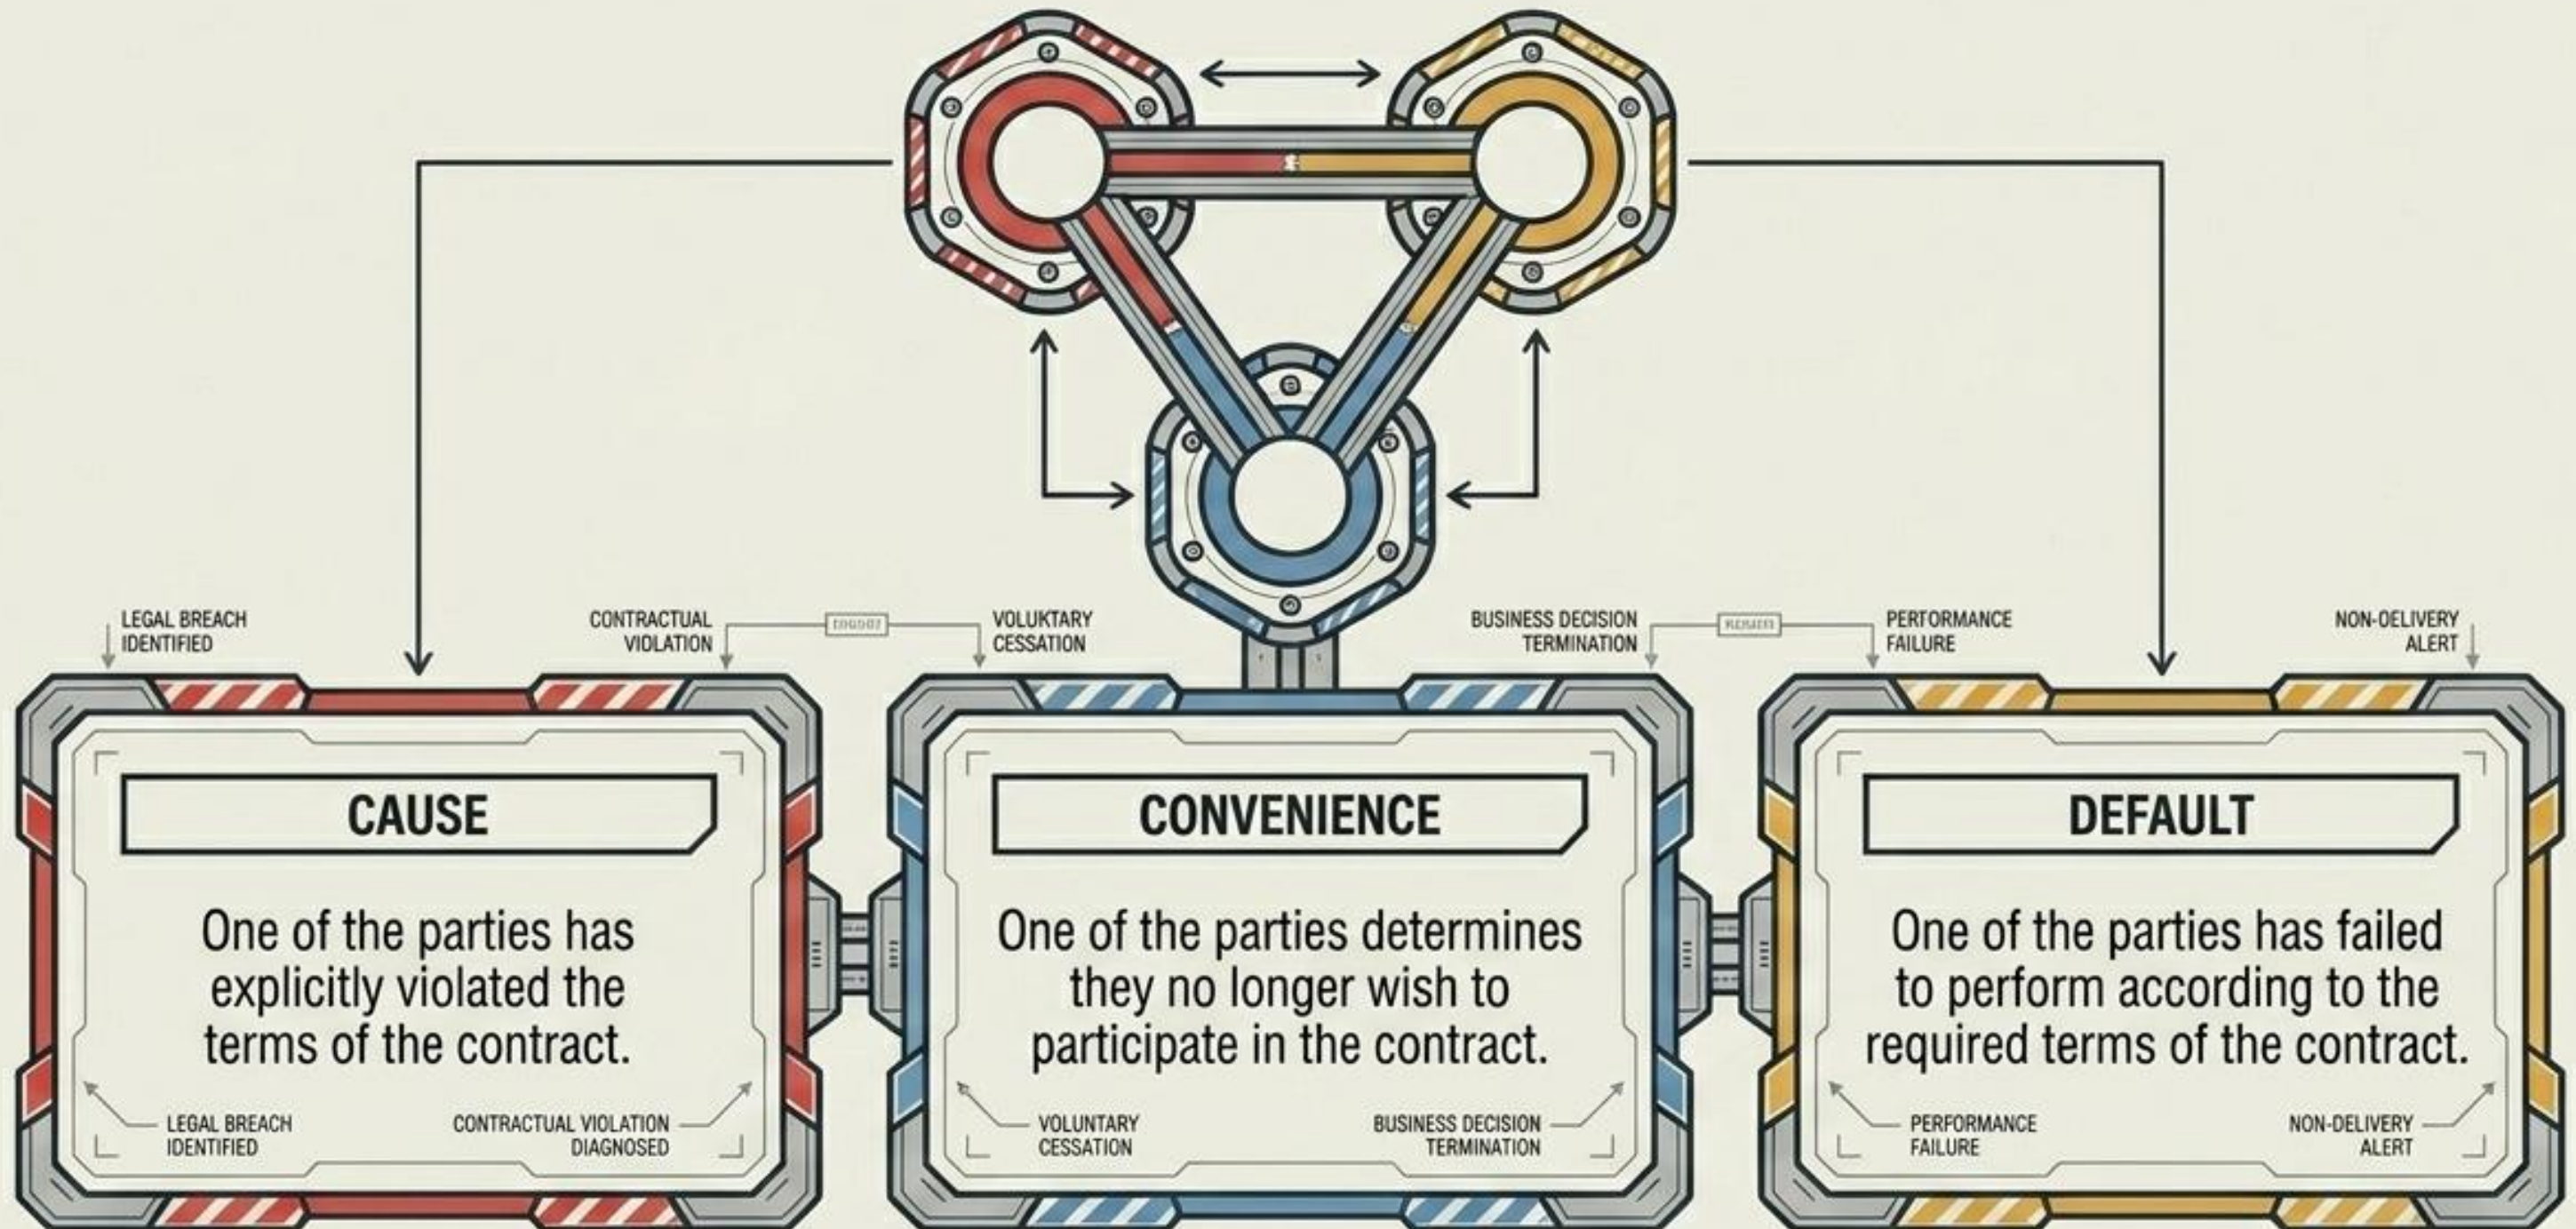

THE PROCESSING ENGINE: PROCUREMENT PERFORMANCE REVIEWS




CONTRACT CHANGE CONTROL SYSTEM


A formal system to submit change requests, establish

approval processes, outline authority levels, and track
Includes defined dispute resolution procedures.

CLAIMS ADMINISTRATION: DISPUTE RESOLUTION SPECTRUM

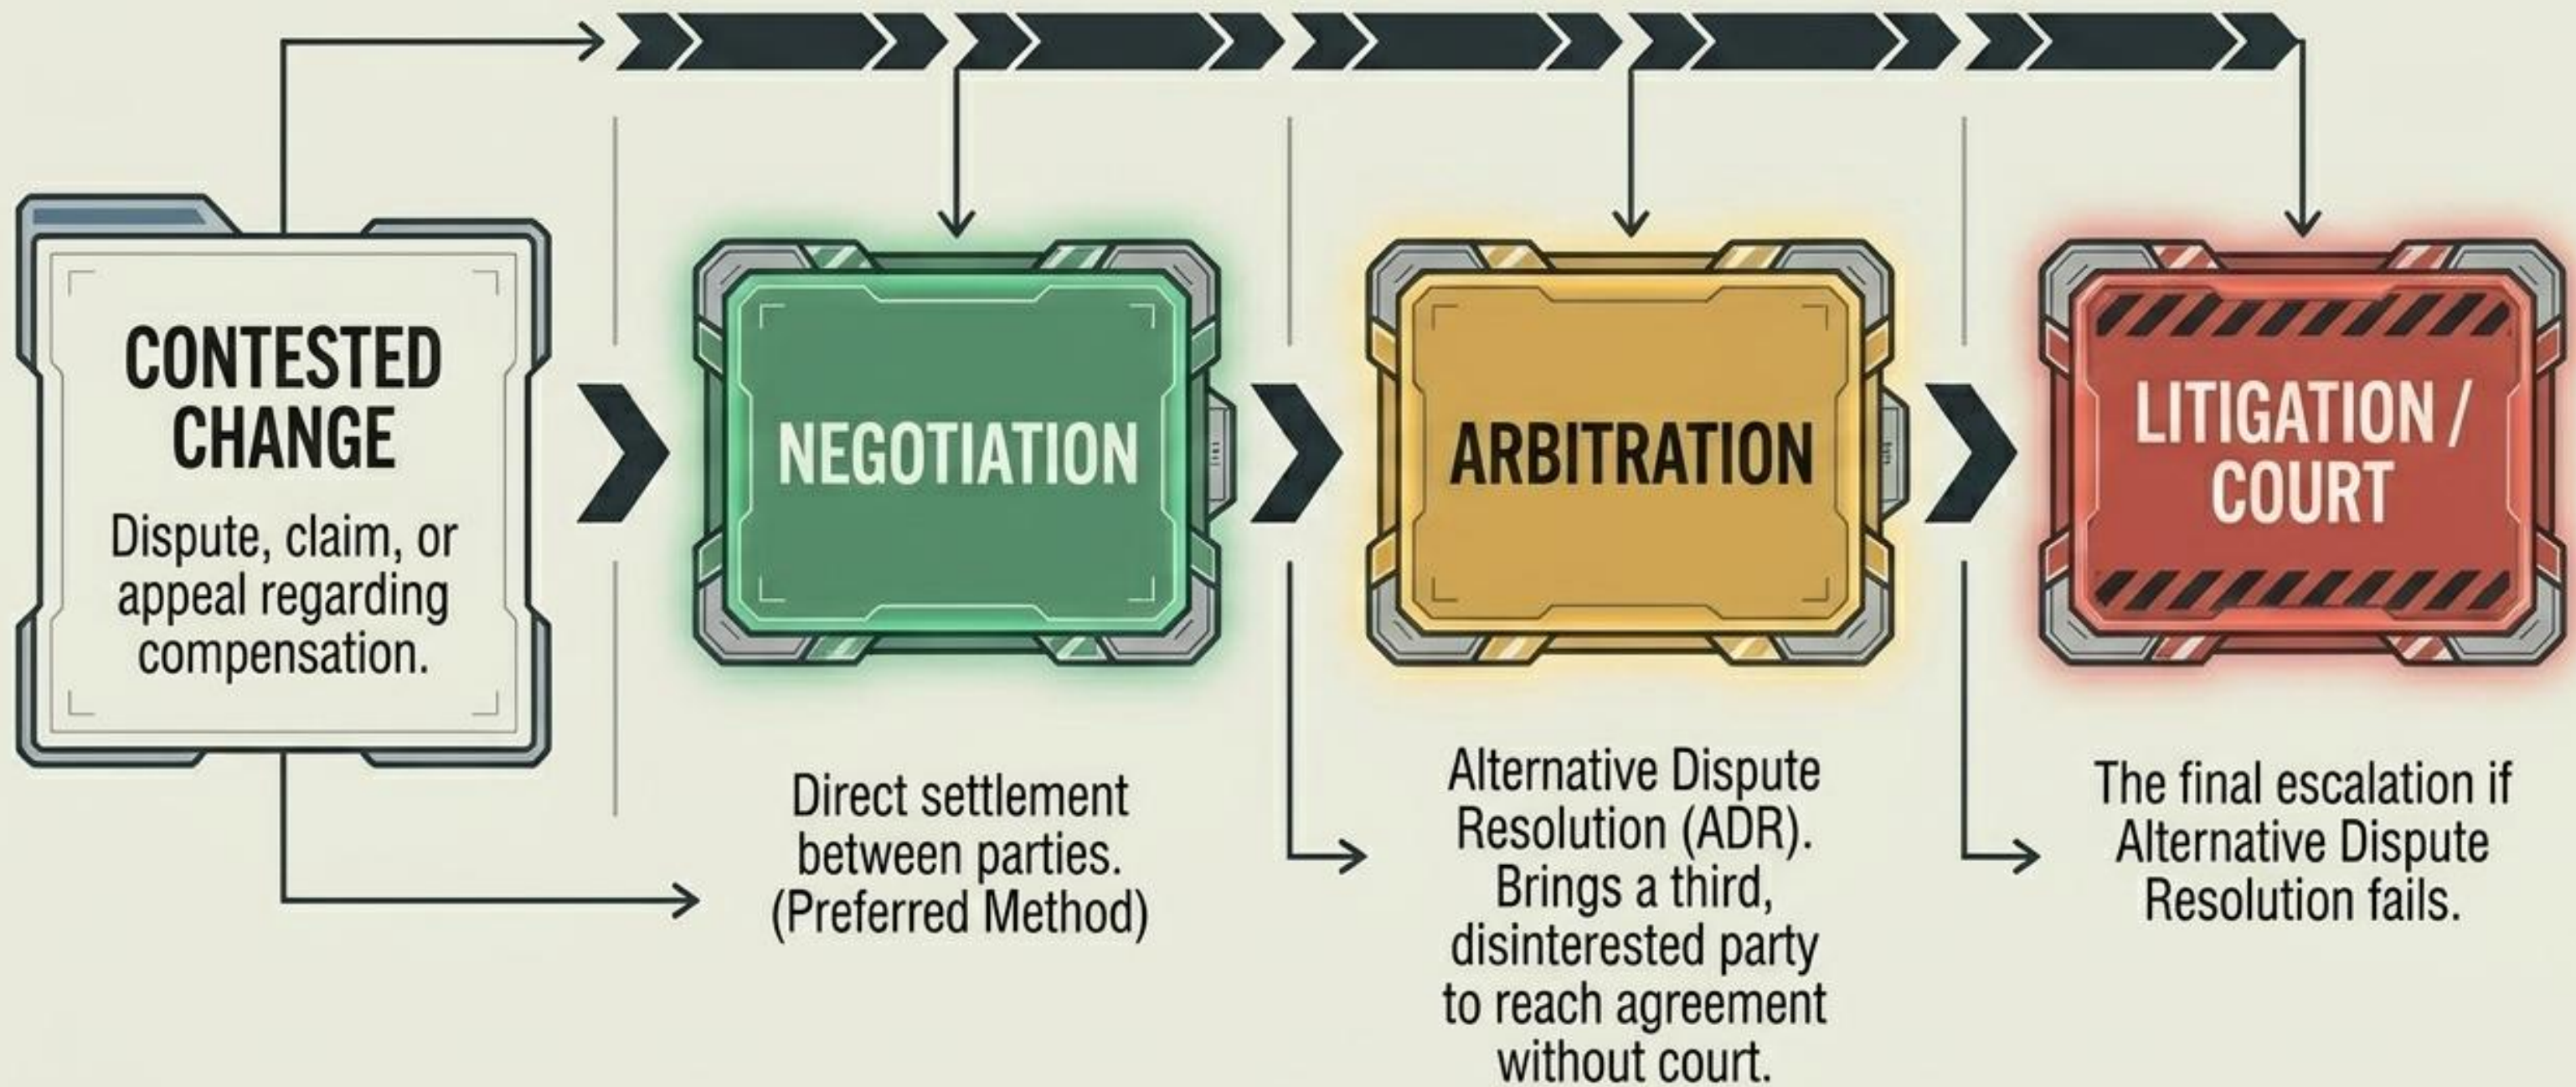

SYSTEM OUTPUTS: REAL-TIME PROJECT UPDATES

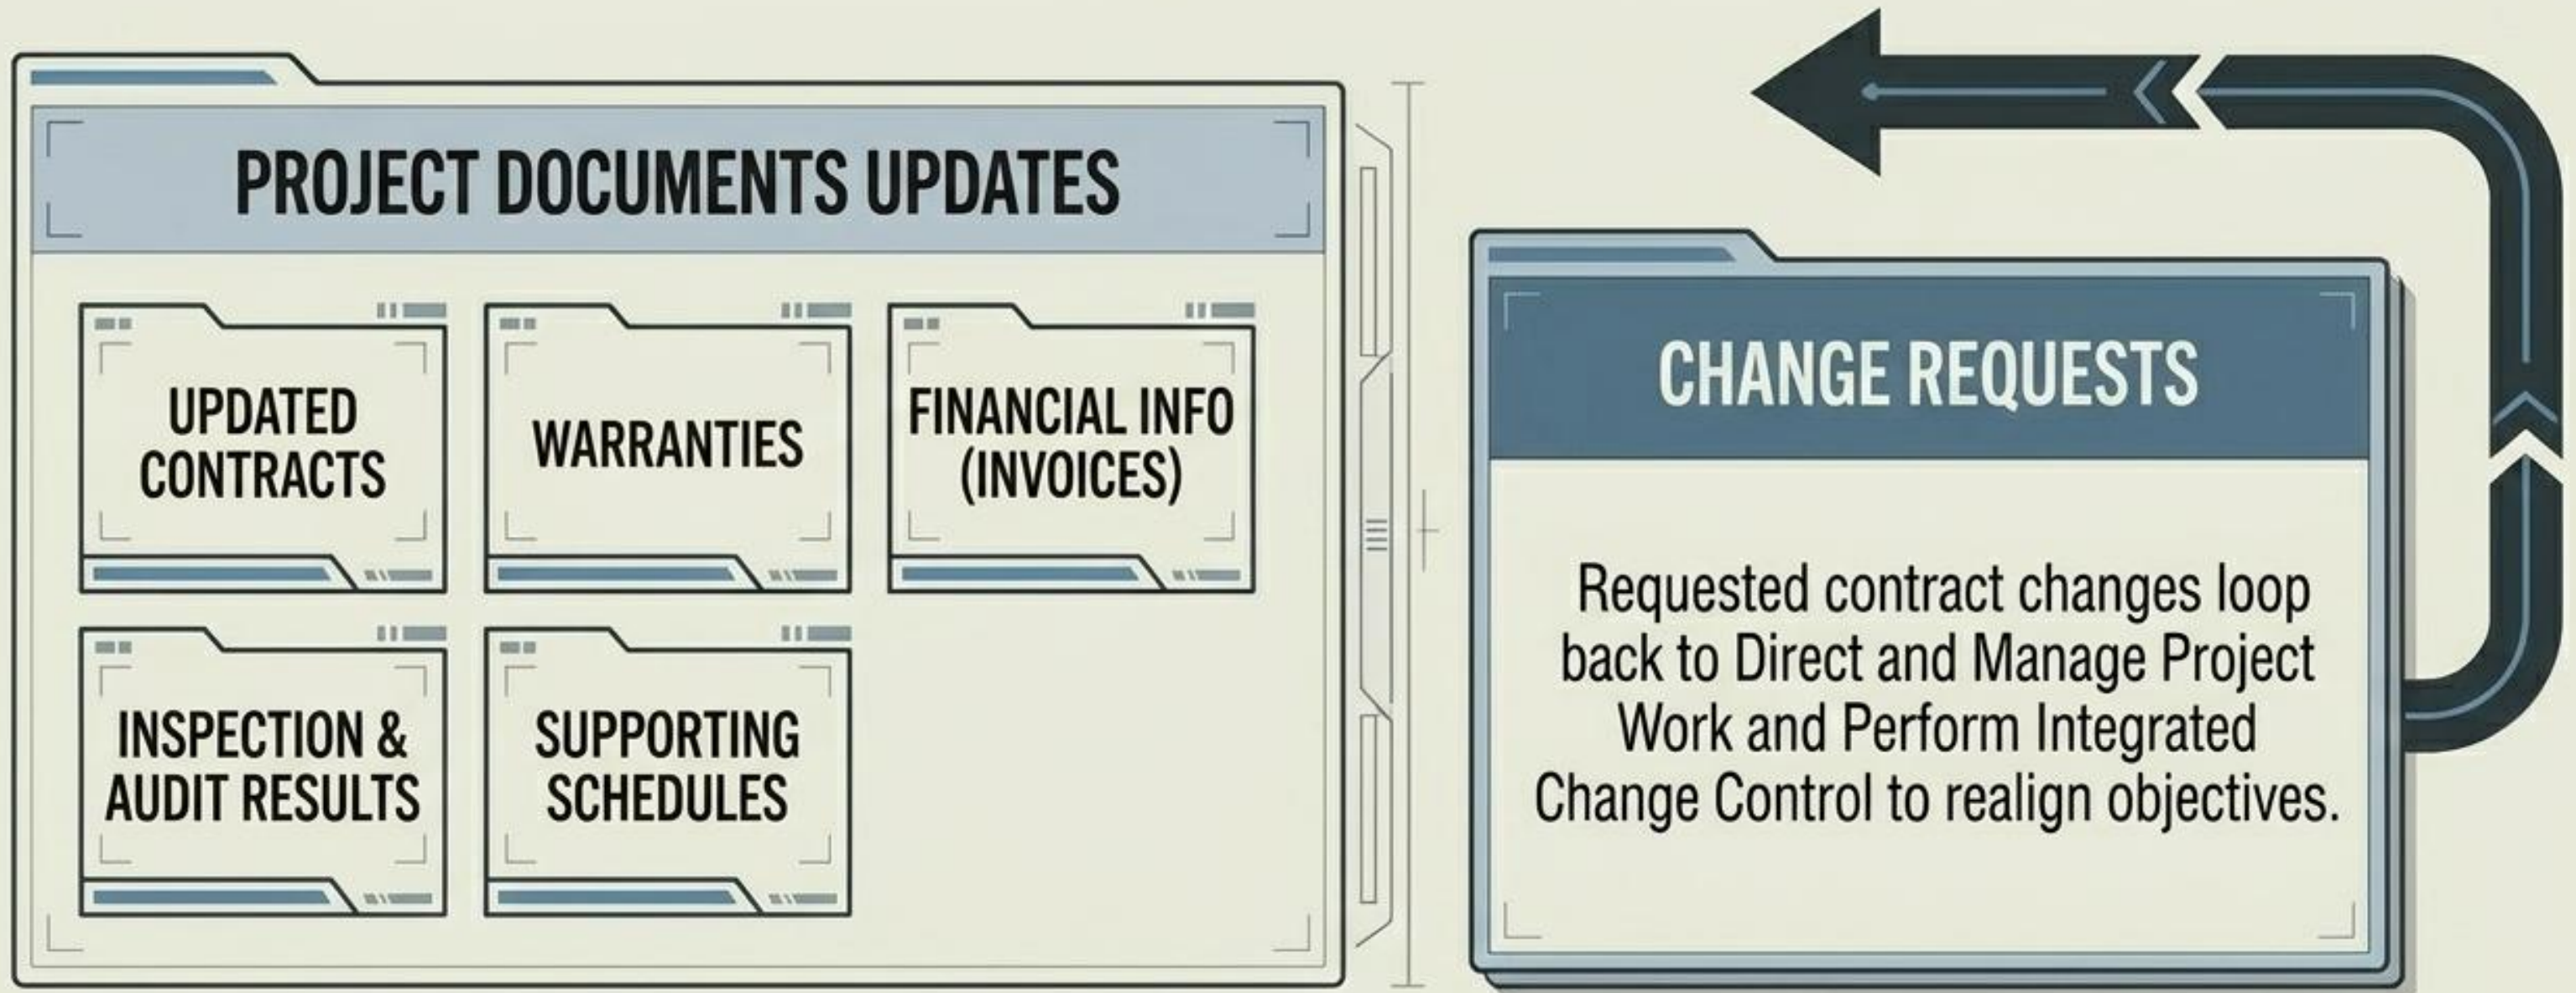


NOTE: Changes may require jumping back to Planning/Executing processes to update cost/schedule baselines.


ORGANIZATIONAL PROCESS ASSETS: ARCHIVING PERFORMANCE



PAYMENT SYSTEMS: VERIFICATION & AUTHORIZATION TIMELINE

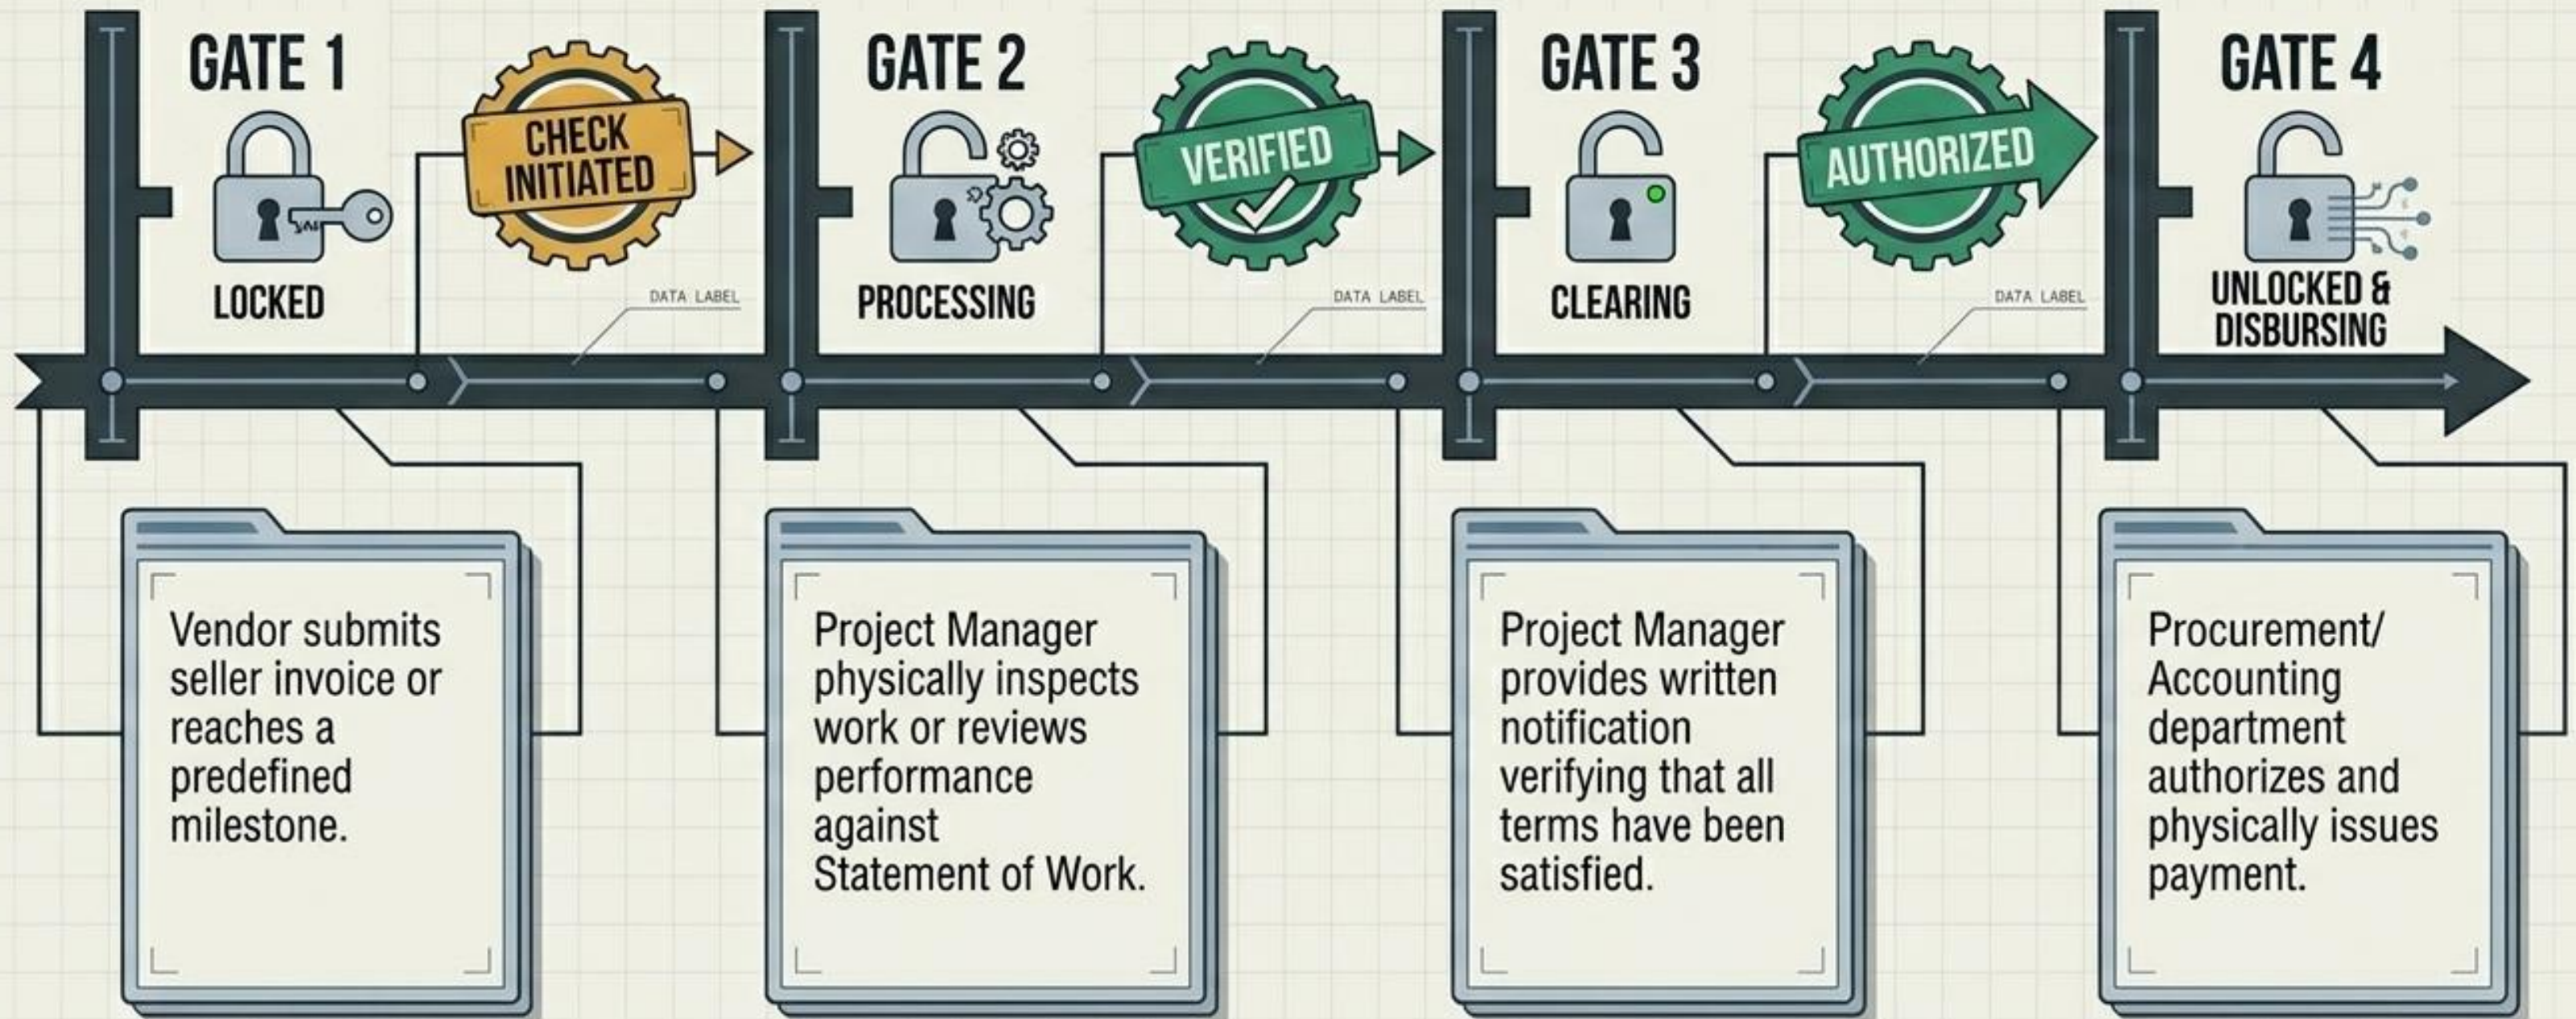

THE MASTER INTEGRATION ENGINE

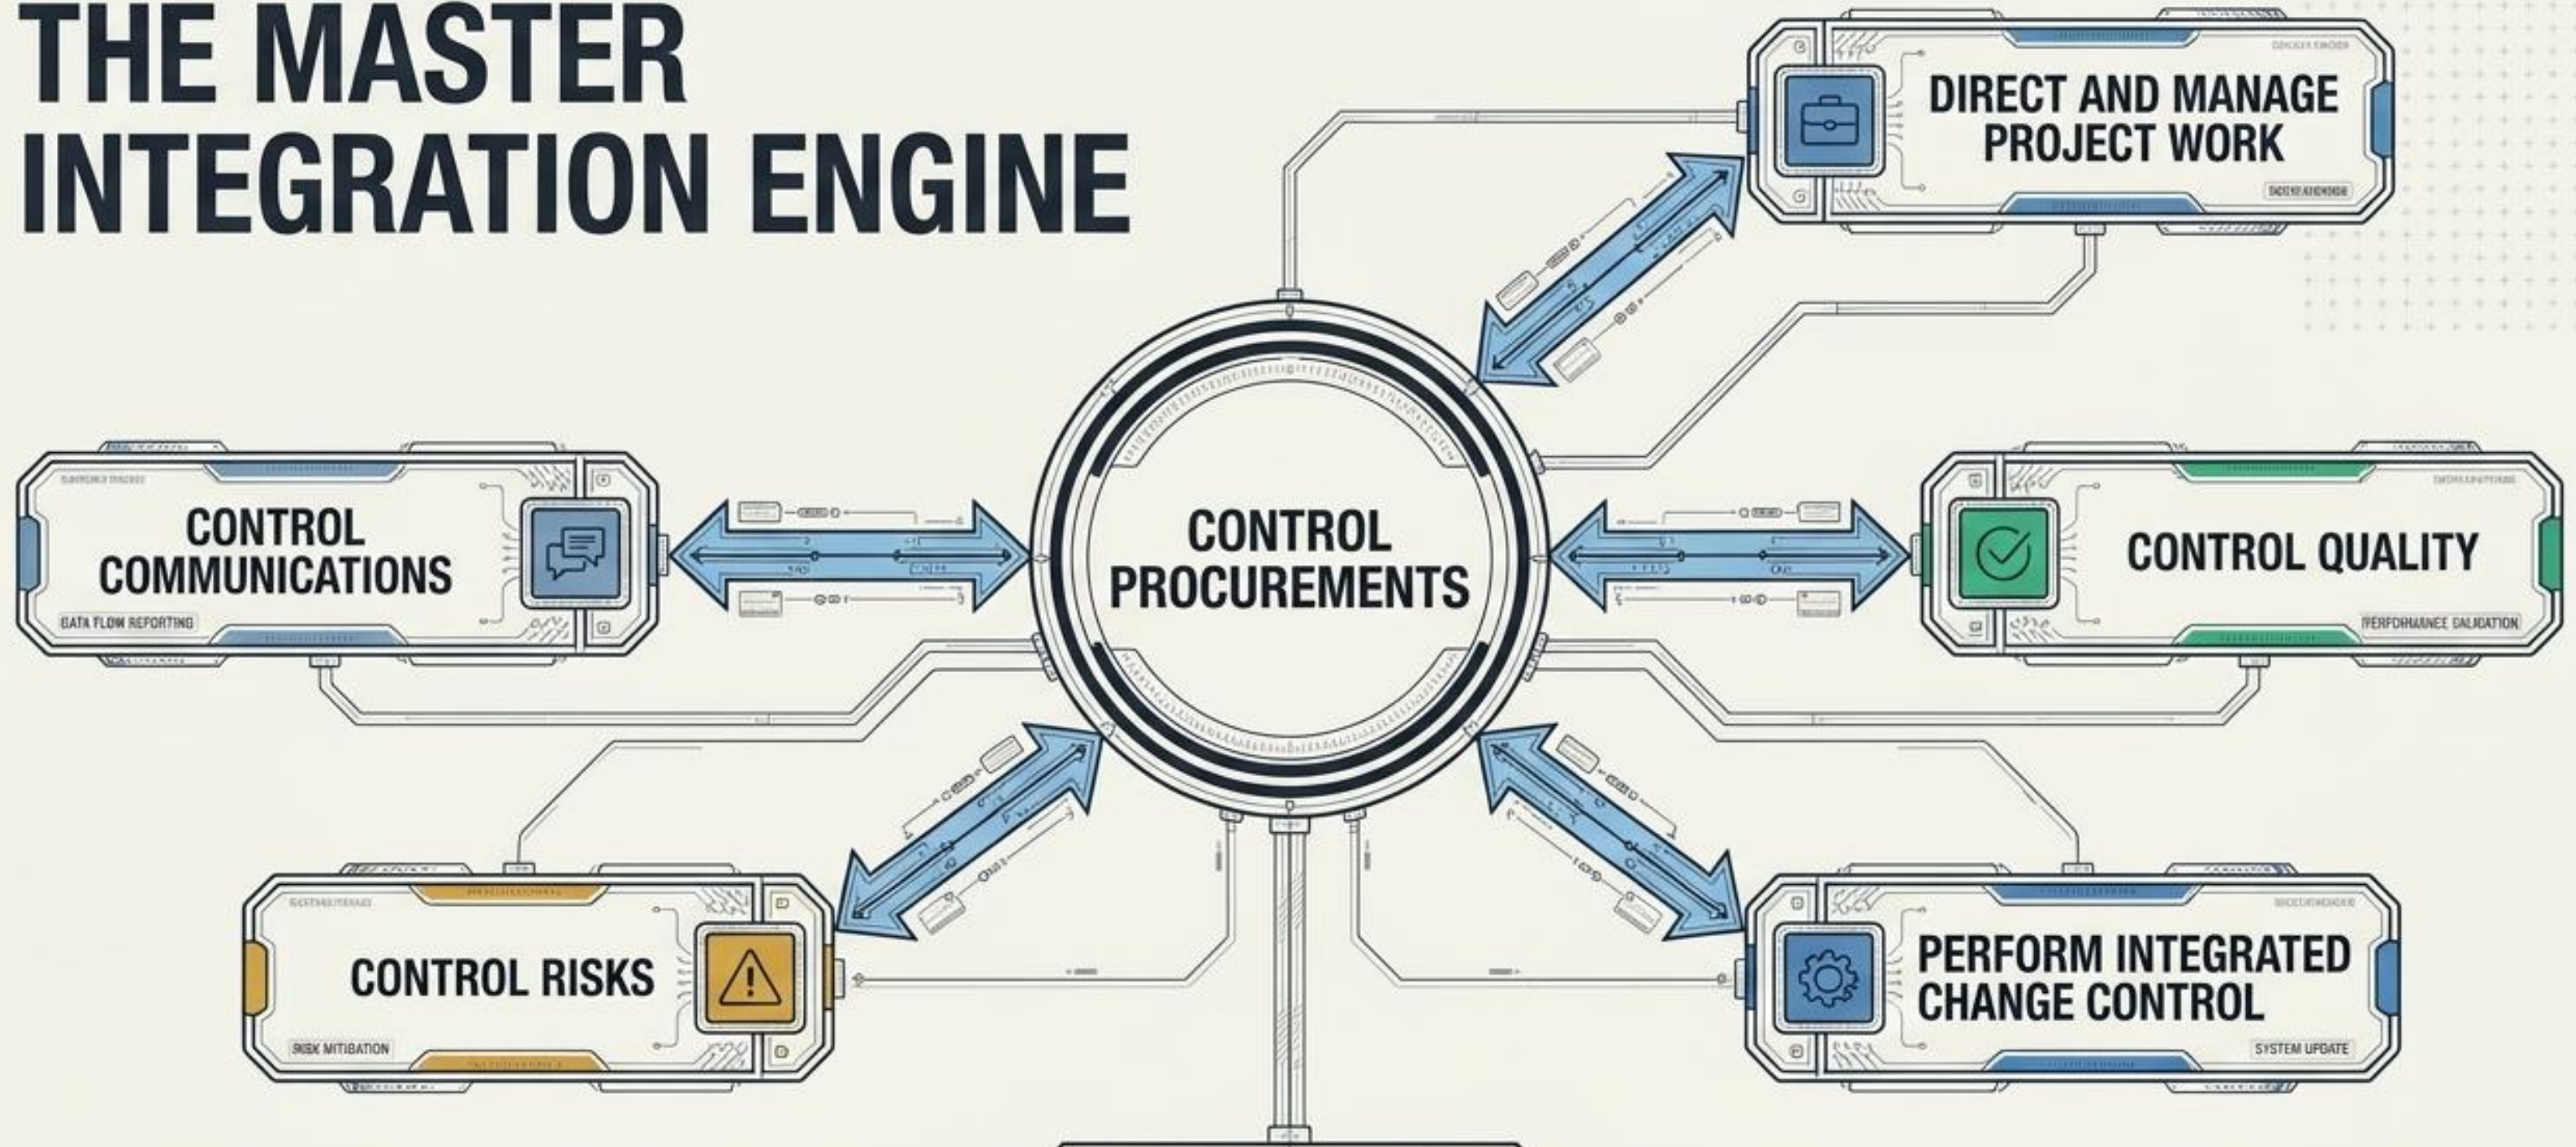

Managing a contract requires executing plans, tracking costs, taking corrective actions, and reporting status exactly as you do for the project itself. Procurements cannot be controlled in a silo.
