



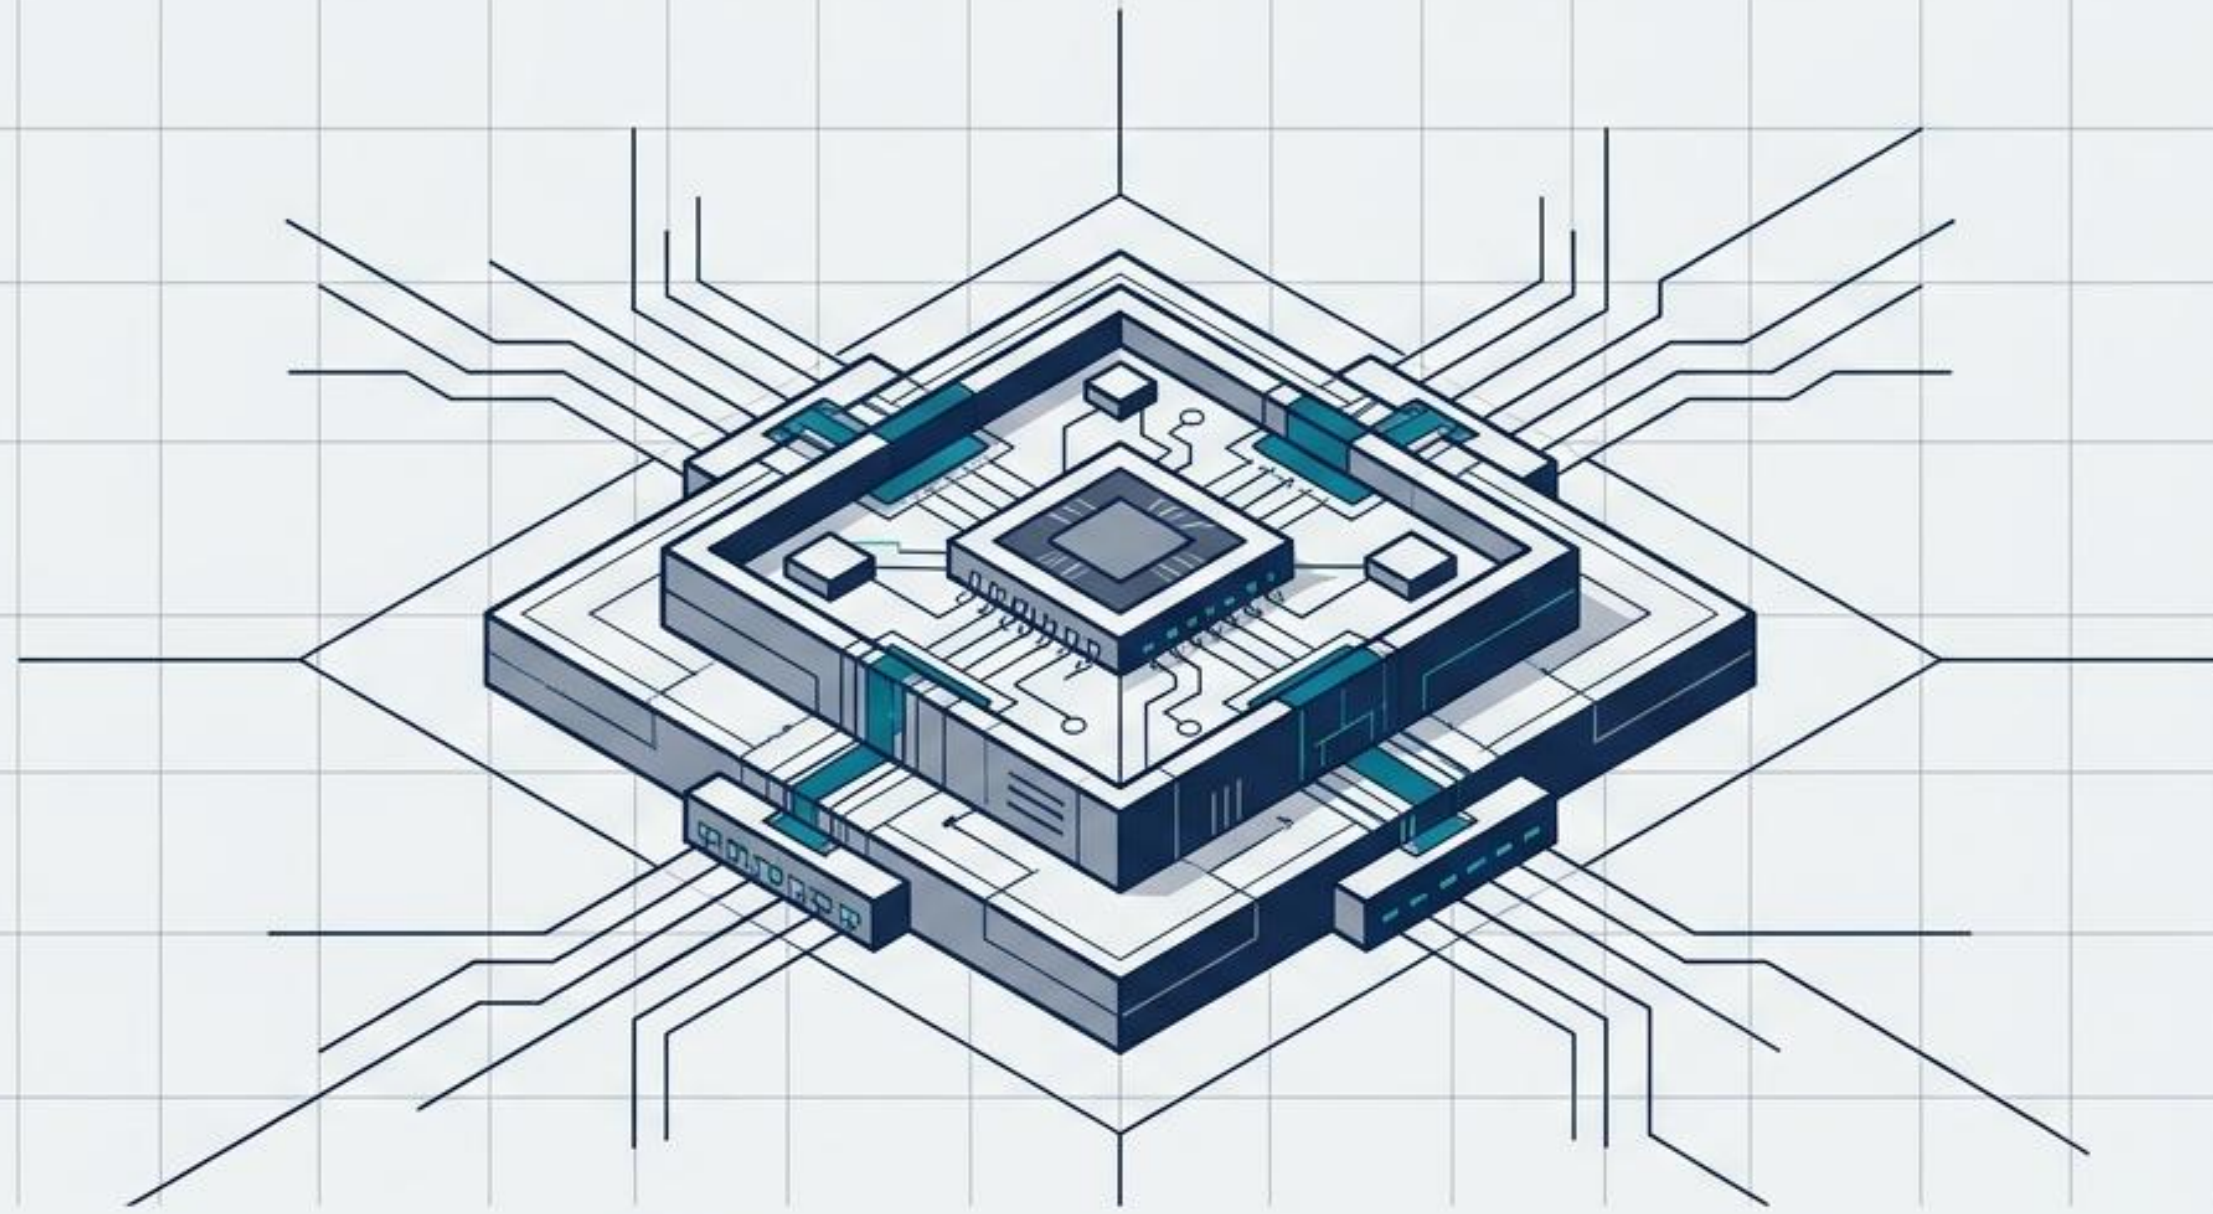

Certyfikat PMP: Project Communication Controlling

dr Zbigniew Galar


Delivering the right message to the right people at the right time

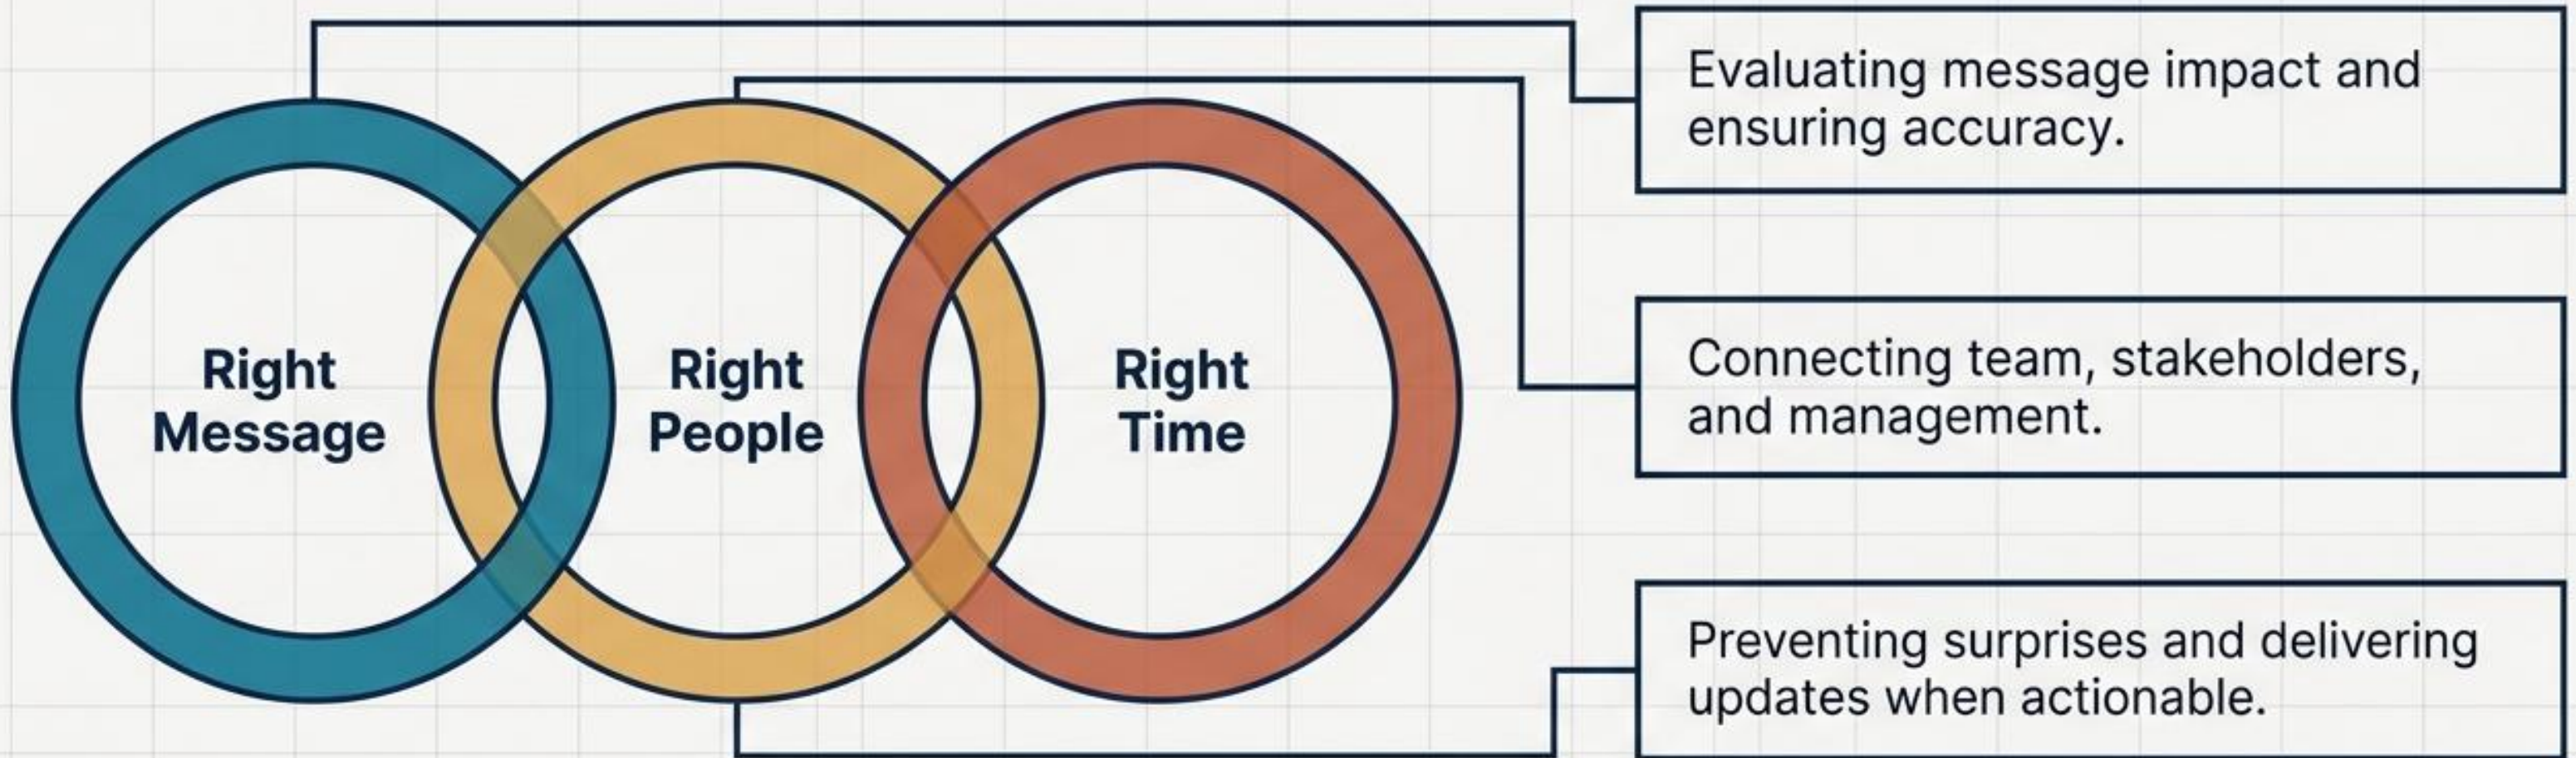


Control Communications Definition

The Monitoring and Controlling process that evaluates and controls the impact of project messages. It collects progress data, measures performance against baselines, and distributes actionable information. Variances discovered here trigger feedback loops to Plan or Manage Communications to correct course.


The Information Refinery Pipeline

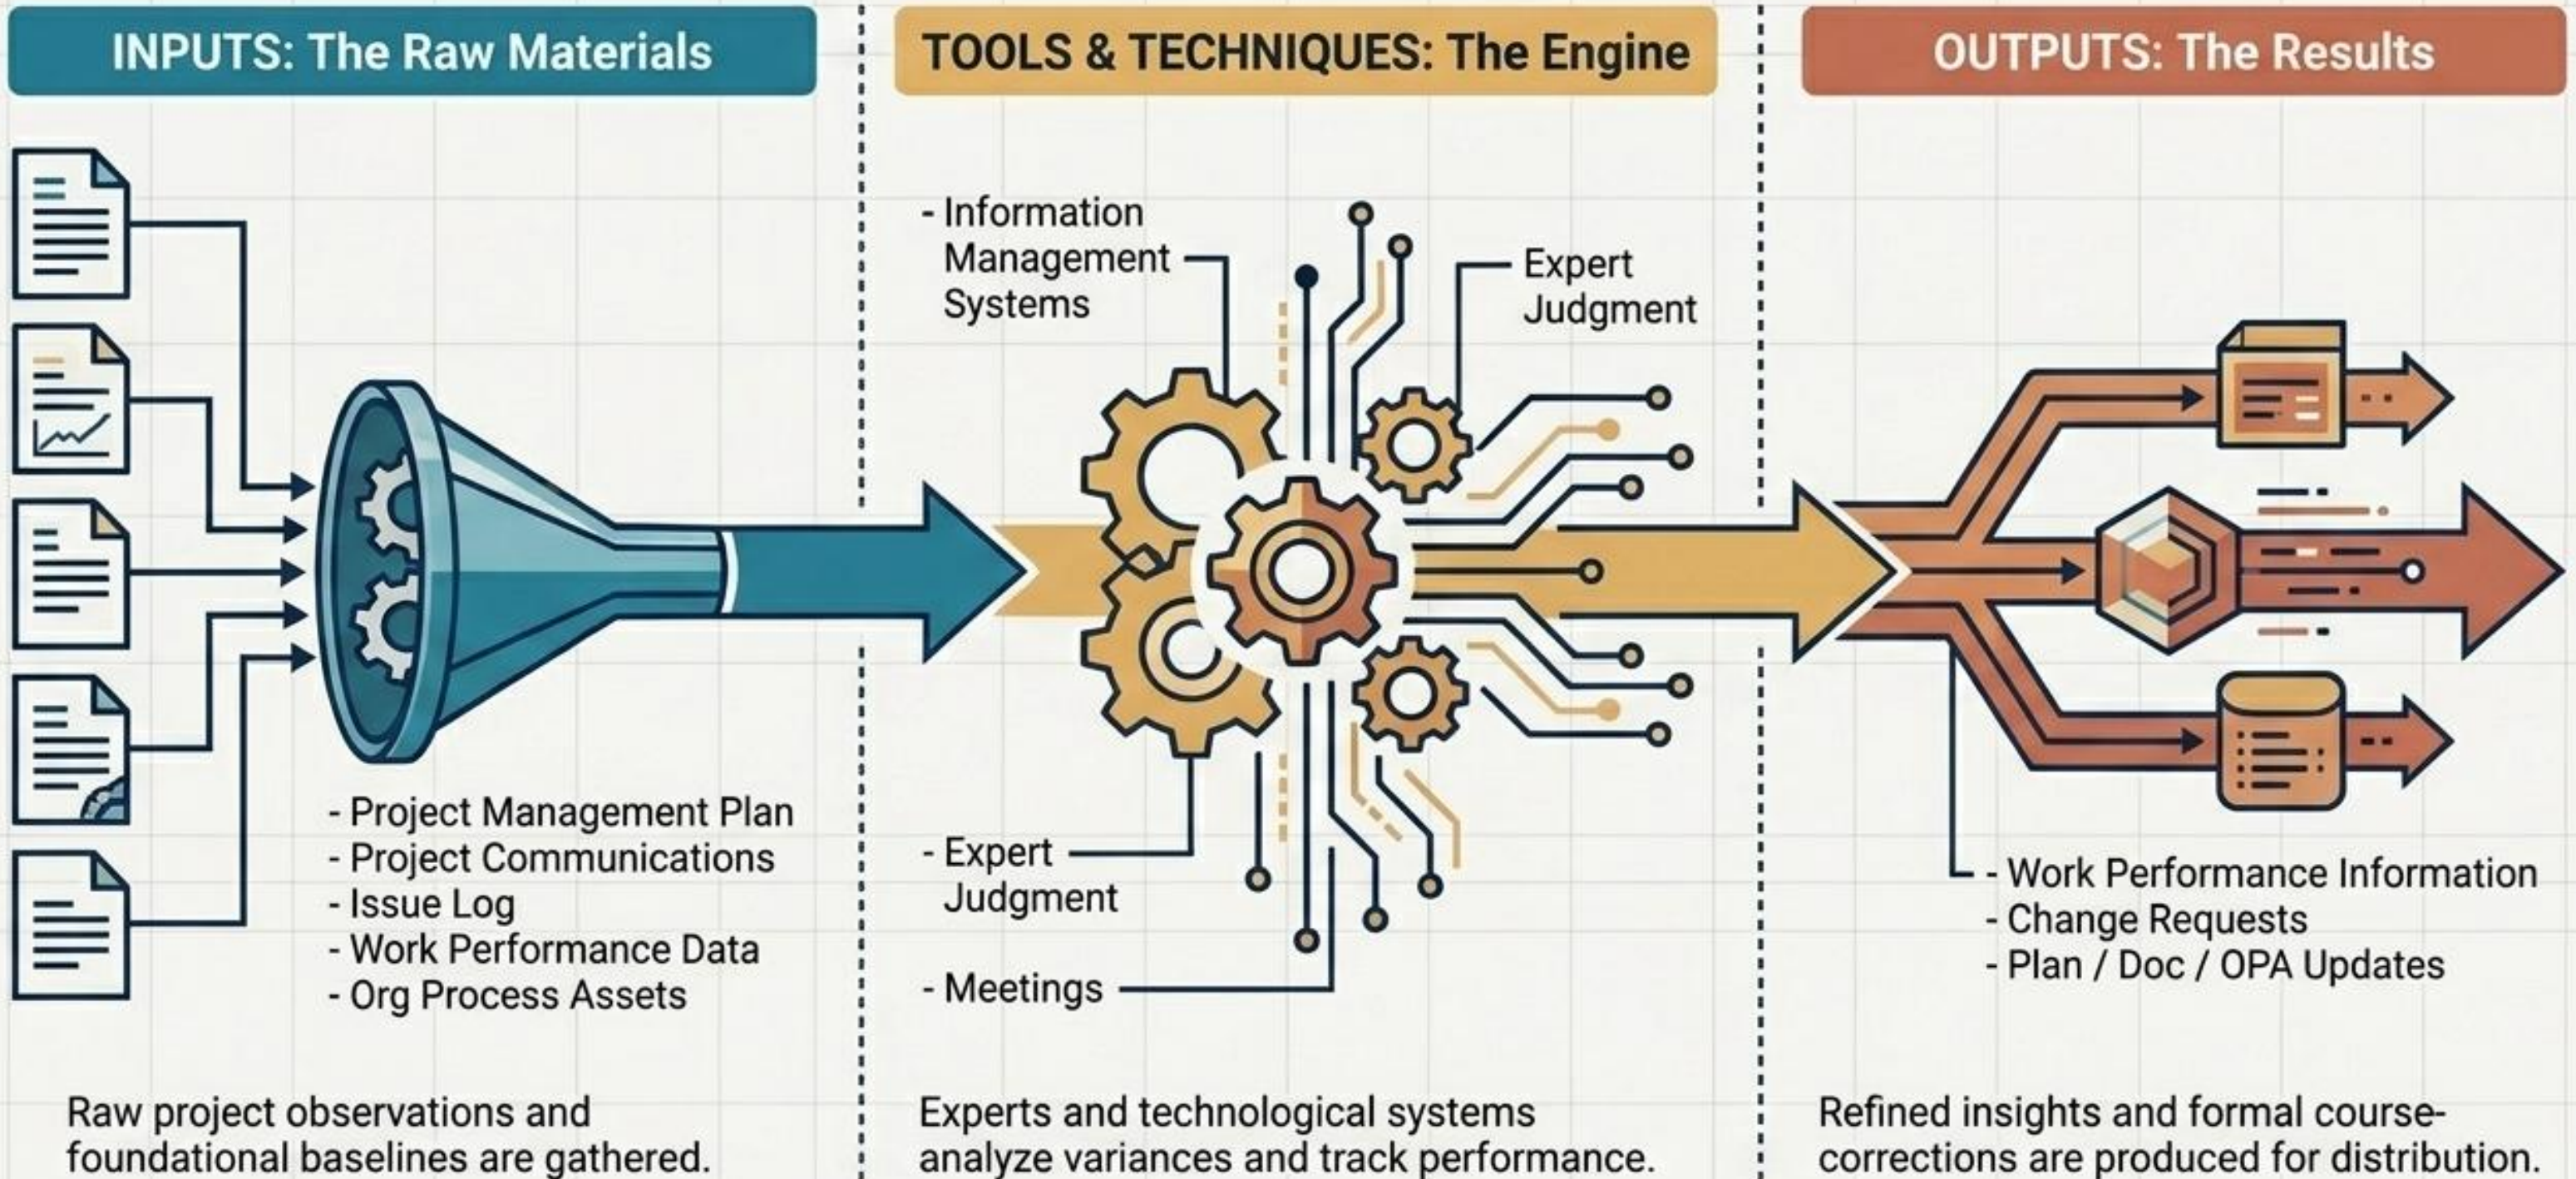

Gathering the raw materials for communication control

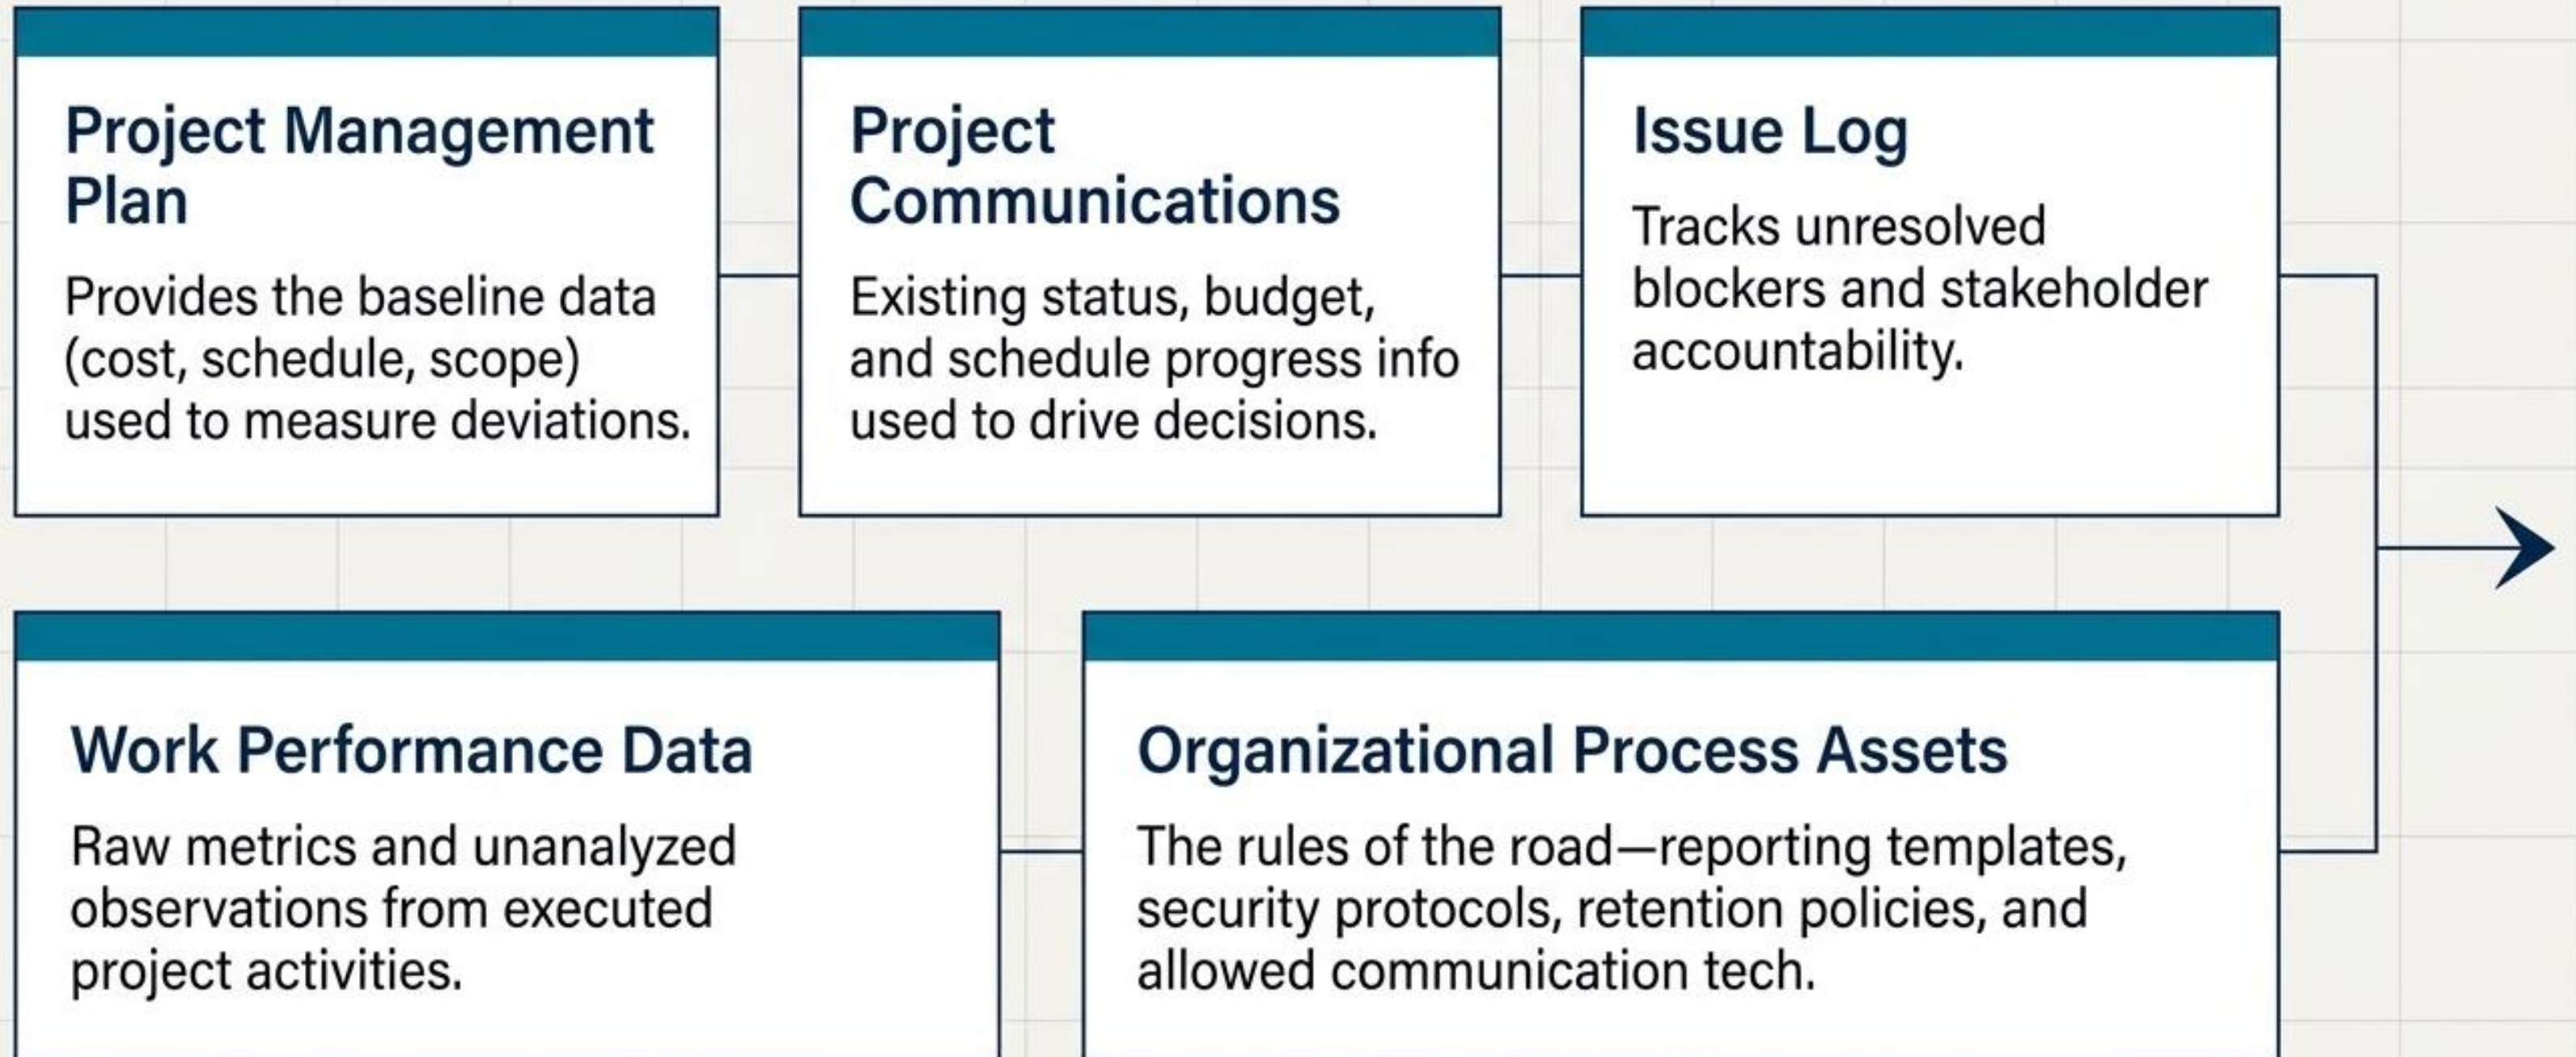

Anatomy of a functional Issue Log

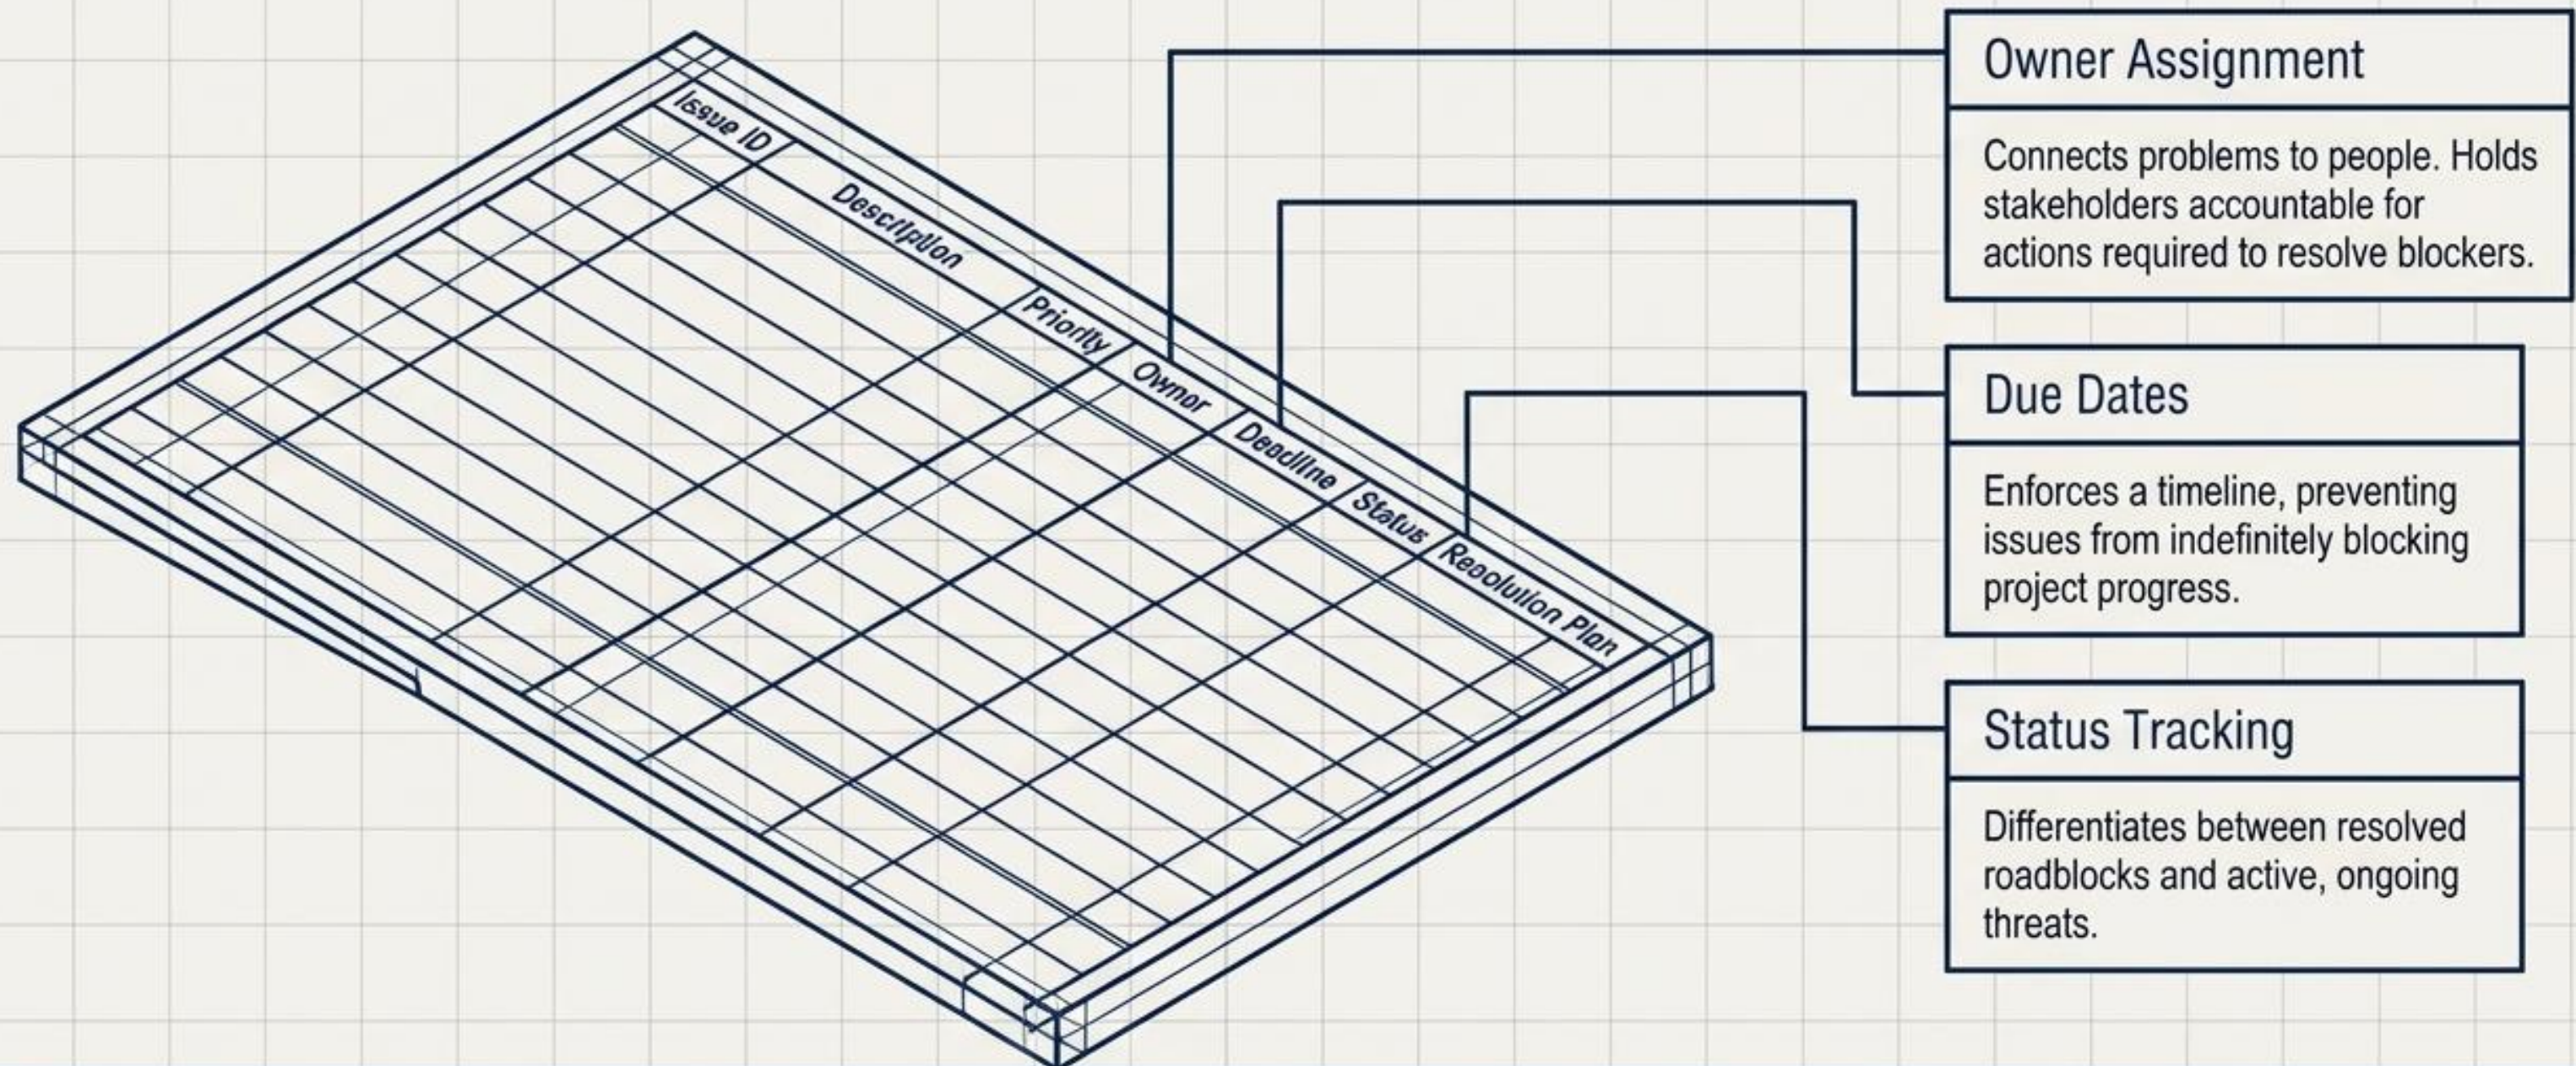


CONSULTANT INSIGHT: Reviewing issue logs at every single status meeting is the most effective way to maintain stakeholder expectations and force necessary actions.

Processing data through systems and experts

Information Management Systems

The Technological Engine



Systems used to record, store, and distribute cost, schedule, and performance data.

Output Formats:

- Spreadsheet analysis
- Table reporting
- Graphic capabilities
- Structured presentations

Expert Judgment

The Human Engine




Data cannot interpret itself. Experts must translate variances into actionable decisions to realign work with the management plan.

The Brain Trust:

- Project team members
- Specialized consultants
- Industry groups
- Project Management Office (PMO)
- Key stakeholders


The anatomy of a high-leverage status meeting

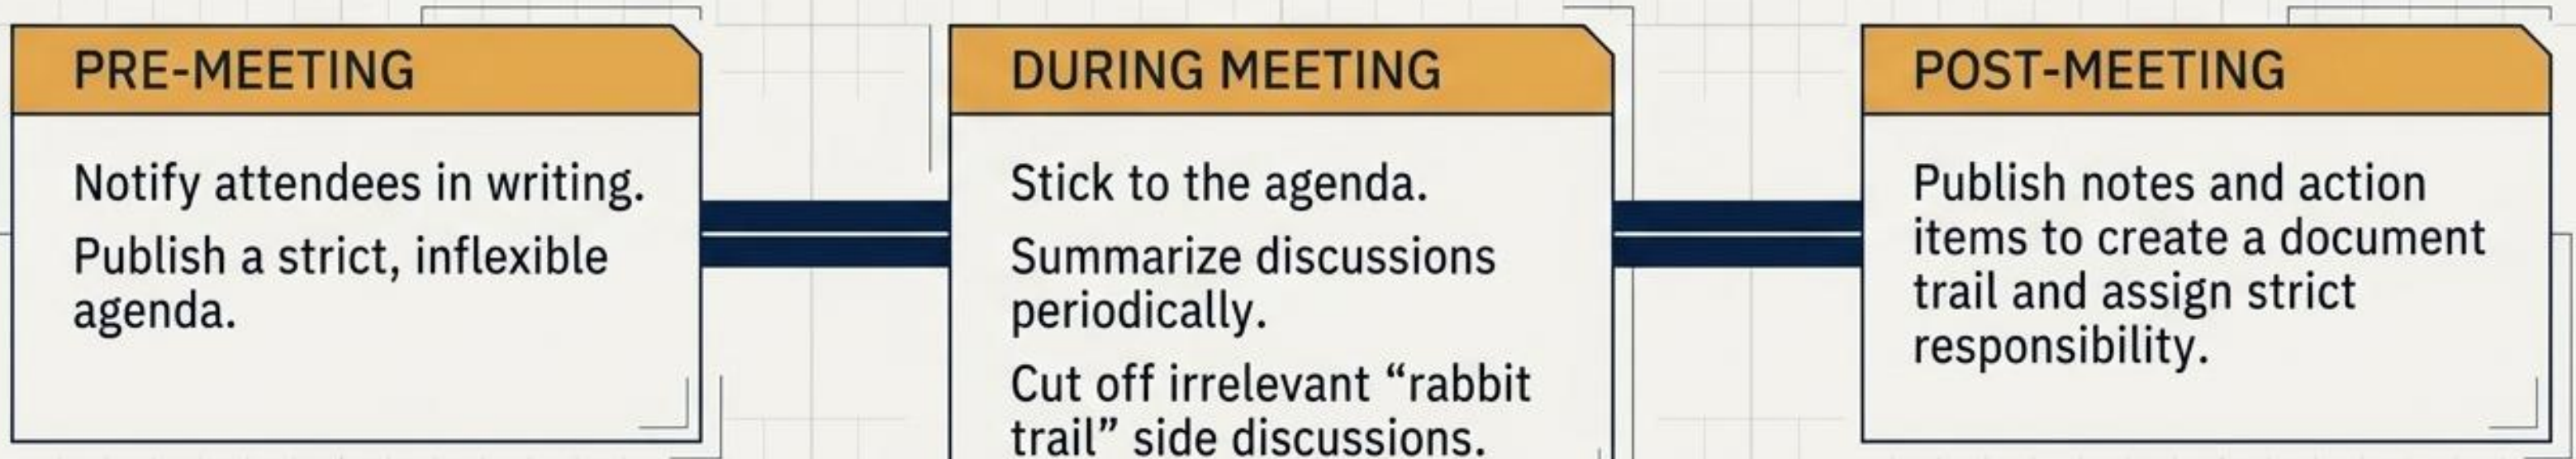

Scorecard

DO	DON'T
- Limit to 3-4 meetings per month to prevent severe meeting fatigue. - Use different meetings for different audiences (e.g., project team vs. end users vs. executive management).	- Treat status meetings as “show-and-tell” sessions. - Conduct prototype demos. Schedule a separate, dedicated time for demonstrations.

The exponential cost of dishonest reporting

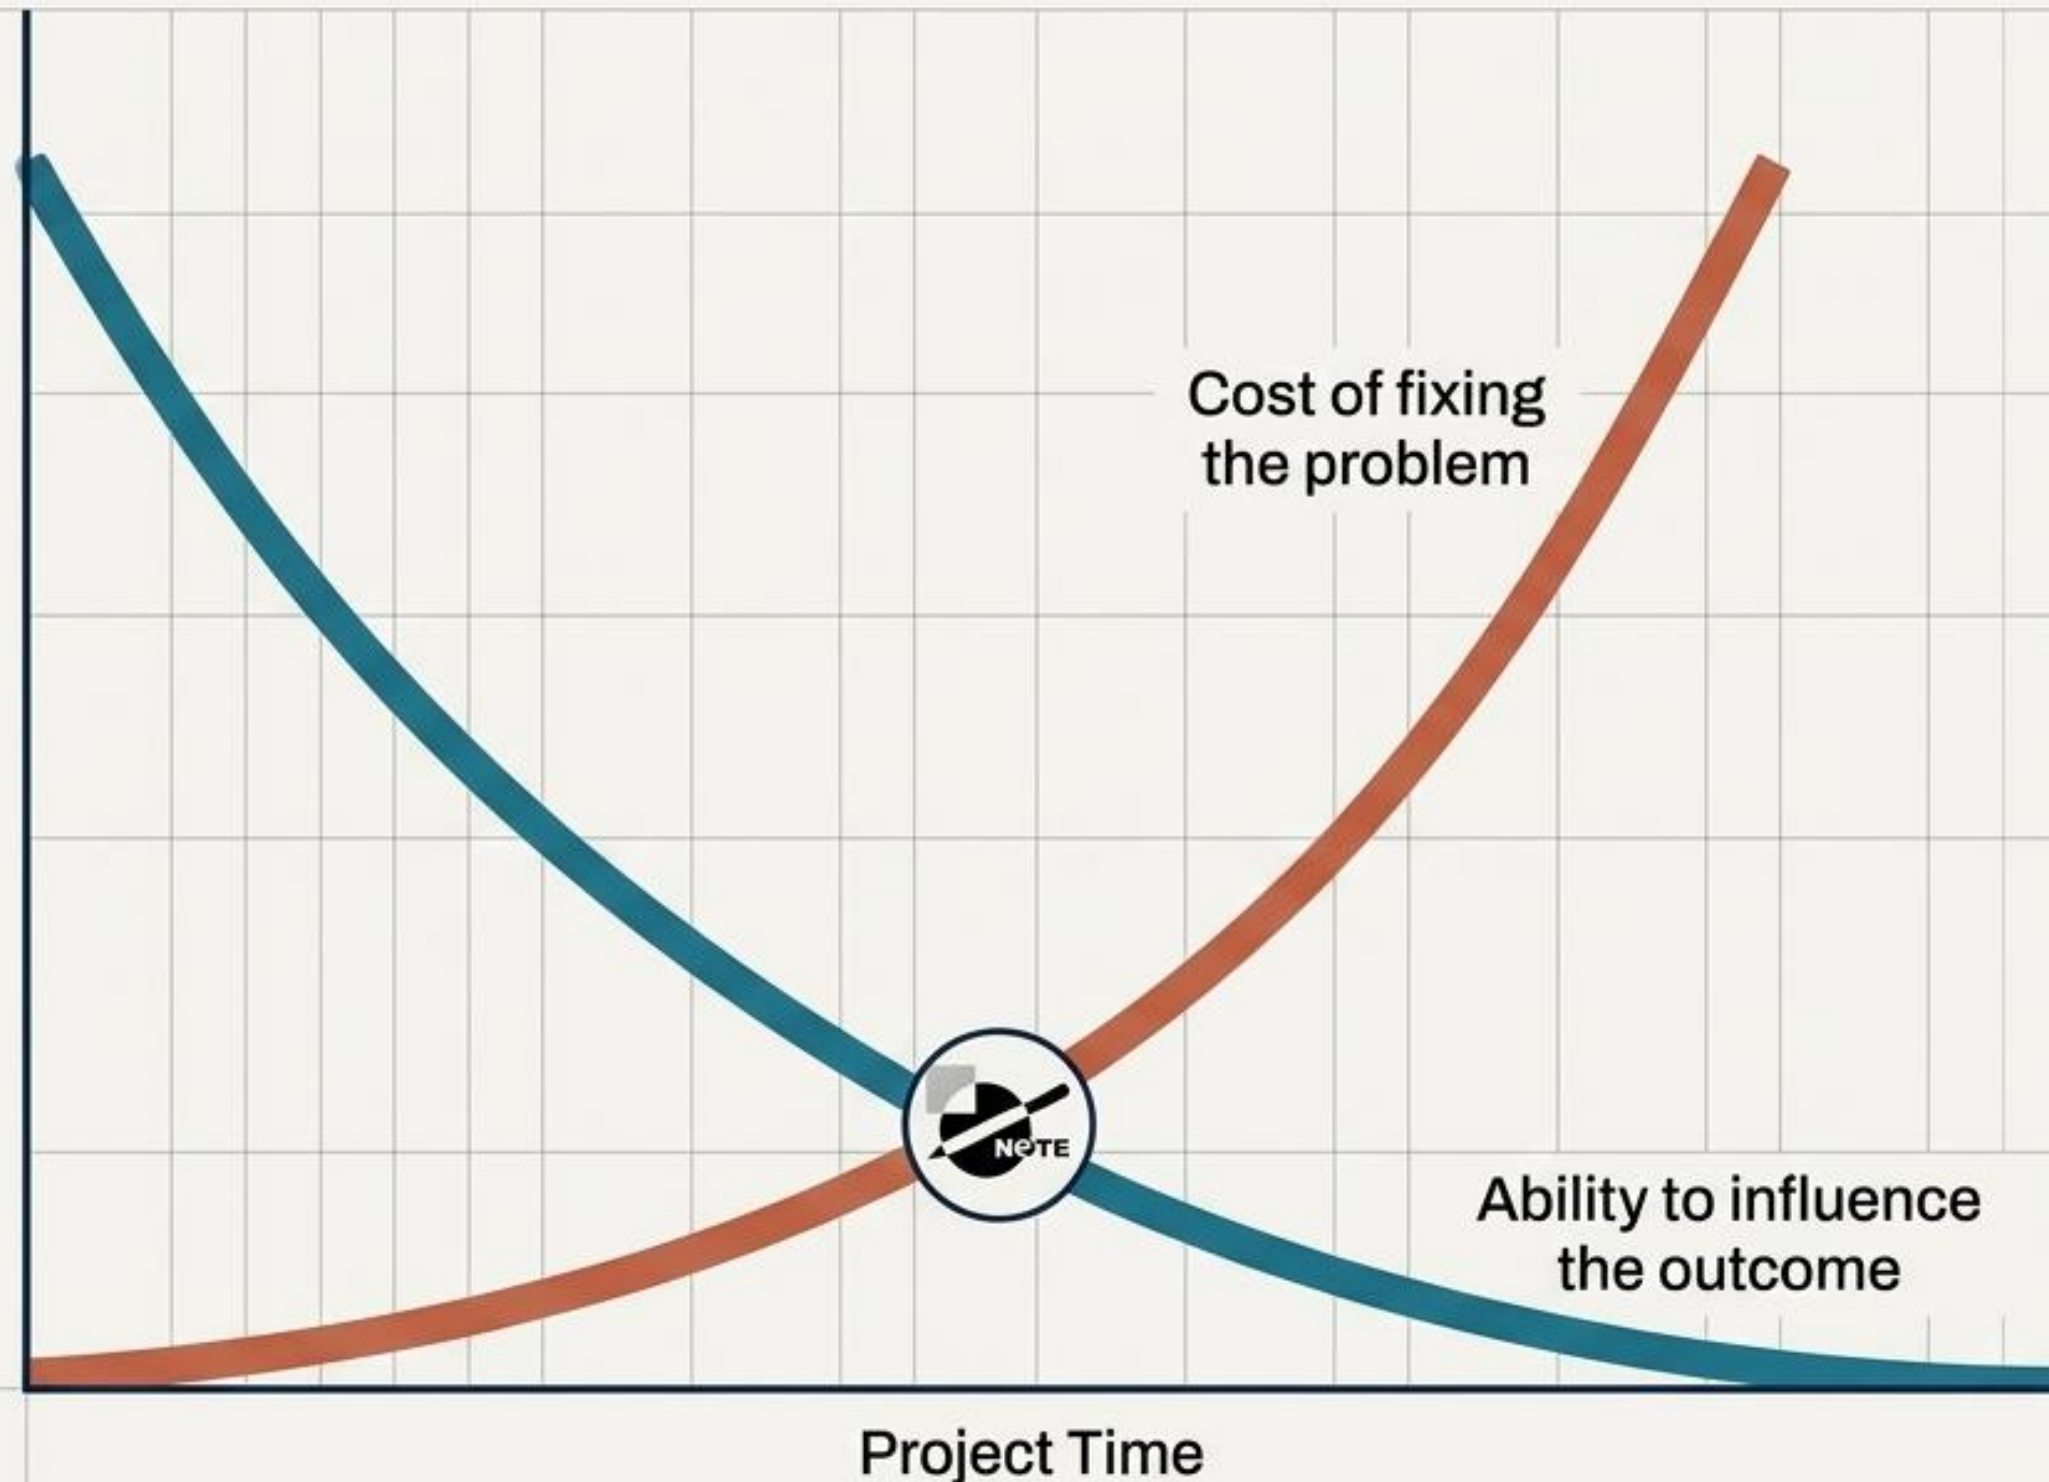


The “Chicken Little” Failure

A multi-million dollar failure occurred when a PM ignored skilled team members warning of setbacks. Refusing to believe ‘the sky was falling,’ she falsified reports to oversight committees.

The Lesson

Regular, honest team status meetings alert PMs to risks before they reach the uncontrollable stage. Bad news delivered too late is a guaranteed career showstopper.

Generating actionable insights and course corrections

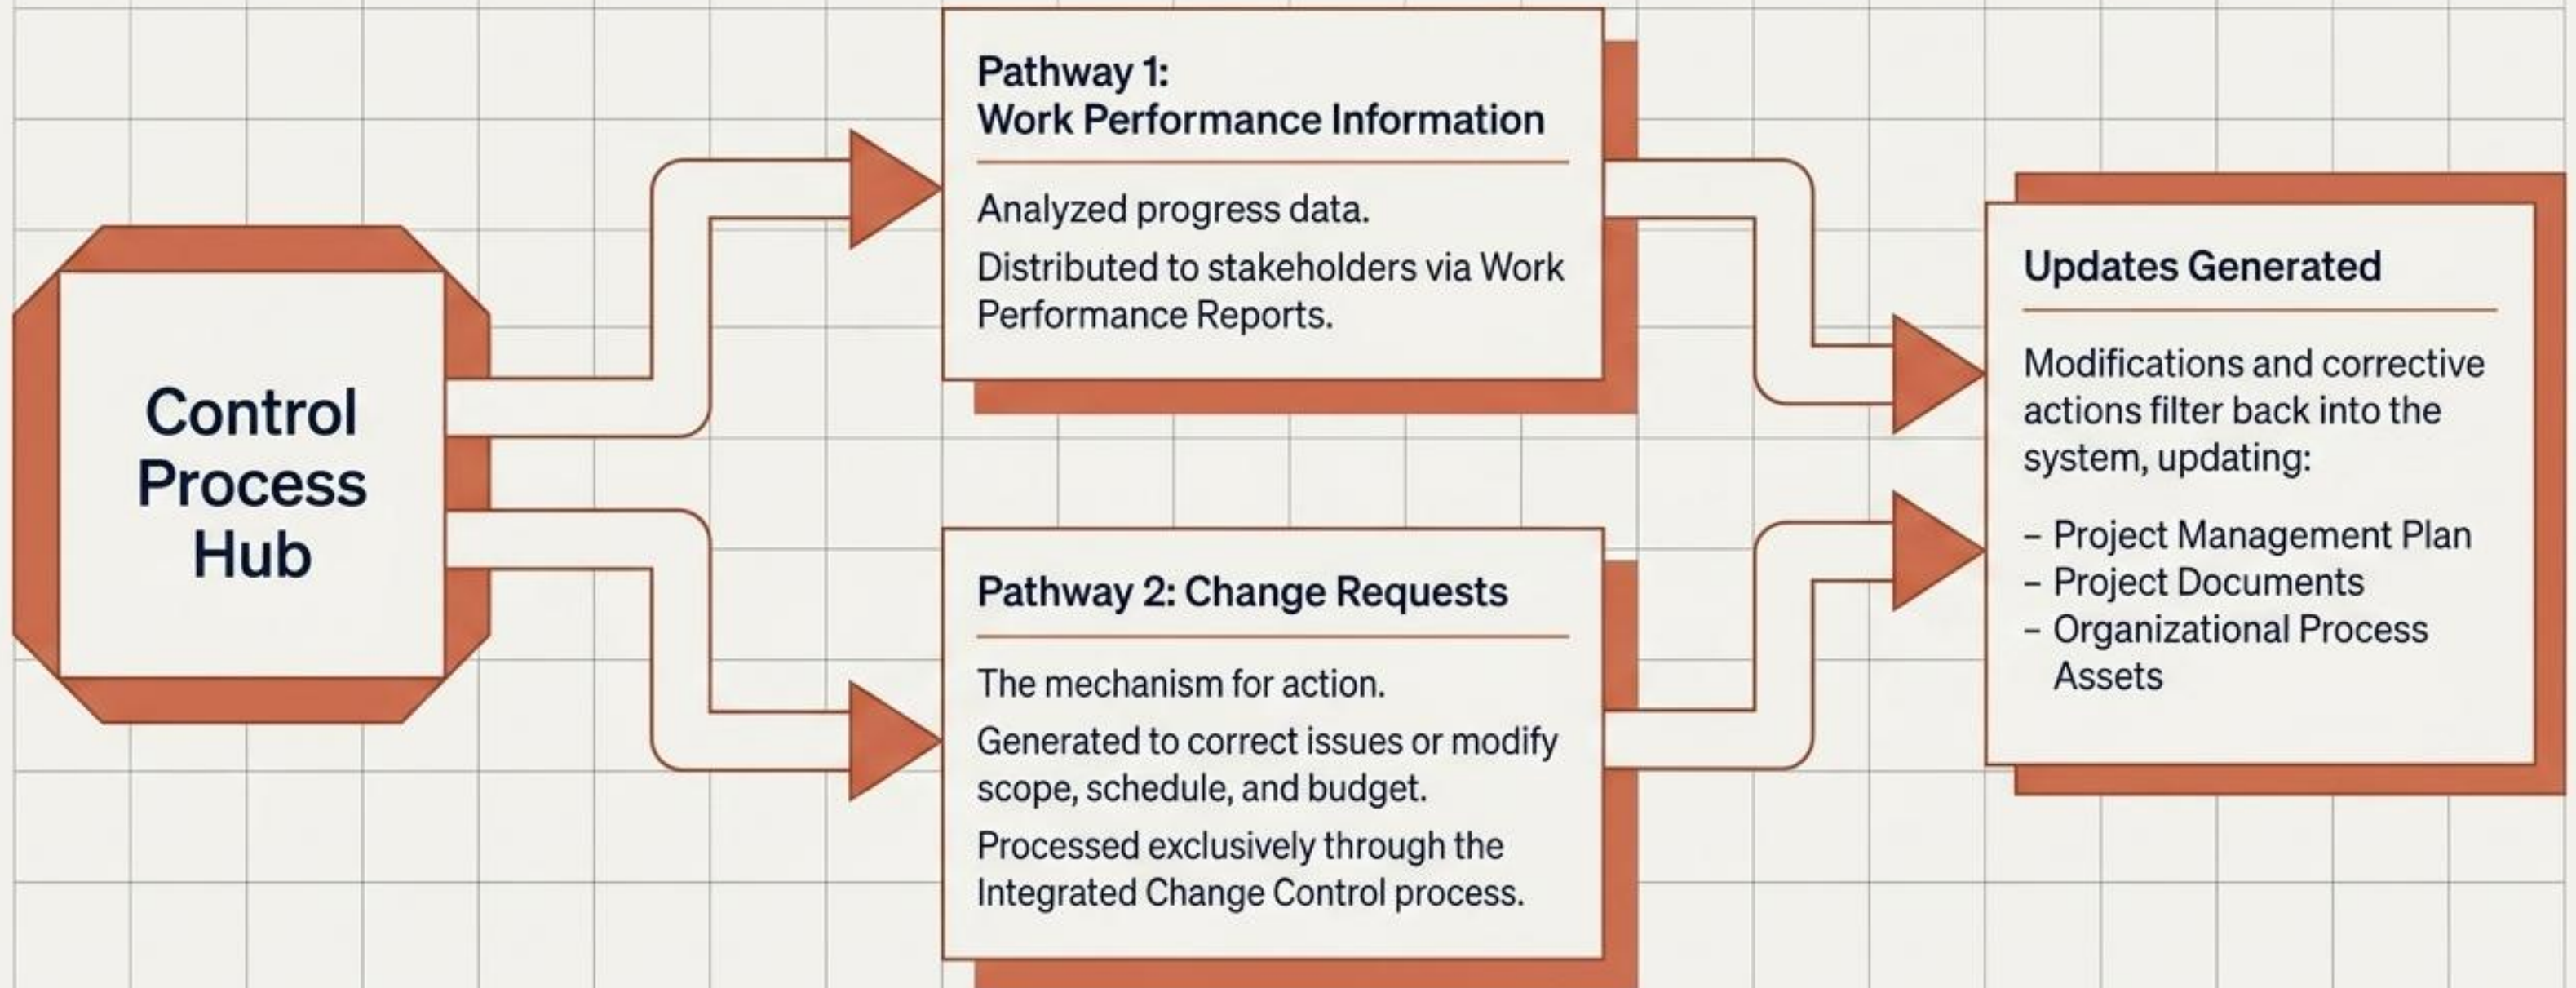

PMP Exam Matrix:

The evolution of project metrics

	Work Performance Data	Work Performance Information	Work Performance Reports
Definition	Raw observations and measurements of executed project activities.	Analyzed data used to determine exact project status and generate forecasts.	The physical, documented manifestation of the compiled information.
Examples	% work complete, actual start/finish dates, number of defects, costs incurred.	Status of deliverables, status of change requests, Estimate to Complete (ETC).	Status reports, memos, dashboard updates distributed directly to stakeholders.

The metrics lifecycle across PMBOK processes

