


# Certyfikat PMP: Project Change Control

Author: dr Zbigniew Galar




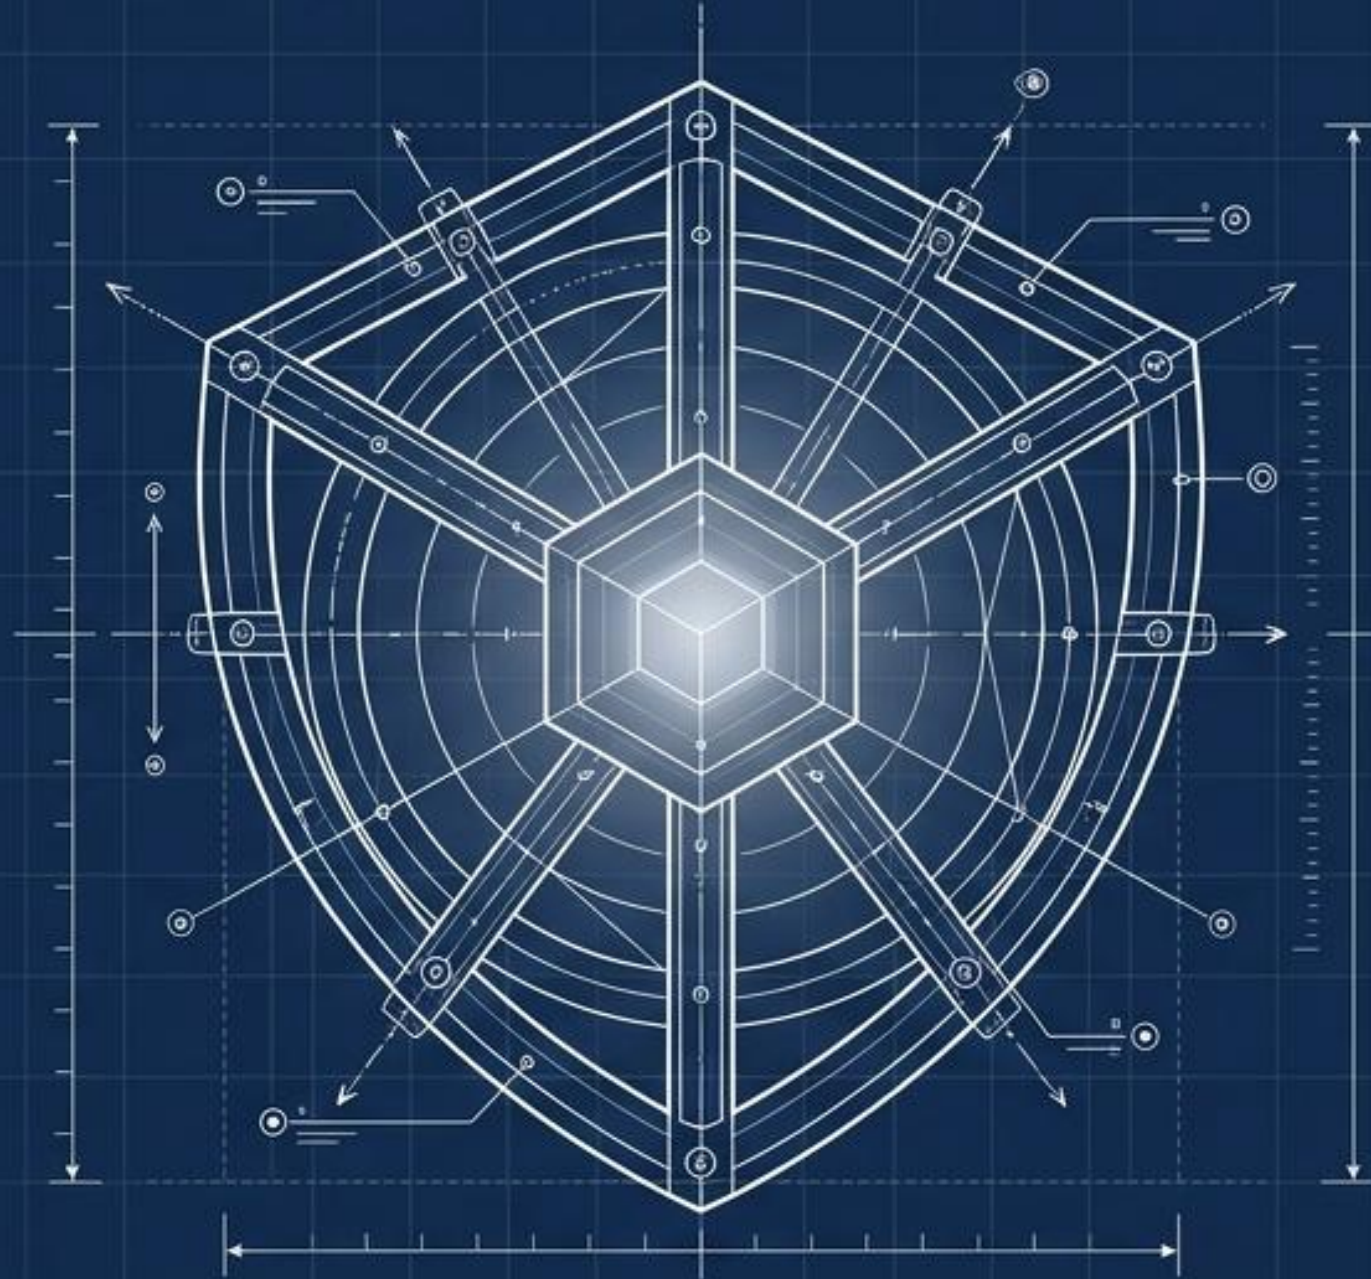

# The Overseer Process


Perform Integrated Change Control serves as the absolute overseer of all Monitoring and Controlling processes. It is the centralized gatekeeper for corrective actions, preventive actions, and defect repairs.

**A single unmanaged change shatters the equilibrium of Cost, Time, Scope, and Quality.**

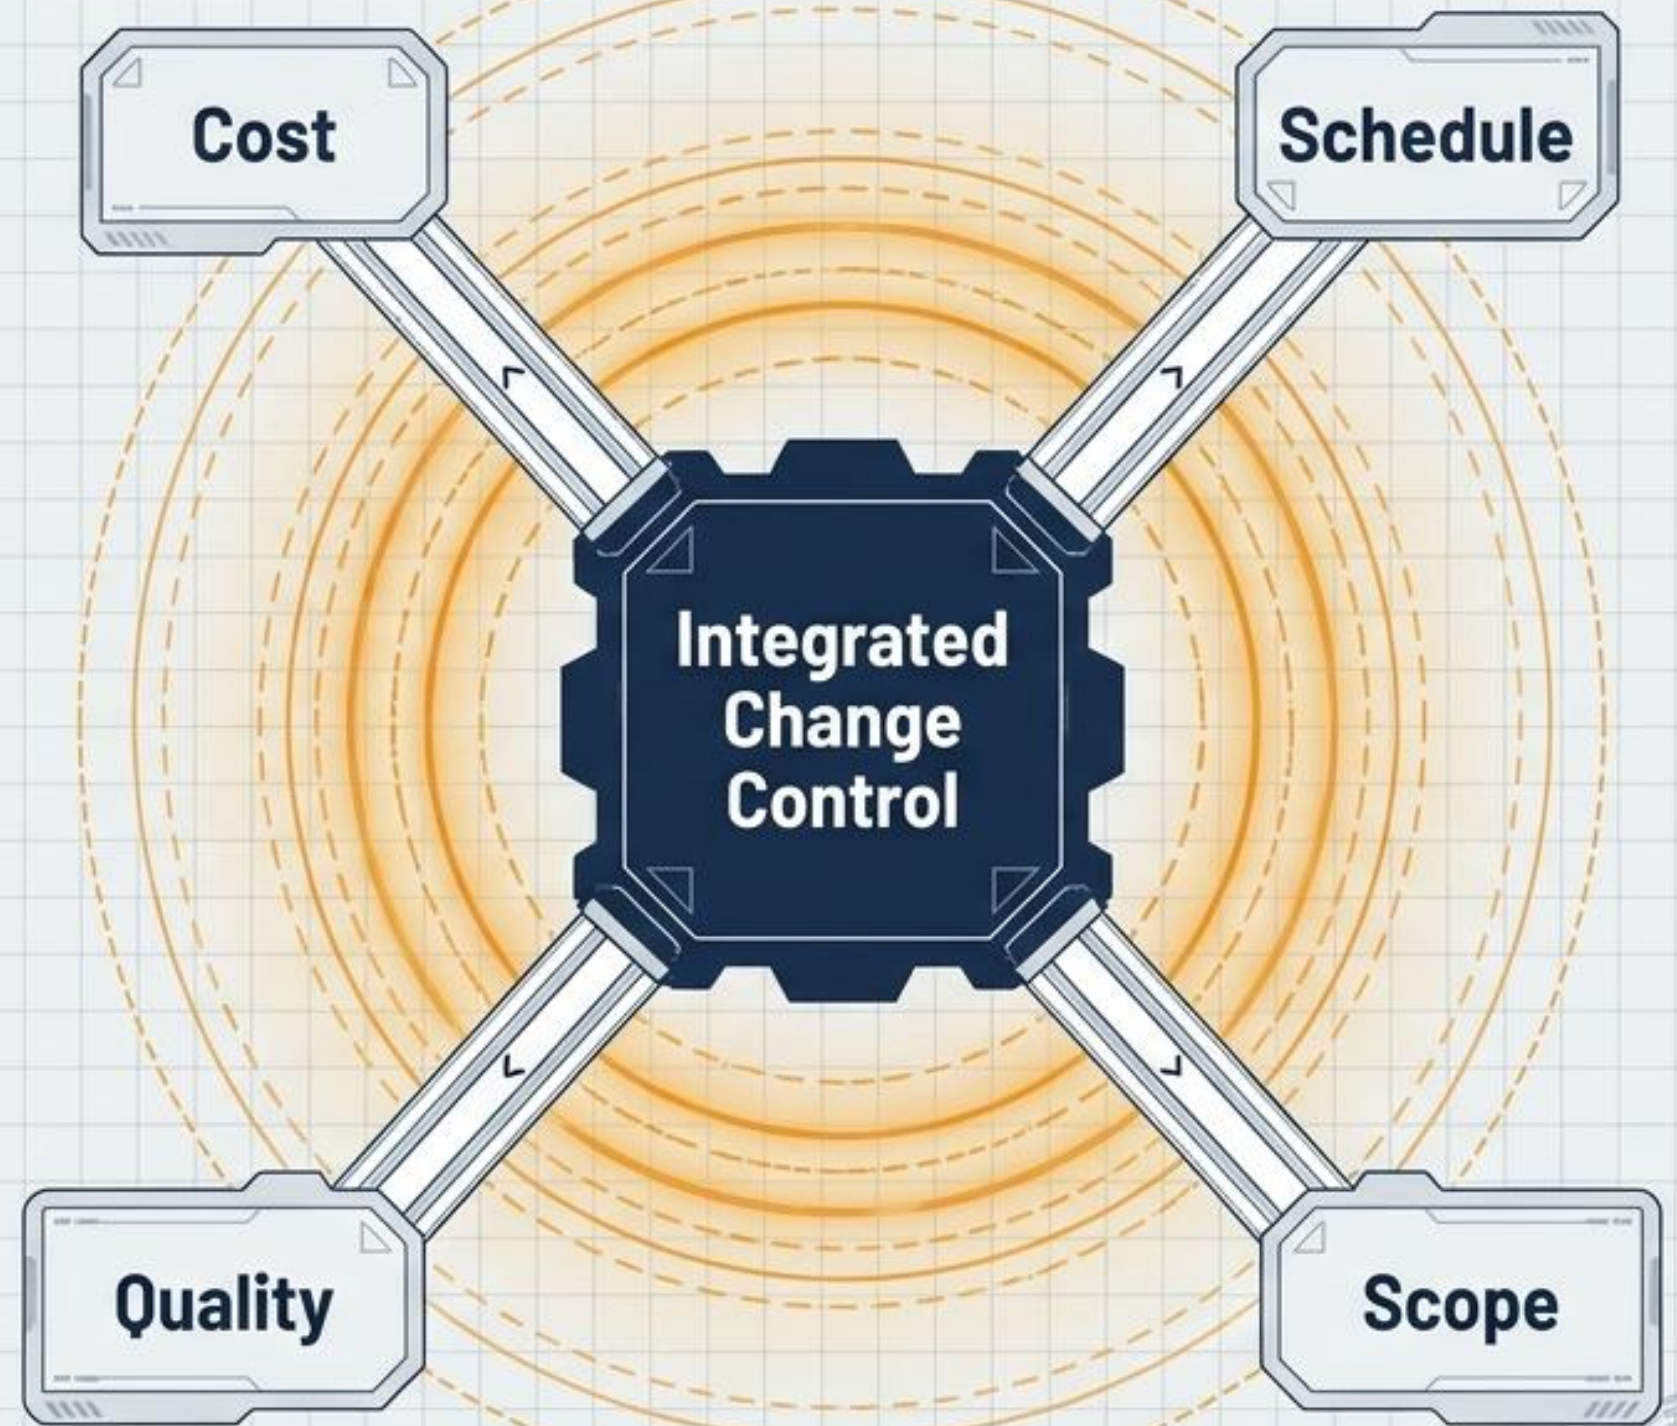




# The Origins of Change (Change Vectors)

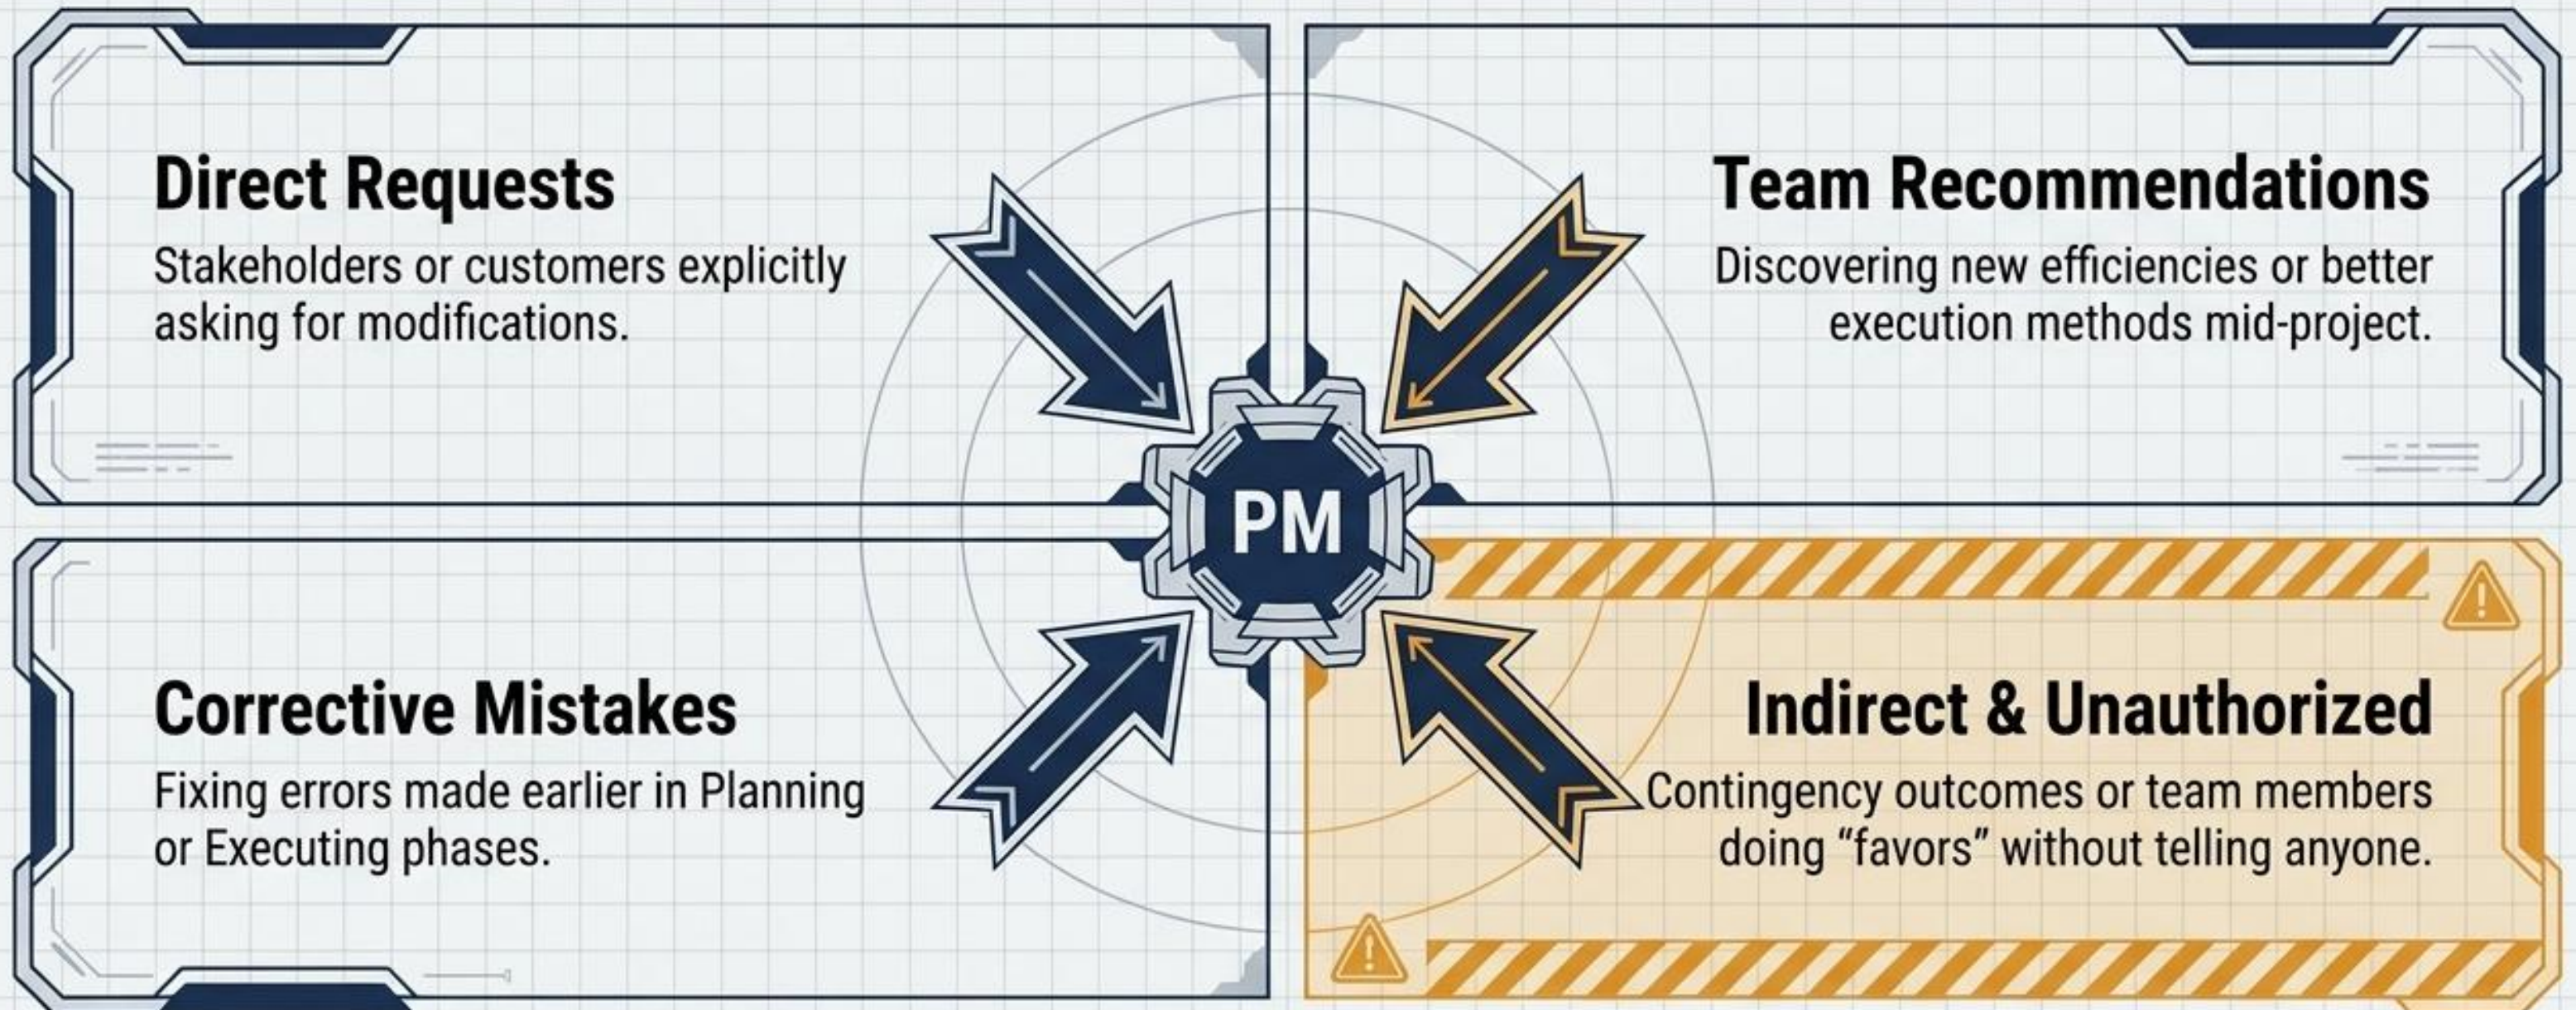

**If a dozen little changes slip through, your project scope suddenly exits stage left.**



# The Gatekeeper's Interrogation

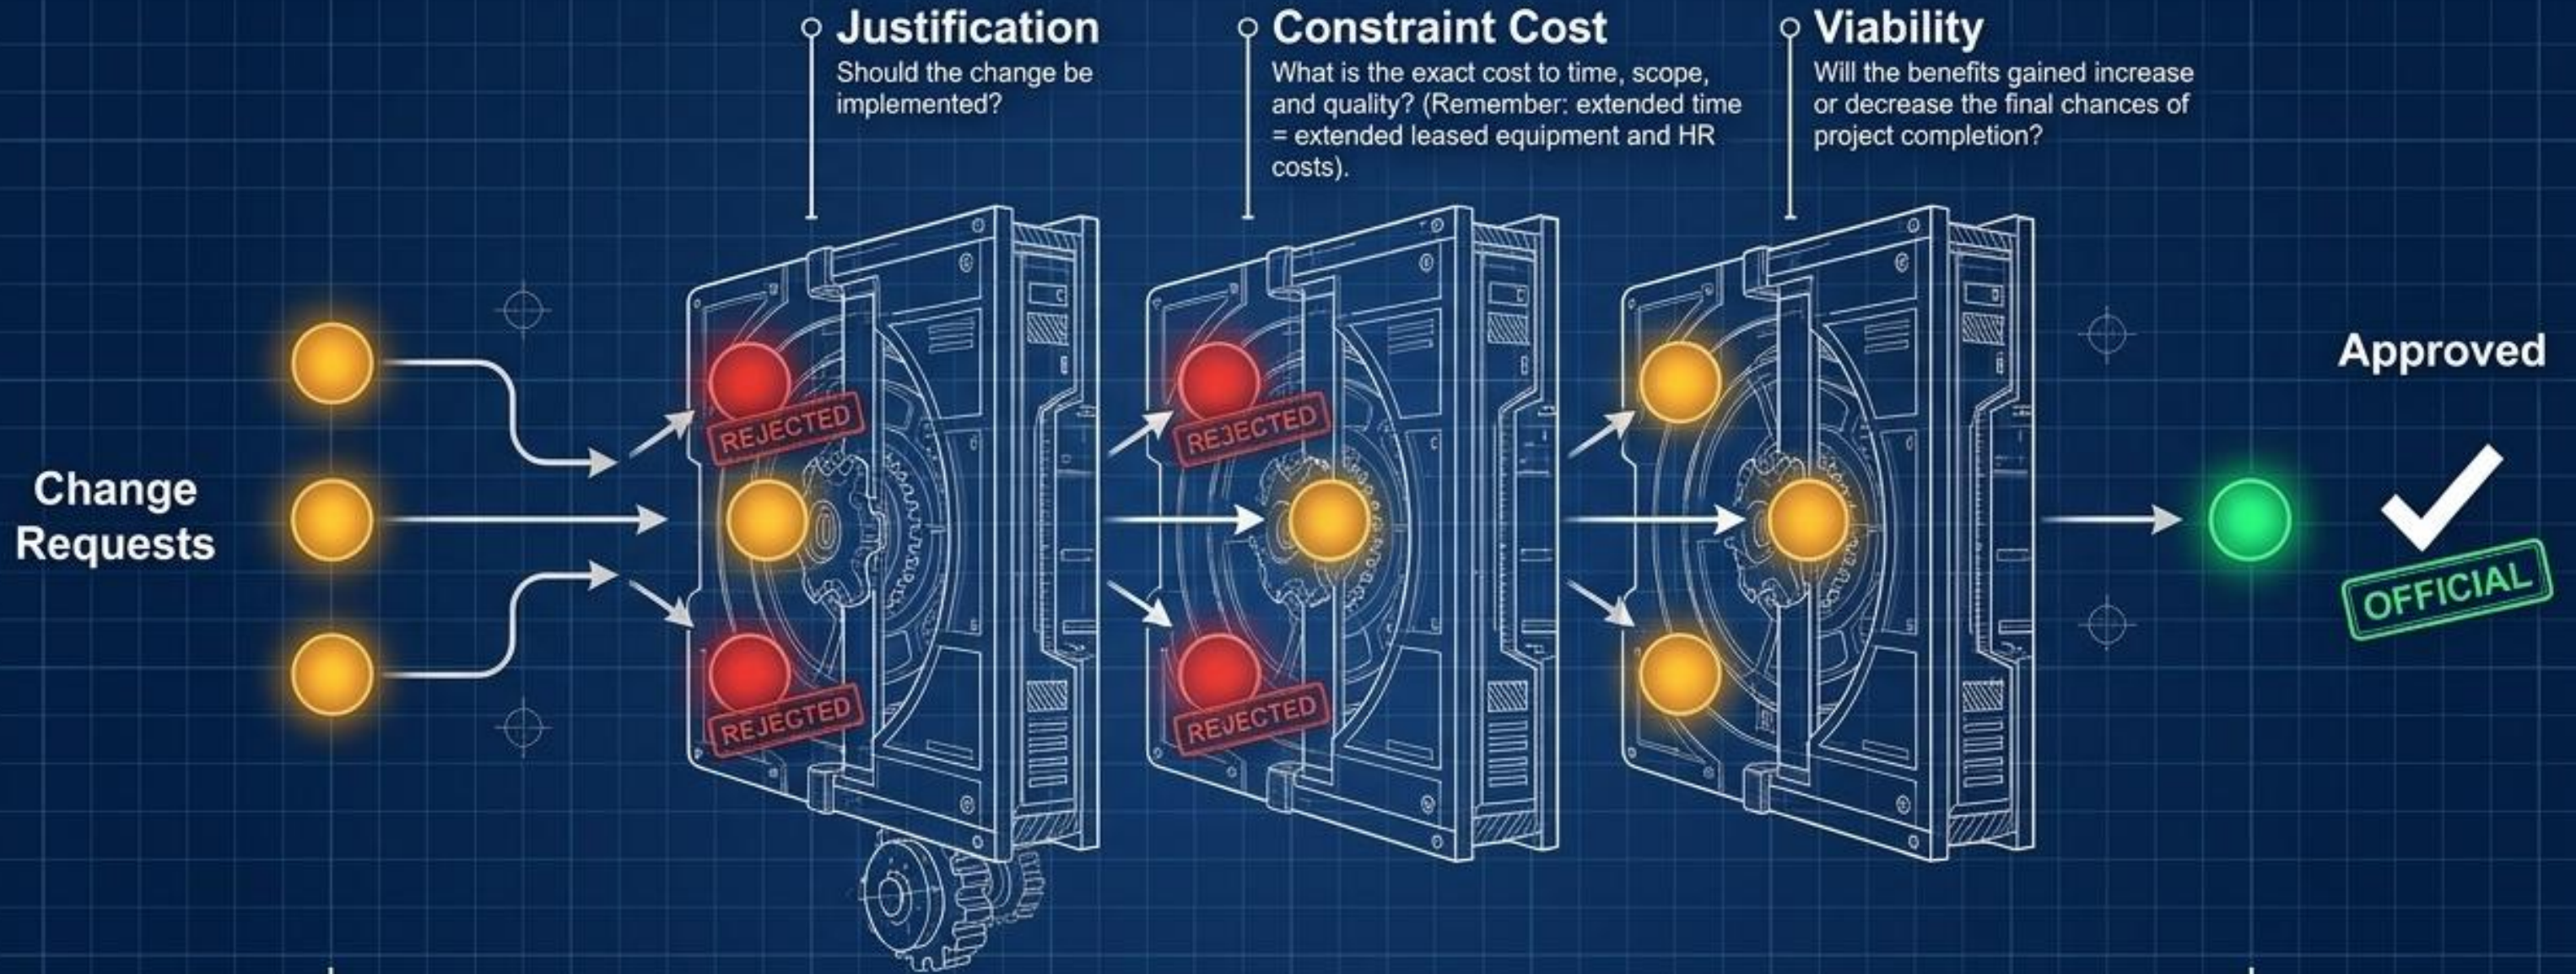


Just because a change is requested doesn't mean it's implemented.  
Every request must prove its value against the baselines.



# Infrastructure: The Change Control System

Documented procedures to control, change, and approve project deliverables.

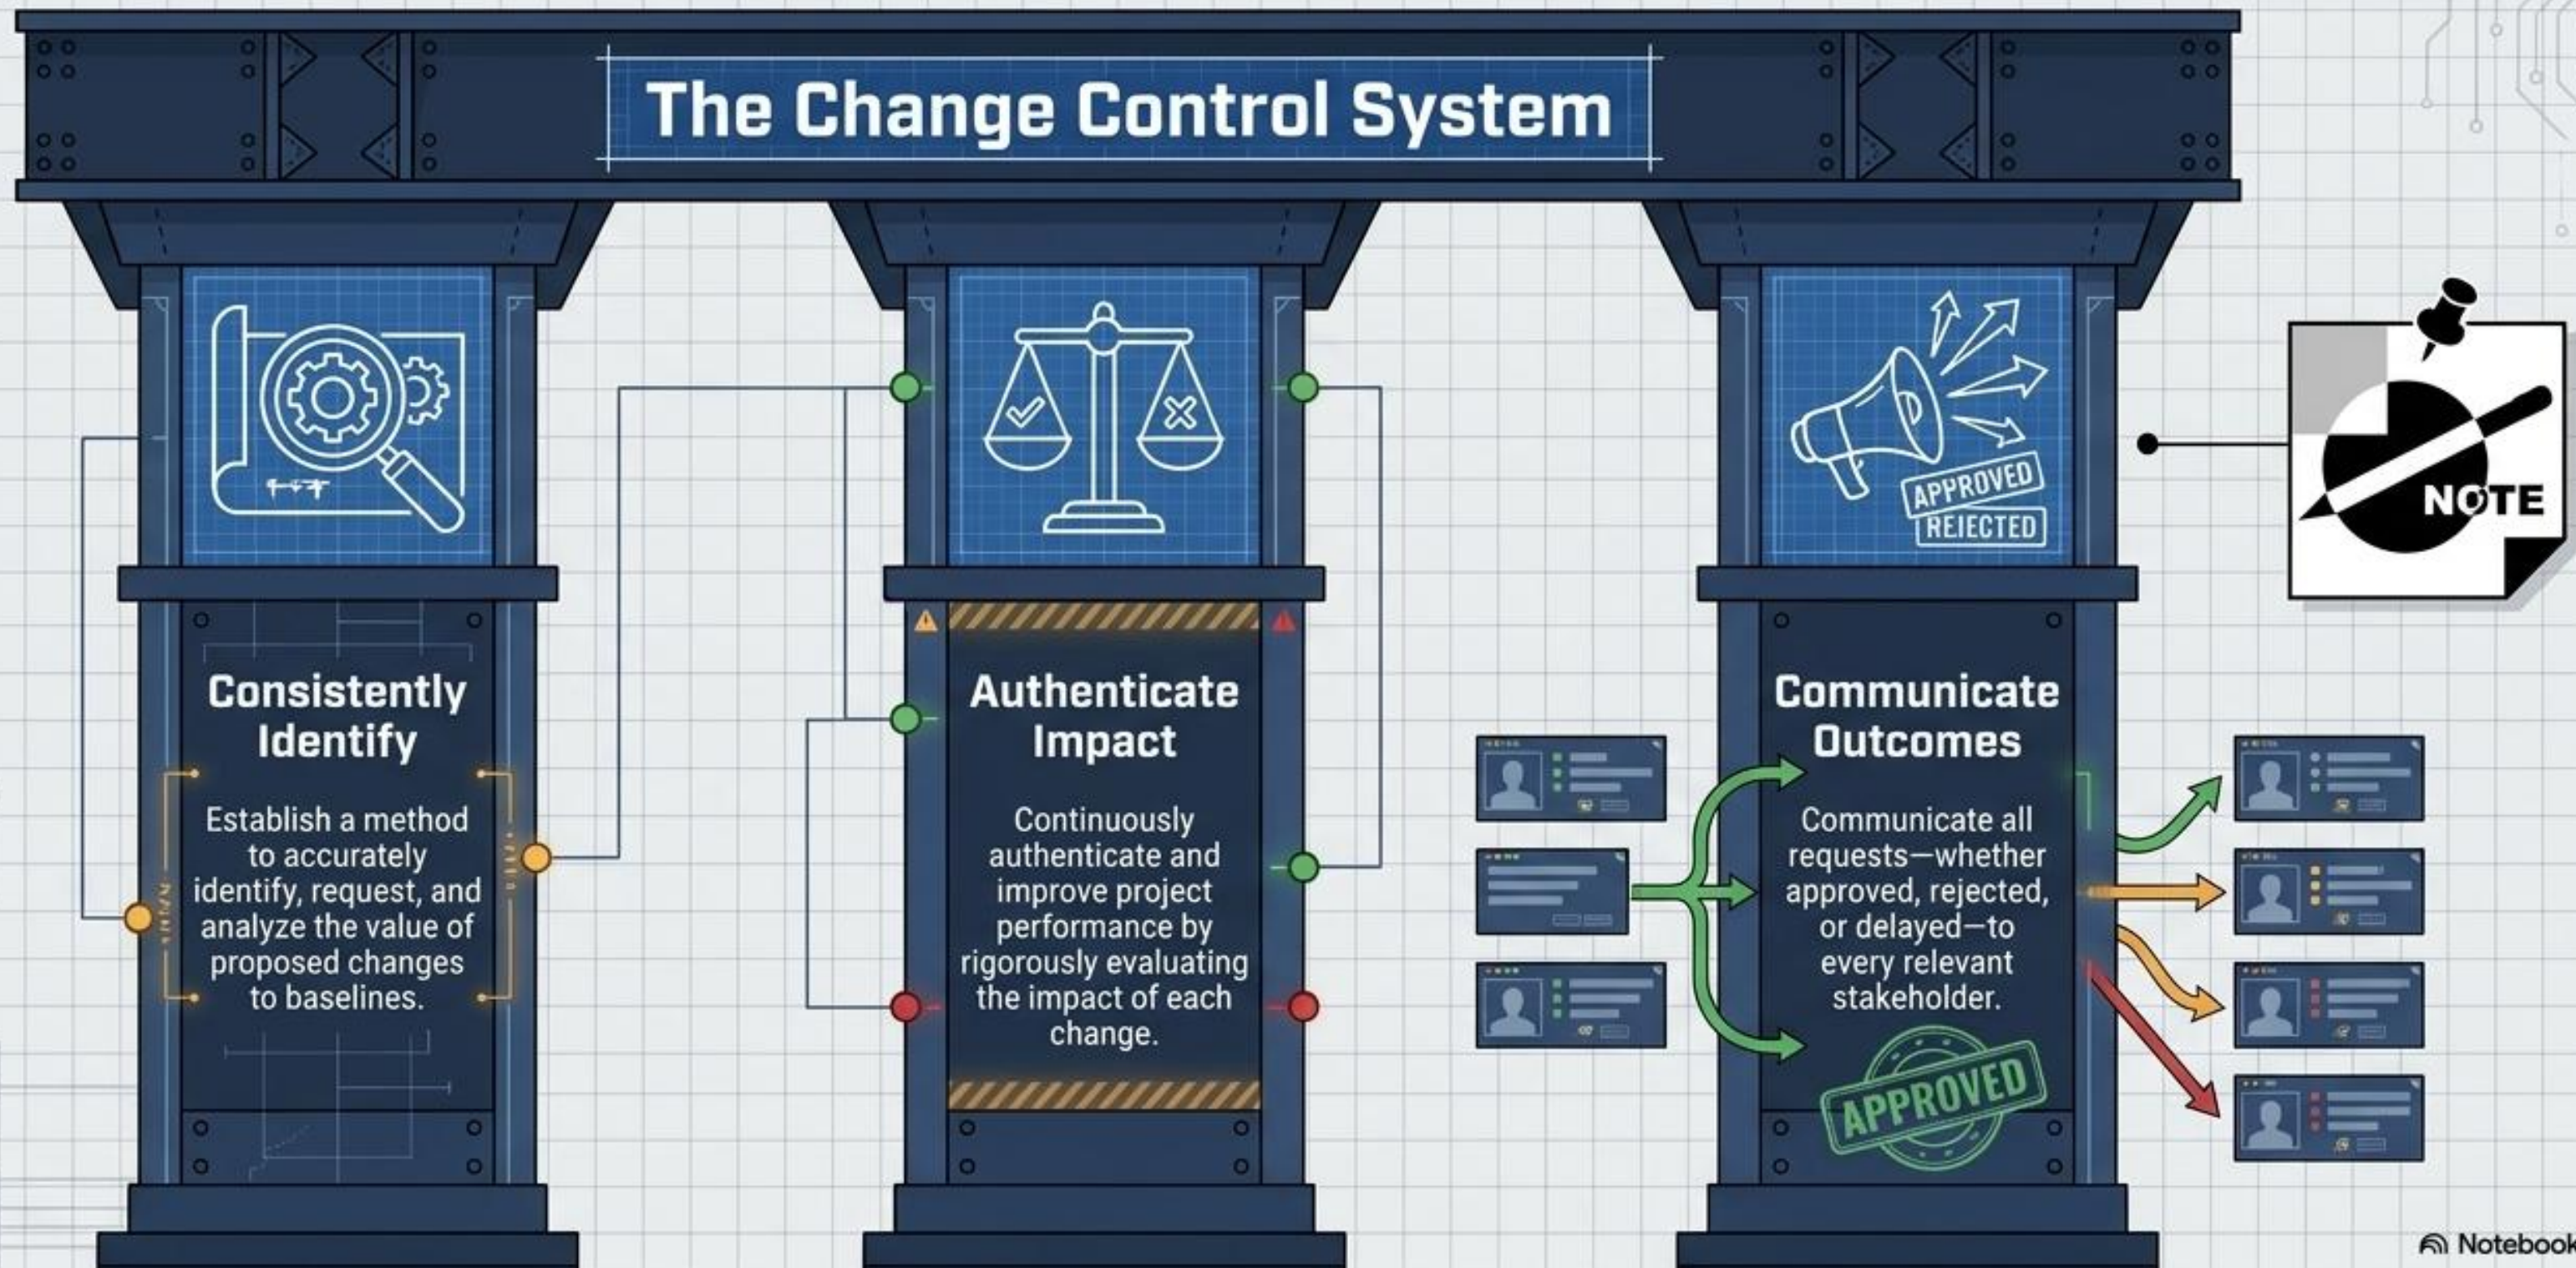



# Diagnostic Matrix: Configuration vs. Change Control

## Configuration Control

|                                                                                                       |                                                                            |
|-------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------|
|  <b>Focus:</b>       | The physical characteristics and specifications of the deliverables.       |
|  <b>System:</b>    | Managed through the configuration management system (a subsystem of PMIS). |
|  <b>Objective:</b> | Verifying that functional and physical requirements are met.               |

## Change Control

|                                                                                                         |                                                                                 |
|---------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------|
|  <b>Focus:</b>       | The project baselines (scope, schedule, cost) and project management documents. |
|  <b>System:</b>    | Managed through the Change Control System.                                      |
|  <b>Objective:</b> | Managing the impact on project constraints and authorizing plan updates.        |



# The Configuration Control Cycle

GOVERNANCE  
PROTOCOL  
ACTIVE

SYSTEMATIC  
CONTROL

## Configuration Verification and Auditing

Ensuring accuracy. Verifying performance requirements are met and changes are correctly assessed, approved, and tracked.



## Configuration Identification

Describing characteristics of the product/service. The baseline for managing and verifying changes. Labeling products and documents.



## Configuration Status Accounting


(Not financial). Documenting and storing status information: approved ID, status of proposed changes, and implementation status.



SYSTEMATIC  
CONTROL



# The CCB & Emergency Protocols

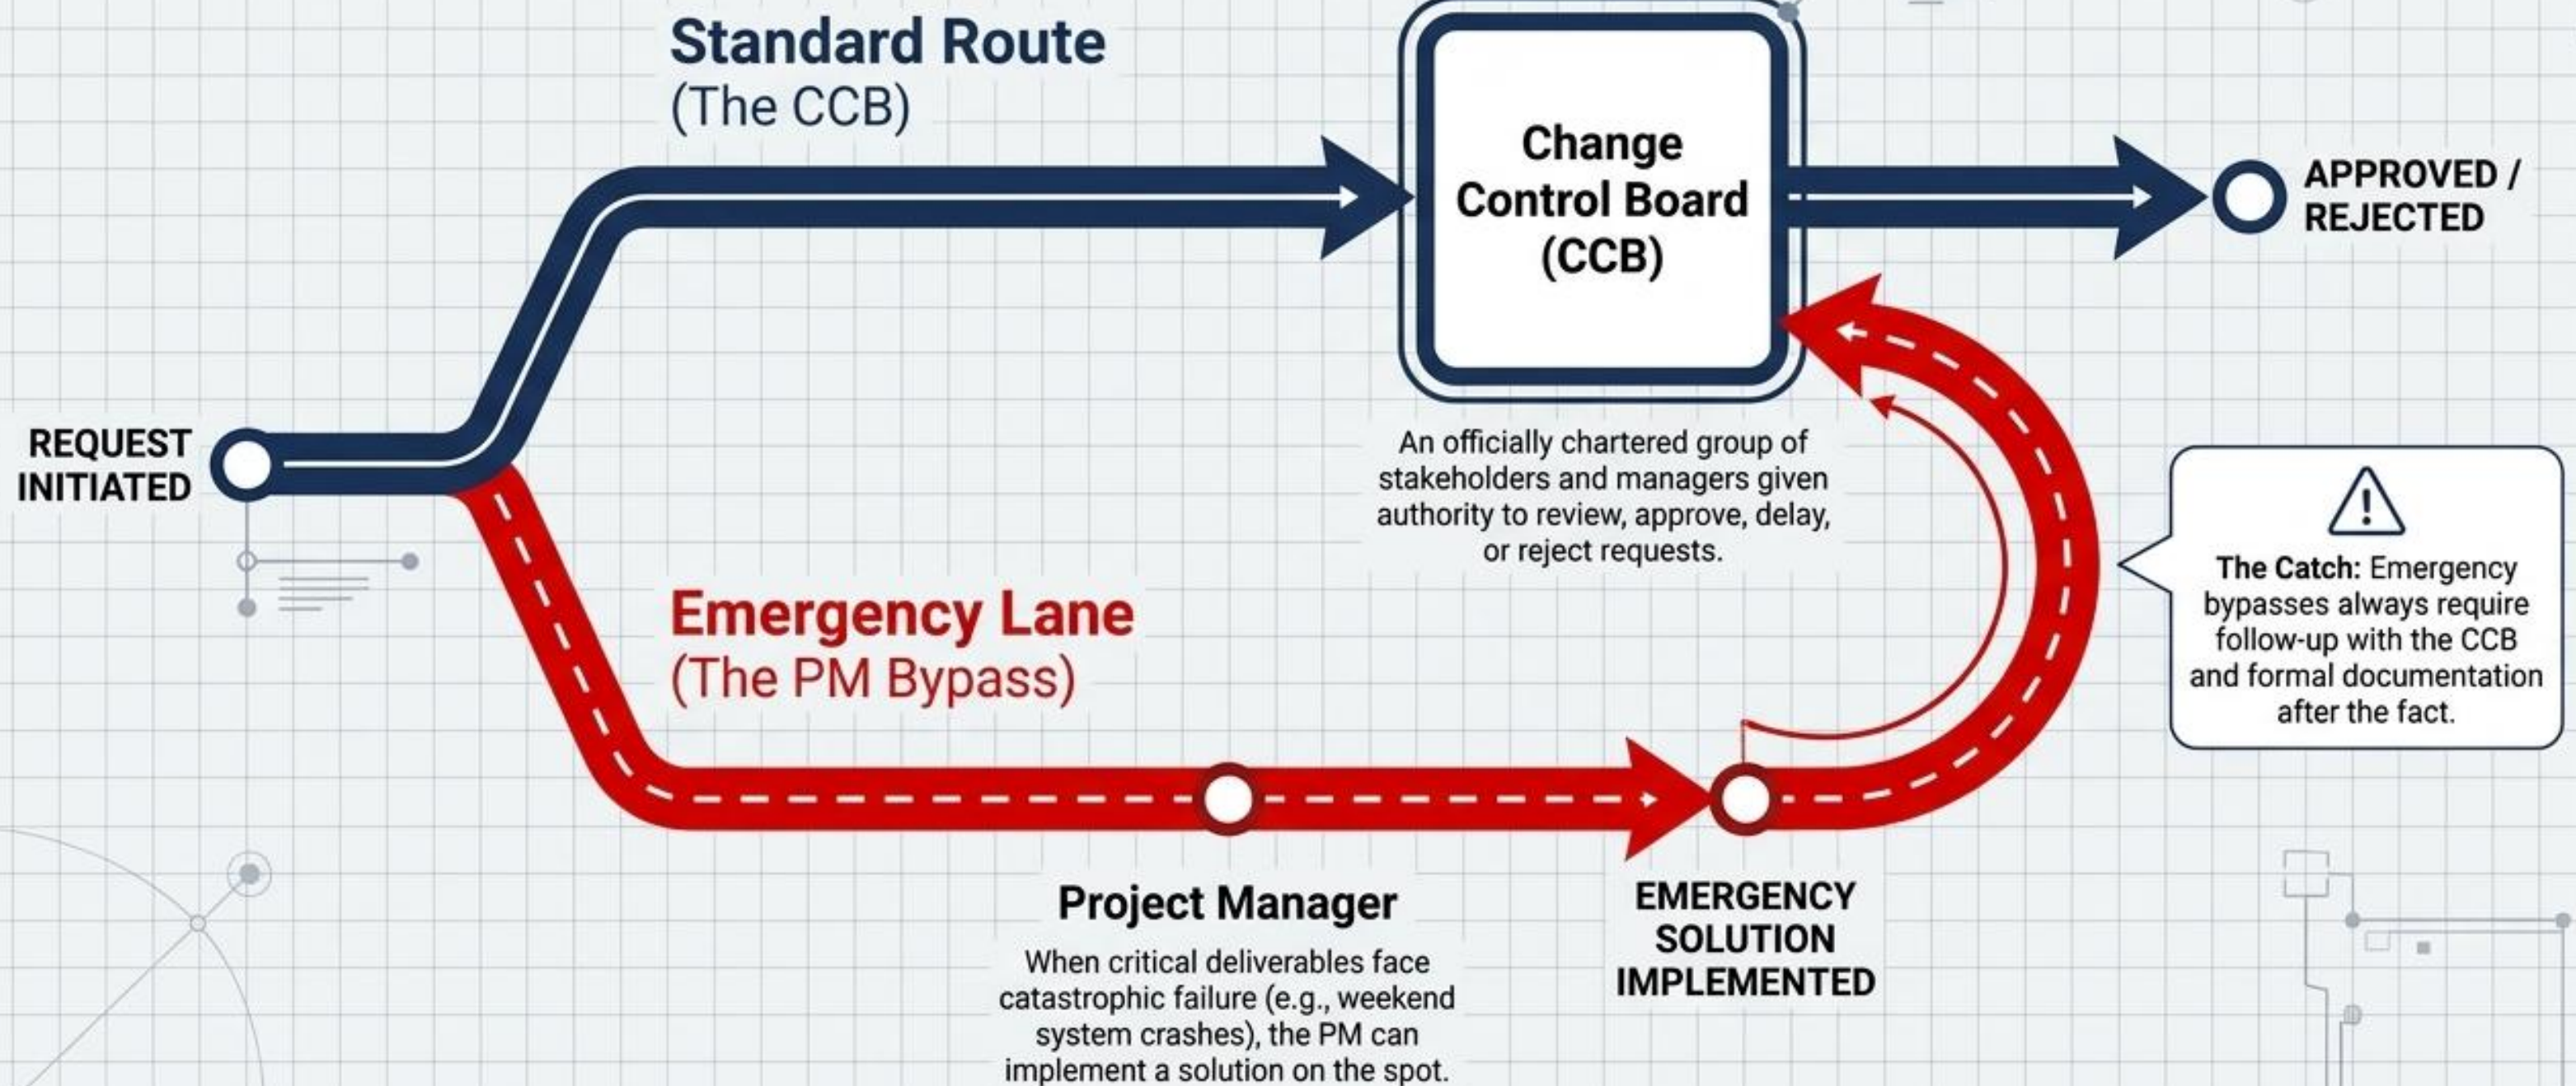



# The Two Golden Rules of Change

**Rule 01:** All change requests must be in writing.

(Clarifies the request, eliminates confusion, and allows precise time/cost estimation).

**Rule 02:** All changes must flow through the formal system.

(No backstage favors. Going around the PM leads to schedule delays, cost overruns, and sacrificed quality).




**WARNING: Stakeholders are notorious for verbal requests. If they refuse to write it down, the project team must log it.**



# Anatomy of a Failure: The “Minor” Update




## Real World Scenario

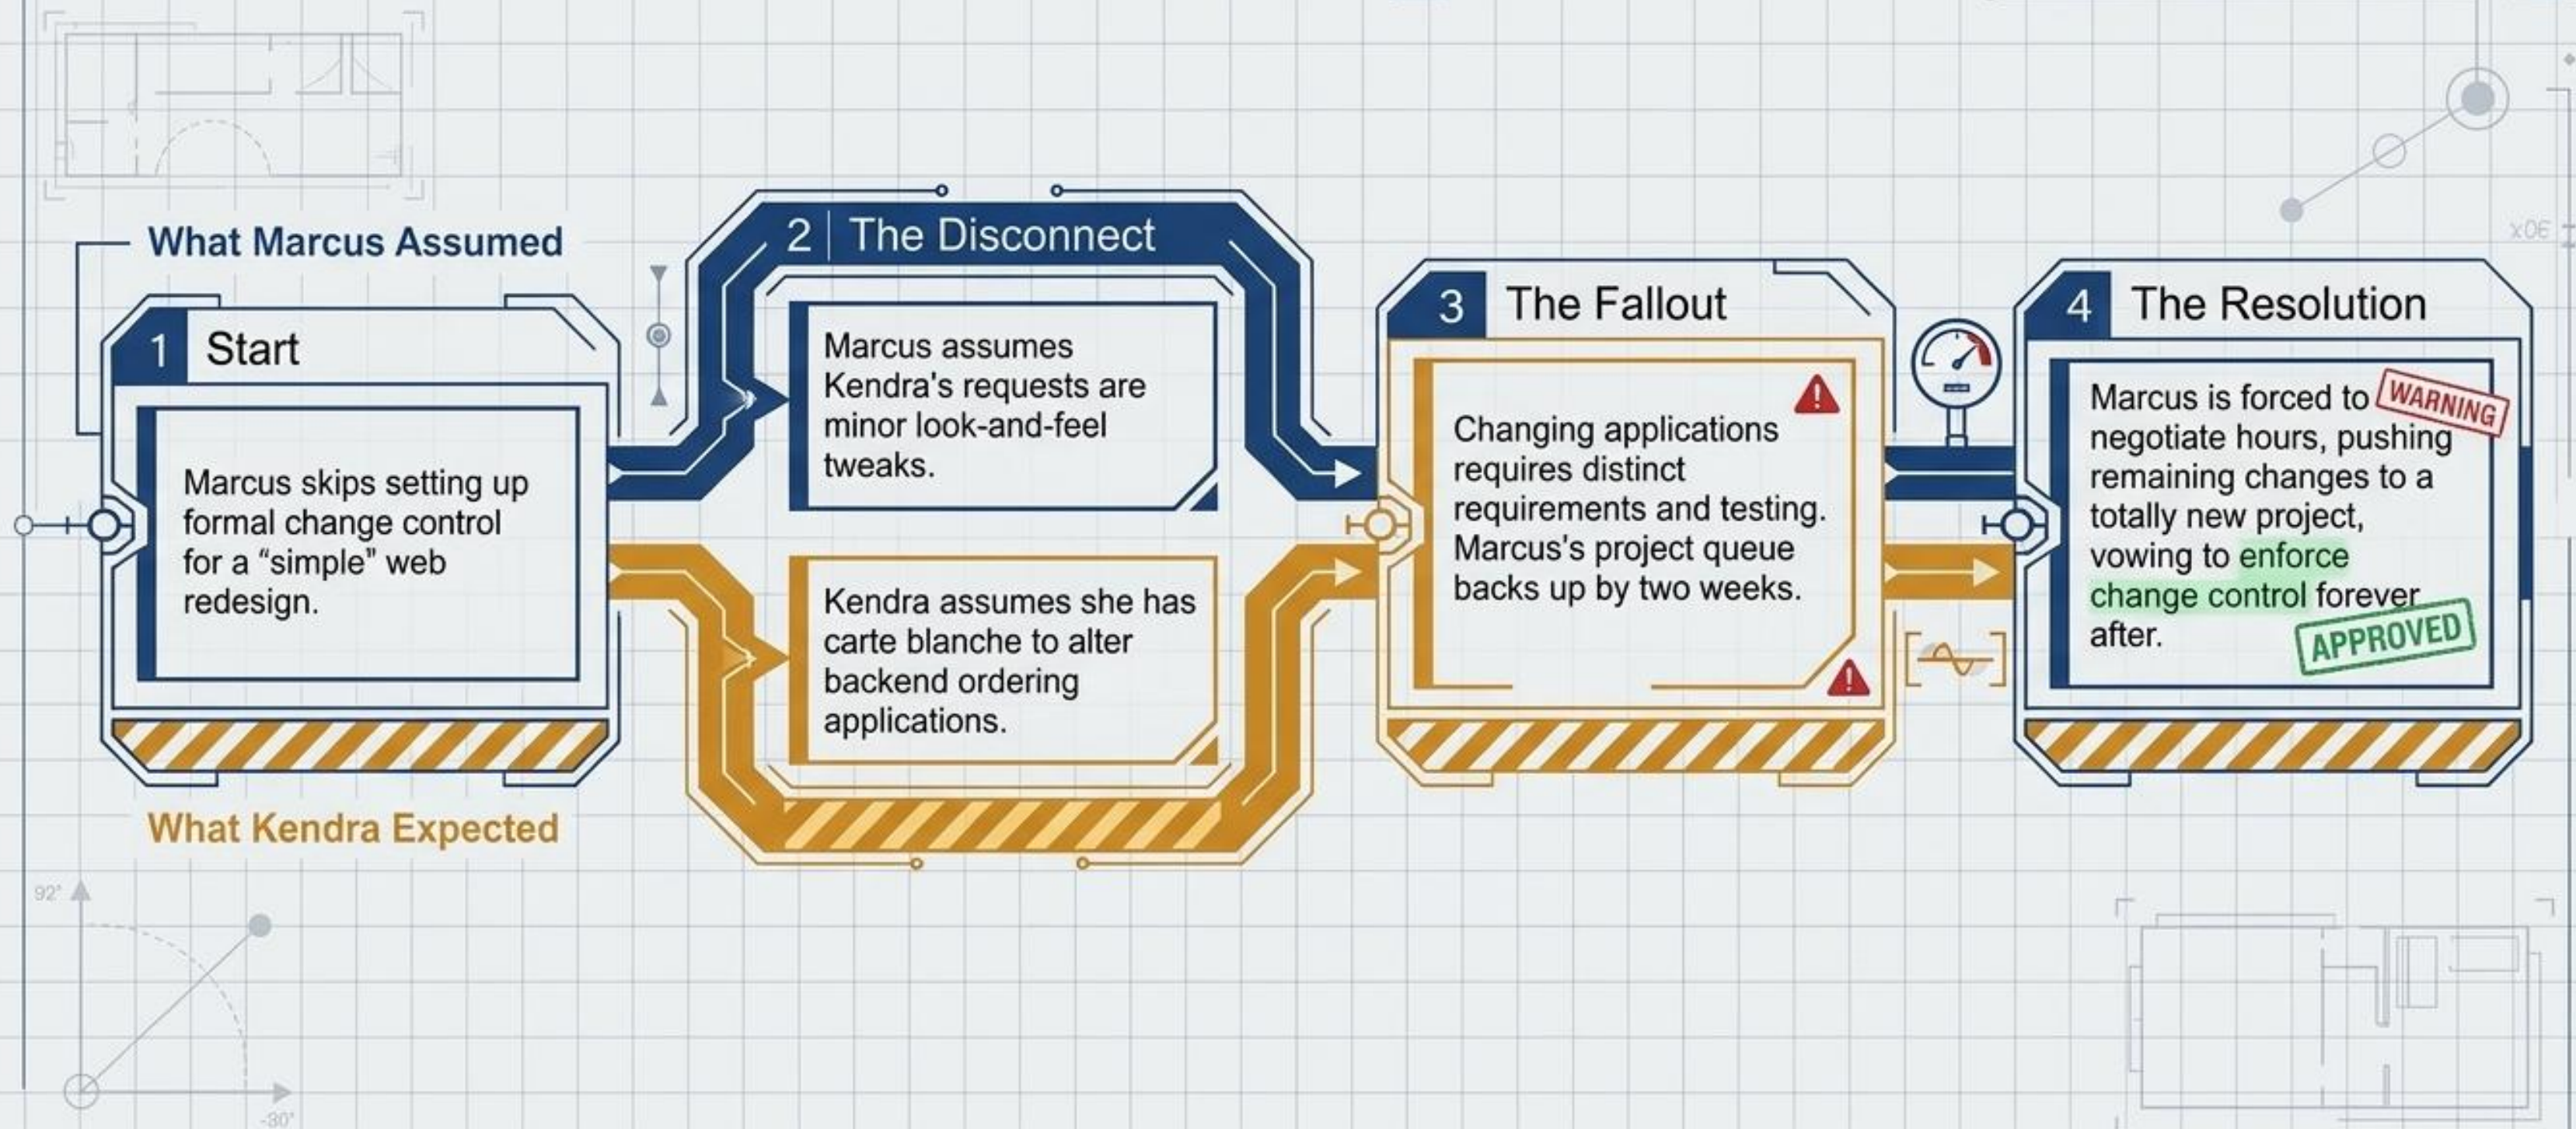



# The Process Blueprint (ITT0s)

## Manufacturing Pipeline

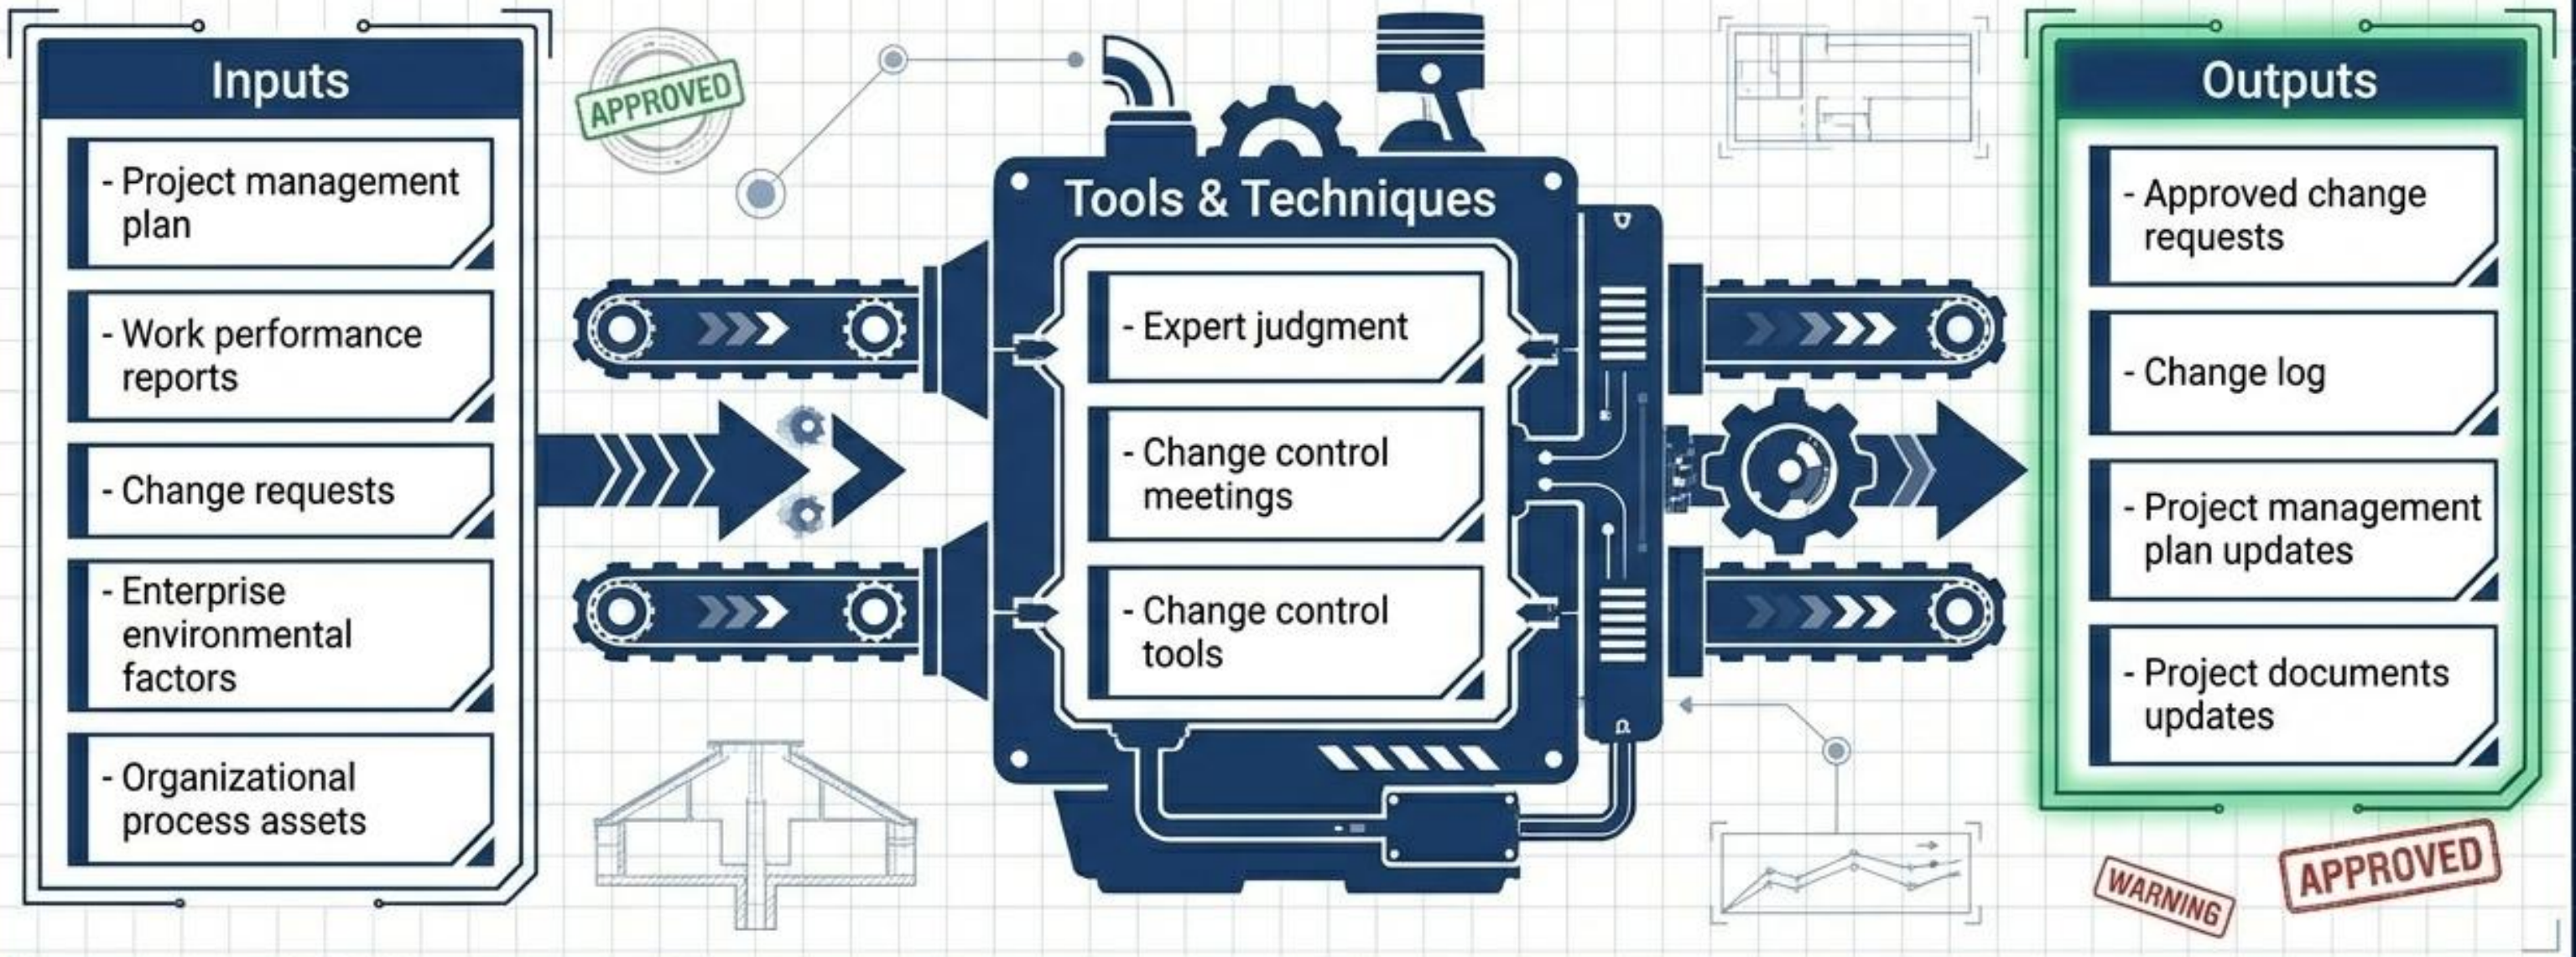



# Baseline Integrity & Implementation

Present Day

You cannot change past performance.  
Past baselines are preserved for variance  
comparison and lessons learned.



Change  
Approved

**The Golden Timeline Rule:**  
Changes made to baselines only  
reflect trajectory from the current  
point in time forward.

**Implementation Execution:** Approved change requests are an output here,  
but they are physically implemented in the Direct and Manage Project  
Work process (an Executing process).




# Controlling Stakeholder Engagement





# Synthesis: The Complete Ecosystem

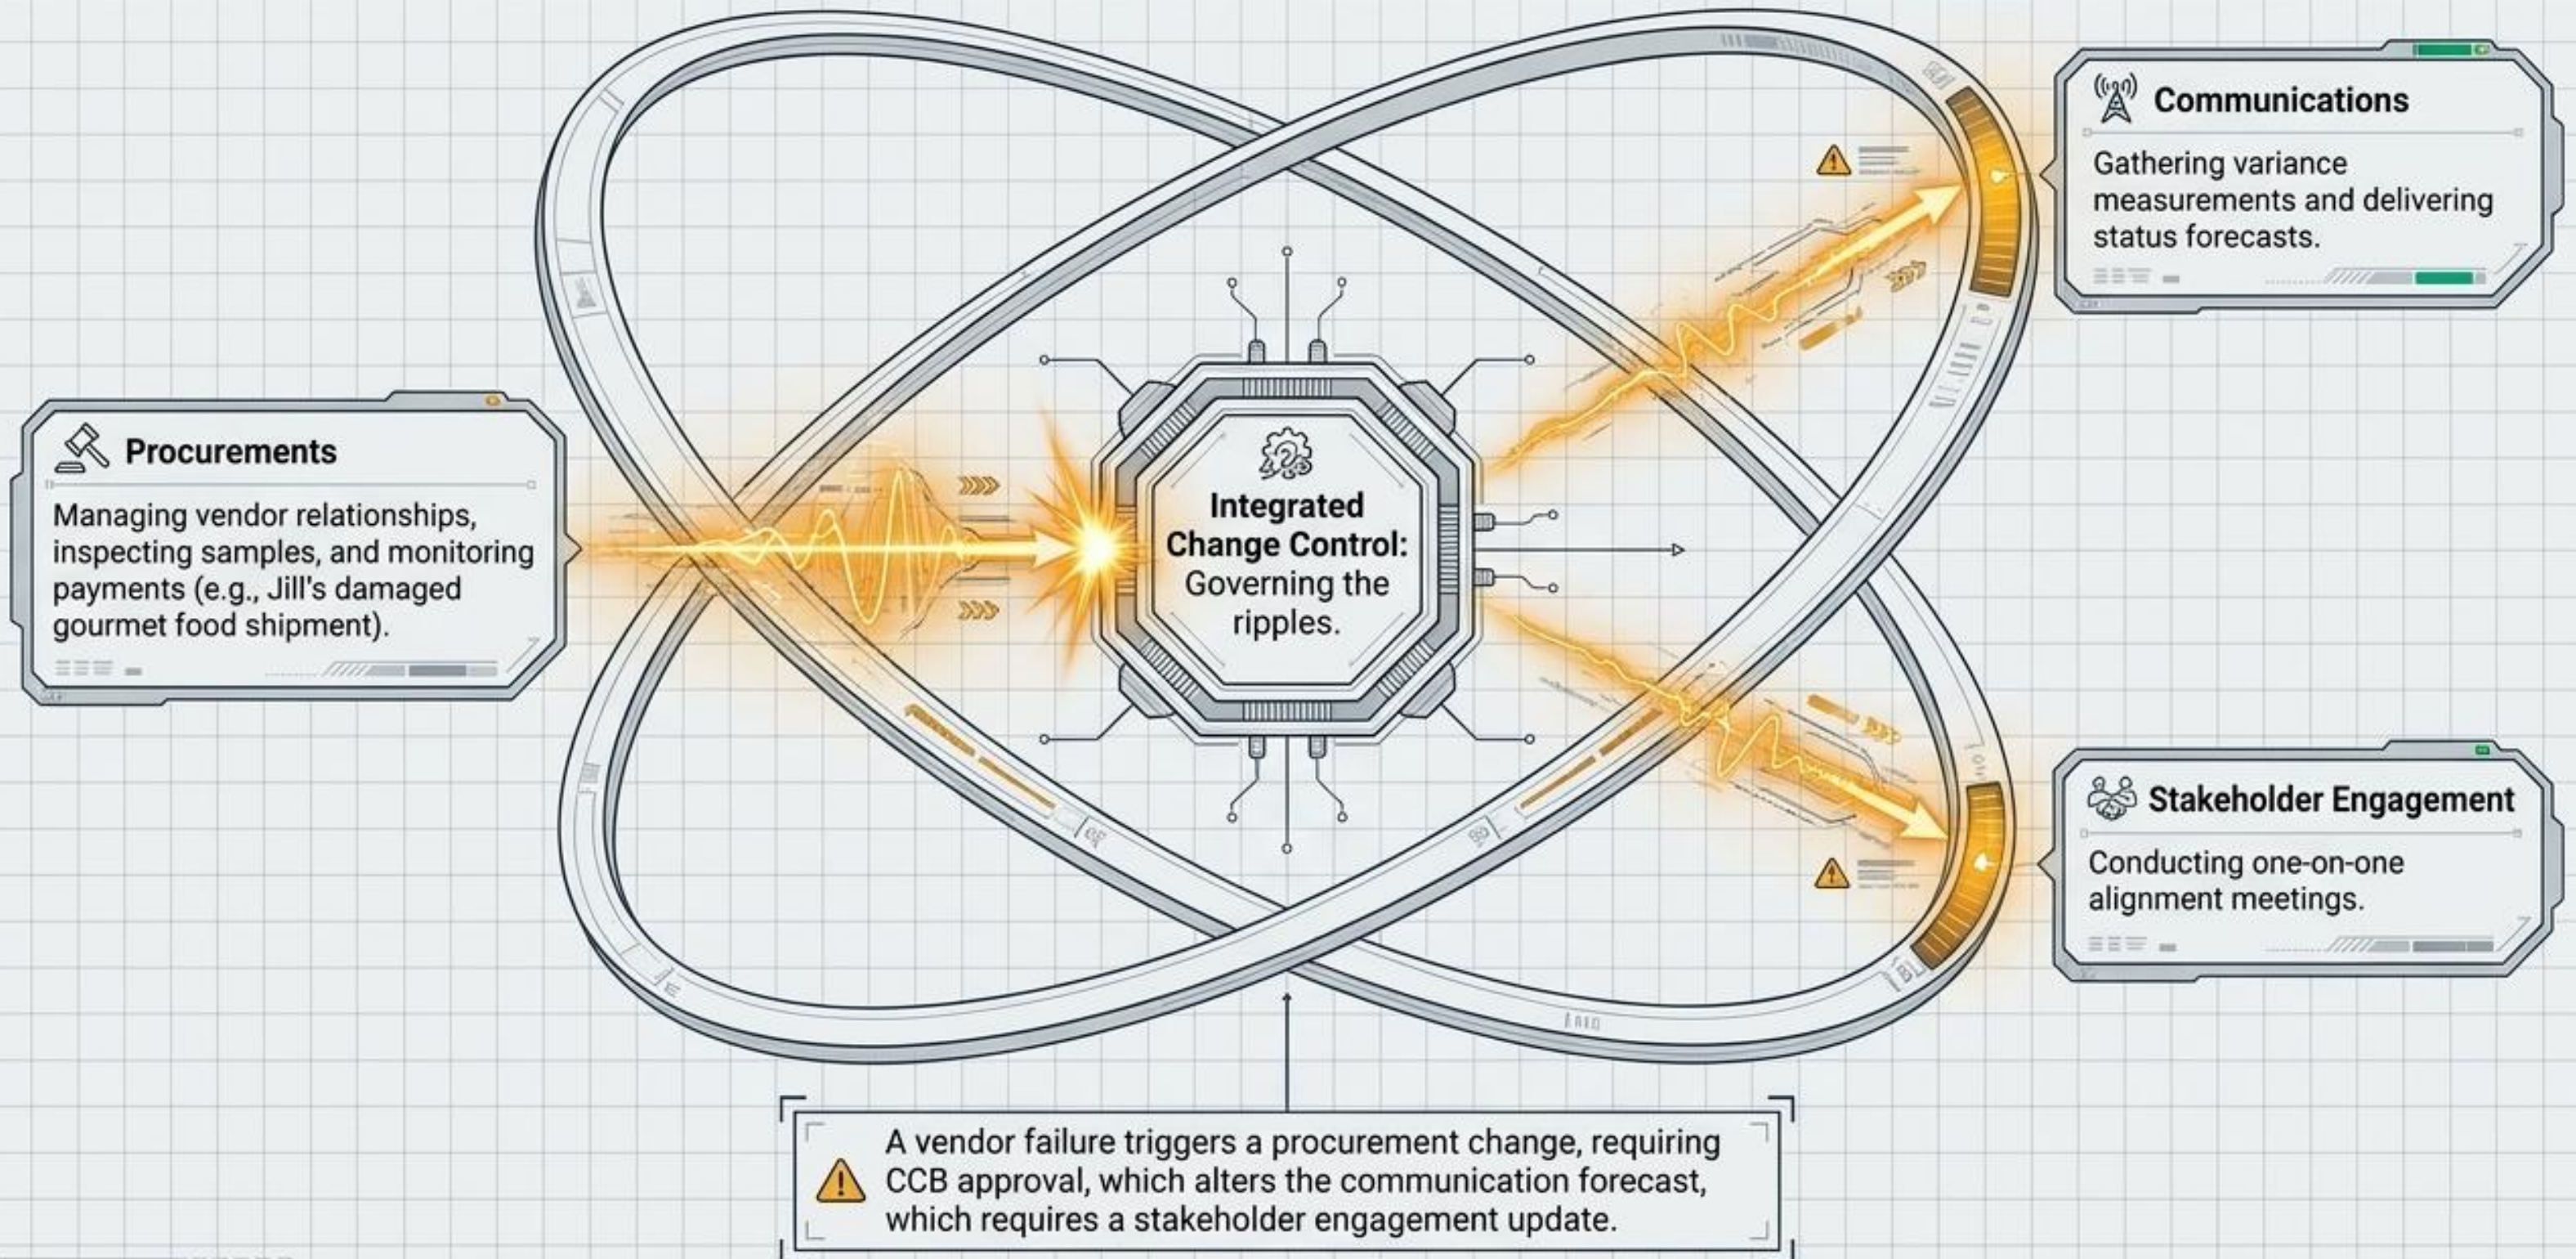



# PMP Exam Essentials: Change Control

## Monitor & Control Outputs

Change requests (corrective, preventive, defect repair), work performance reports, plan updates, document updates.

## Direct & Manage Integration

Approved change requests are generated in Perform Integrated Change Control but implemented in Direct and Manage Project Work.

## Configuration vs. Change

Configuration = physical characteristics / deliverable specs.

Change = baselines, plans, and documents.

## CCB Purpose

A defined group of stakeholders tasked strictly to review, approve, delay, or reject change requests.
