


Certyfikat PMP: Work Effects Control

dr Zbigniew Galar

Monitoring and Controlling
Project Performance Domain

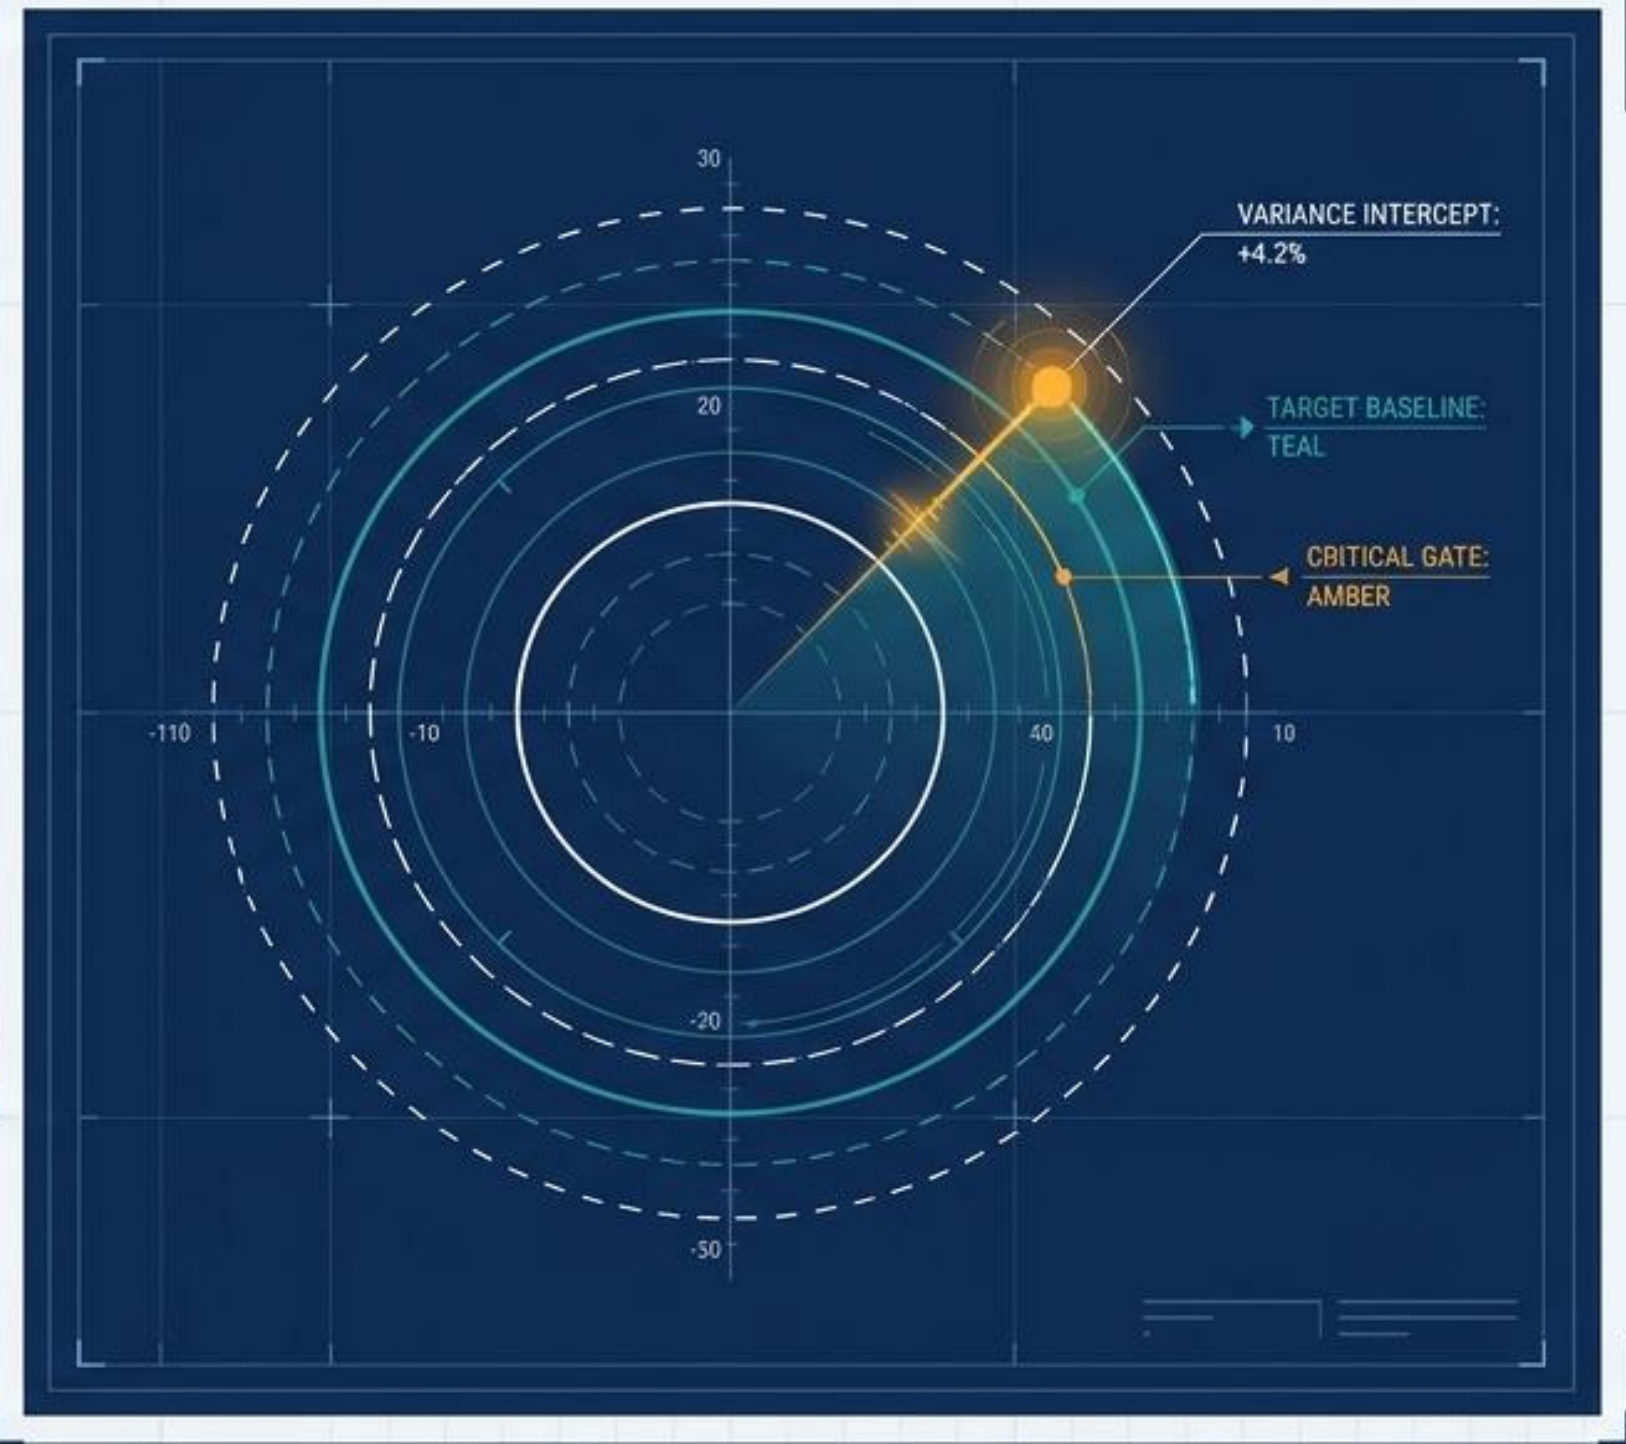

Navigating the Homestretch of Project Delivery

Core Objectives

Ensure Alignment

Confirm project deliverables conform to established quality standards and business needs.


Manage Variance

Prepare and communicate earned value measurements, forecasts, and status.

Control Impact

Assess corrective actions and minimize impact on schedule, cost, and resources.

Variance & Trend Analysis Model

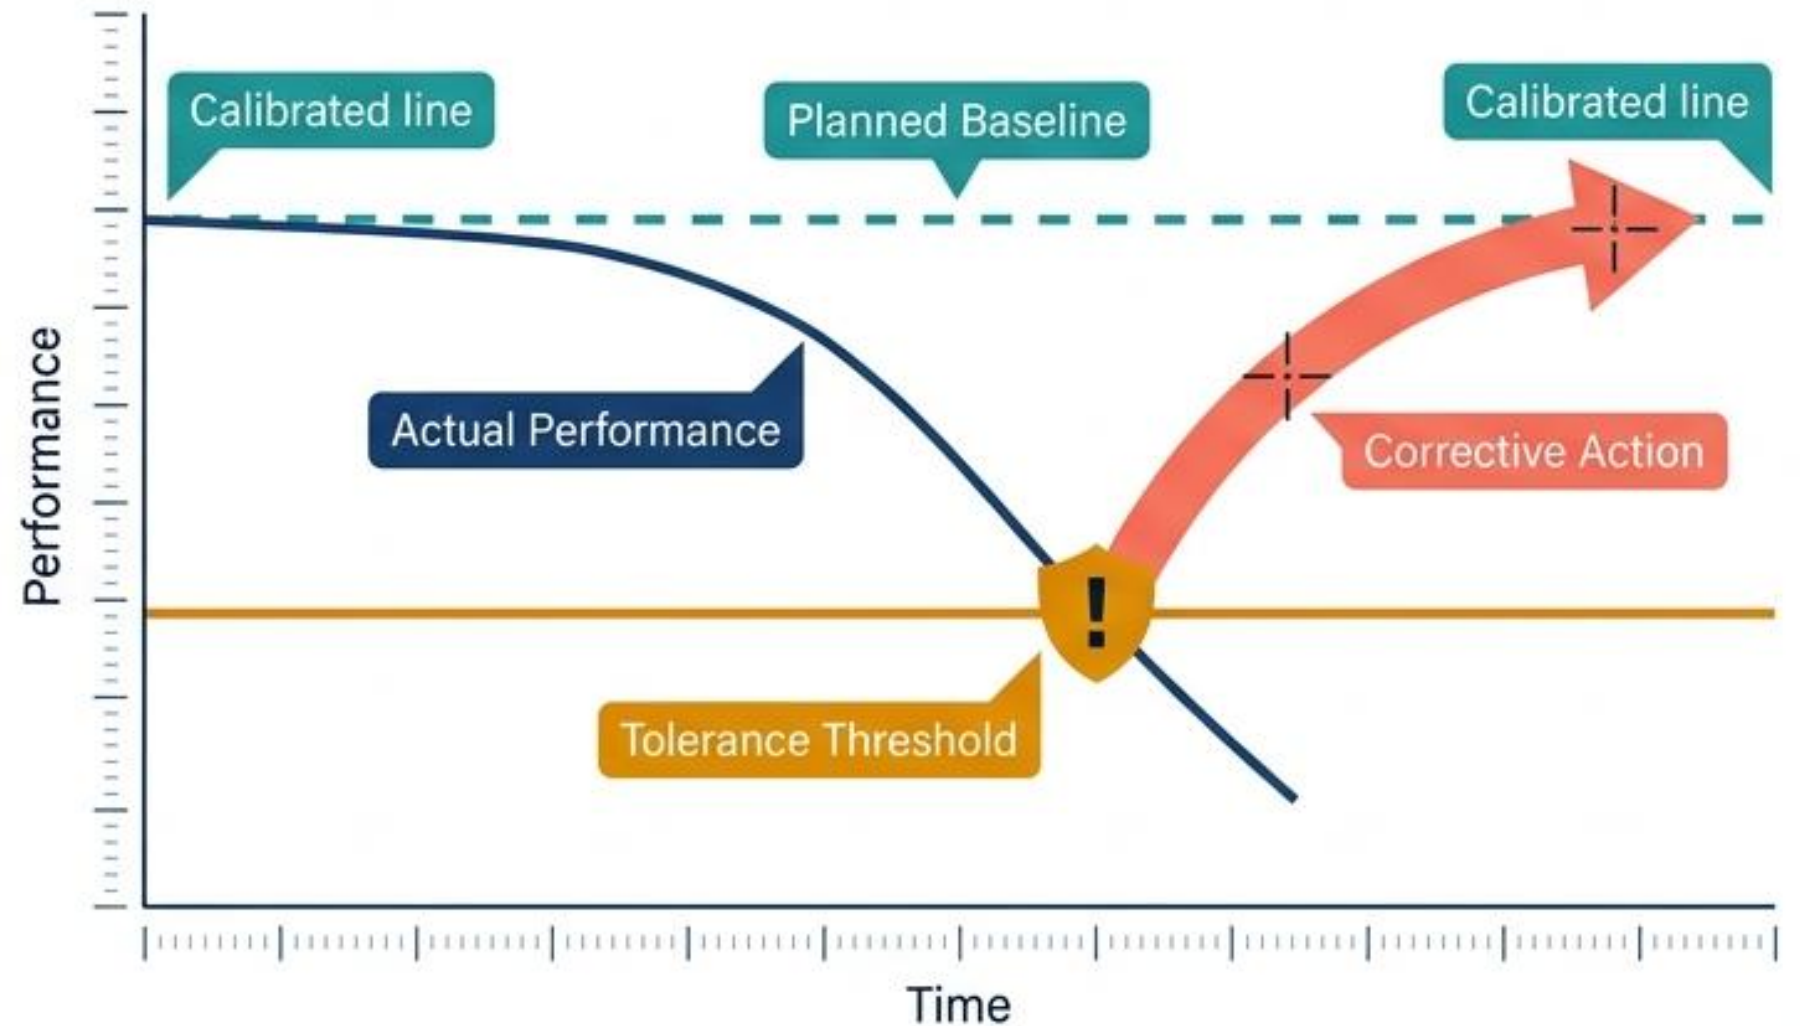

The Six Pillars of Project Control



Control Risks

Tracking triggers and executing response plans.



Control Costs

Managing changes to the authorized cost baseline.



Control Schedule

Monitoring status to update project progress and manage schedule baseline changes.



Control Quality

Ensuring deliverables meet established quality standards.



Validate Scope

Formalizing the acceptance of completed project deliverables.



Control Scope

Monitoring project and product scope status and managing baseline changes.

The Objective of Continuous Risk Control

Track & Respond

Implement response plans, track identified risks, and actively monitor the project for risk triggers.

Identify & Reassess


Reexamine existing risks for validity, identify newly emerging risks, and reassess project assumptions.

Evaluate Effectiveness


Audit policies, ensure contingency reserves are updated, and judge the overall effectiveness of the Risk processes.



Processing Risk Data Through the ITTO Funnel

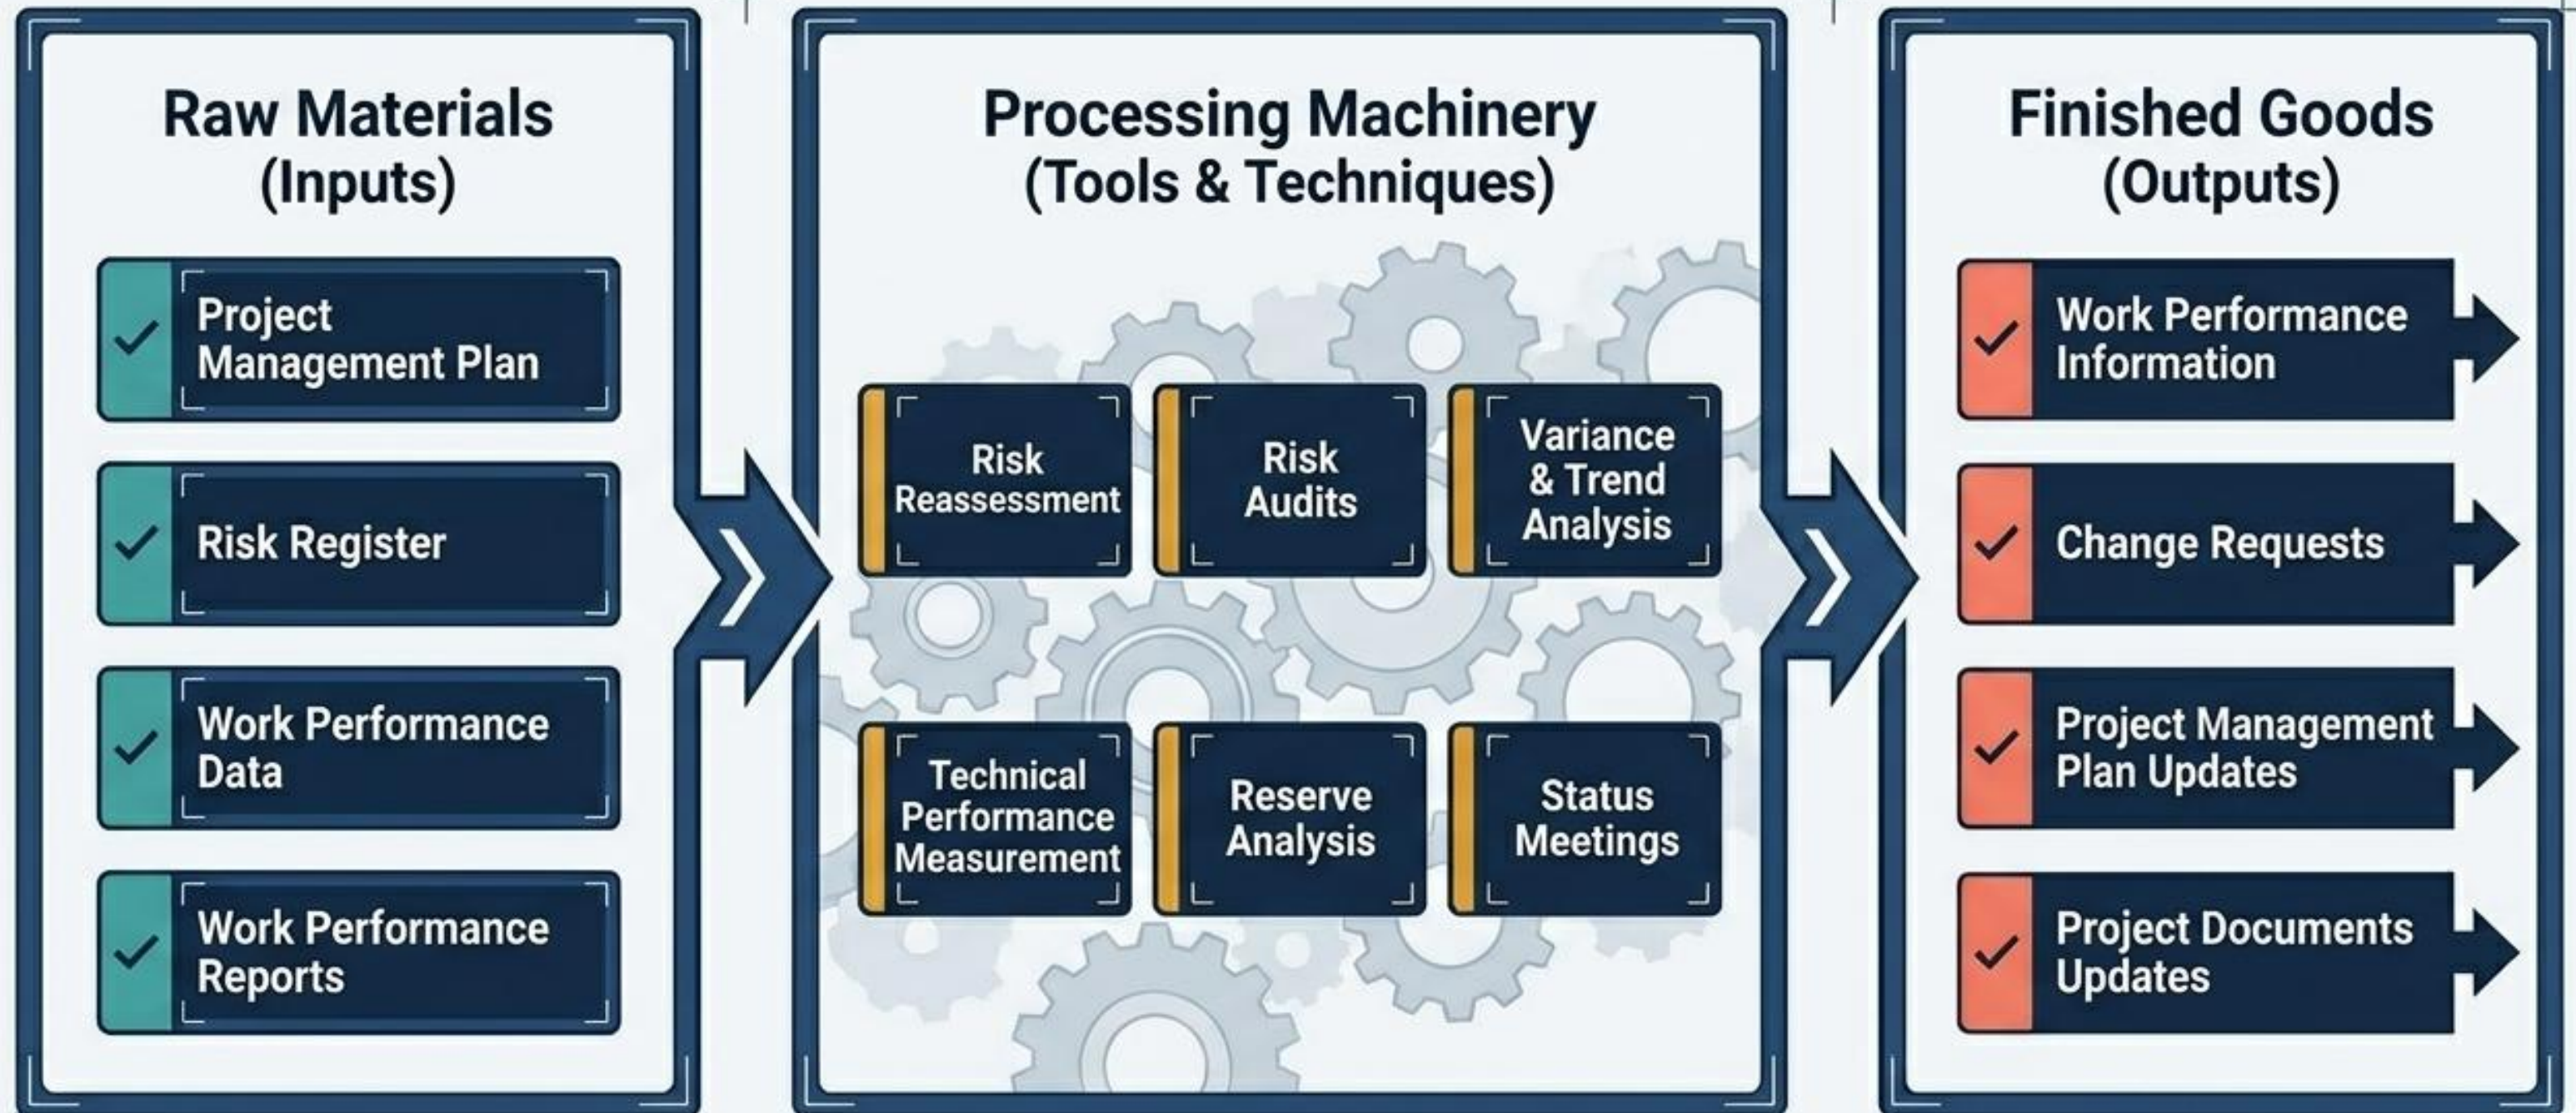

Monitoring the Triggers: From Data to Decision

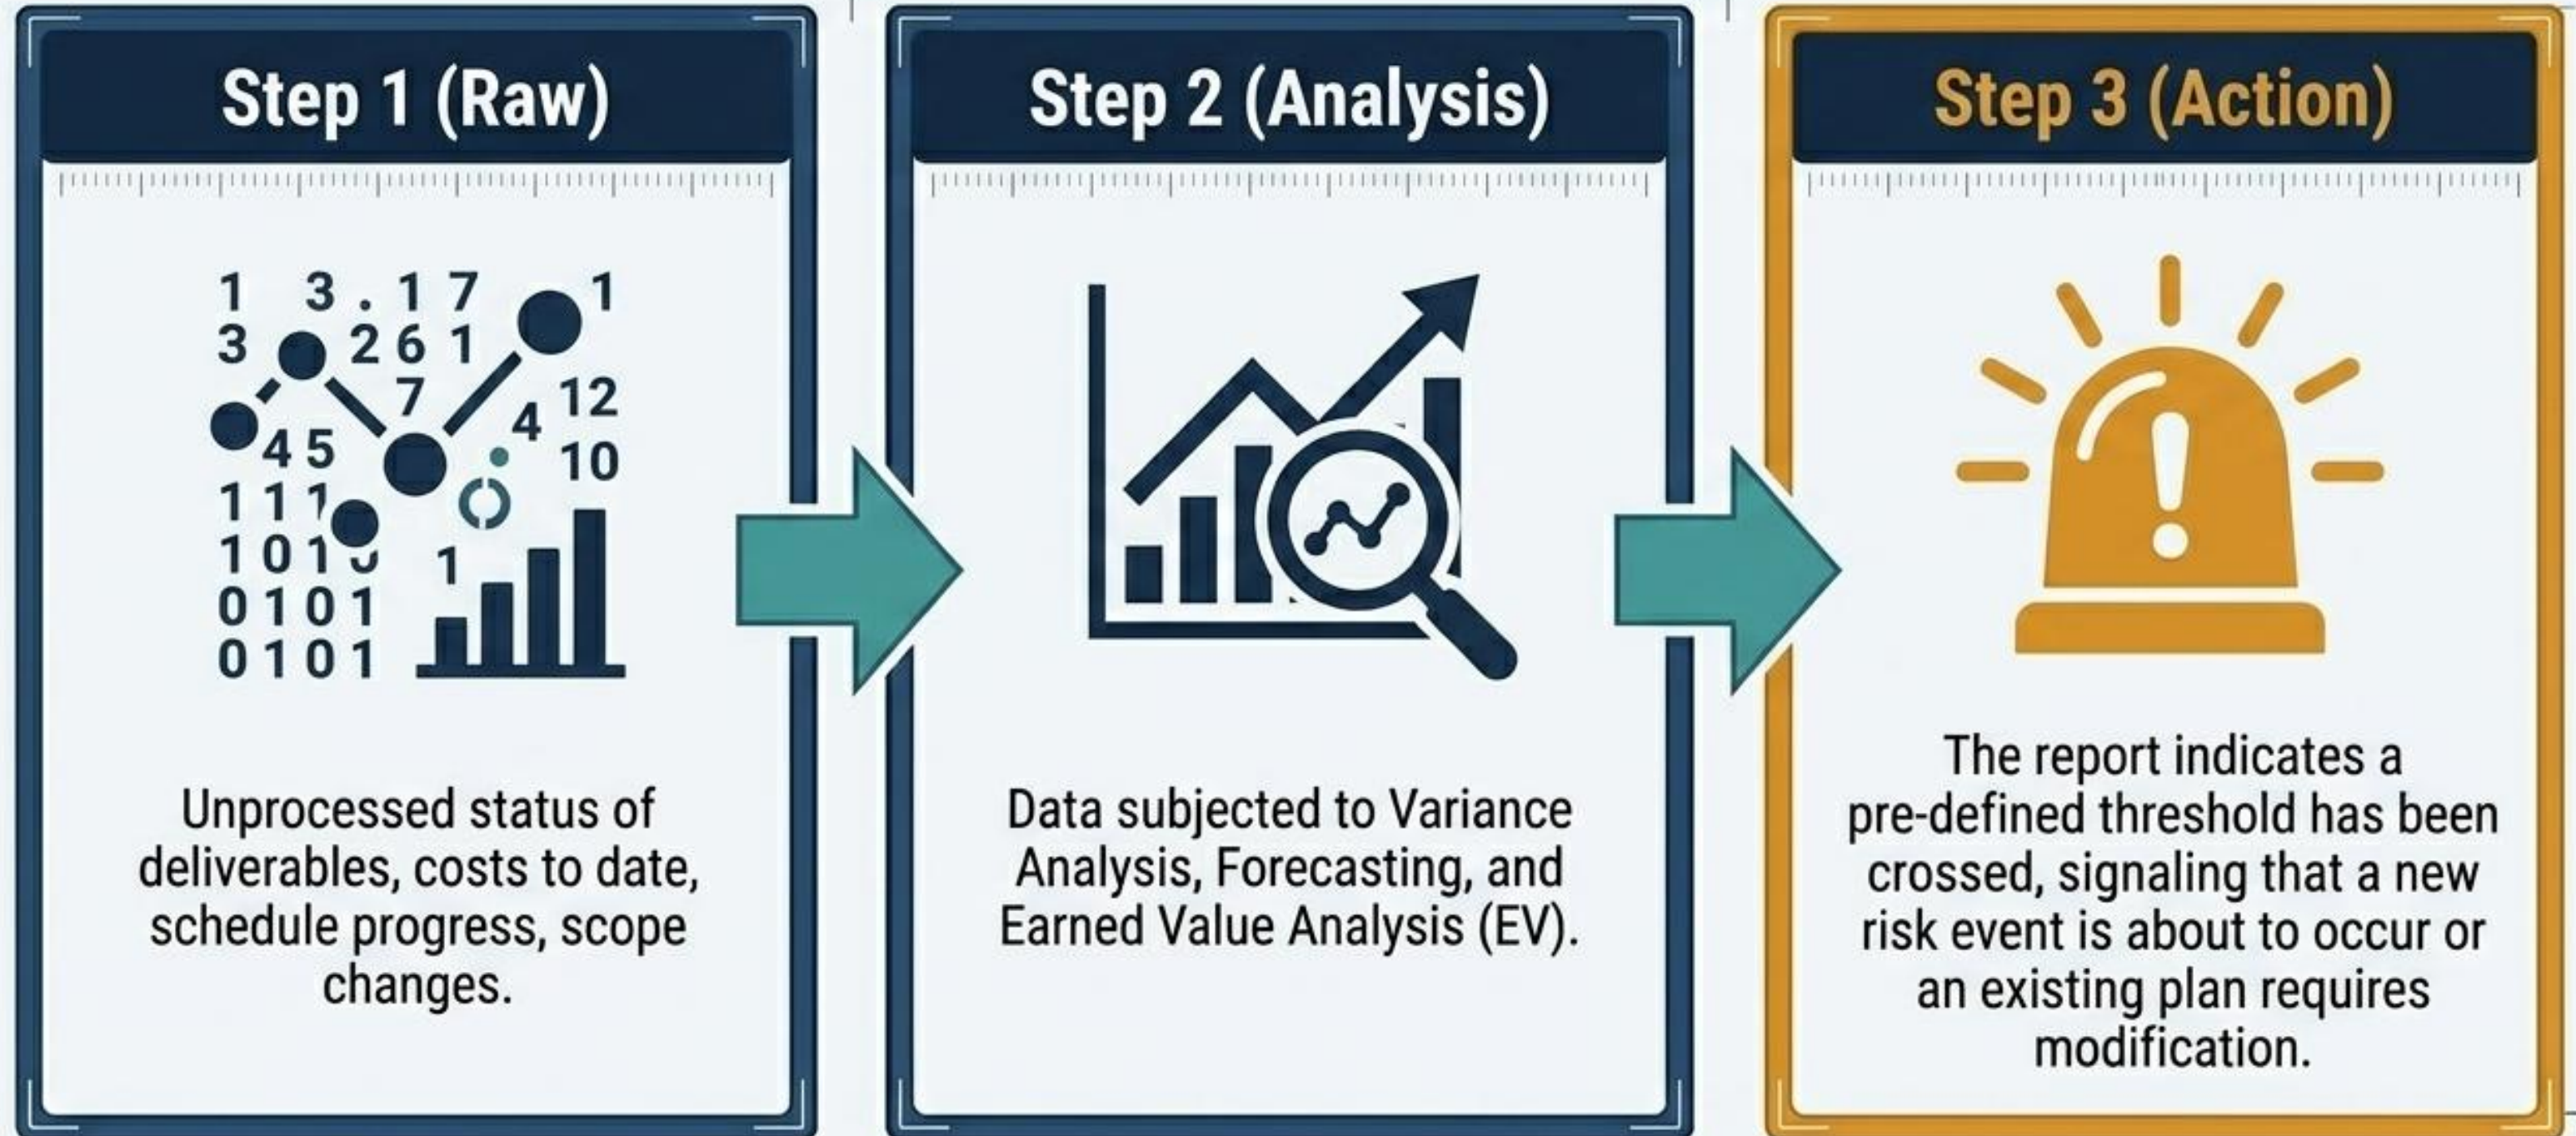


Diagnostic Matrix: Risk Audits vs. Risk Reassessments

Dimension	Risk Reassessment	Risk Audits
Primary Actor	Project Team	External Experts (Risk Auditors)
Focus	Specific risks, priorities, and viability (should the risk be closed?)	Overall process effectiveness, root causes, and response plan implementation
Timing	Periodic, scheduled reviews during status meetings	Carried out during the entire life of the project

If the risk is no longer viable, close it. If new risk consequences are discovered, revisit Qualitative and Quantitative Risk Analysis.

Measuring Technical Performance Deviations

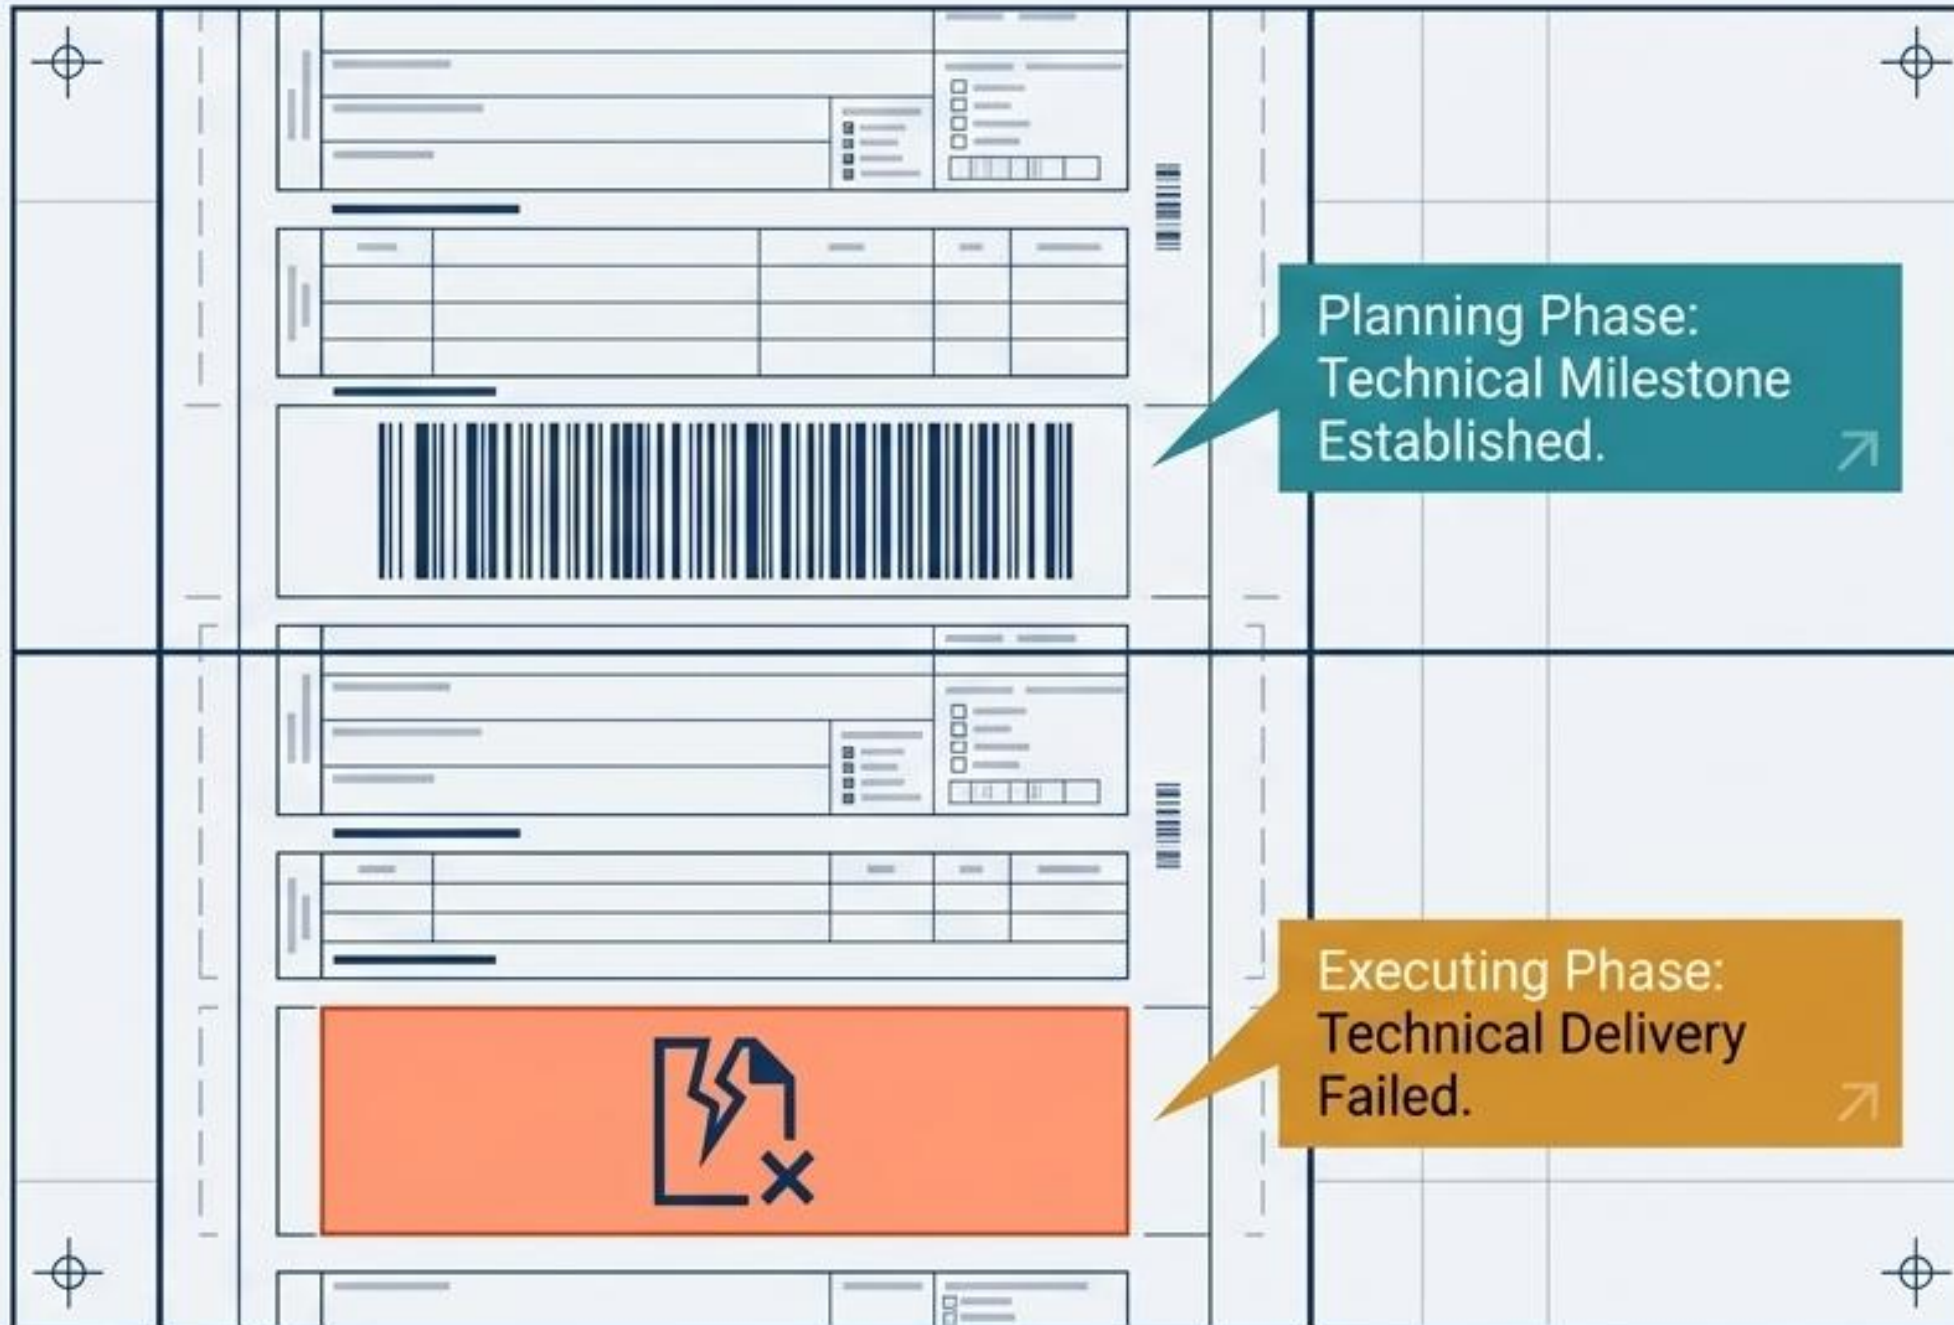

The Mechanism


Compares the technical accomplishments executed during the project to the technical milestones defined in the planning processes.

The Consequence



A technical deviation exists. This variance indicates a looming project risk—specifically, that the project scope is highly vulnerable. Reexamination of project risks is immediately required.

The Anatomy of a Risk-Driven Change Request

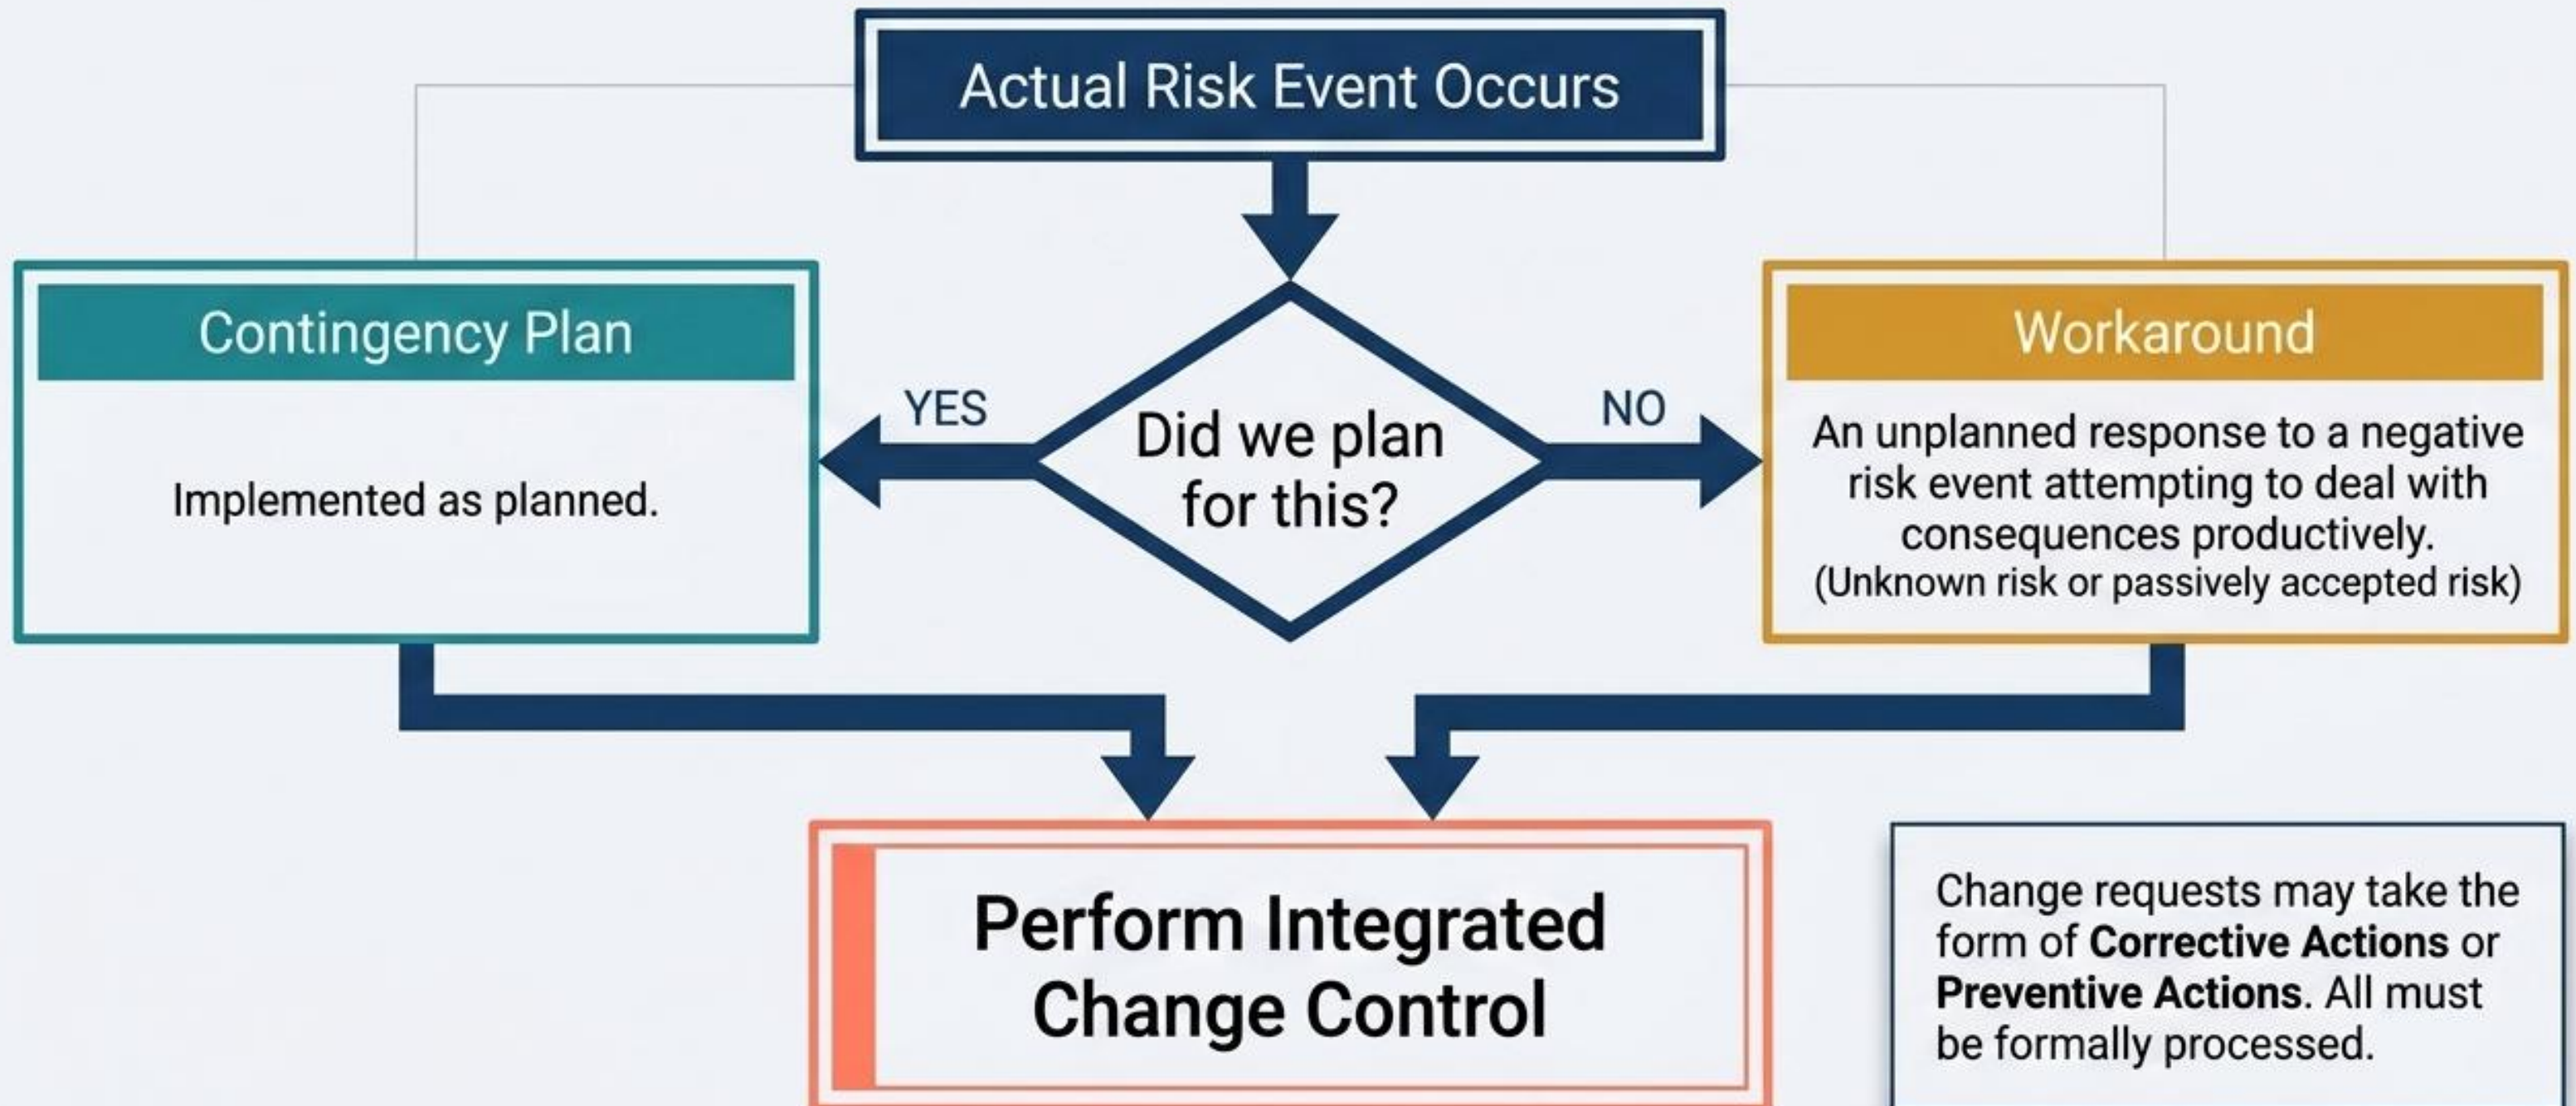

Managing Cost Changes and Baseline Integrity

Prevent Unauthorized Costs


Monitor the project budget strictly to prevent incorrect or unapproved costs from entering the cost baseline.

Manage Overruns


Ensure the budget does not exceed acceptable limits by taking definitive action when cost overruns become imminent.

Communicate Variance


Inform stakeholders of all approved budget changes, which must be submitted as change requests through Integrated Change Control.

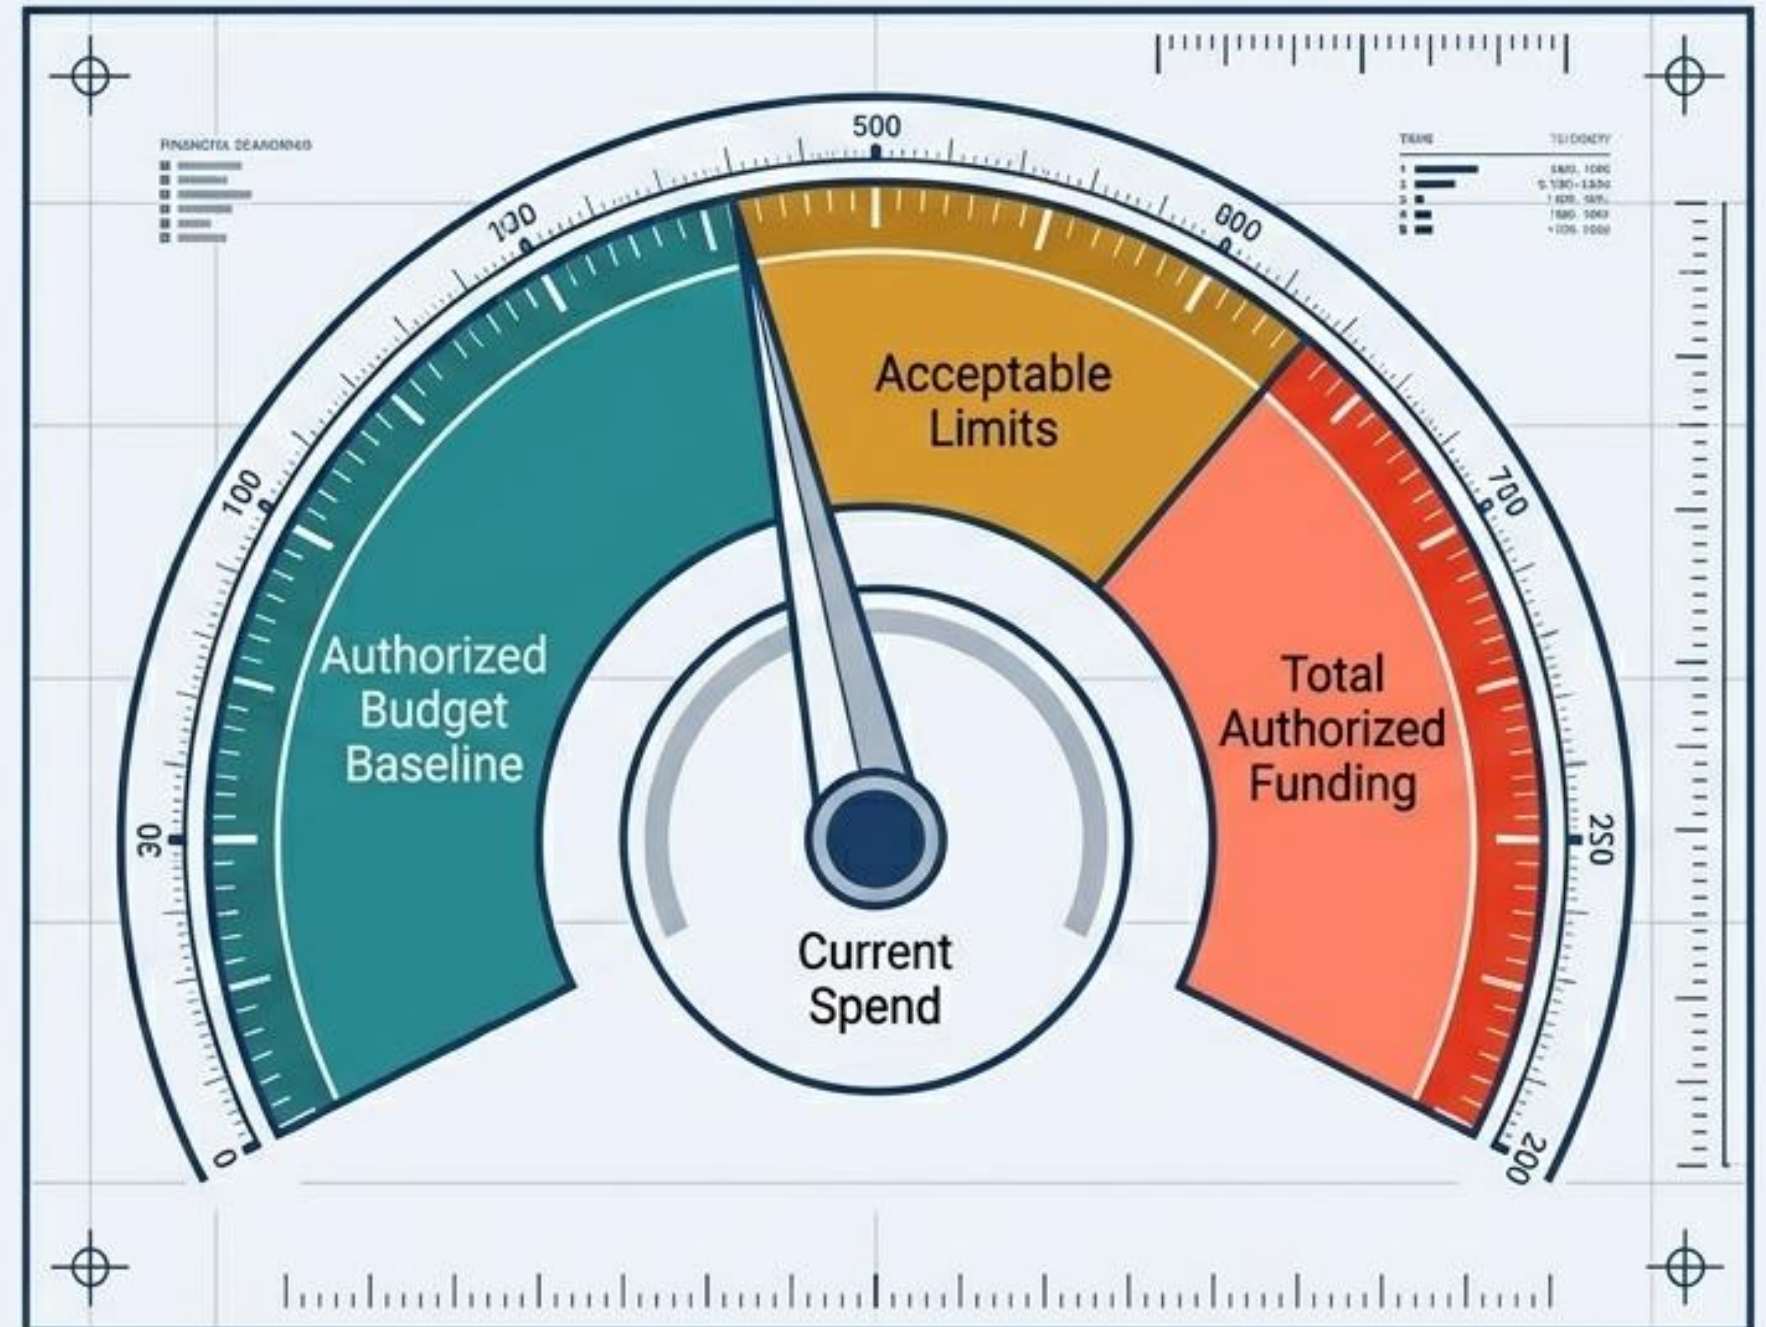

The Foundational Inputs for Cost Control

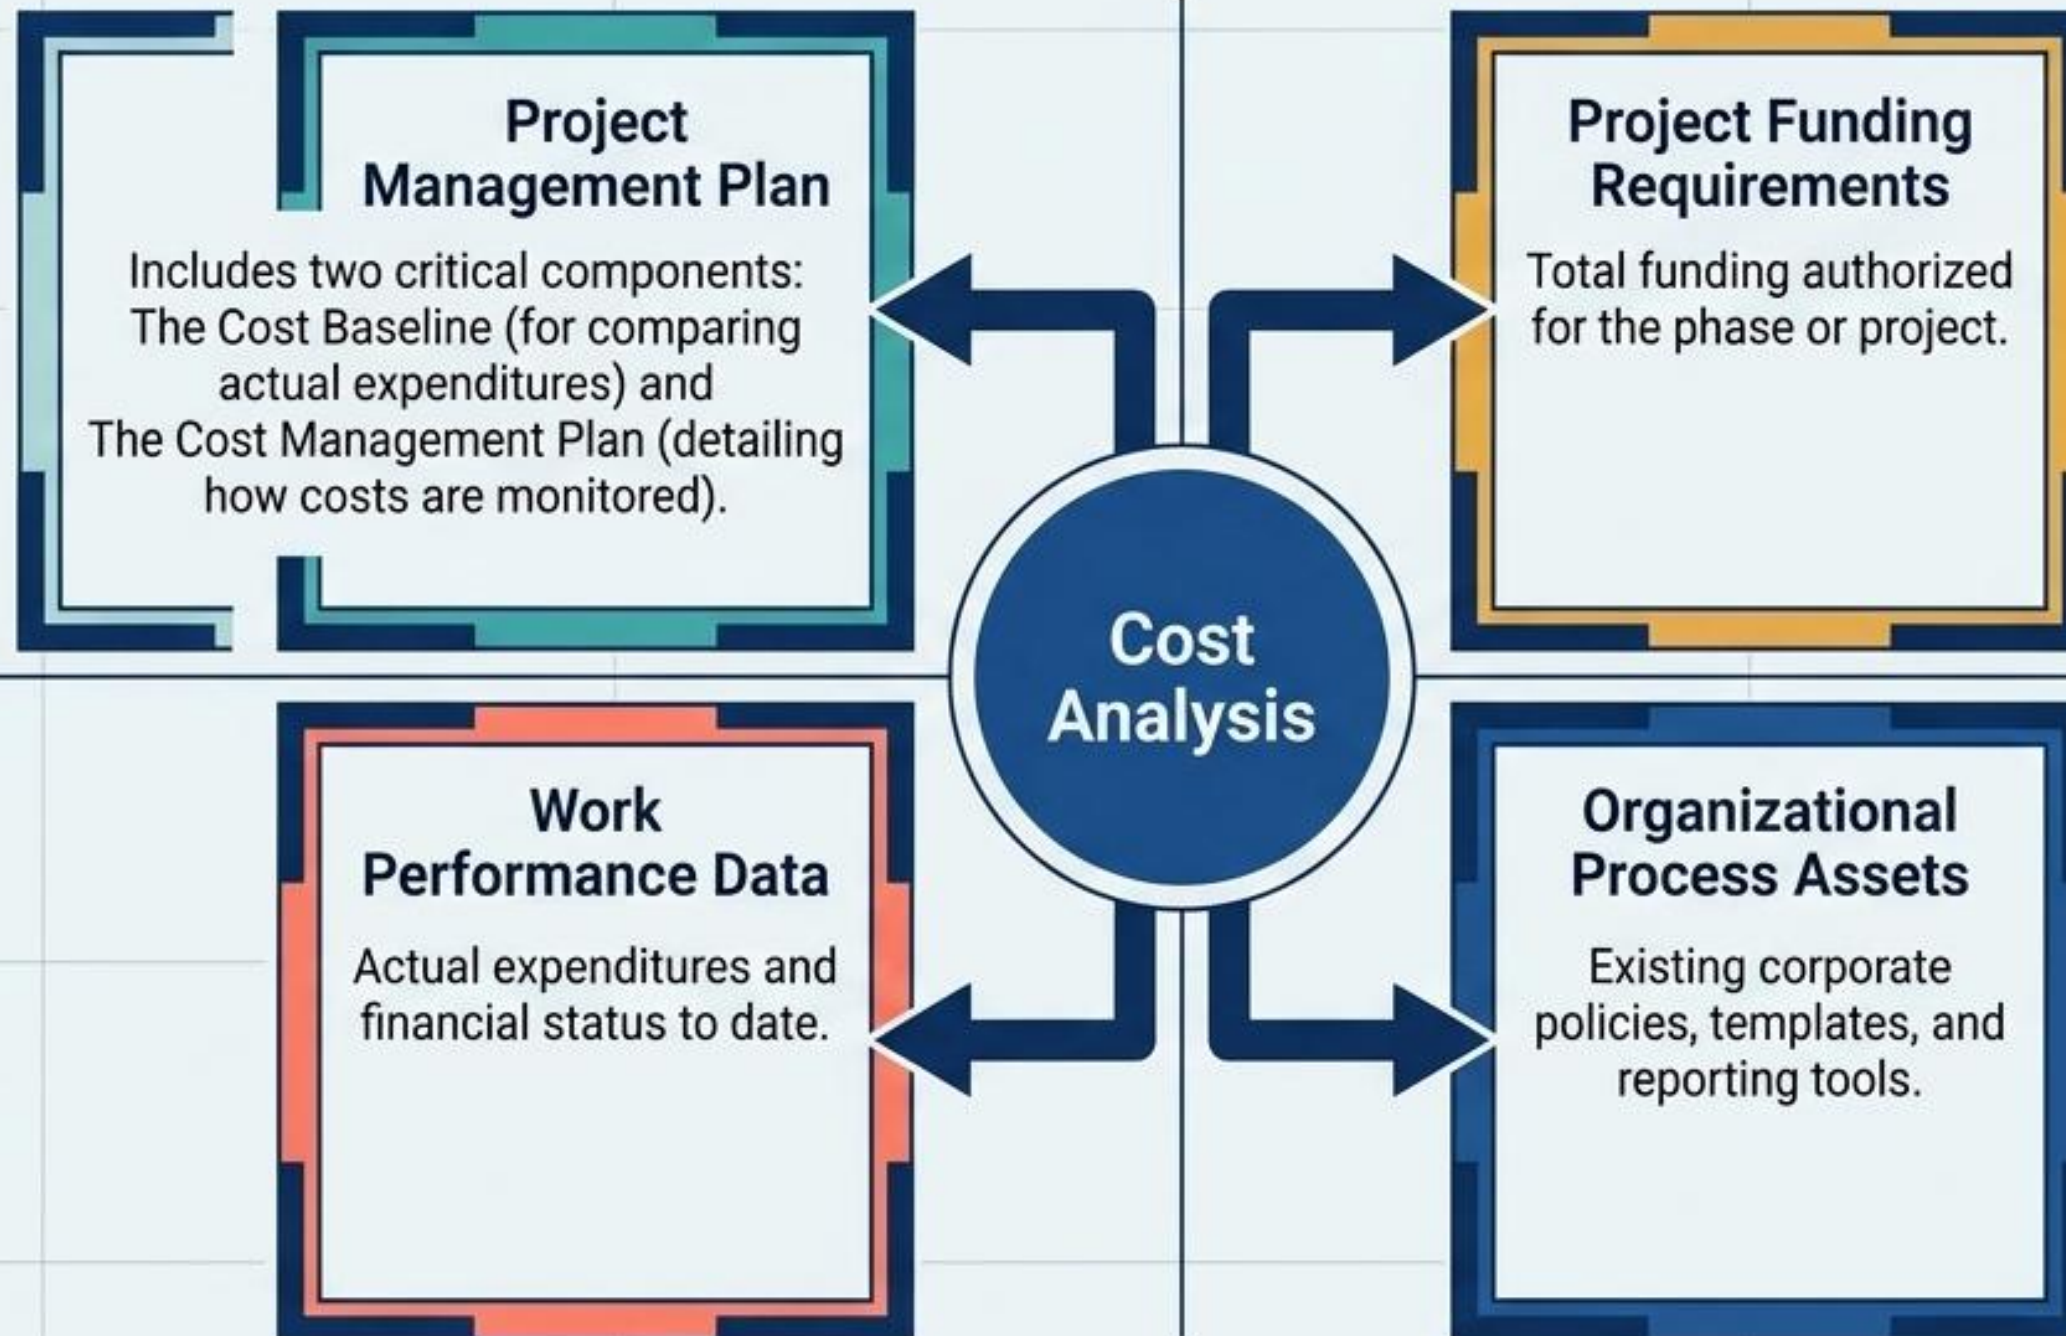

Synthesis: The Universal Control Loop

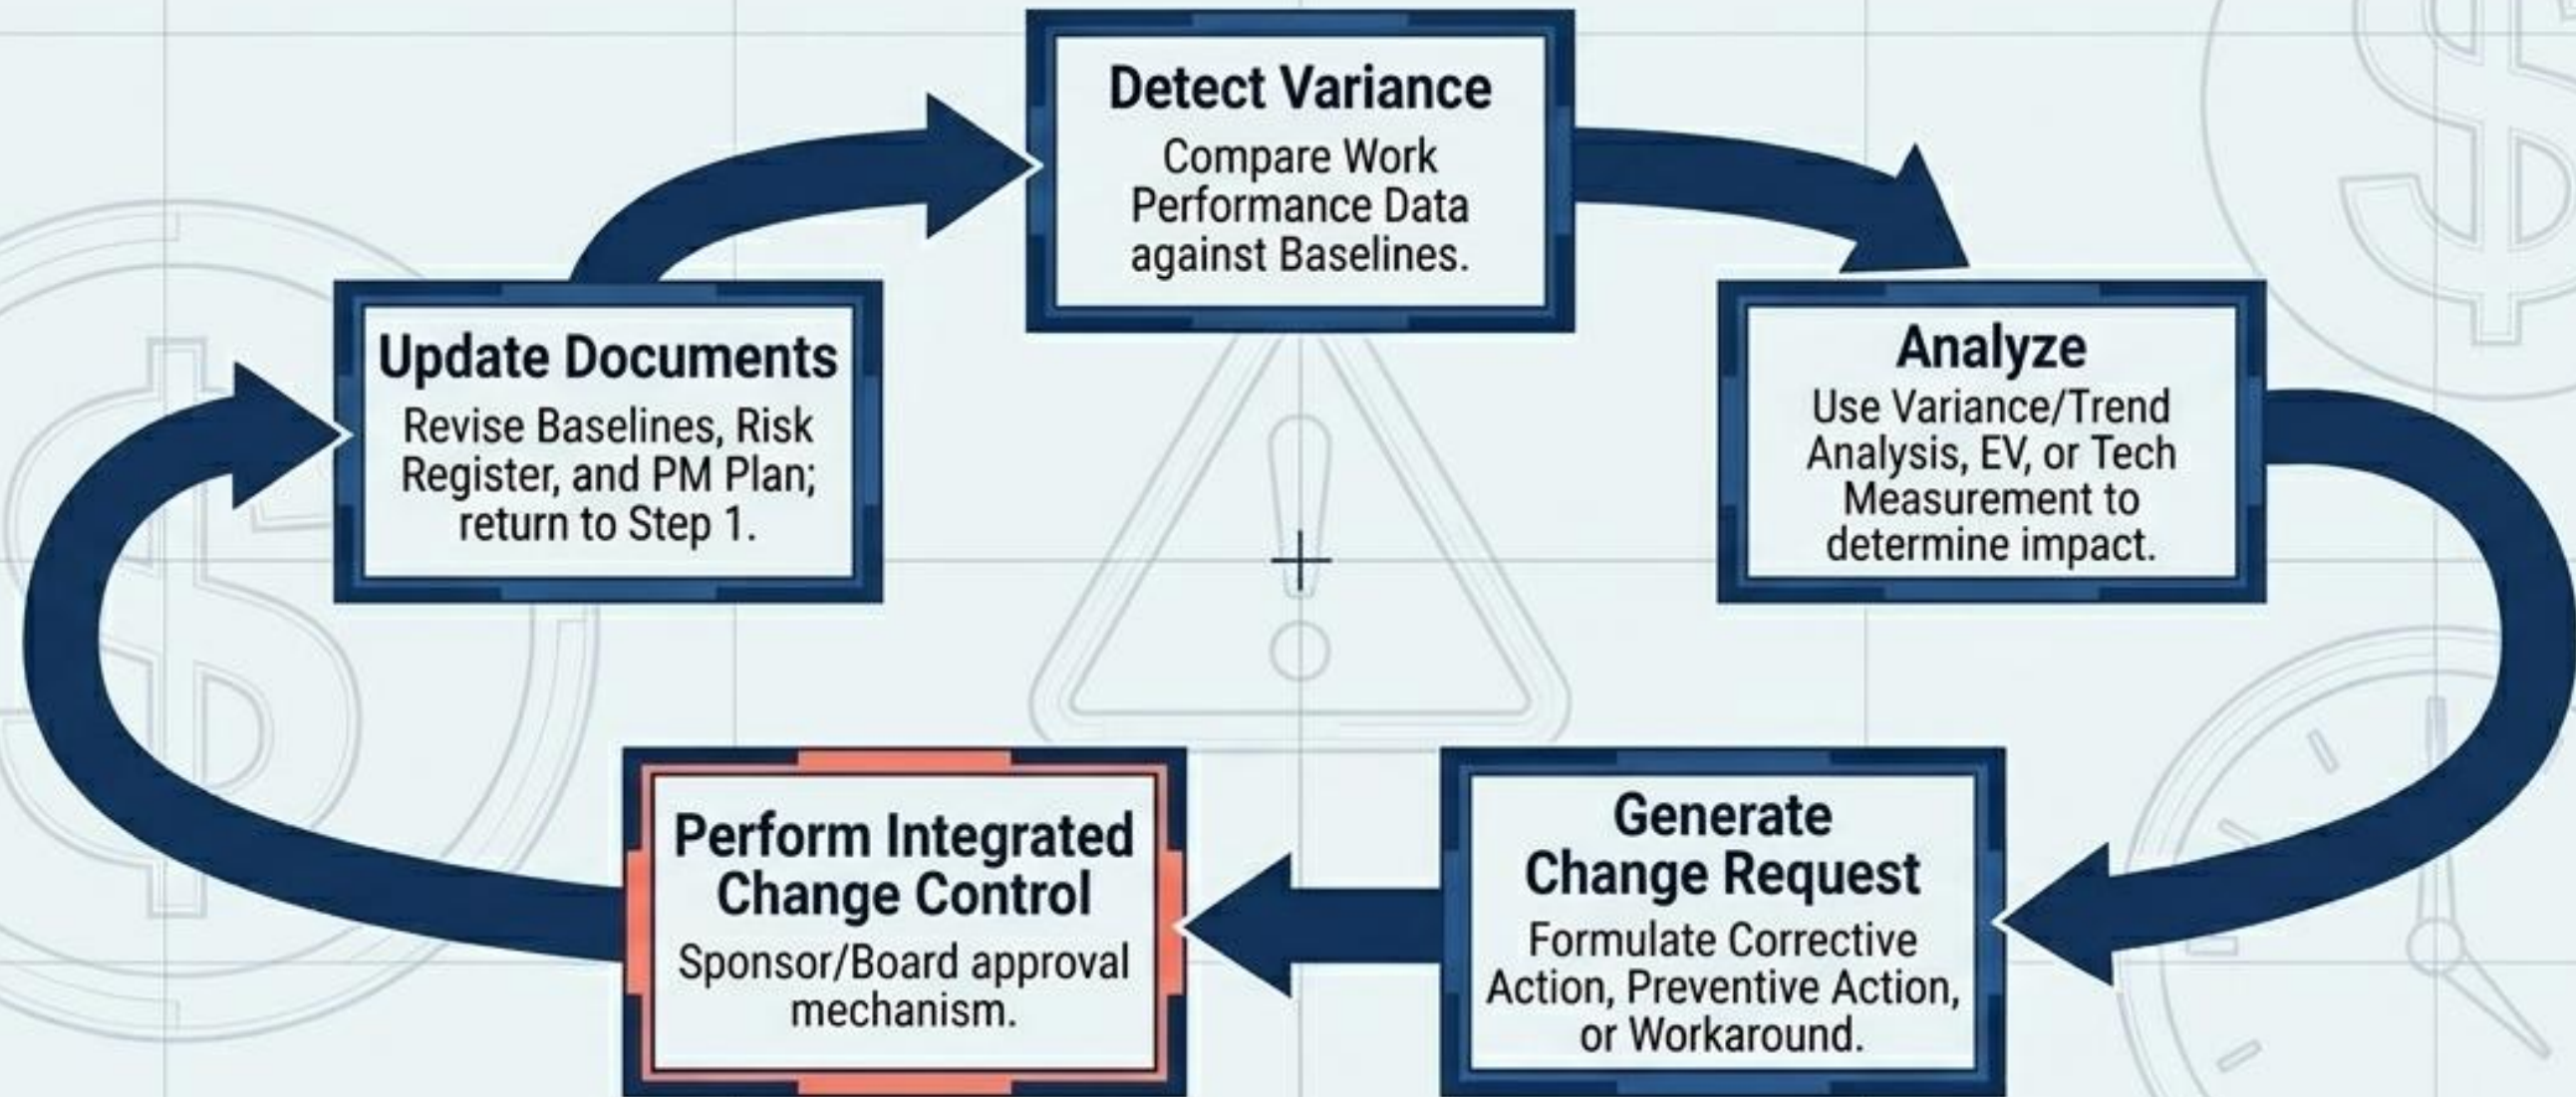

Whether reacting to a triggered risk, a schedule delay, or a cost overrun, the resolution mechanism remains identical. Project Control is a single, integrated ecosystem.
