

GRID UNIT: 10MM

PROJECTION: ORTHOGRAPHIC

Certyfikat PMP: Project Scope Control

dr Zbigniew Galar




GRID UNIT: 10MM

GRID UNIT: 10MM :3EAY7

Premium Executive Diagnostic Report

Macro-level node map: process groups

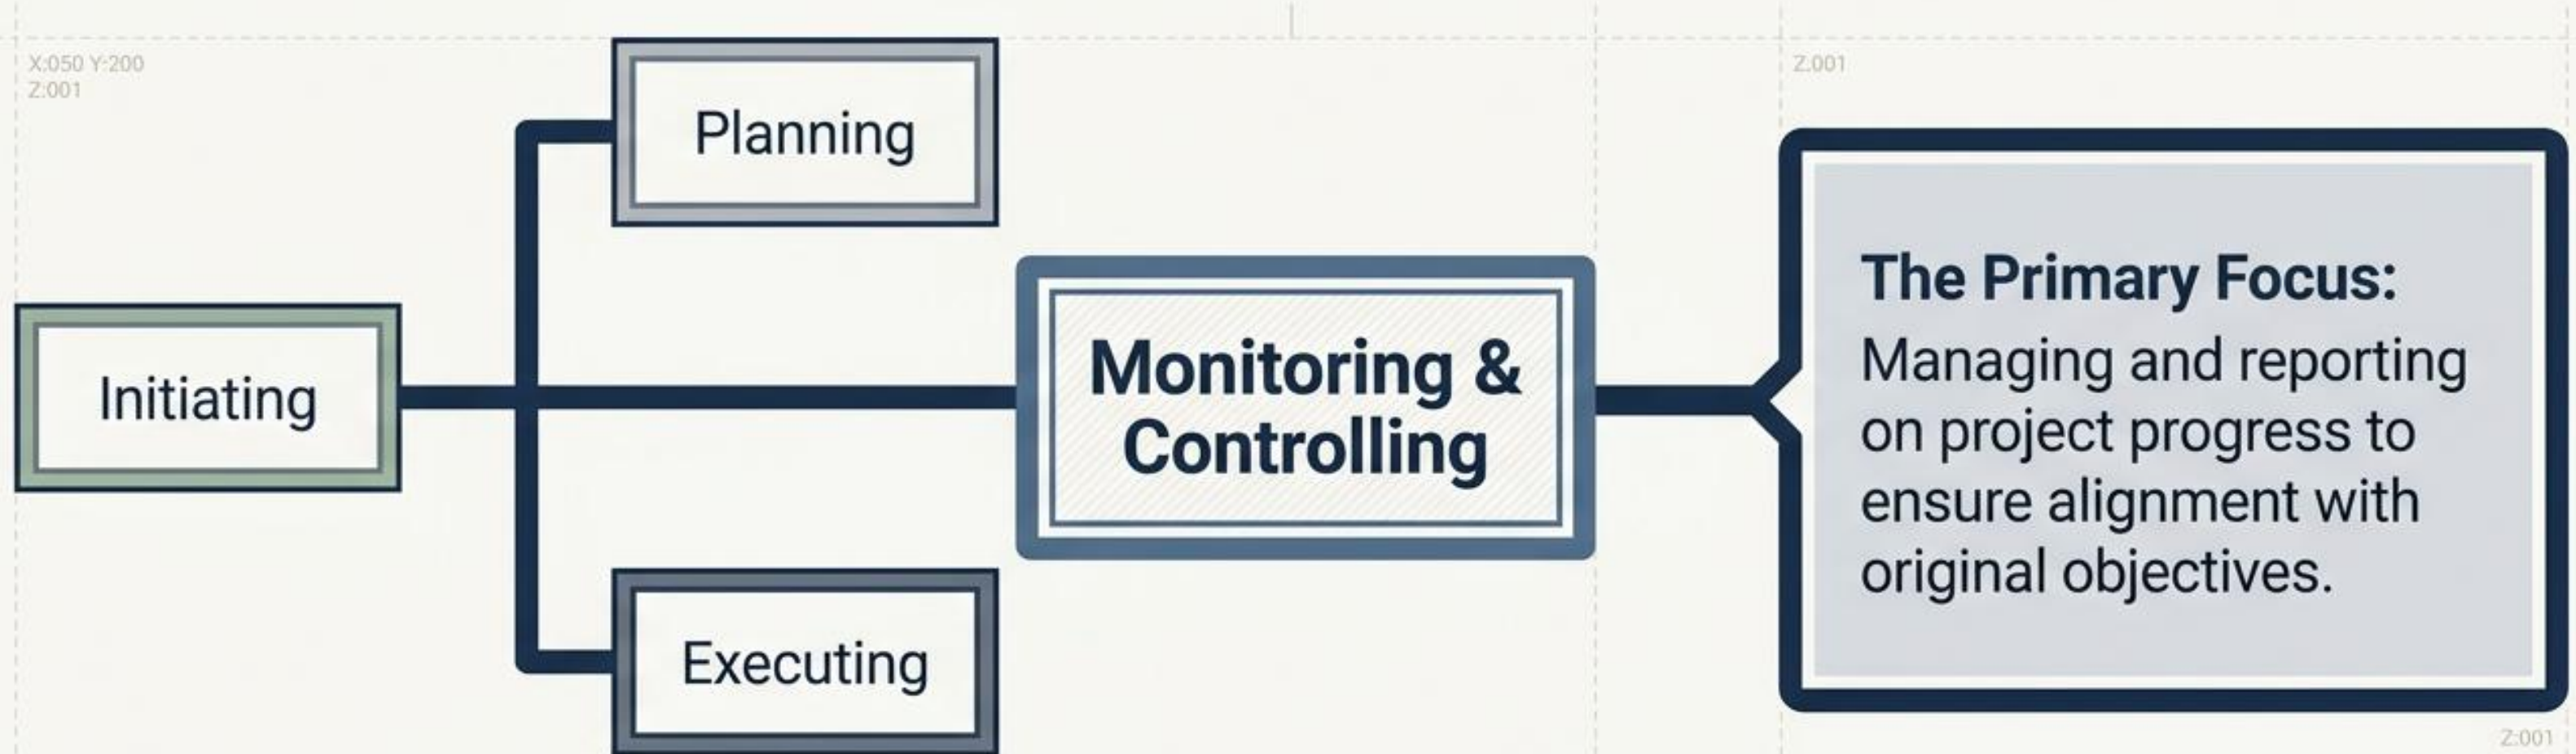

Key Insight:

Failure to monitor results in rework. Rework causes schedule delays, budget overruns, and morale collapse. Control processes keep rework to an absolute minimum.

Premium Executive Diagnostic Report

Architectural Blueprint: Deliverable Verification & Acceptance Flow




Control Quality ensures the work is correct.
Validate Scope ensures the customer accepts it.


PMP Exam Spotlight

	 Control Quality	 Validate Scope
Primary Objective	Checking for correct work results & quality standards.	Formalizing acceptance of the project scope.
Key Action	Inspecting for accuracy.	Accepting work results.
Primary Output	Verified Deliverables.	Accepted Deliverables.
Primary Actor	Project Team / Quality Assurance.	Stakeholders (Customers, Sponsor).

Validating Project Scope

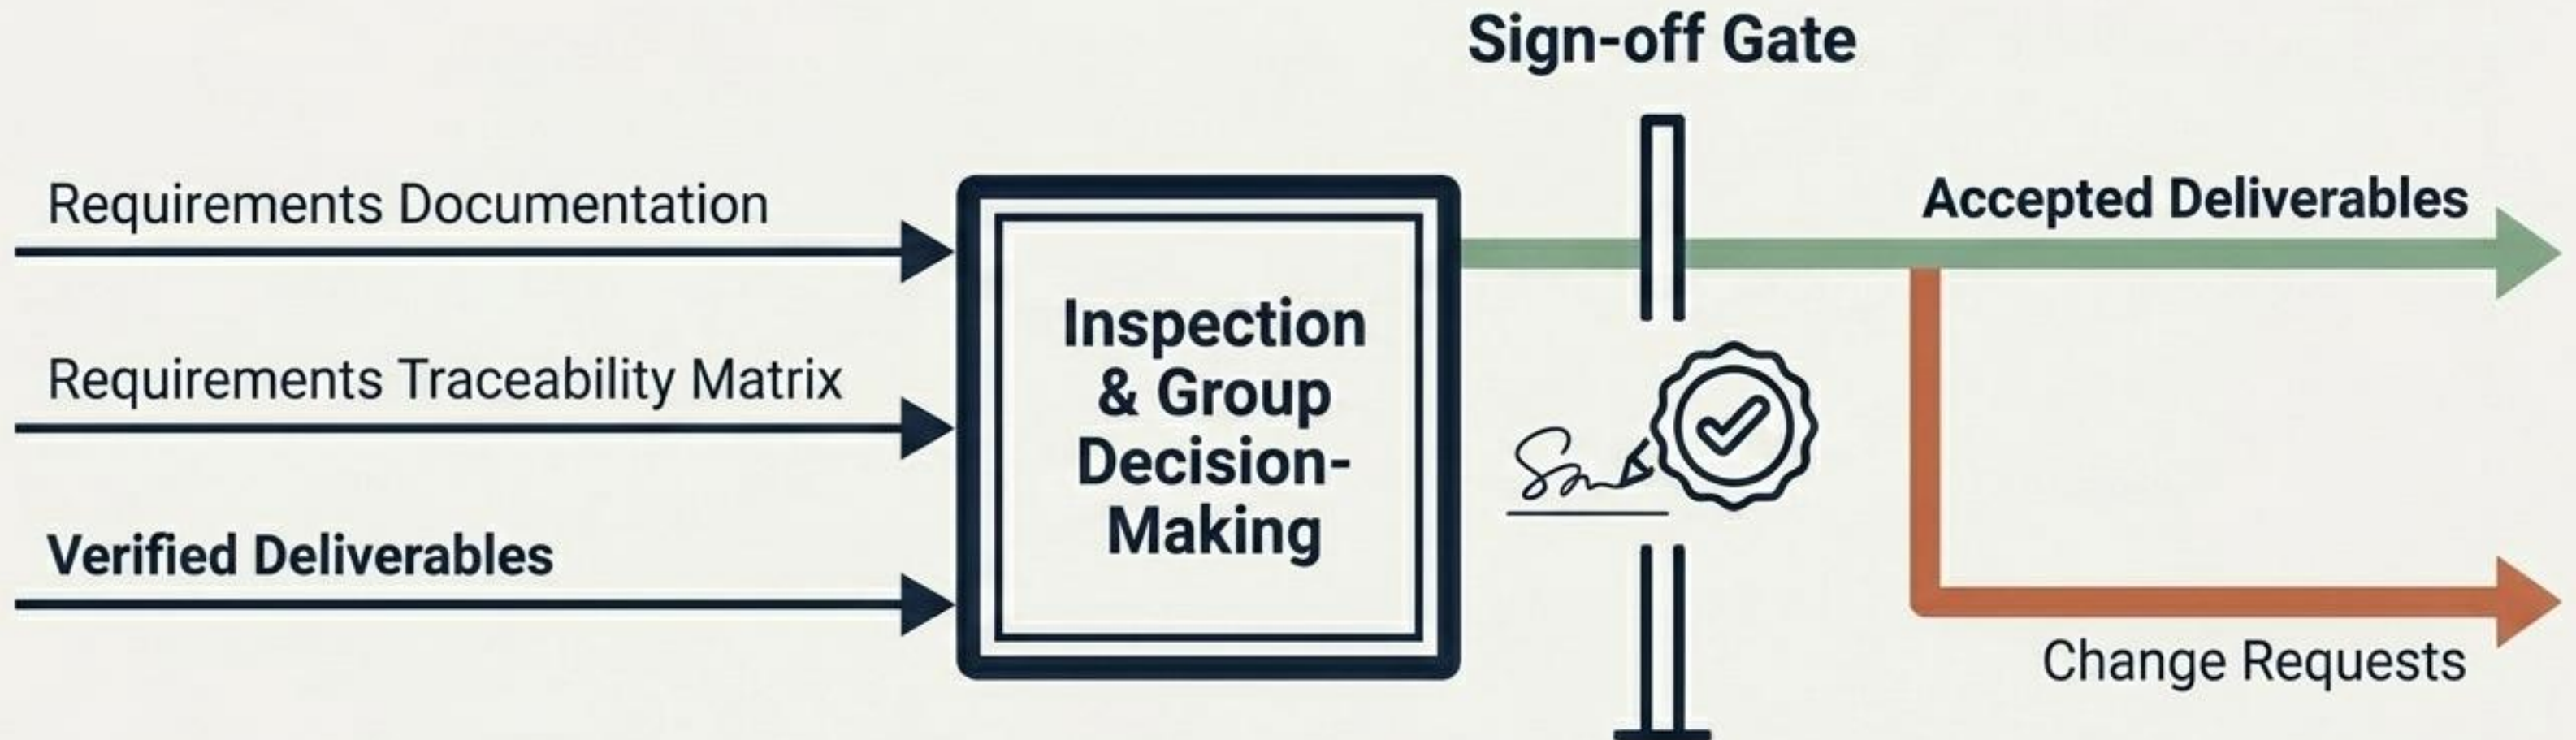

Even if a project is canceled, Validate Scope must be performed to document the degree of completion for historical records.

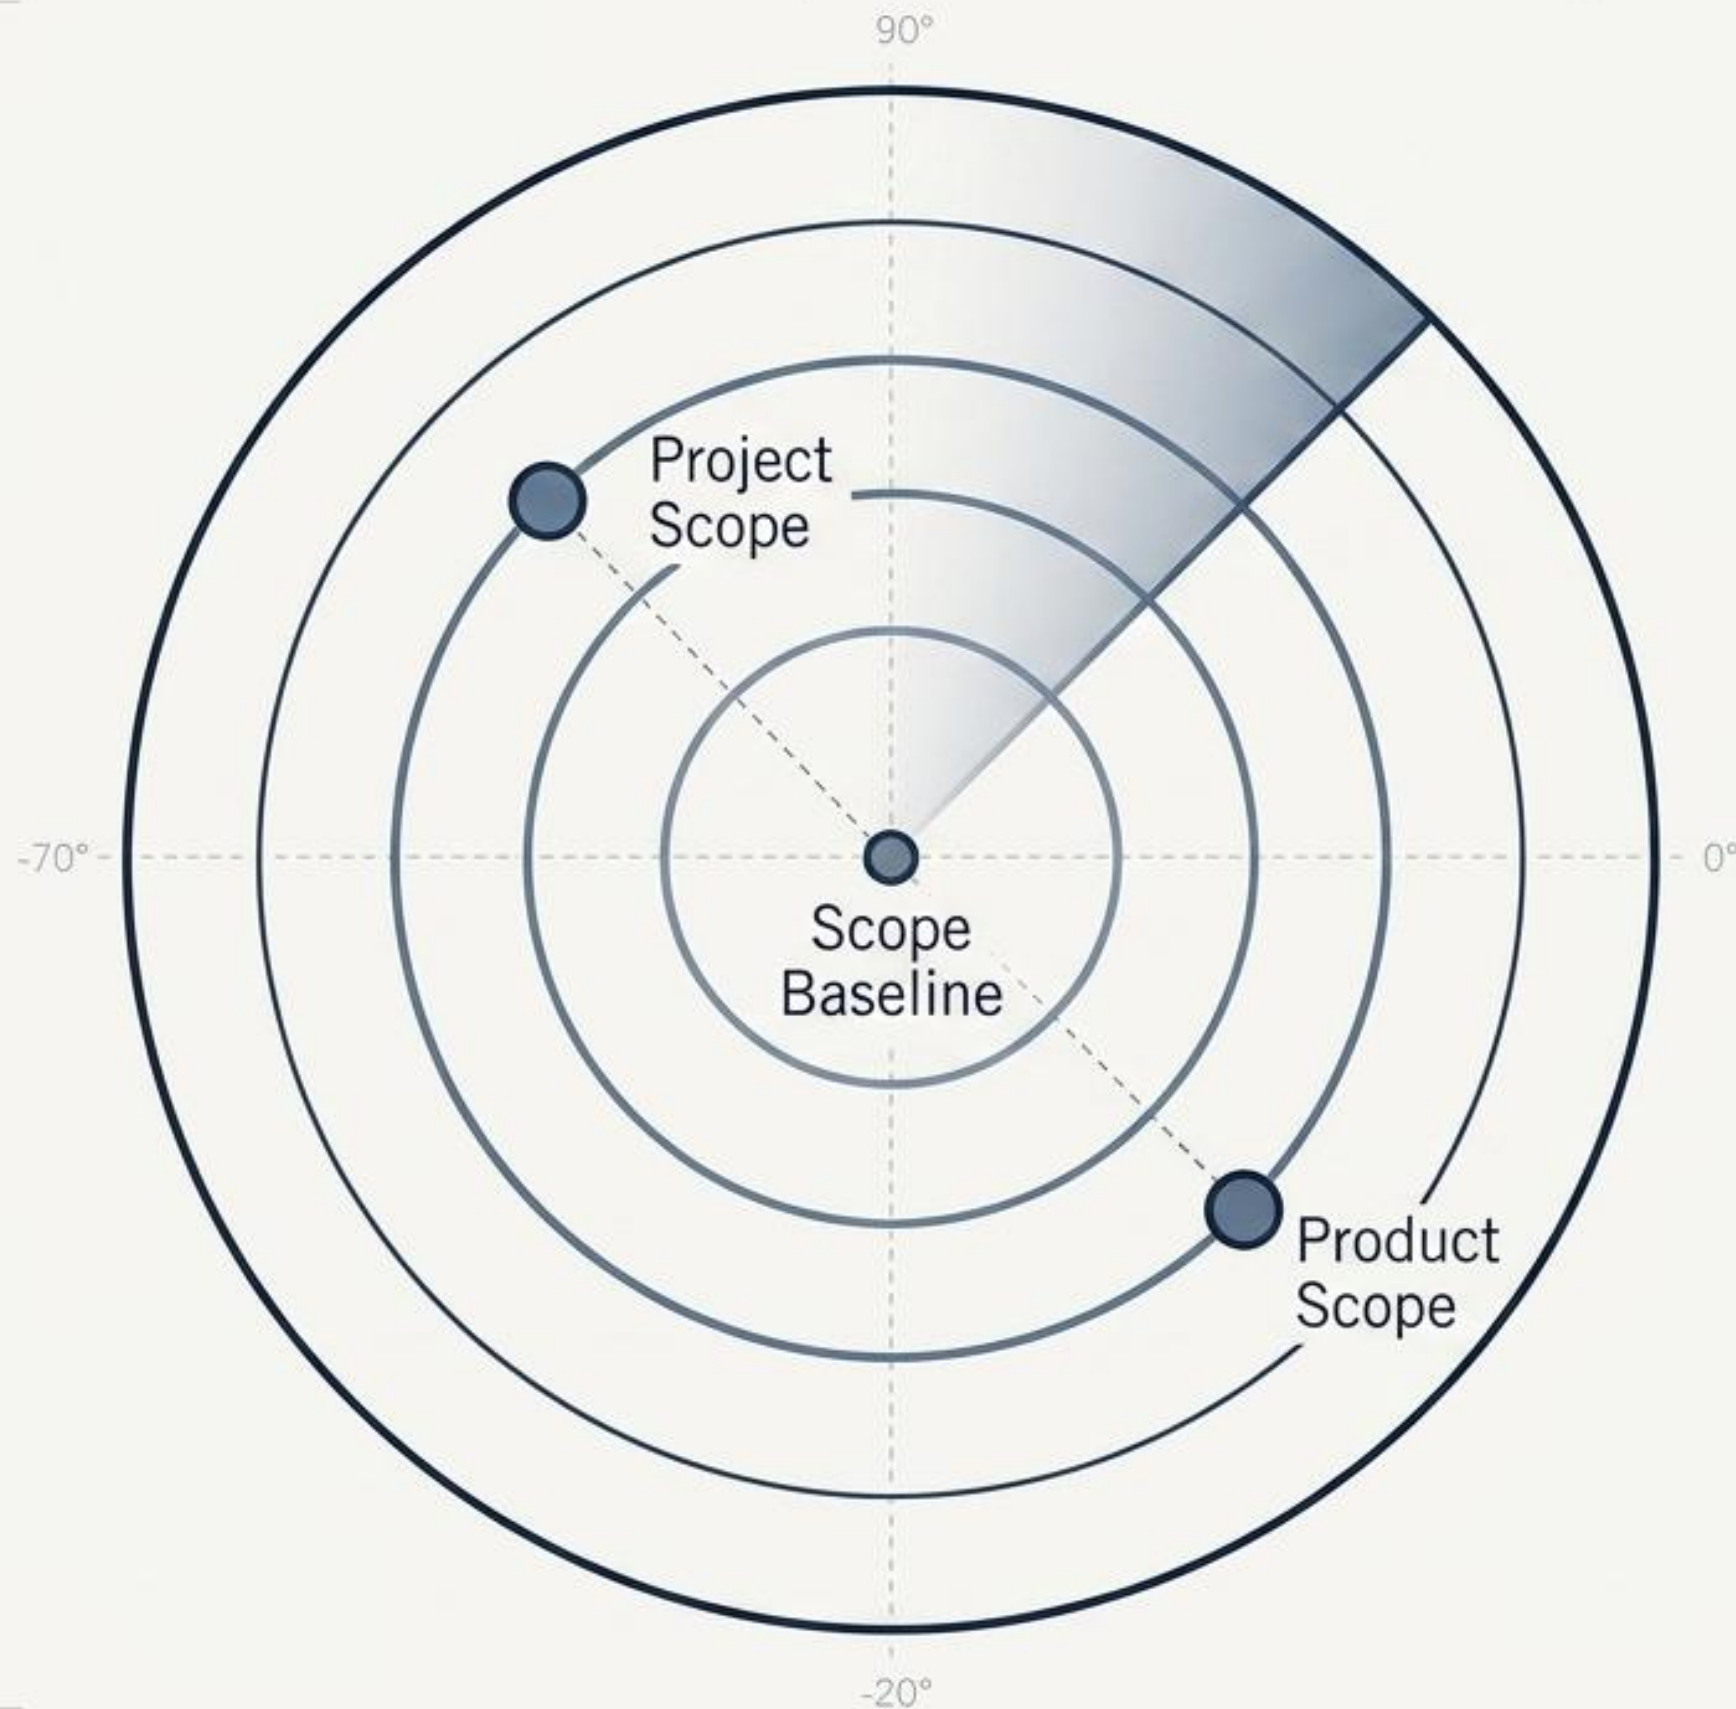


Introduction to Controlling Scope

Core Mandate


- Monitor status of project and product scope.
- Monitor and manage changes to the Scope Baseline.

Interaction Note

Changes in product scope inevitably require changes to the project scope. All modifications must be processed through Integrated Change Control.




The Engine of Scope Control: Variance Analysis

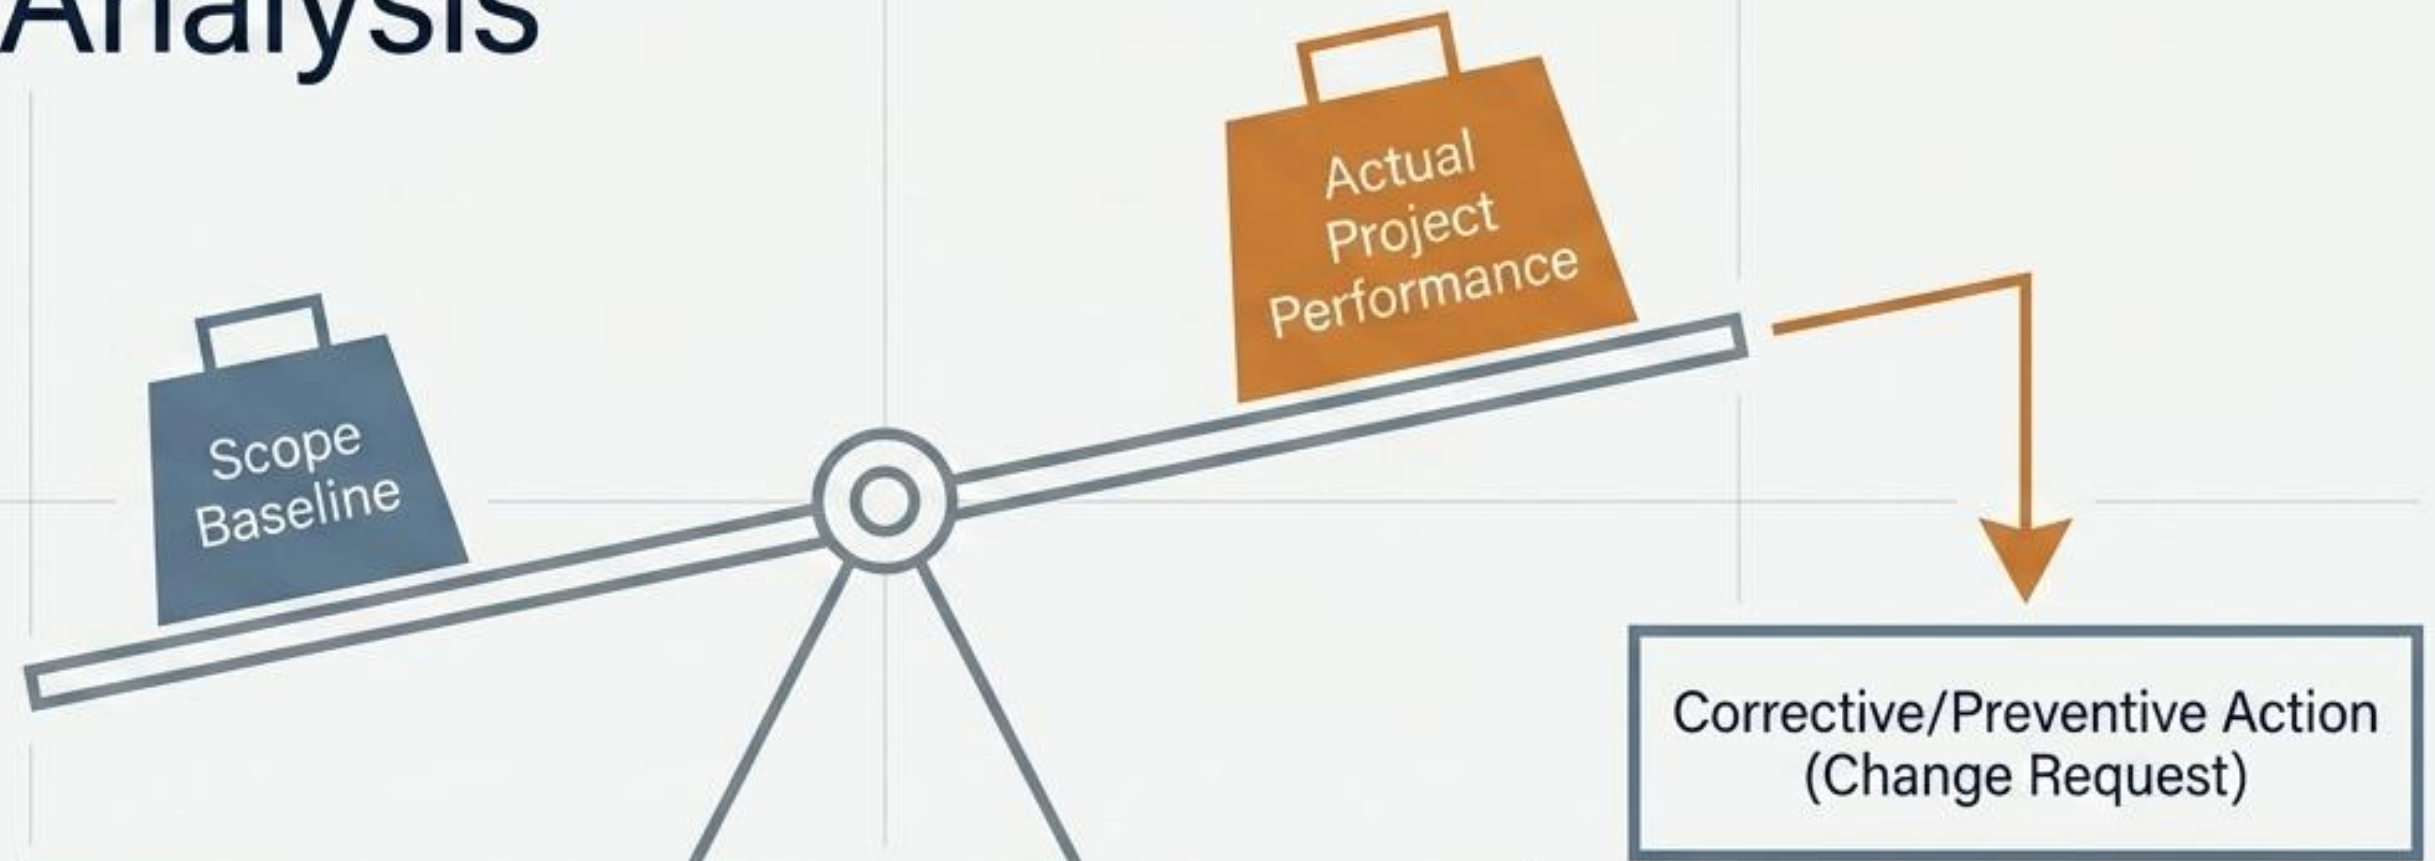


Variance Analysis is the sole tool of Control Scope. It determines the cause and degree of variance relative to the baseline to decide if corrective action is required.

Anatomy of a Scope Change

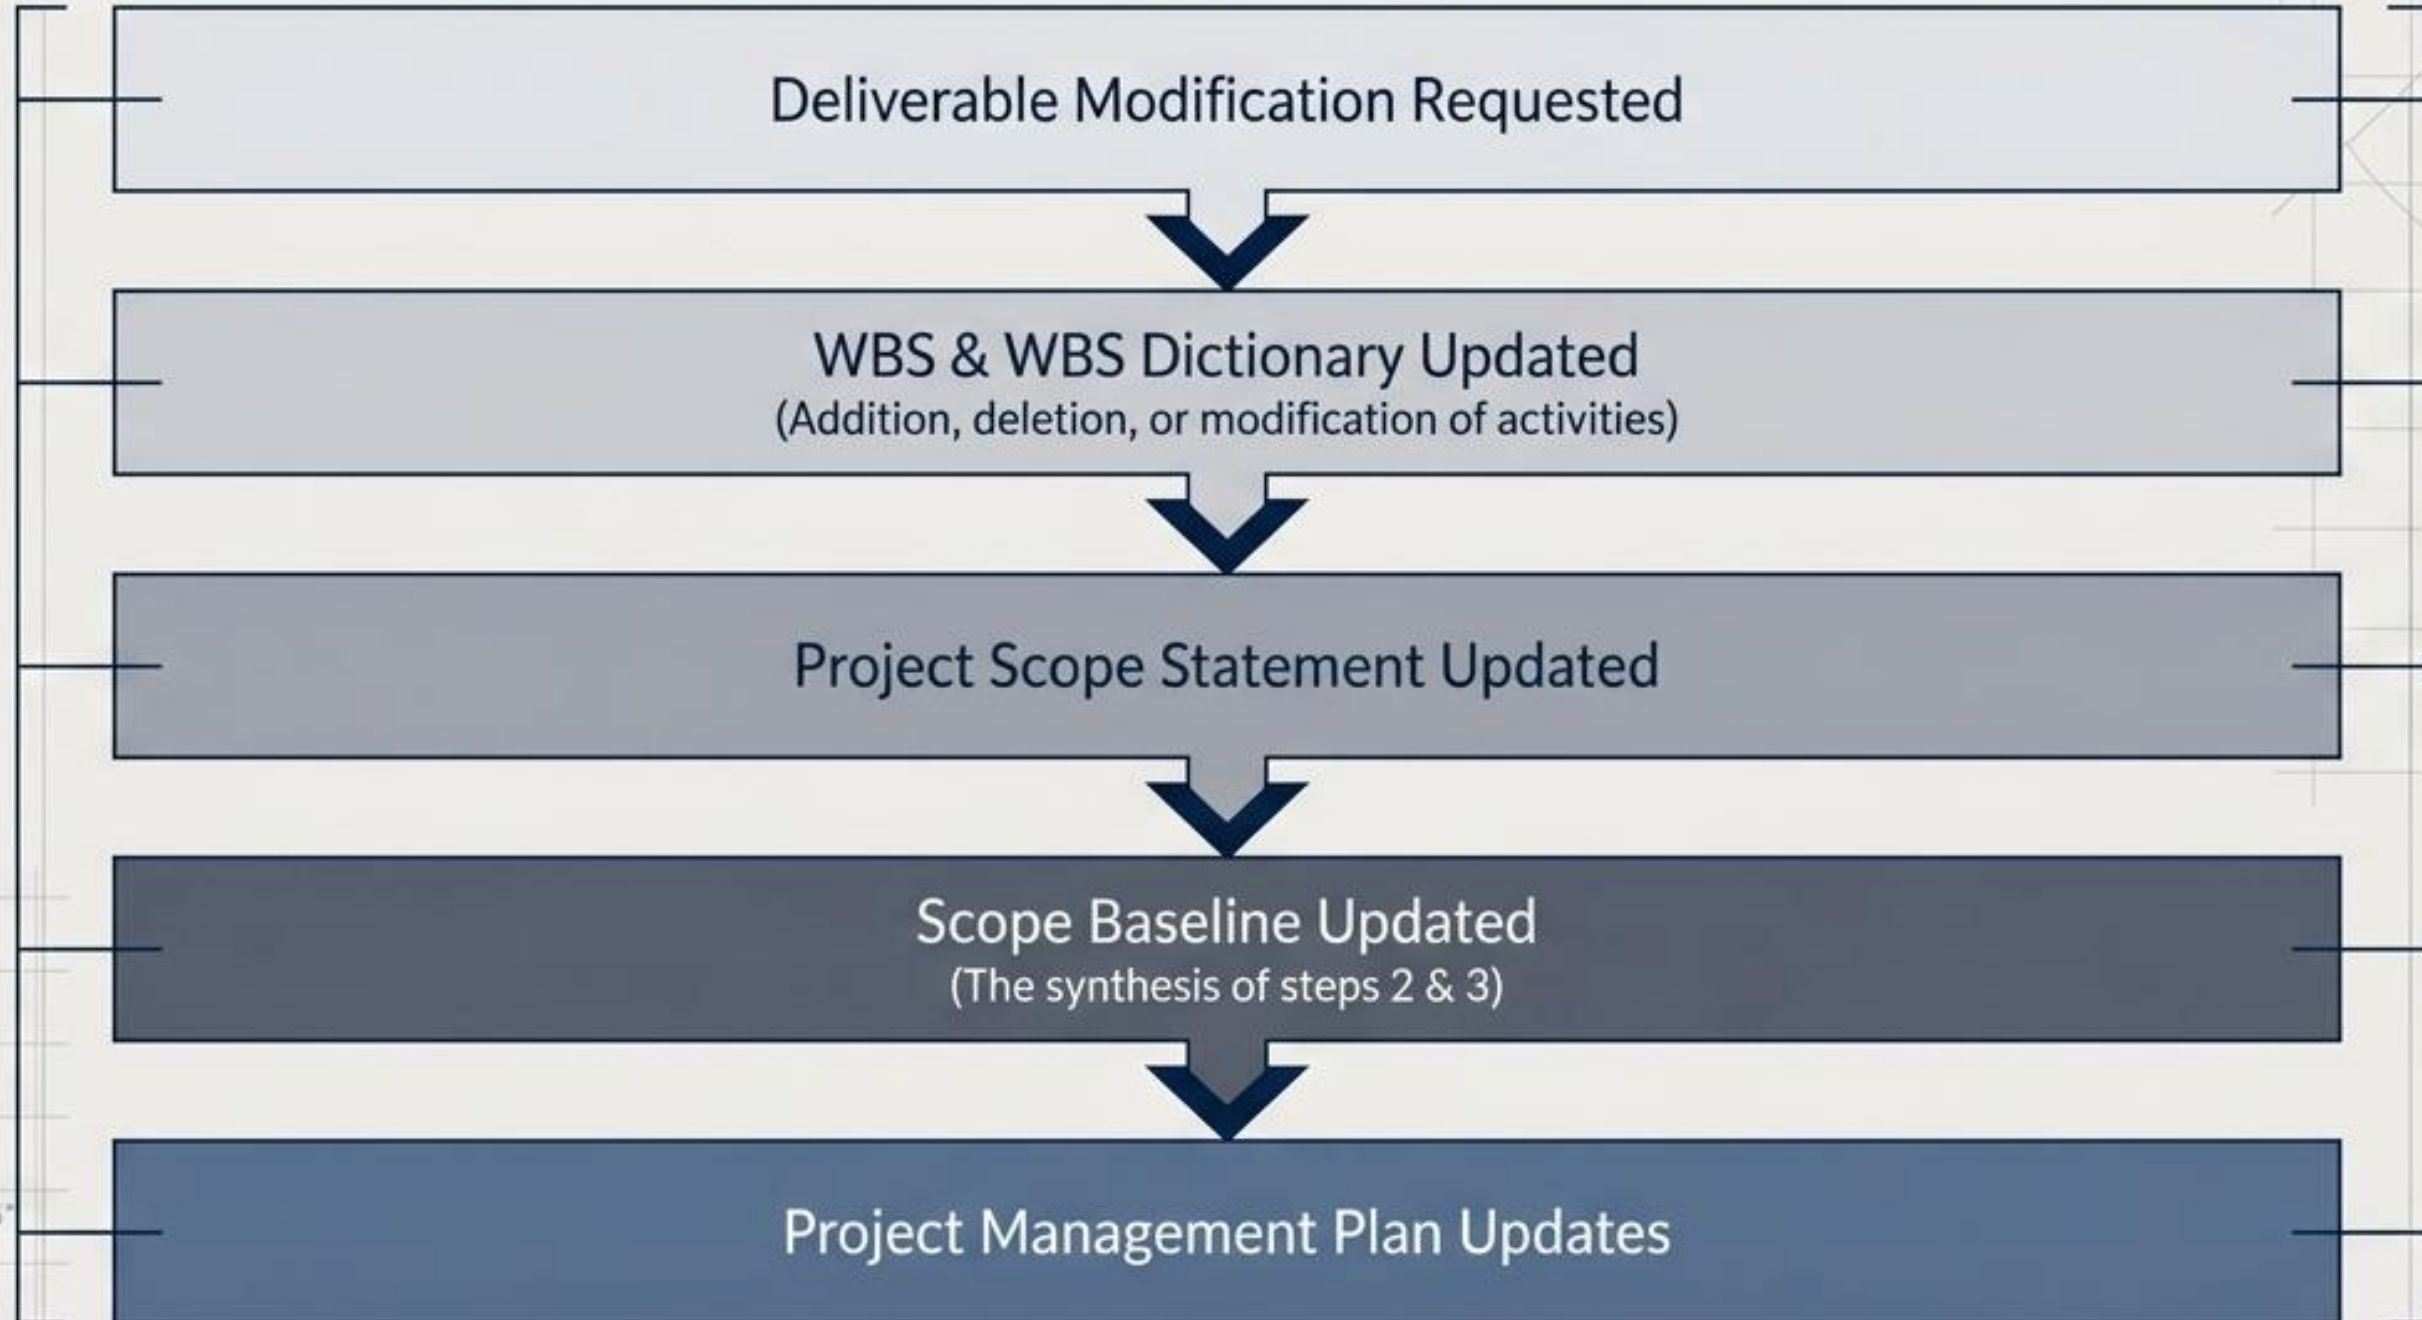

The Ripple Effect on Cost and Schedule

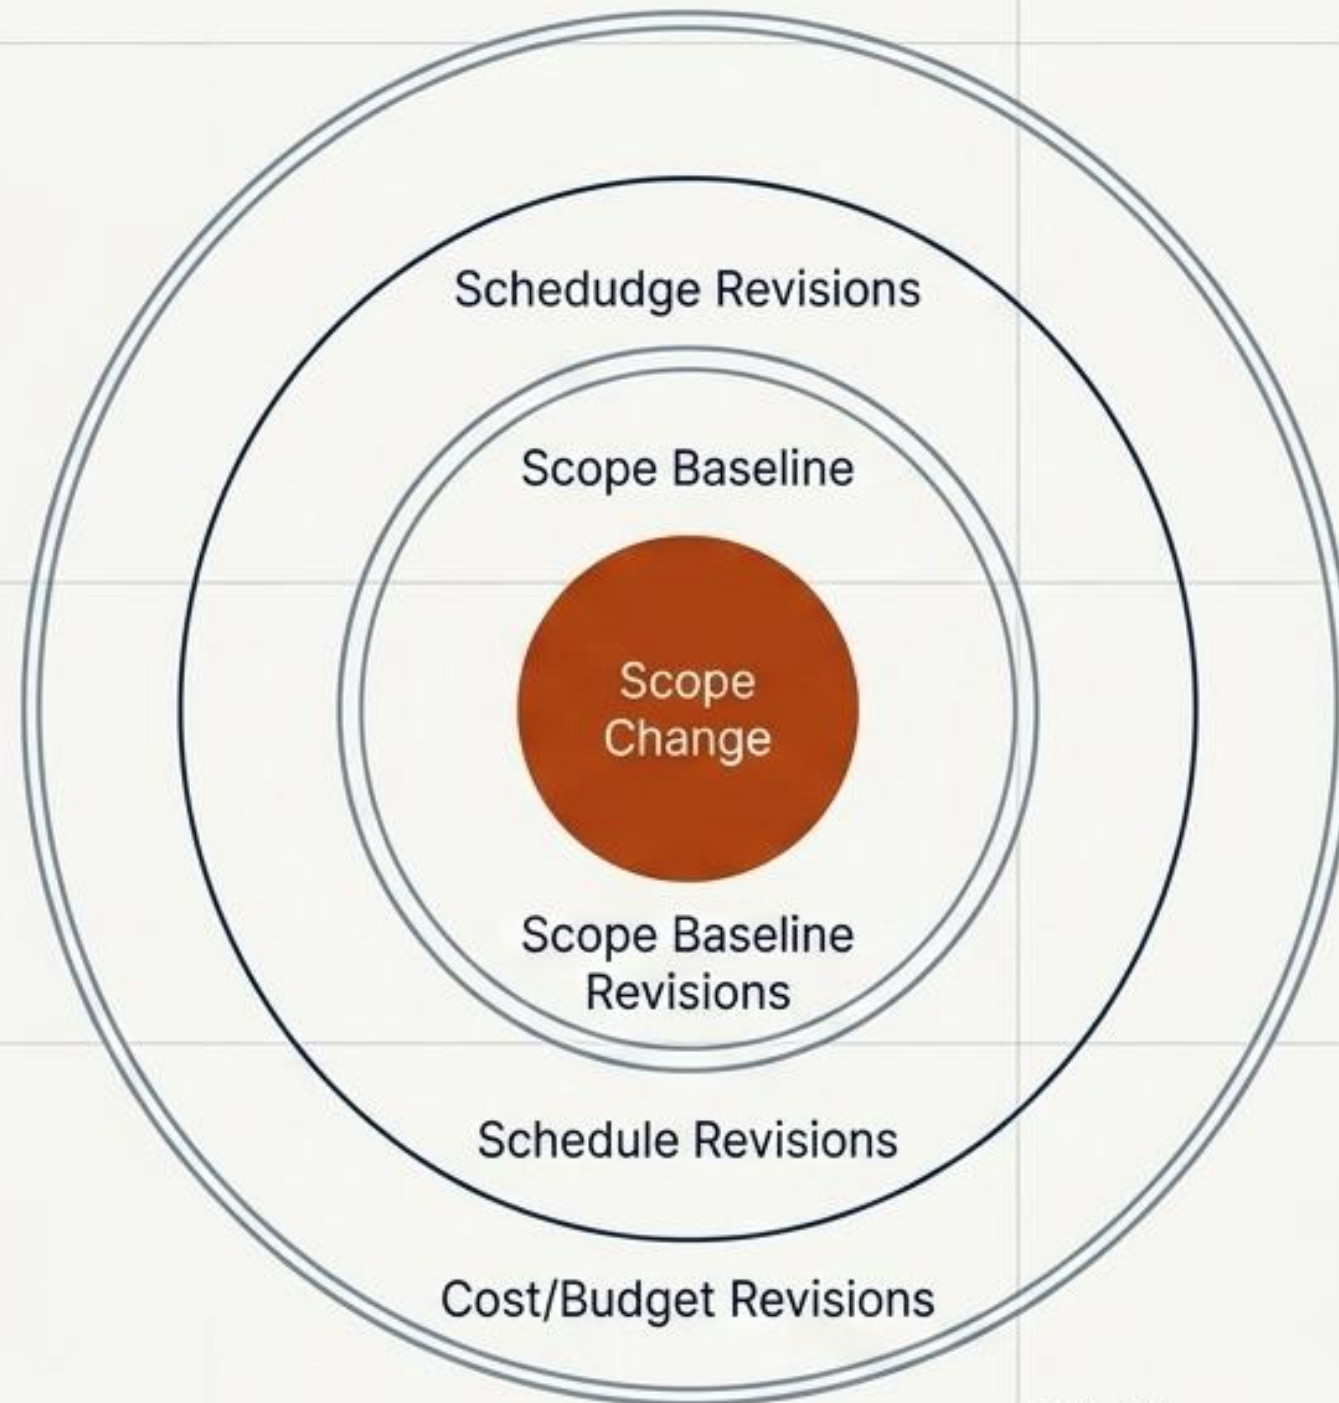

Context Panel

Scope changes almost always affect project costs and require schedule revisions.

Note: Not all changes lengthen schedules. A reduction in requirements can reduce hours and budget, usually when the schedule is the primary unyielding constraint.



Real-World Application: The Kitchen Heaven Case

Project: New Kitchen Heaven Retail Store Build-out.

Project Dossier

The Conflict

Build-out is severely **behind schedule**. Projected completion slipped from **Jan 15th** to **Jan 24th**.

The Constraint

Stakeholder (**Jill**) **begins interviews** on the 16th and absolutely requires the store **empty for shelf-stocking by Jan 22nd**.

Status

Sign-off obtained for completed deliverables to date.

Quality inspections passed to stakeholders' satisfaction.

The immediate threat is **schedule variance**.

Project Performance Dashboard (EVM Synthesis)



Cost Performance: Good return.
\$1.03 value for every \$1 spent.



Schedule Performance: Lagging.
Progressing at 94% of planned rate.



Estimate at Completion: Under the
\$2.00M initial budget.



Estimate to Complete remaining work.

Raw Data

BAC = 2.0

PV = 1.86


EV = 1.75

AC = 1.70

(all figures in millions)

Corrective Actions & Change Strategies

Rejected Option: Overlap Schedule (Fast-Tracking)

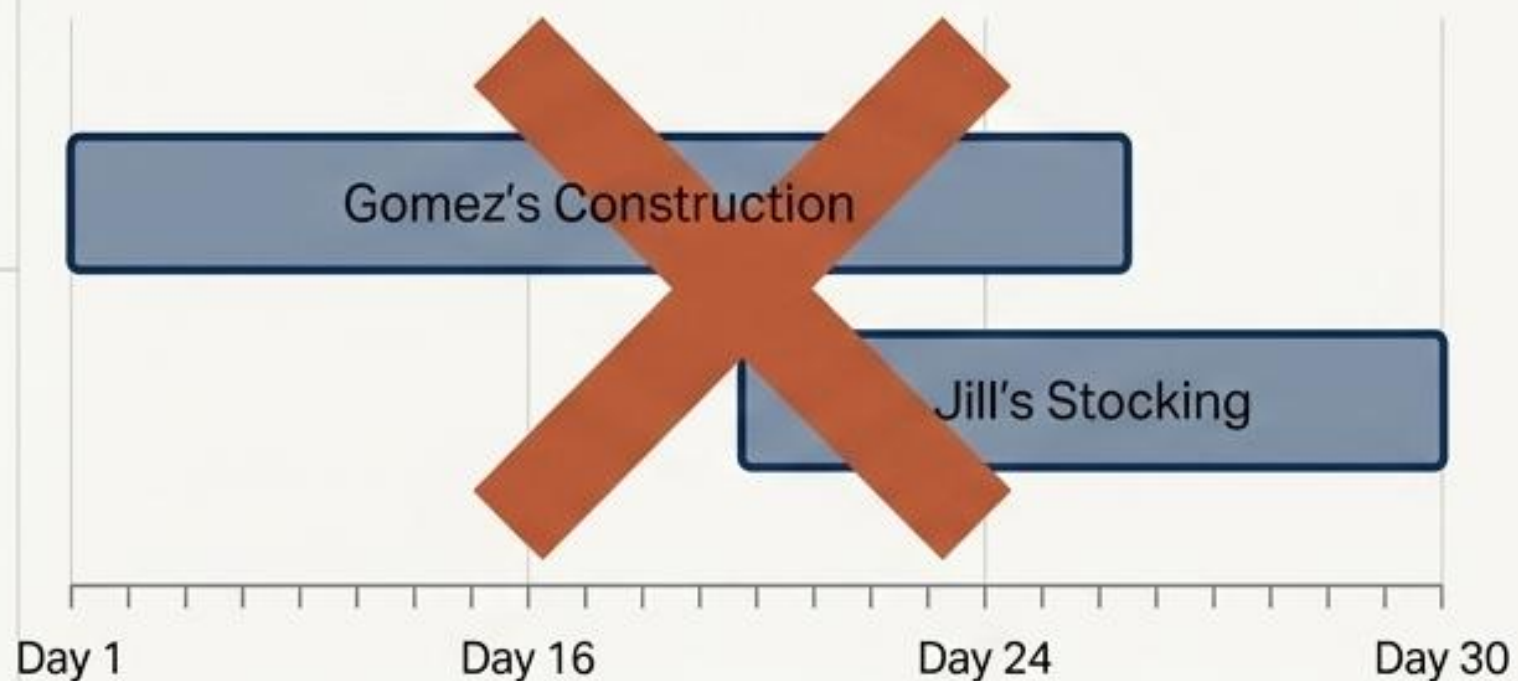


Result: Rejected due to risk of merchandise damage and worker collision.

Accepted Option: Increase Resources (Crashing)



Result: Contract provision allows enforcing additional crew members. Storefront remains clear for Jill on the 22nd.

Integrating with Configuration Management

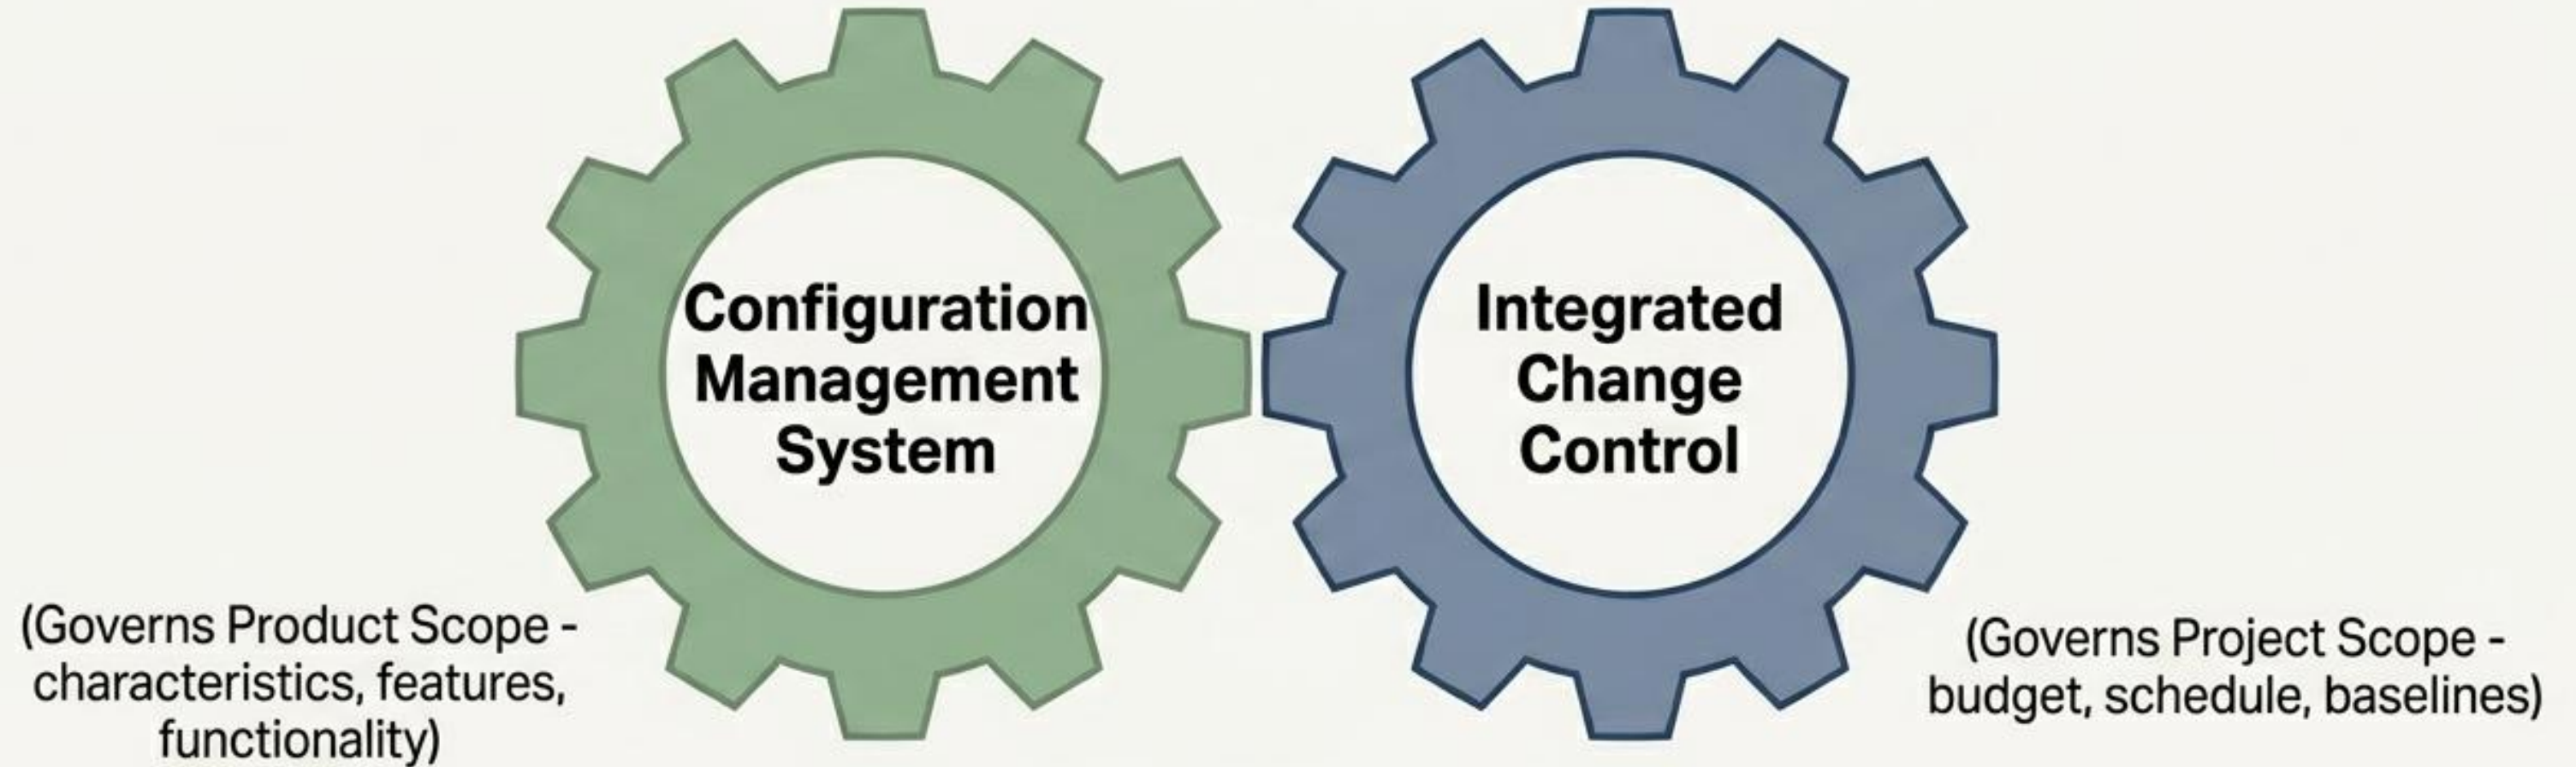

If using a configuration management system, the change control system must seamlessly integrate with it. It ensures changes to the product are reasonable and logical before they are formally processed through Integrated Change Control.

Executive Summary & Exam Essentials

EVM Formulas (Control Costs)

CV (Cost Variance) & **SV** (Schedule Variance)

$$CV = EV - AC$$

$$SV = EV - PV$$

CPI (Cost Performance Index) & **SPI** (Schedule Performance Index)

$$CPI = EV / AC$$

$$SPI = EV / PV$$

Earned Value Management monitors PV, EV, and AC.

The Core 3 Processes

Control Quality: Monitors work against quality standards (**Inspection**).

Validate Scope: Determines if work is complete and satisfies objectives (**Product Verification/Acceptance**).

Control Scope: Manages changes to the agreed-on WBS / scope baseline (**Variance Analysis**).

Risk Management Truths

Control Risks identifies and responds to new risks as they occur.

Both known-unknowns (contingency reserve) and unknown-unknowns (management reserve) will happen. **Monitor continuously.**
