

Certyfikat PMP: Closing the Project

dr Zbigniew Galar

THE FINAL DOMAIN



VALIDATION & ACCEPTANCE

Obtain formal acceptance of the project deliverables. Verify the scope baseline is accurate and exit criteria are met.



TRANSITION & OPERATIONS


Transfer ownership of the final product, service, or result to the organization's operational arm.



ADMINISTRATION & ARCHIVING


Index and file project records, measure customer satisfaction, and distribute the final project report to stakeholders.

THE DYNAMICS OF THE CLOSING PHASE

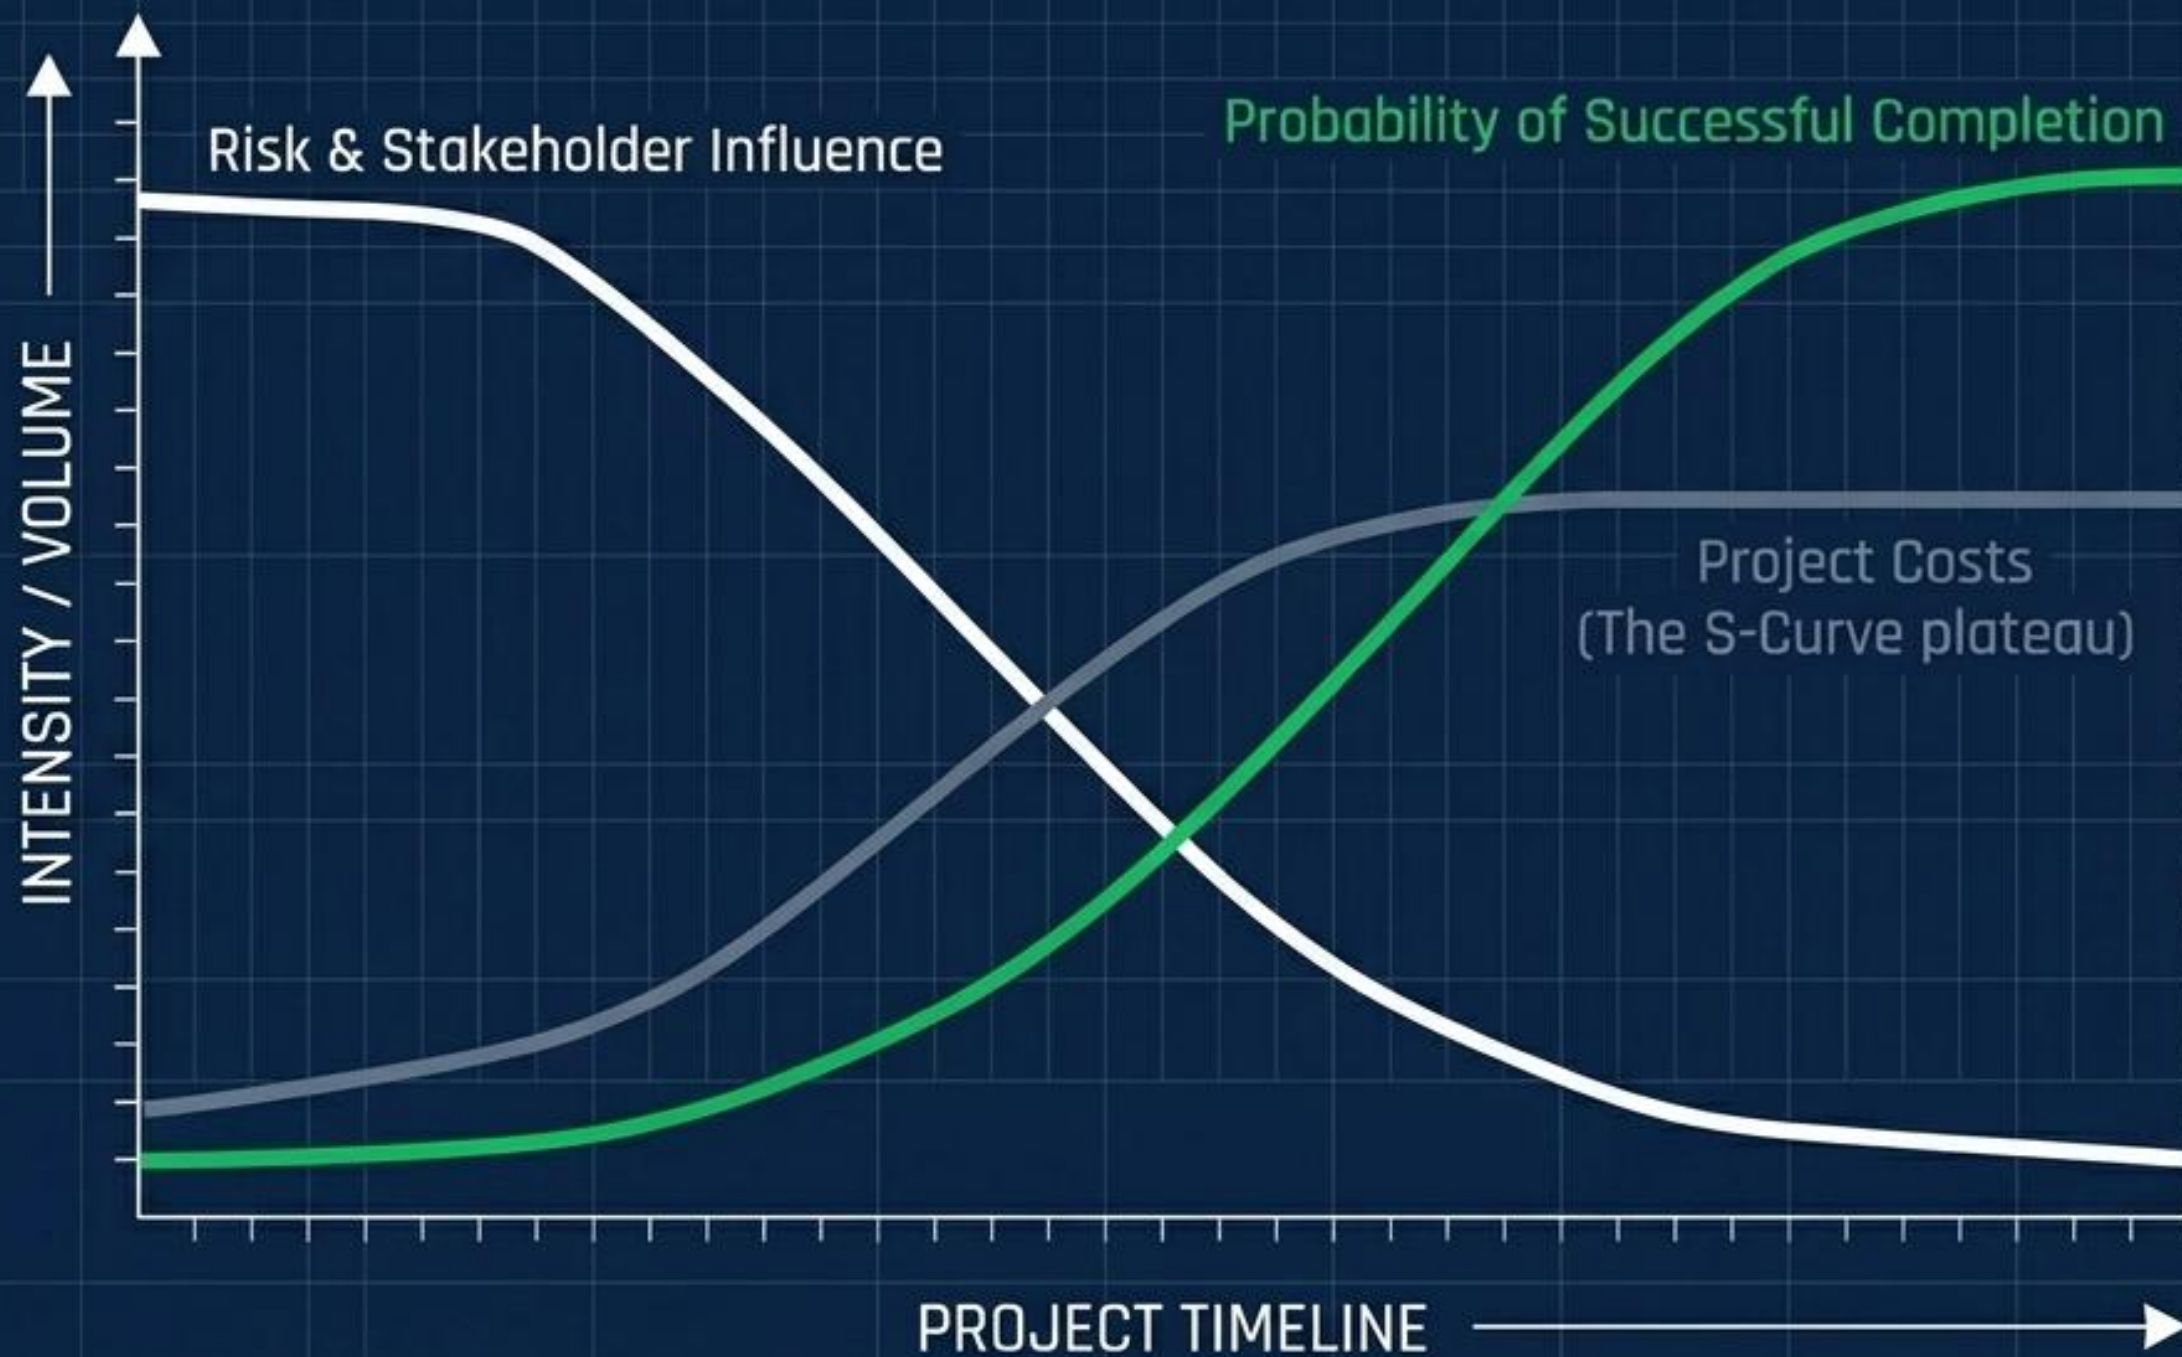

THE MATRIX ADVANTAGE:
Weak Matrix organizations experience the least stress during closure. Functional managers assign all tasks, so team members have a secure job to return to without changes in reporting structure.

INTRODUCTION TO PROJECT ENDINGS

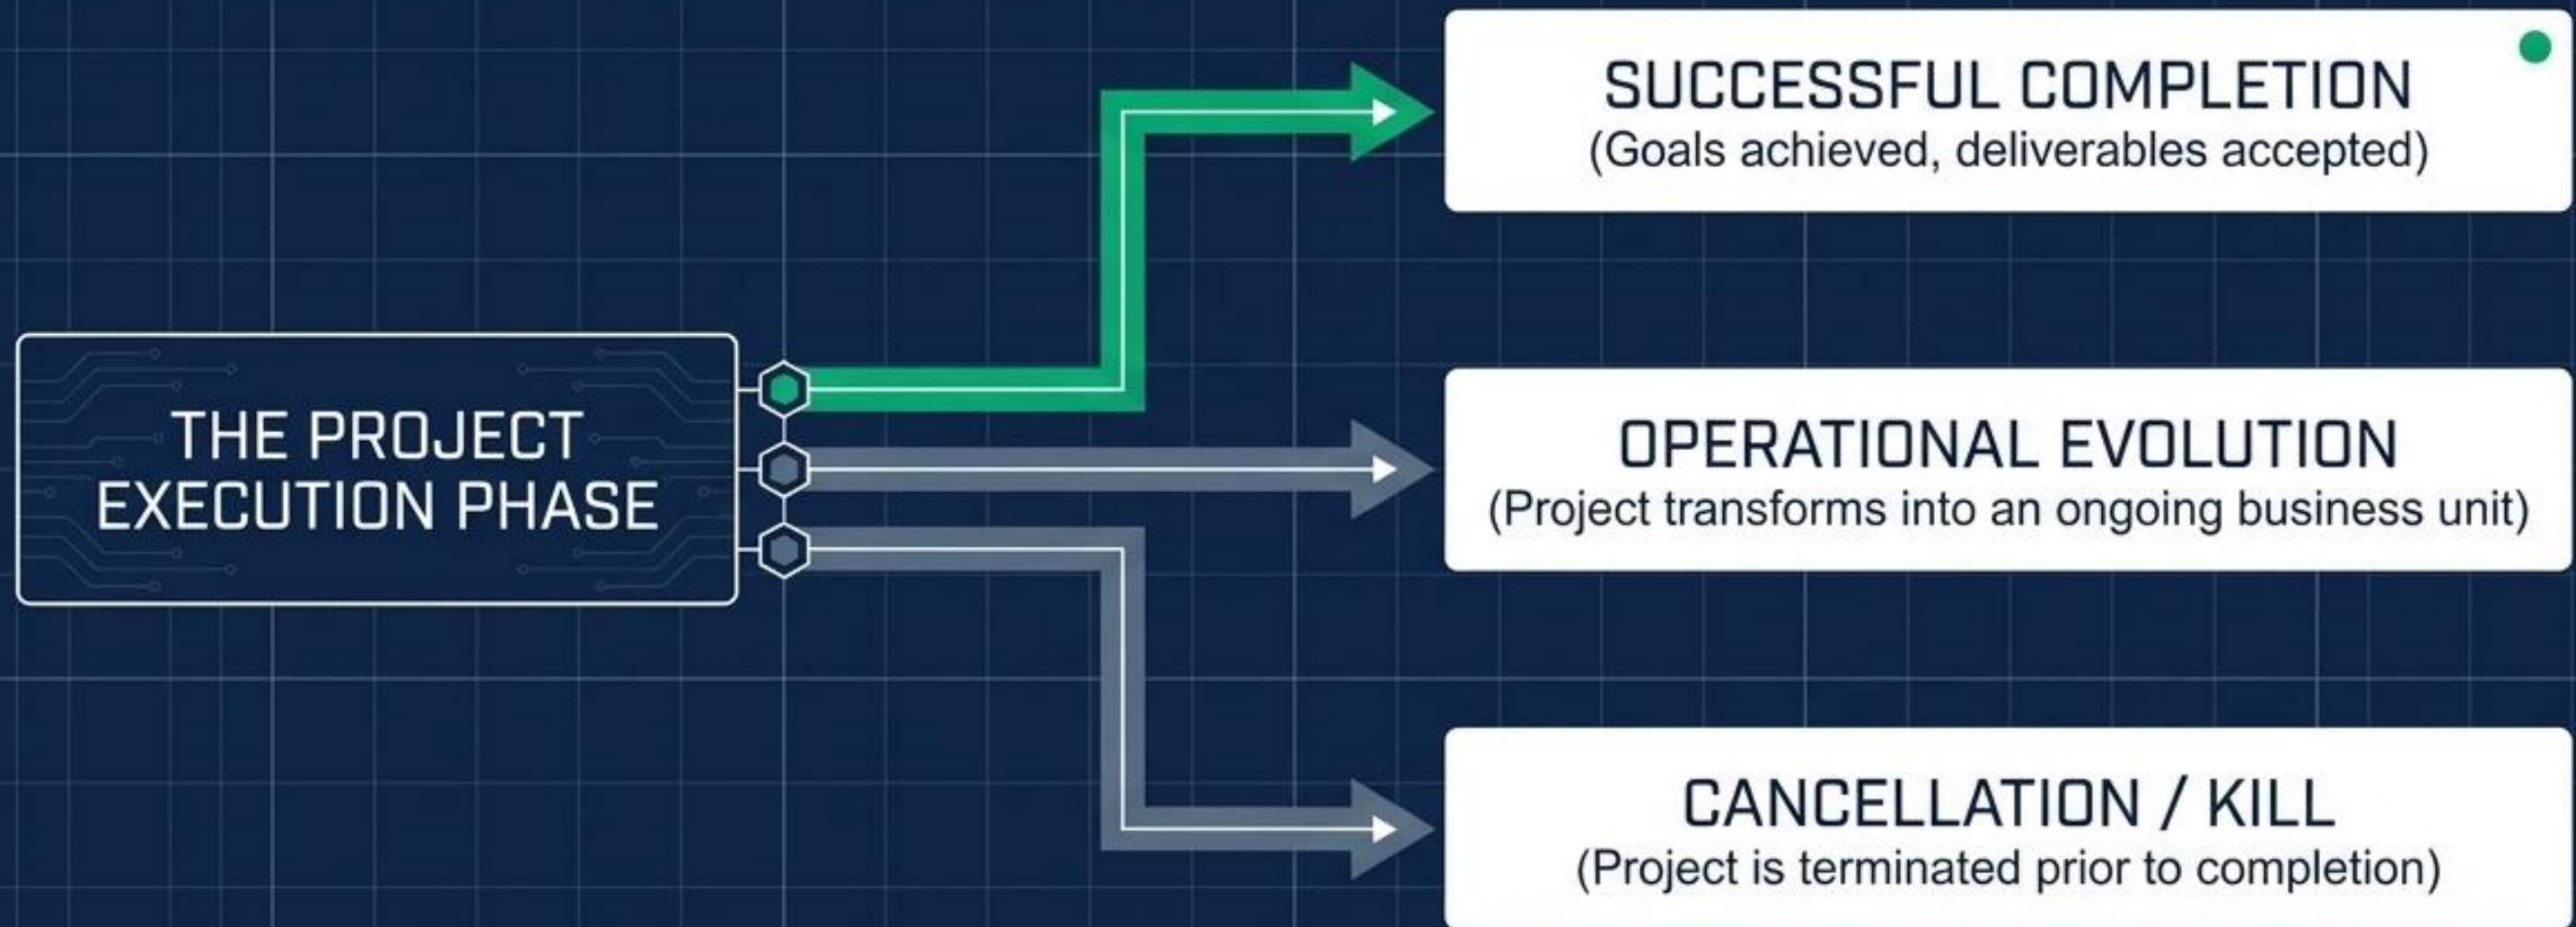

All projects eventually end. The PMP framework categorizes these endings into four definitive, formal types.

Matrix - The 4 Types of Project Endings


	Addition	Starvation	Integration	Extinction
Definition	Evolves into ongoing operations (e.g., ERP installation).	Resources are cut off prematurely.	Resources are distributed elsewhere.	Completed and formally accepted.
Catalyst (Why it ends)	Project becomes a permanent business necessity.	Budget cuts, order curtailments, or key resource loss.	Shift in organizational focus or competing priorities.	All goals achieved and exit criteria met.
Resource Fate	Transitioned to full-time operational staff.	Withheld or eliminated.	Redeployed to other projects/areas.	Released.
Success Status	Successful transformation.	Unfinished / Abrupt termination.	Unfinished via reassignment.	Absolute Success.

CASE STUDY: DEATH BY INTEGRATION



Real World Scenario

STEP 1: THE ORIGINAL STATE

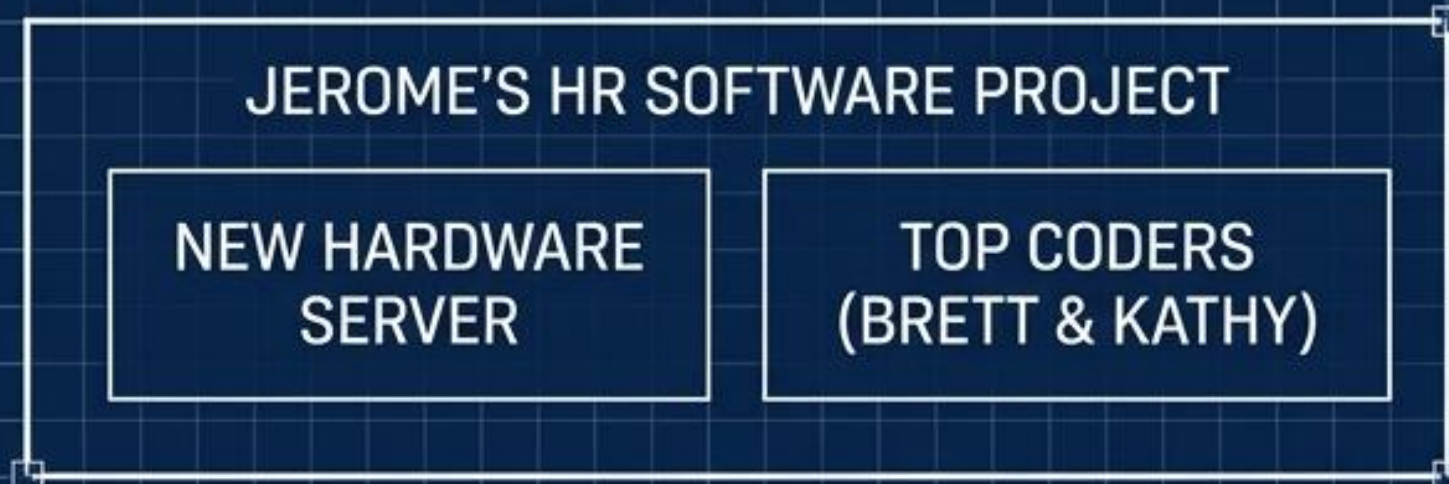

STEP 2: THE CATALYST




STEP 3: THE RESULT



THE HR PROJECT IS NOT OUTRIGHT CANCELED (STARVATION), BUT ITS ESSENTIAL RESOURCES ARE REASSIGNED TO A HIGHER-PRIORITY VENDOR PROJECT. THE HR PROJECT ENDS VIA **INTEGRATION**.

The “Close Project or Phase” Process Engine

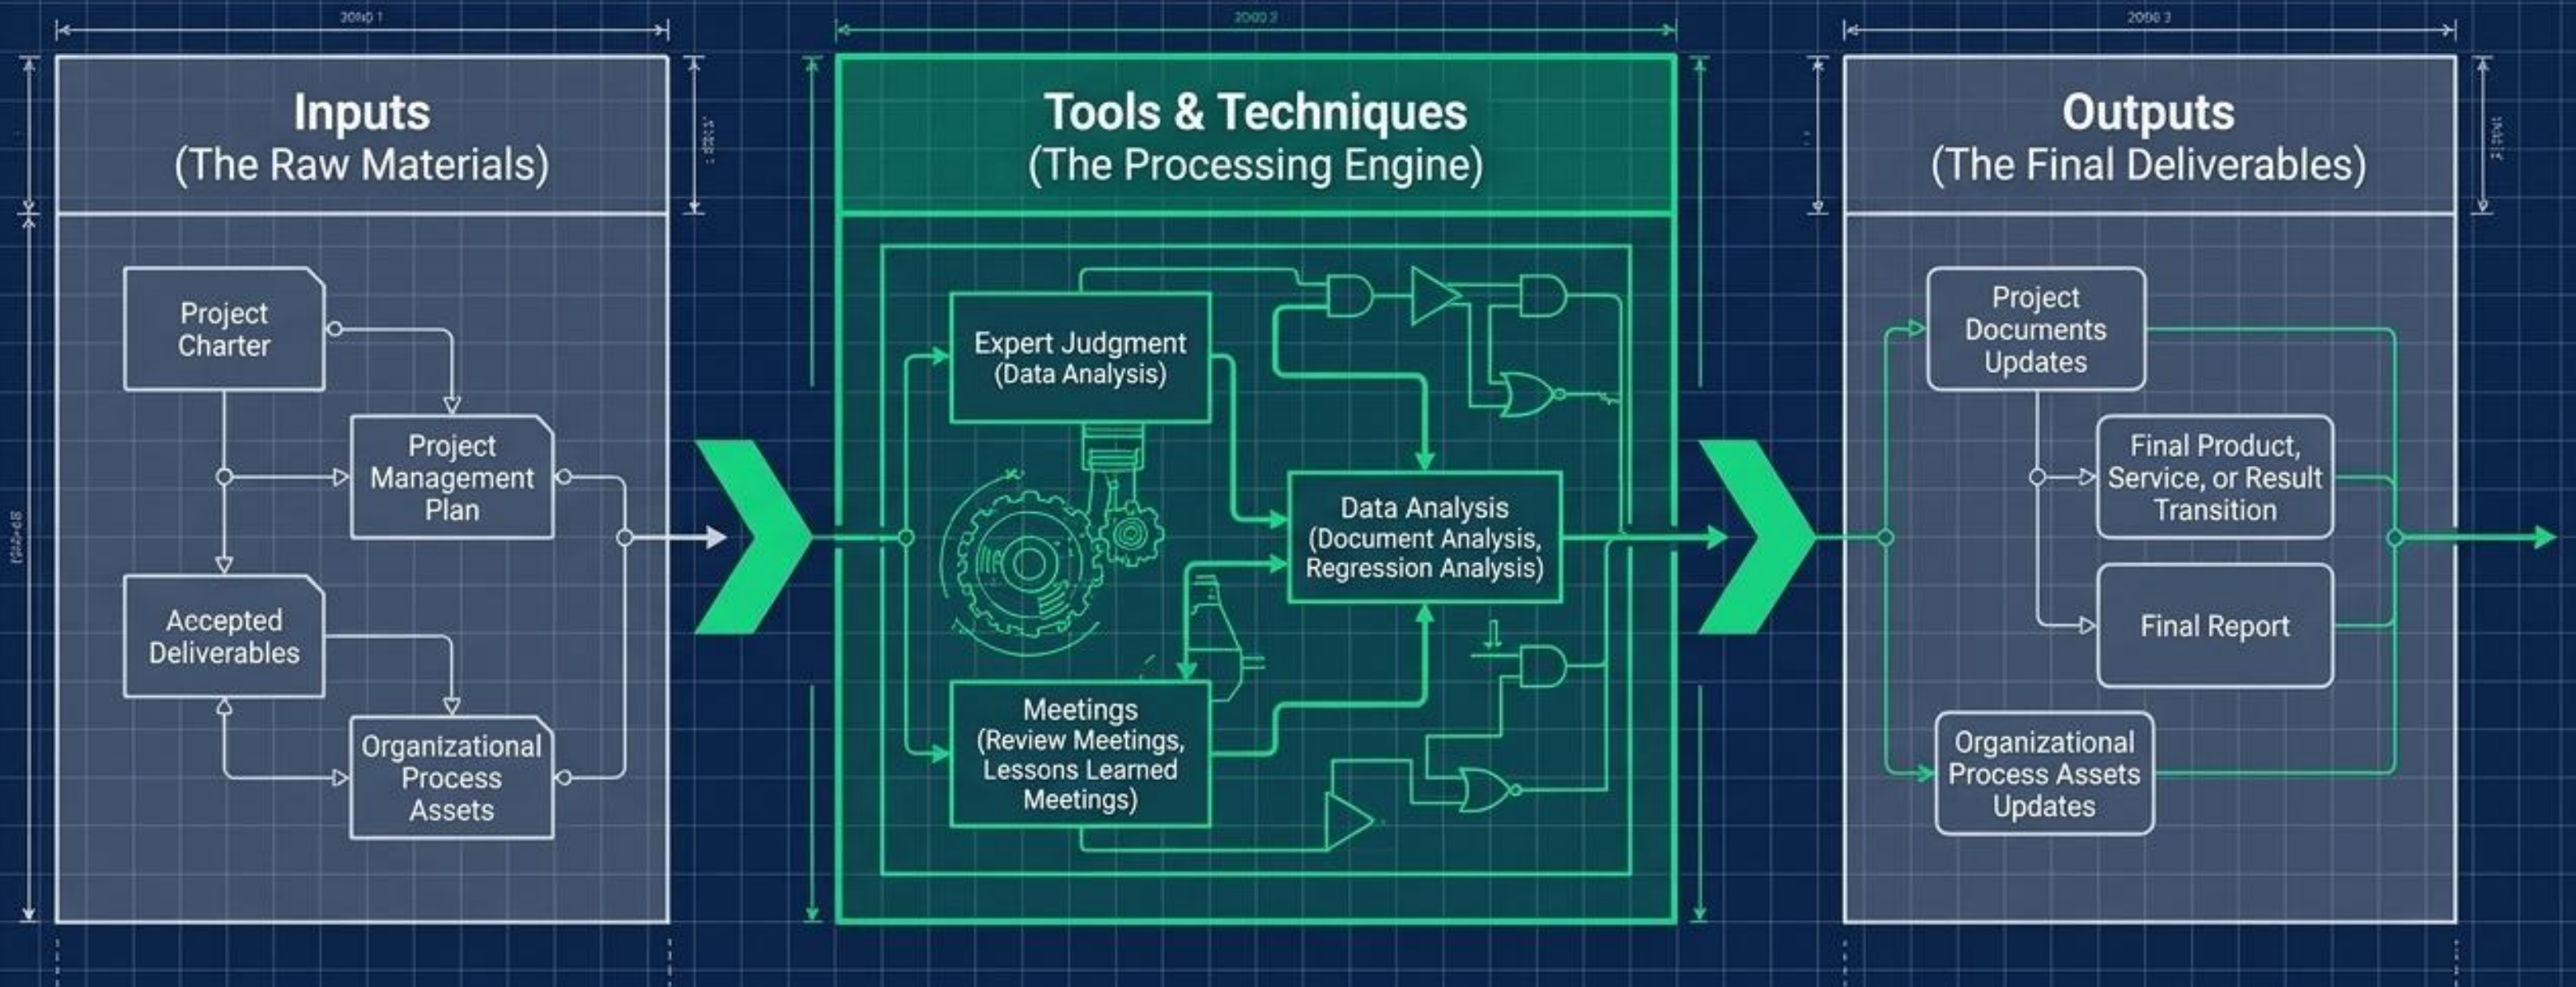

As part of the Project Integration Management Knowledge Area, this process ensures all activities across all process groups are finalized.

Process Inputs (The Raw Materials)

Project Management Plan

The master blueprint. Ensures the final product perfectly reflects the baseline scope and documented specifications, including any implemented scope change requests.

Accepted Deliverables


The physical or digital outcomes. Crucial context: These were previously accepted and verified during the Validate Scope process.

Organizational Process Assets (OPAs)


Existing organizational frameworks, templates, and historical data used to guide the closure process.



Process Tools & Techniques (The Mechanisms)

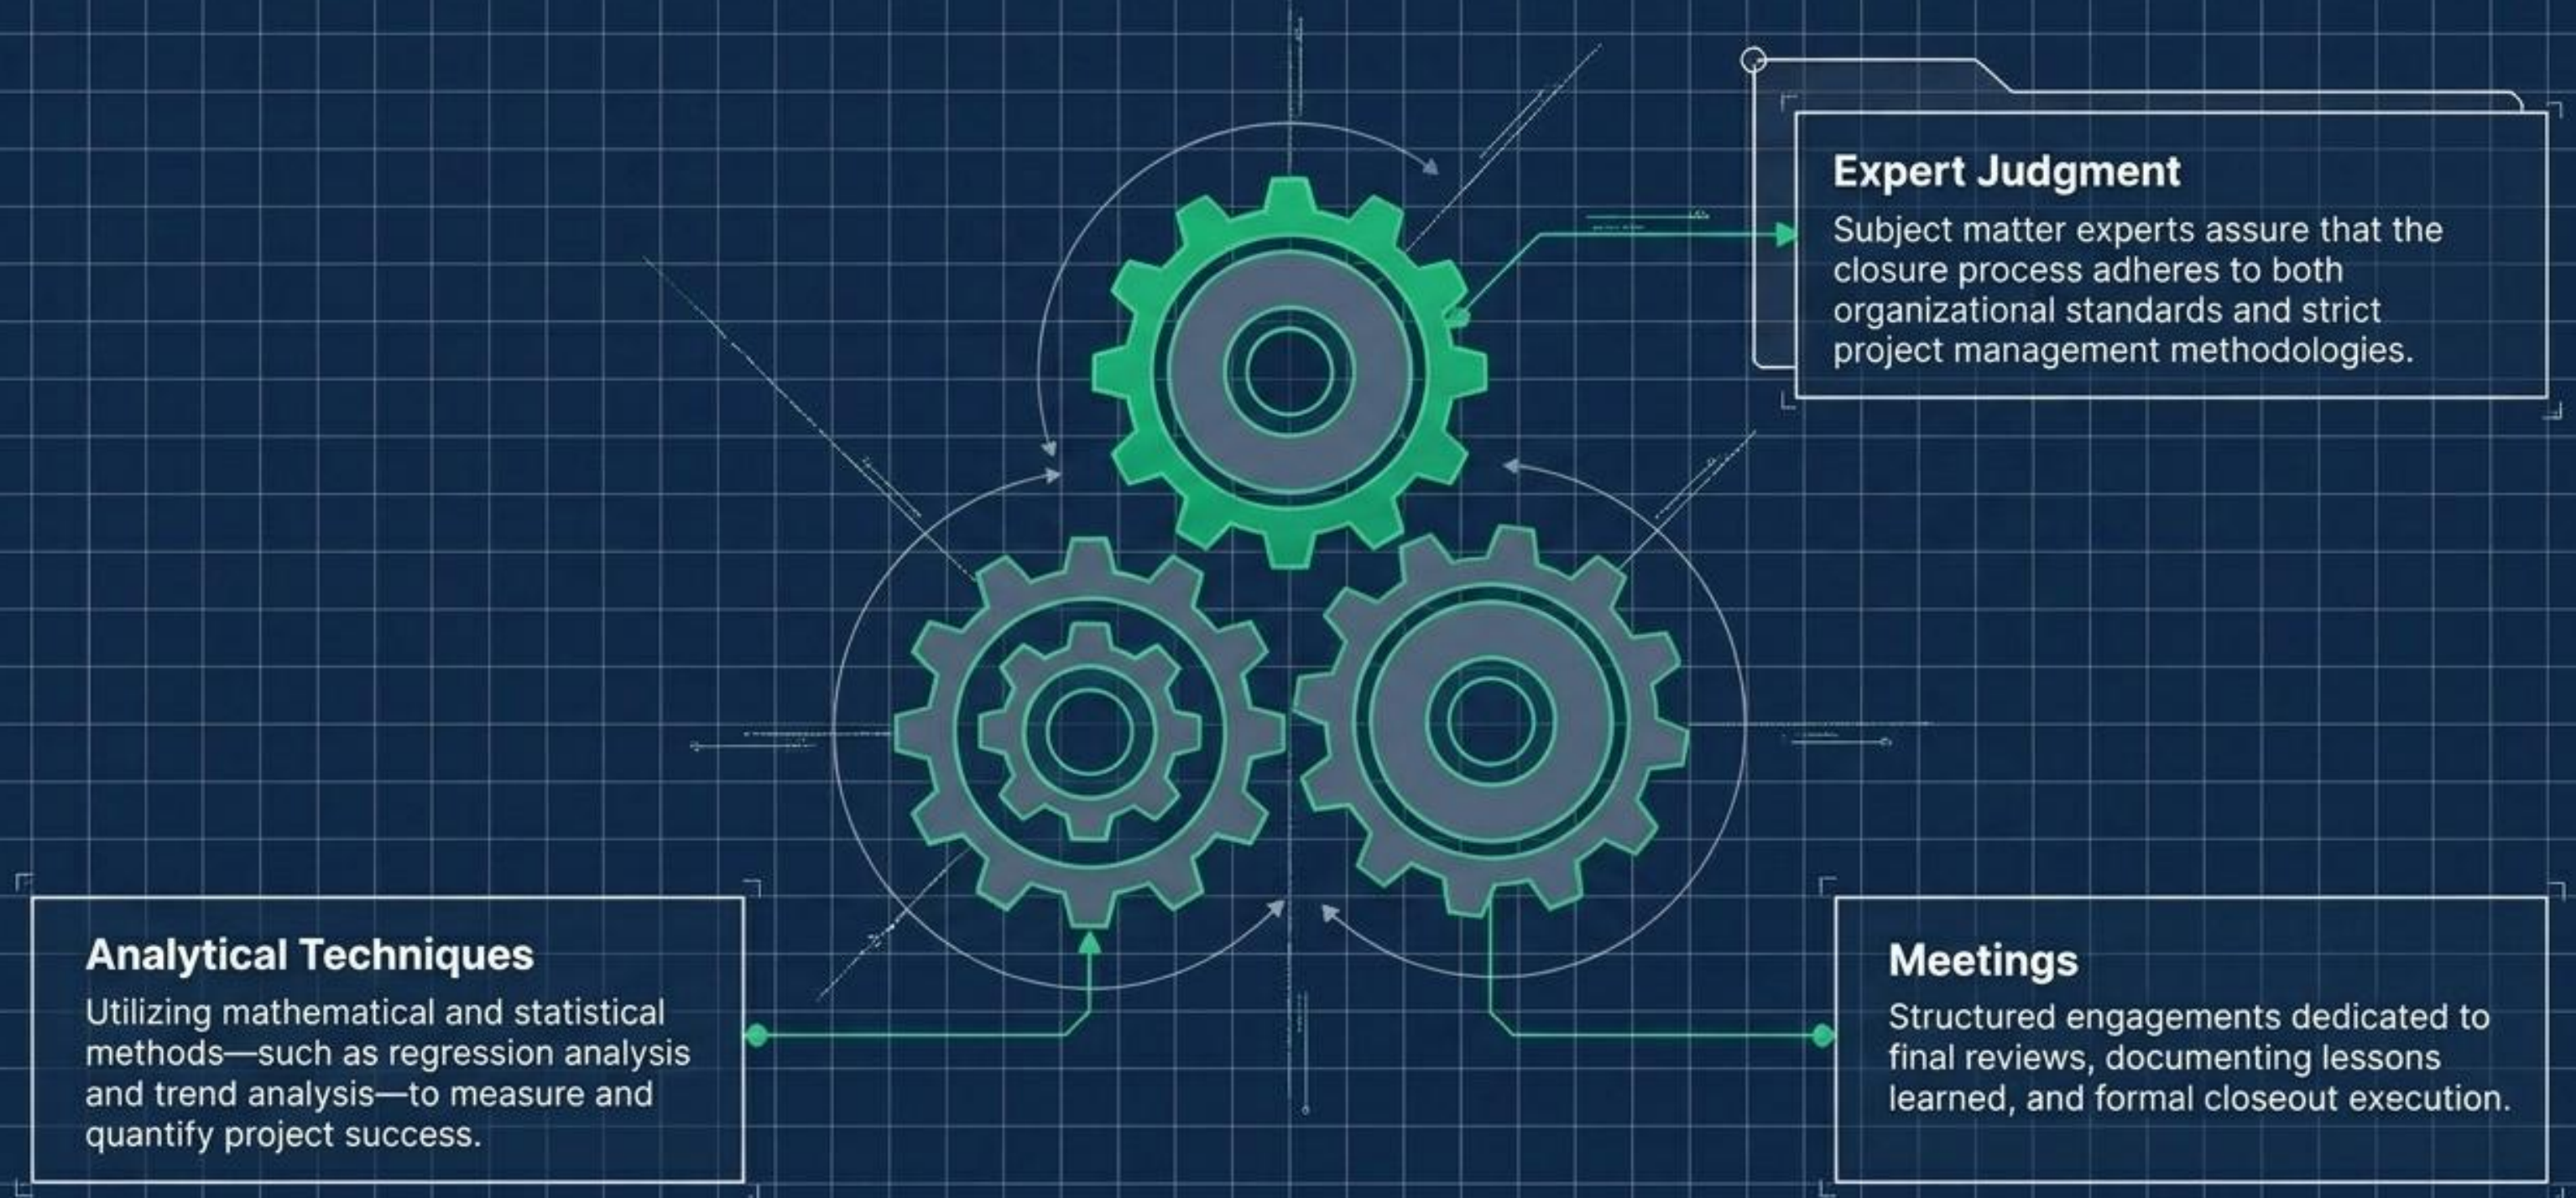

Process Outputs (The Final Deliverables)

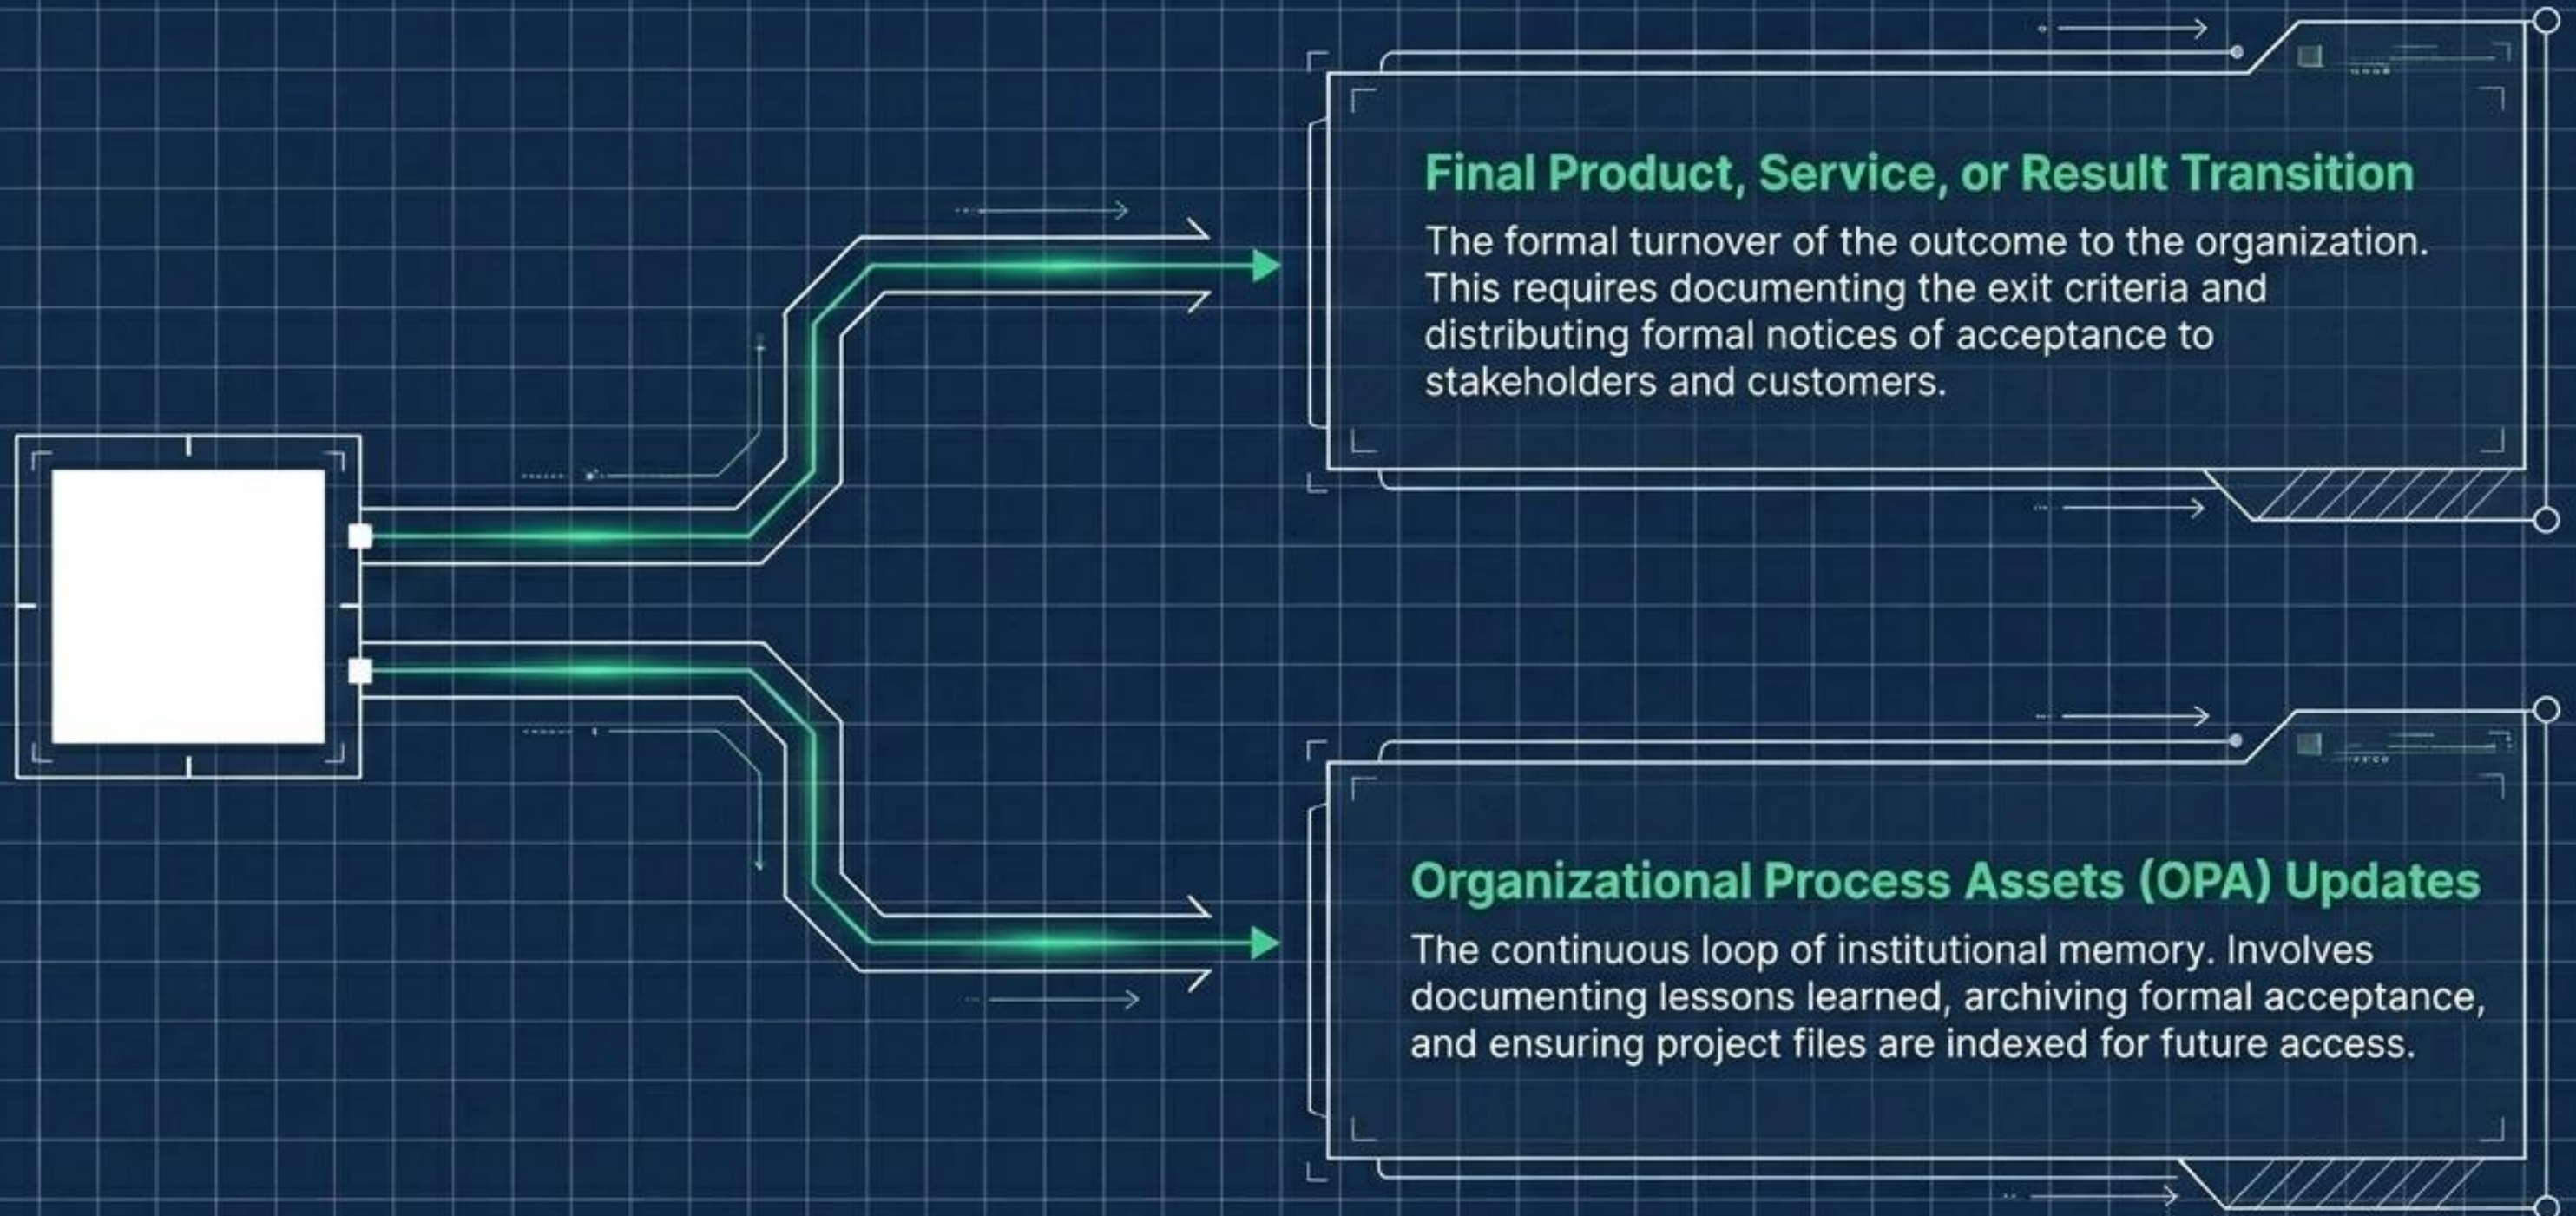

The Imperative of Formal Sign-Off

Validate Scope Process

Action:

Verifying and accepting the actual work.

Focus:

Are the deliverables correct according to the plan?

Timing:

Happens before closure.

Sign-off is the definitive indicator that stakeholder expectations and project goals have been successfully met.

Close Project or Phase Process

Action:

Obtaining final formal sign-off.

Focus:

Have all exit criteria been met and do stakeholders formally accept the project?

Timing:

The ultimate final step.

Administrative Closure Procedures

01

Stakeholder Approval

Confirm approval requirements and verify deliverables meet sponsor/customer specifications.

02

Financial & Record Archiving

Index and store all records safely.

Critical for Contracted Work: Archiving financial records is vital for payment disputes and estimating future project costs.

03

Transfer Operations

Execute all activities necessary to transfer the product/service to the operations arm or the next project phase.


04

Exit Verification

Assure and formally confirm that all project exit criteria are entirely satisfied.



The Lifeblood of Future Projects: Documentation

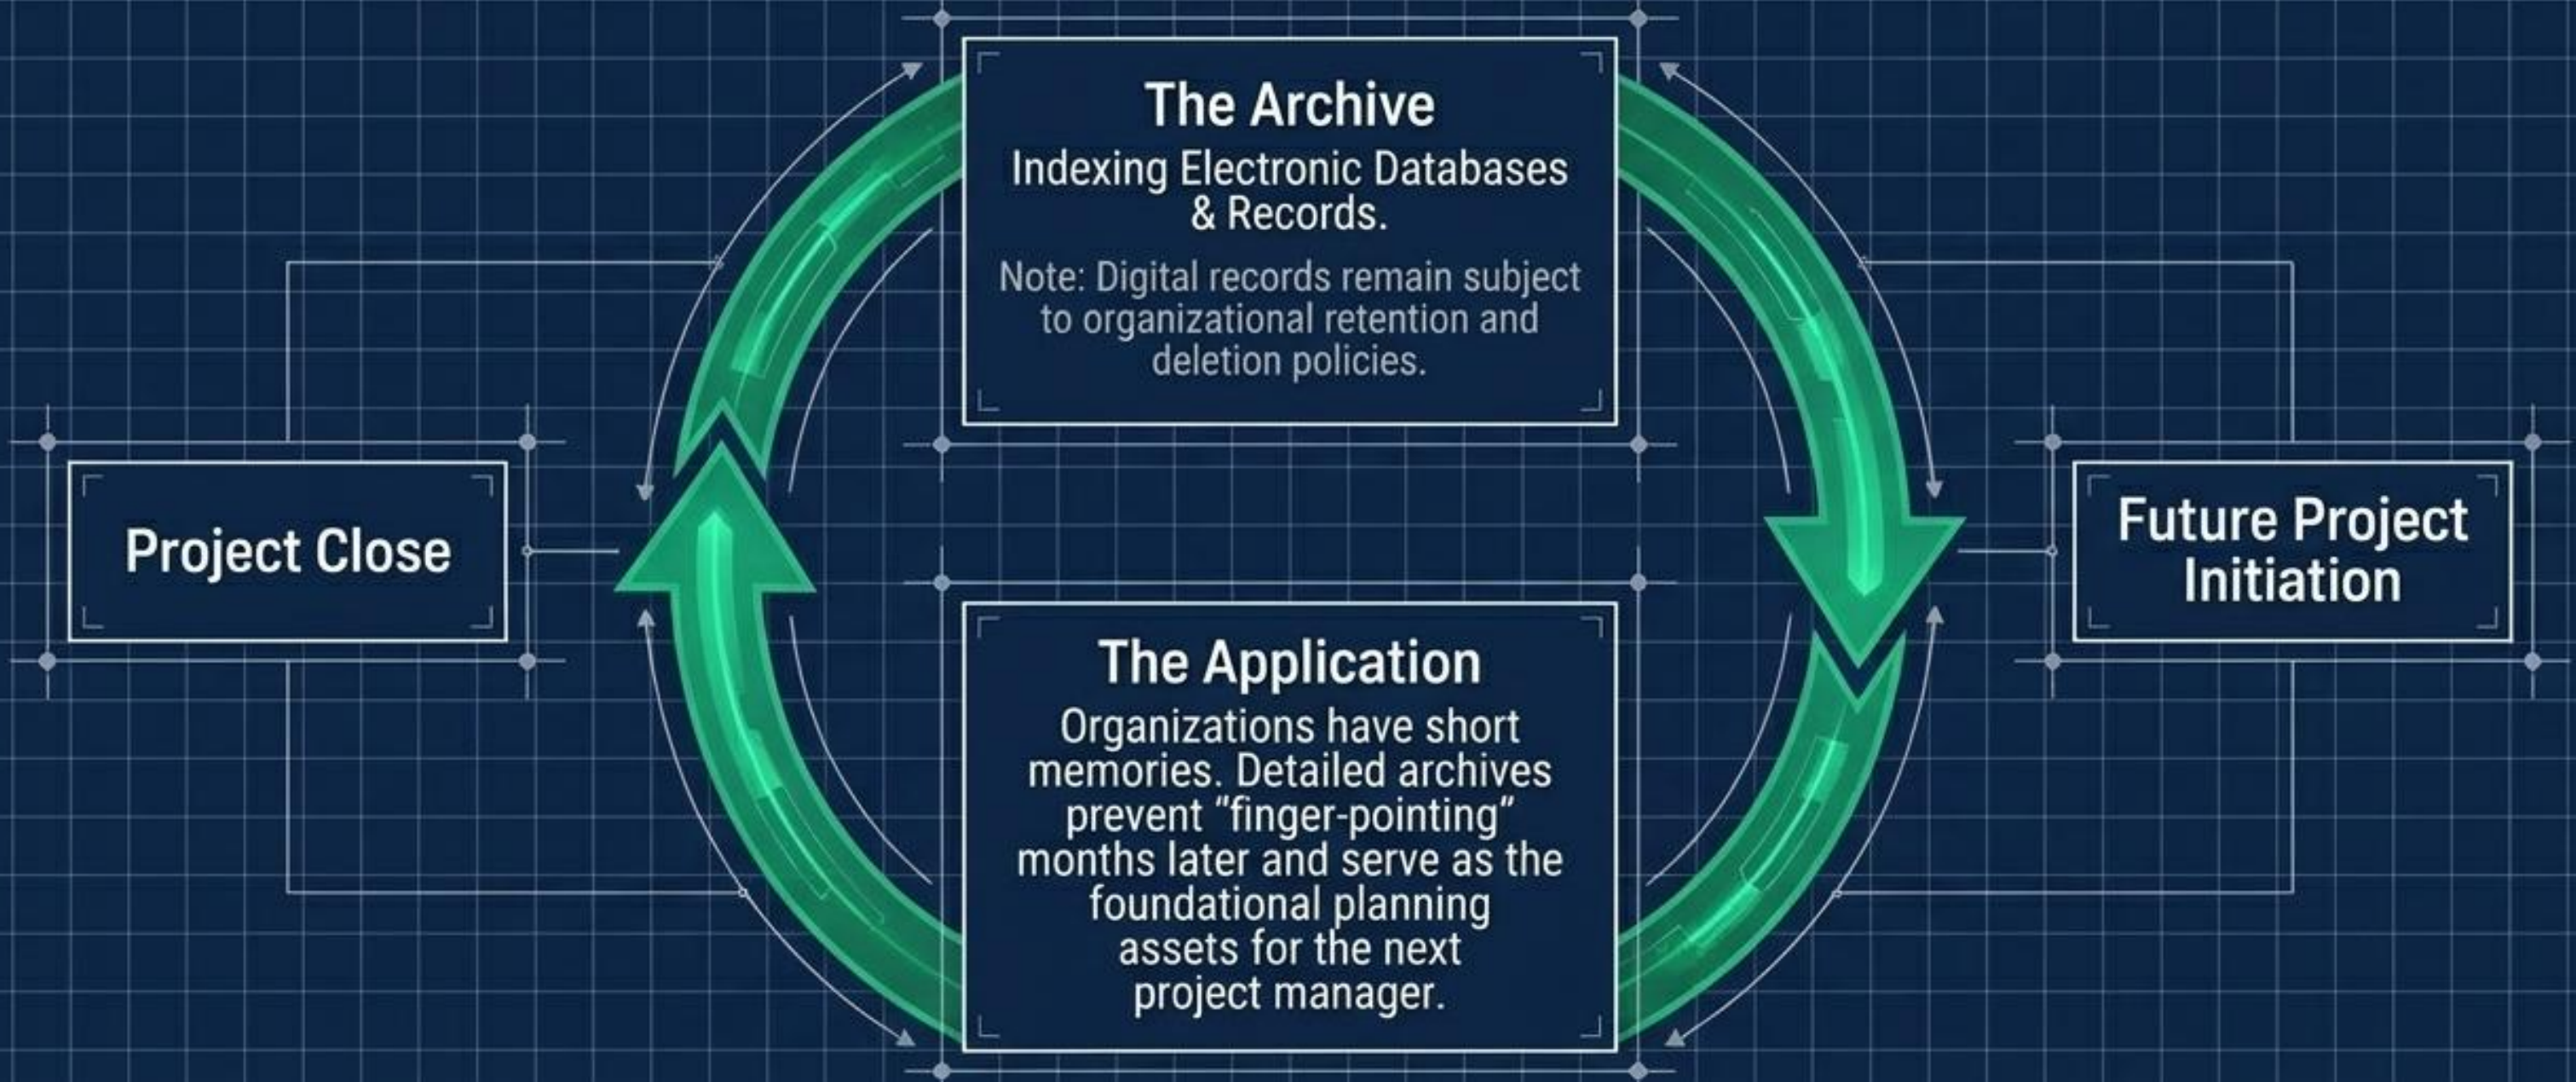

Post-Certification: The PMP Code of Conduct

Integrity & Knowledge

Obligation to maintain unwavering personal integrity and actively apply subject matter and project management expertise.


Stakeholder Balance

The continuous requirement to balance the diverse interests and needs of project stakeholders against the overarching needs of the organization.

Cultural Respect

Operating in diverse, international, or contracted environments demands professional, courteous behavior and deep respect for differing organizational cultures and backgrounds.

Synthesis: The Architect's Final Checklist

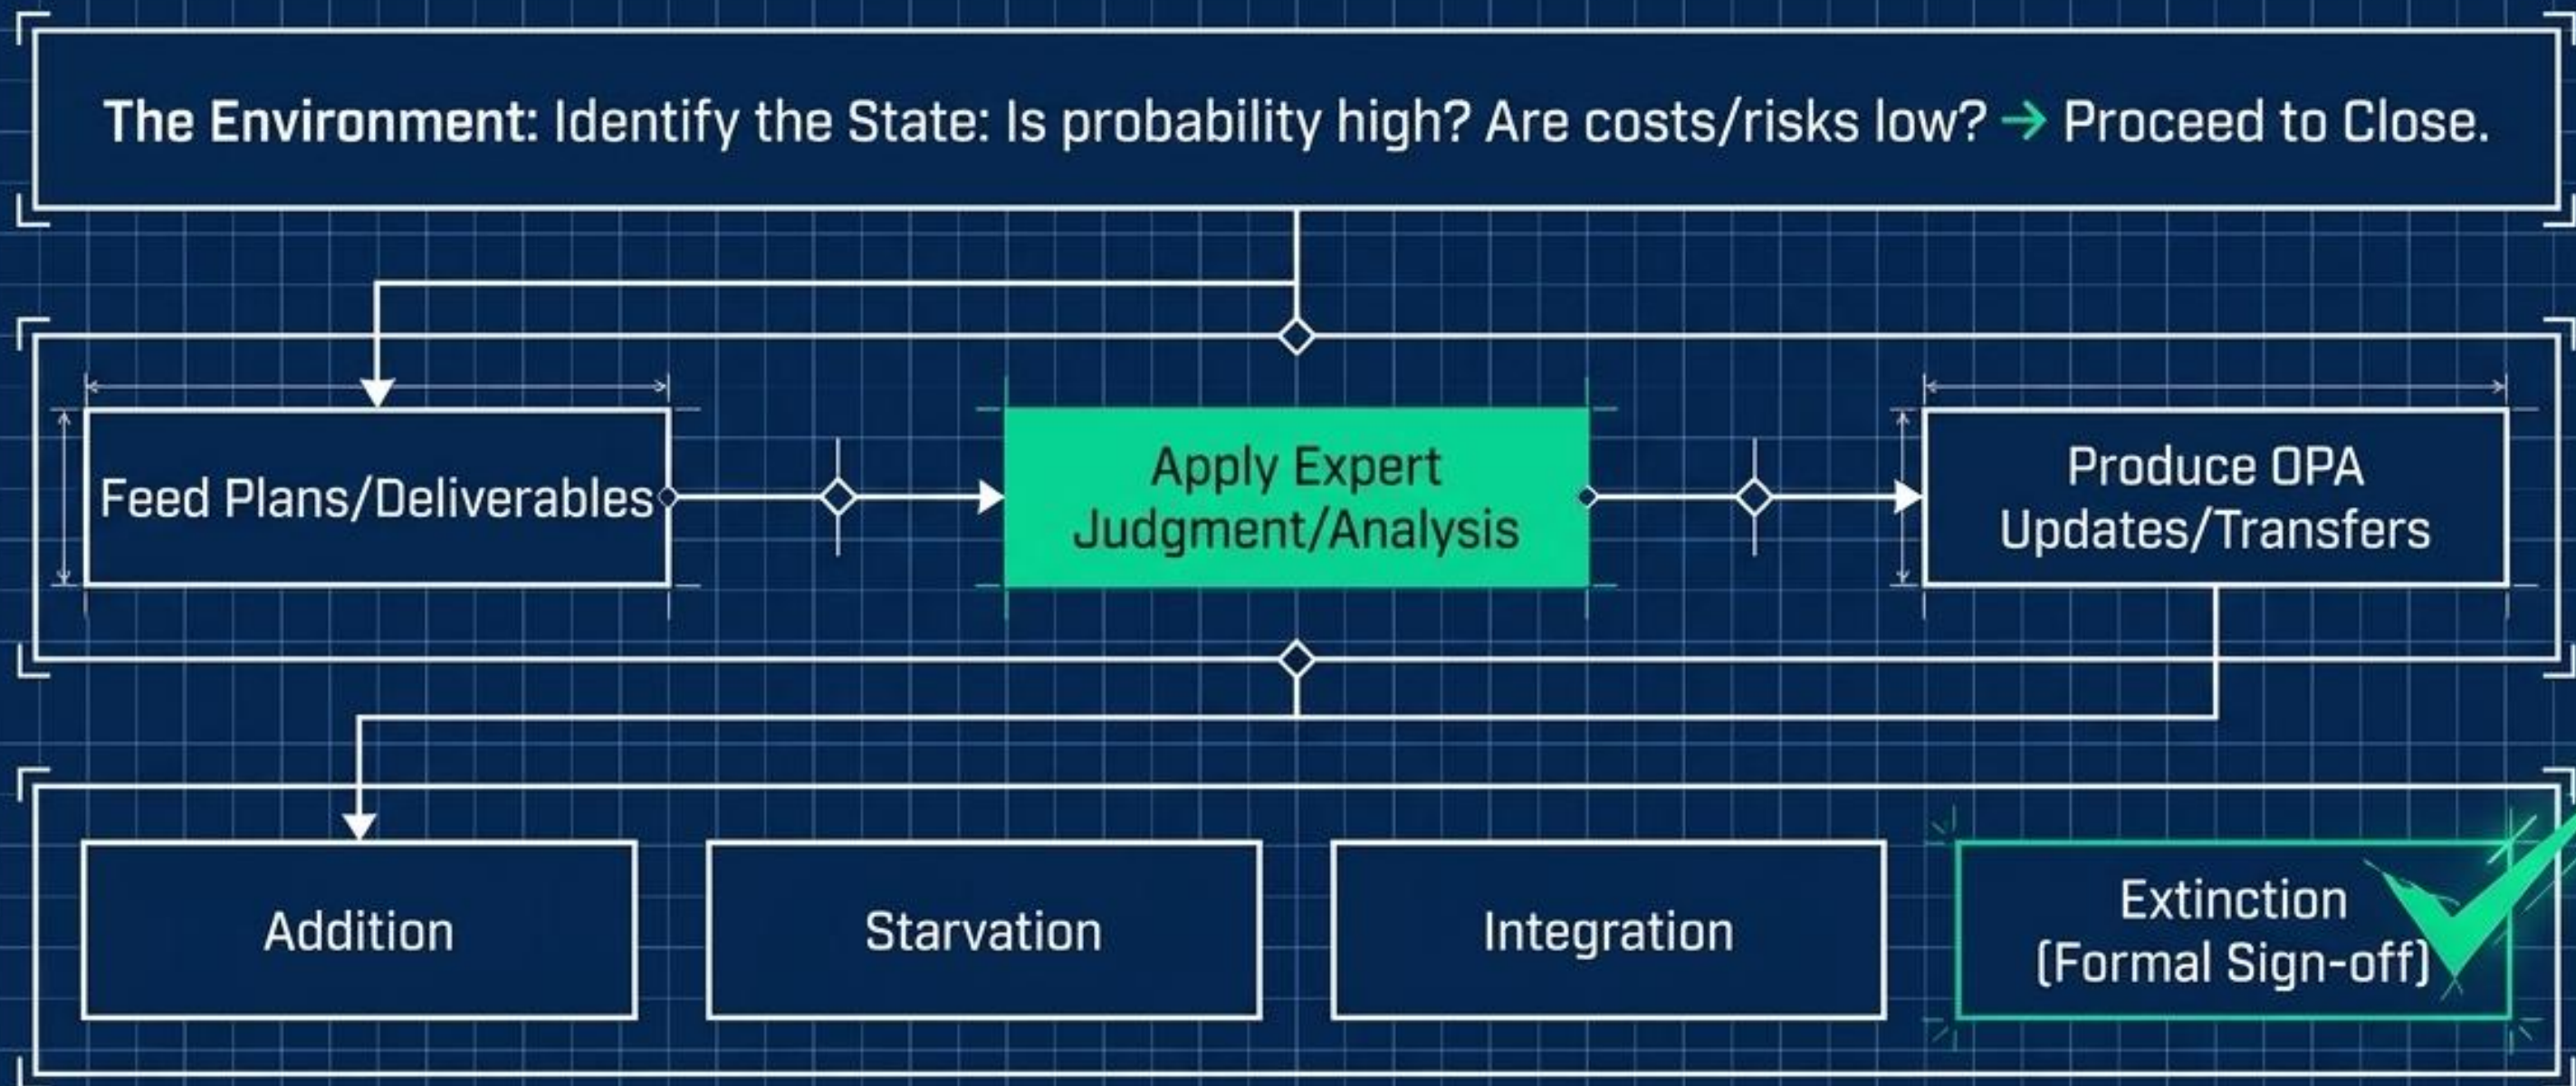

Closure is not merely stopping work; it is the formal, documented transformation of effort into organizational value.
