




Certyfikat PMP: Procurement and Information Sharing

Author: dr Zbigniew Galar

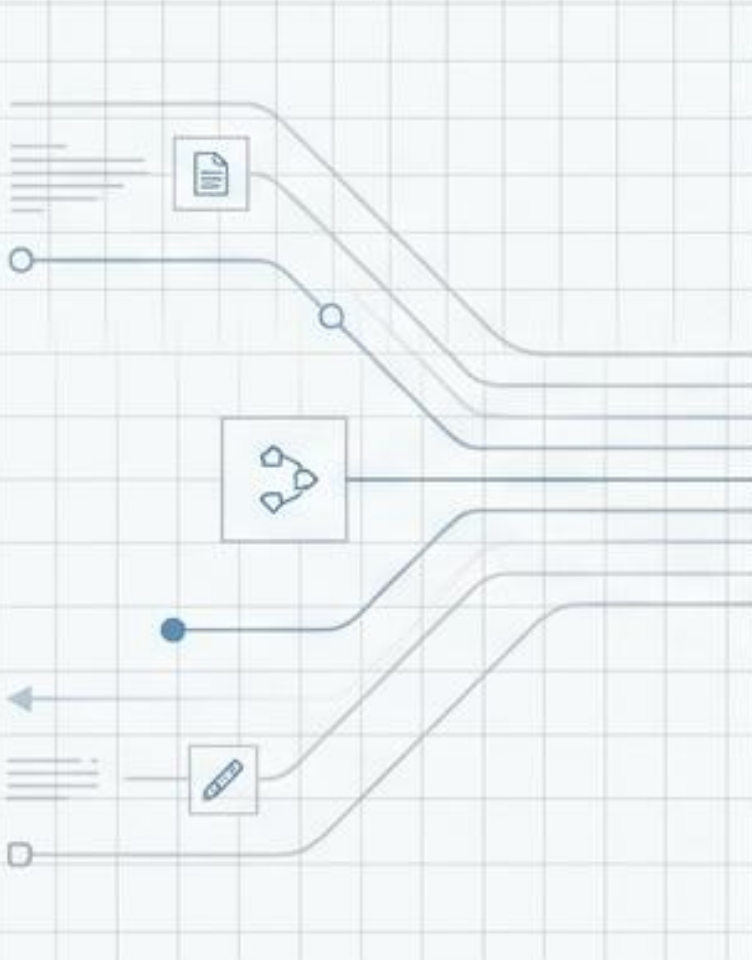

Navigating the Executing Process Group

Perform Quality Assurance



Manage Communications



Manage Stakeholder Engagement




Conduct Procurements

The transition from planning to action. Sellers respond to bids. Contracts are awarded. External resources are secured.




Goal: Obtain and manage project resources to ensure successful project execution.

Prerequisite Data for Conducting Procurements

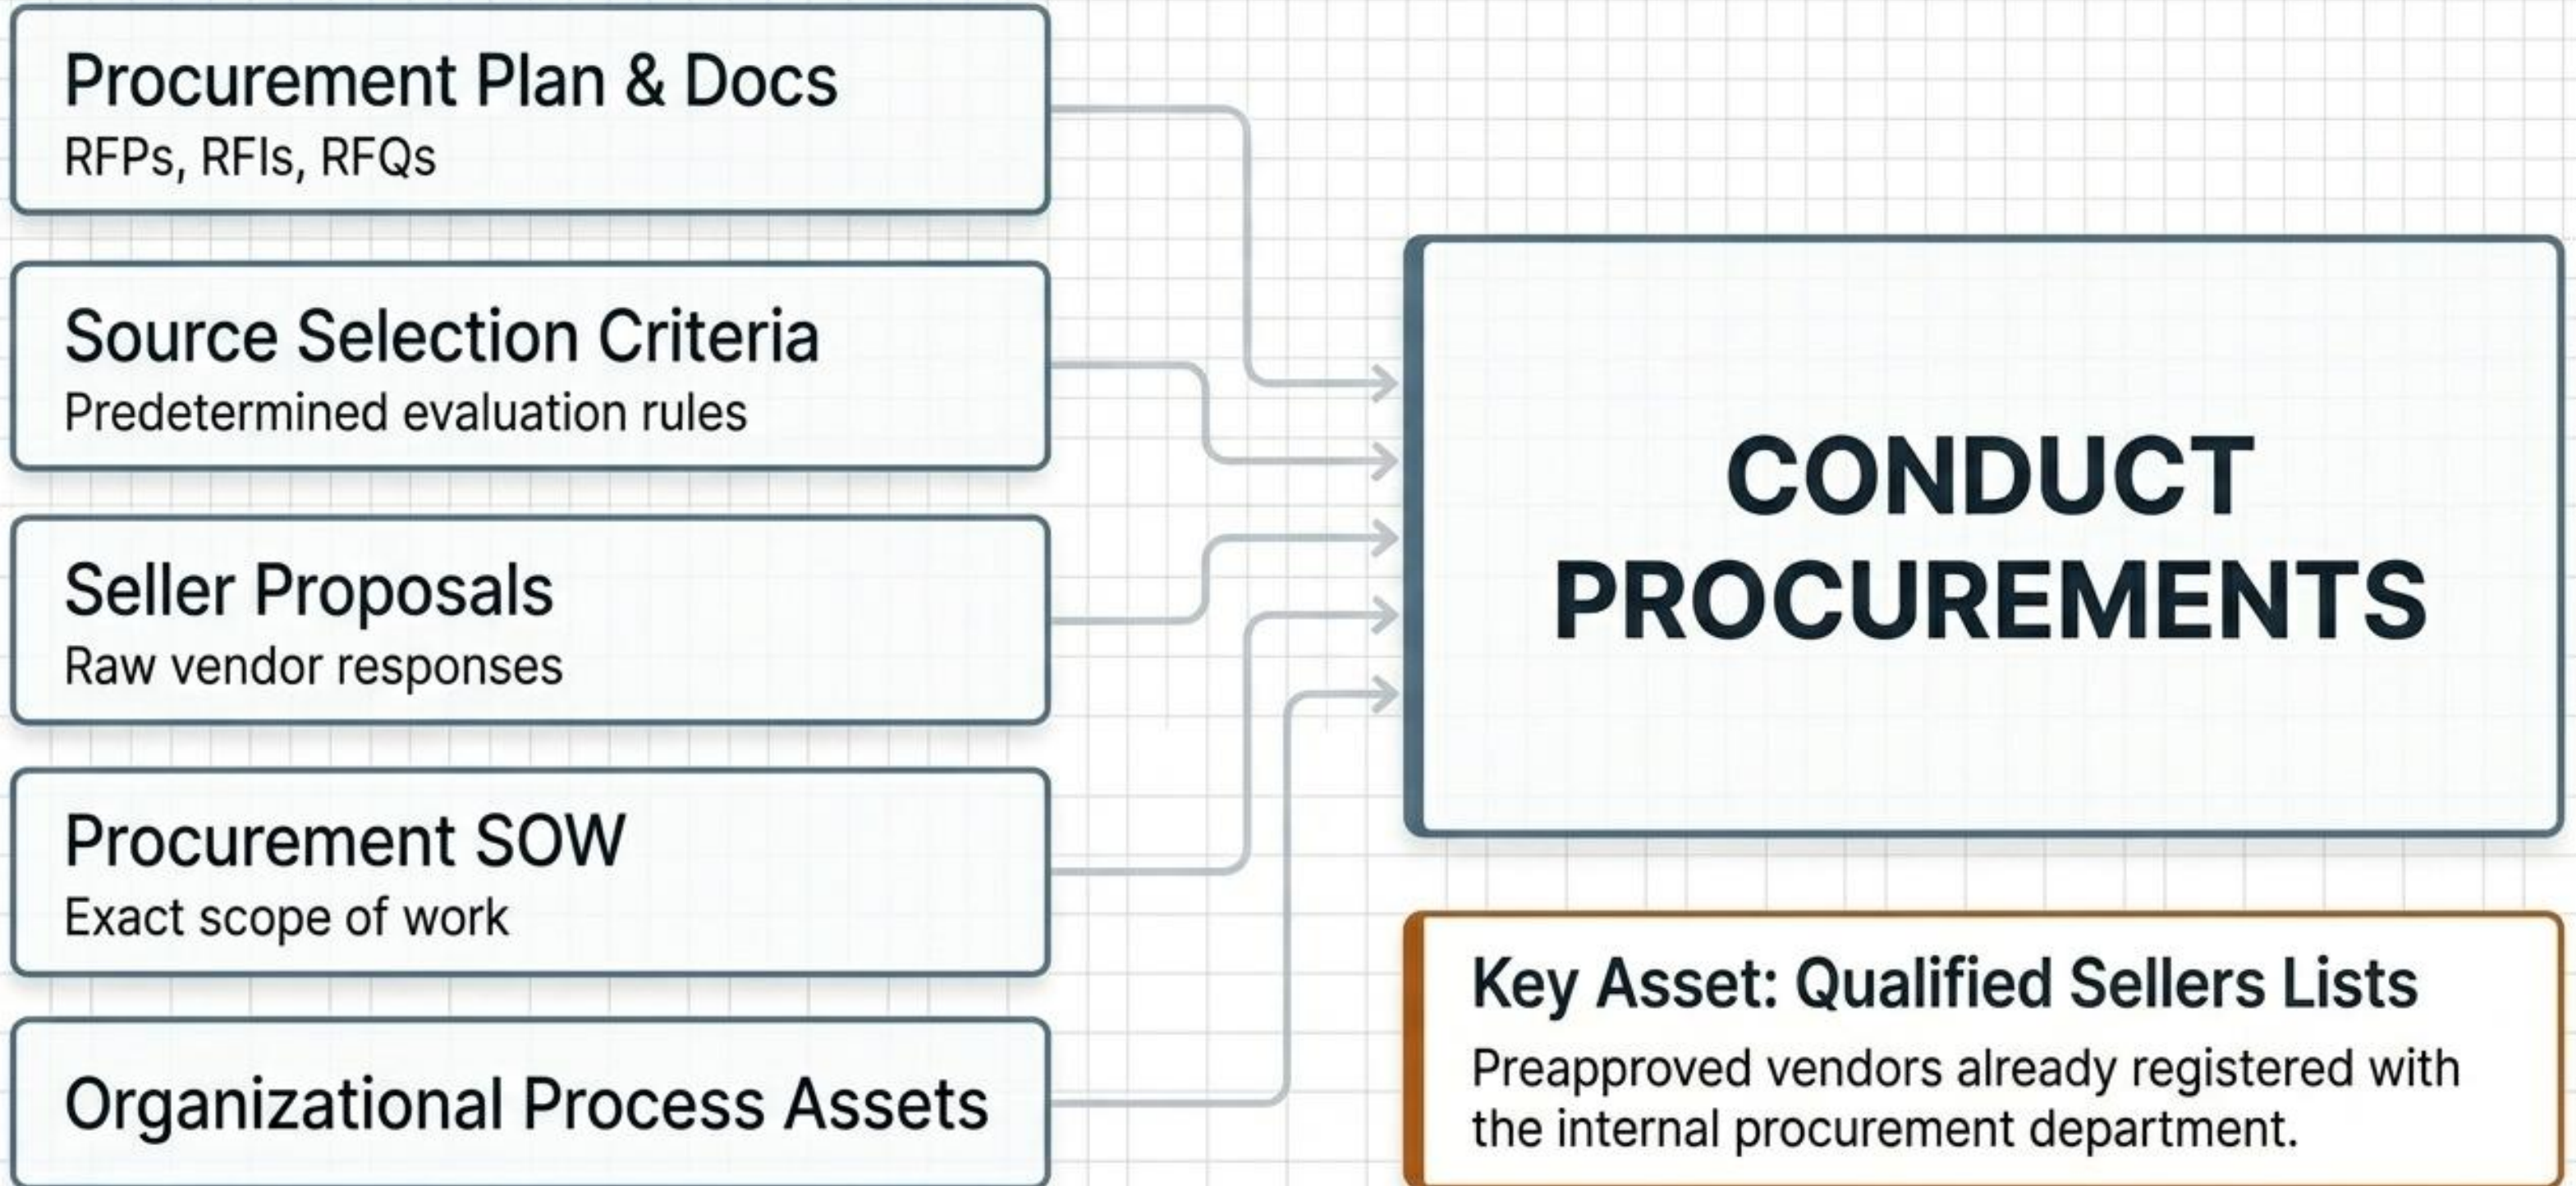

Bidder Conferences Ensure Vendor Equity

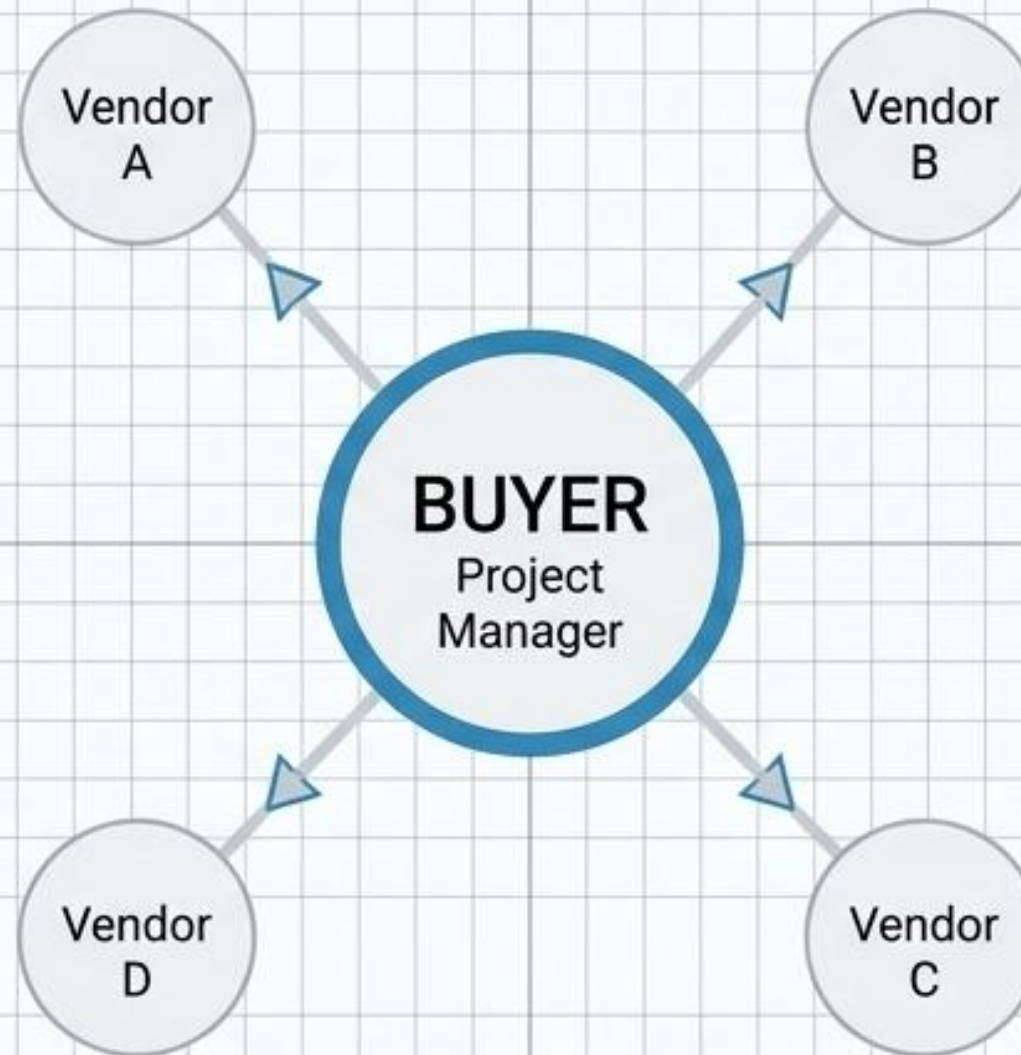


Held once. All vendors attend simultaneously. All questions and answers are restated to the entire group.

Core Purpose: Guarantee all potential vendors have an equal chance at the bid without informational advantages.

Diagnostic Evaluation Systems

	Weighting Systems	Screening Systems	Seller Rating Systems
	Core Mechanism: Assigns numerical weights to criteria, multiplied by scores.	Core Mechanism: Defines minimum baseline requirements.	Core Mechanism: Analyzes historical performance data.
	Primary Use Case: Multiple vendors; ranking proposals to sequence negotiations.	Primary Use Case: Instantly eliminating unsuitable vendors (e.g., lacking certifications).	Primary Use Case: Verifying track records (delivery, compliance).
	Subjectivity Level: Quantifies data to minimize personal bias.	Subjectivity Level: Strictly objective (Pass/Fail).	Subjectivity Level: Empirical, but must be combined with other criteria.

Independent Estimates Identify Critical Disconnects

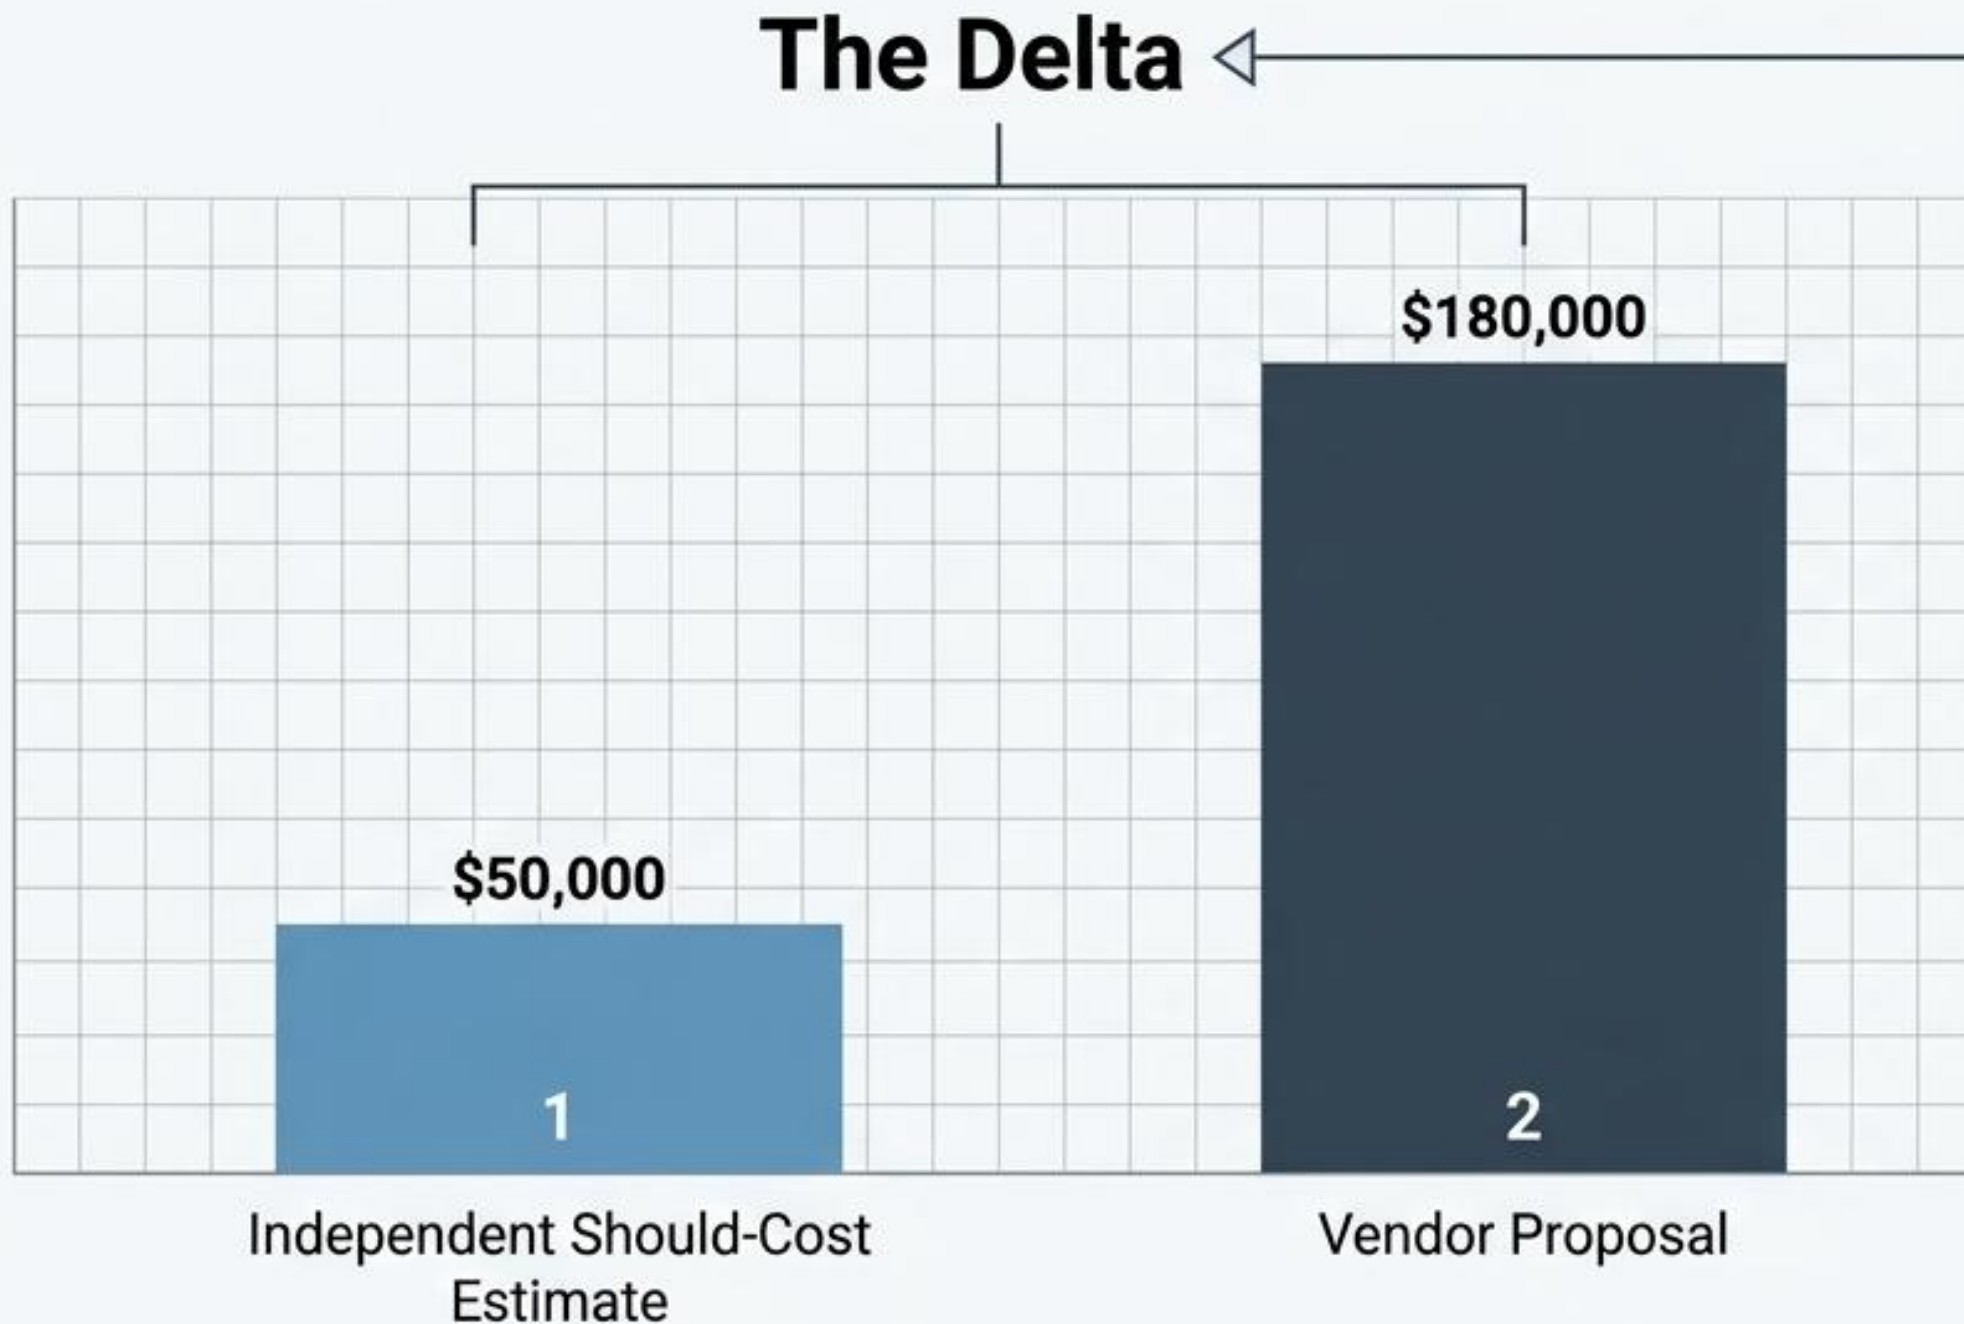

WARNING: A massive gap indicates one of two systemic failures:

1. The Statement of Work (SOW) lacks sufficient detail for accurate pricing.
2. The vendor fundamentally misunderstood the contract requirements.

Supplementary Vendor Verification Tools



Physical Samples (The Quality Check)

Requesting tangible products to test against project needs (e.g., security-thread paper with non-erasable ink).



Financial Records (The Solvency Check)

Verifying the vendor has the fiscal stability to purchase required equipment and survive the project lifecycle without bankruptcy.



Analytical Techniques (The Capability Check)

Internet searches to audit past performance, forecast future performance, and research industry reputation prior to high-risk procurements.

Applied Evaluation: Fitness Counts HR System



Project Manager: Amanda Jacobson

Project Brief

Objective:

Convert nationwide HR data management system.

Screening Criteria Passed:

4 vendors demonstrated prior experience with similar projects.

RFP Requirements (The Weighting Criteria):

Platform compatibility (Weight: 5)



Hardware standards (Weight: 4)



Data conversion included (Weight: 5)



Custom modules & training (Weight: 4)



Calculating the Weighted Scoring Model

$(\text{Raw Score}) \times (\text{Weighting Factor}) = \text{Weighted Score}$

	Platform (x5)	Hardware (x4)	Data Conversion (x5)	Custom Modules (x4)	TOTAL SCORE
Vendor A	15	12	15	16	58
Vendor B	10	12	20	12	54
Vendor C	20	16	20	12	68
Vendor D	15	12	10	16	53

Clear Winner:
Highest aggregate
score dictates the
sequence of final
negotiations.

Recognizing the 'Fait Accompli' Negotiation Tactic

Step 1: The Claim (Distraction)



The vendor claims an issue is non-negotiable and cannot be changed (e.g., "Our key resource will be reassigned elsewhere if we don't start immediately.").

Step 2: The Hidden Reality




The vendor actually has the ability to reserve the resource, but conceals this fact from the buyer.

Step 3: The Intended Outcome




Forced urgency. The buyer is pressured into hiring the resource sooner than planned, bypassing standard negotiation.

Generating the Procurement Outputs

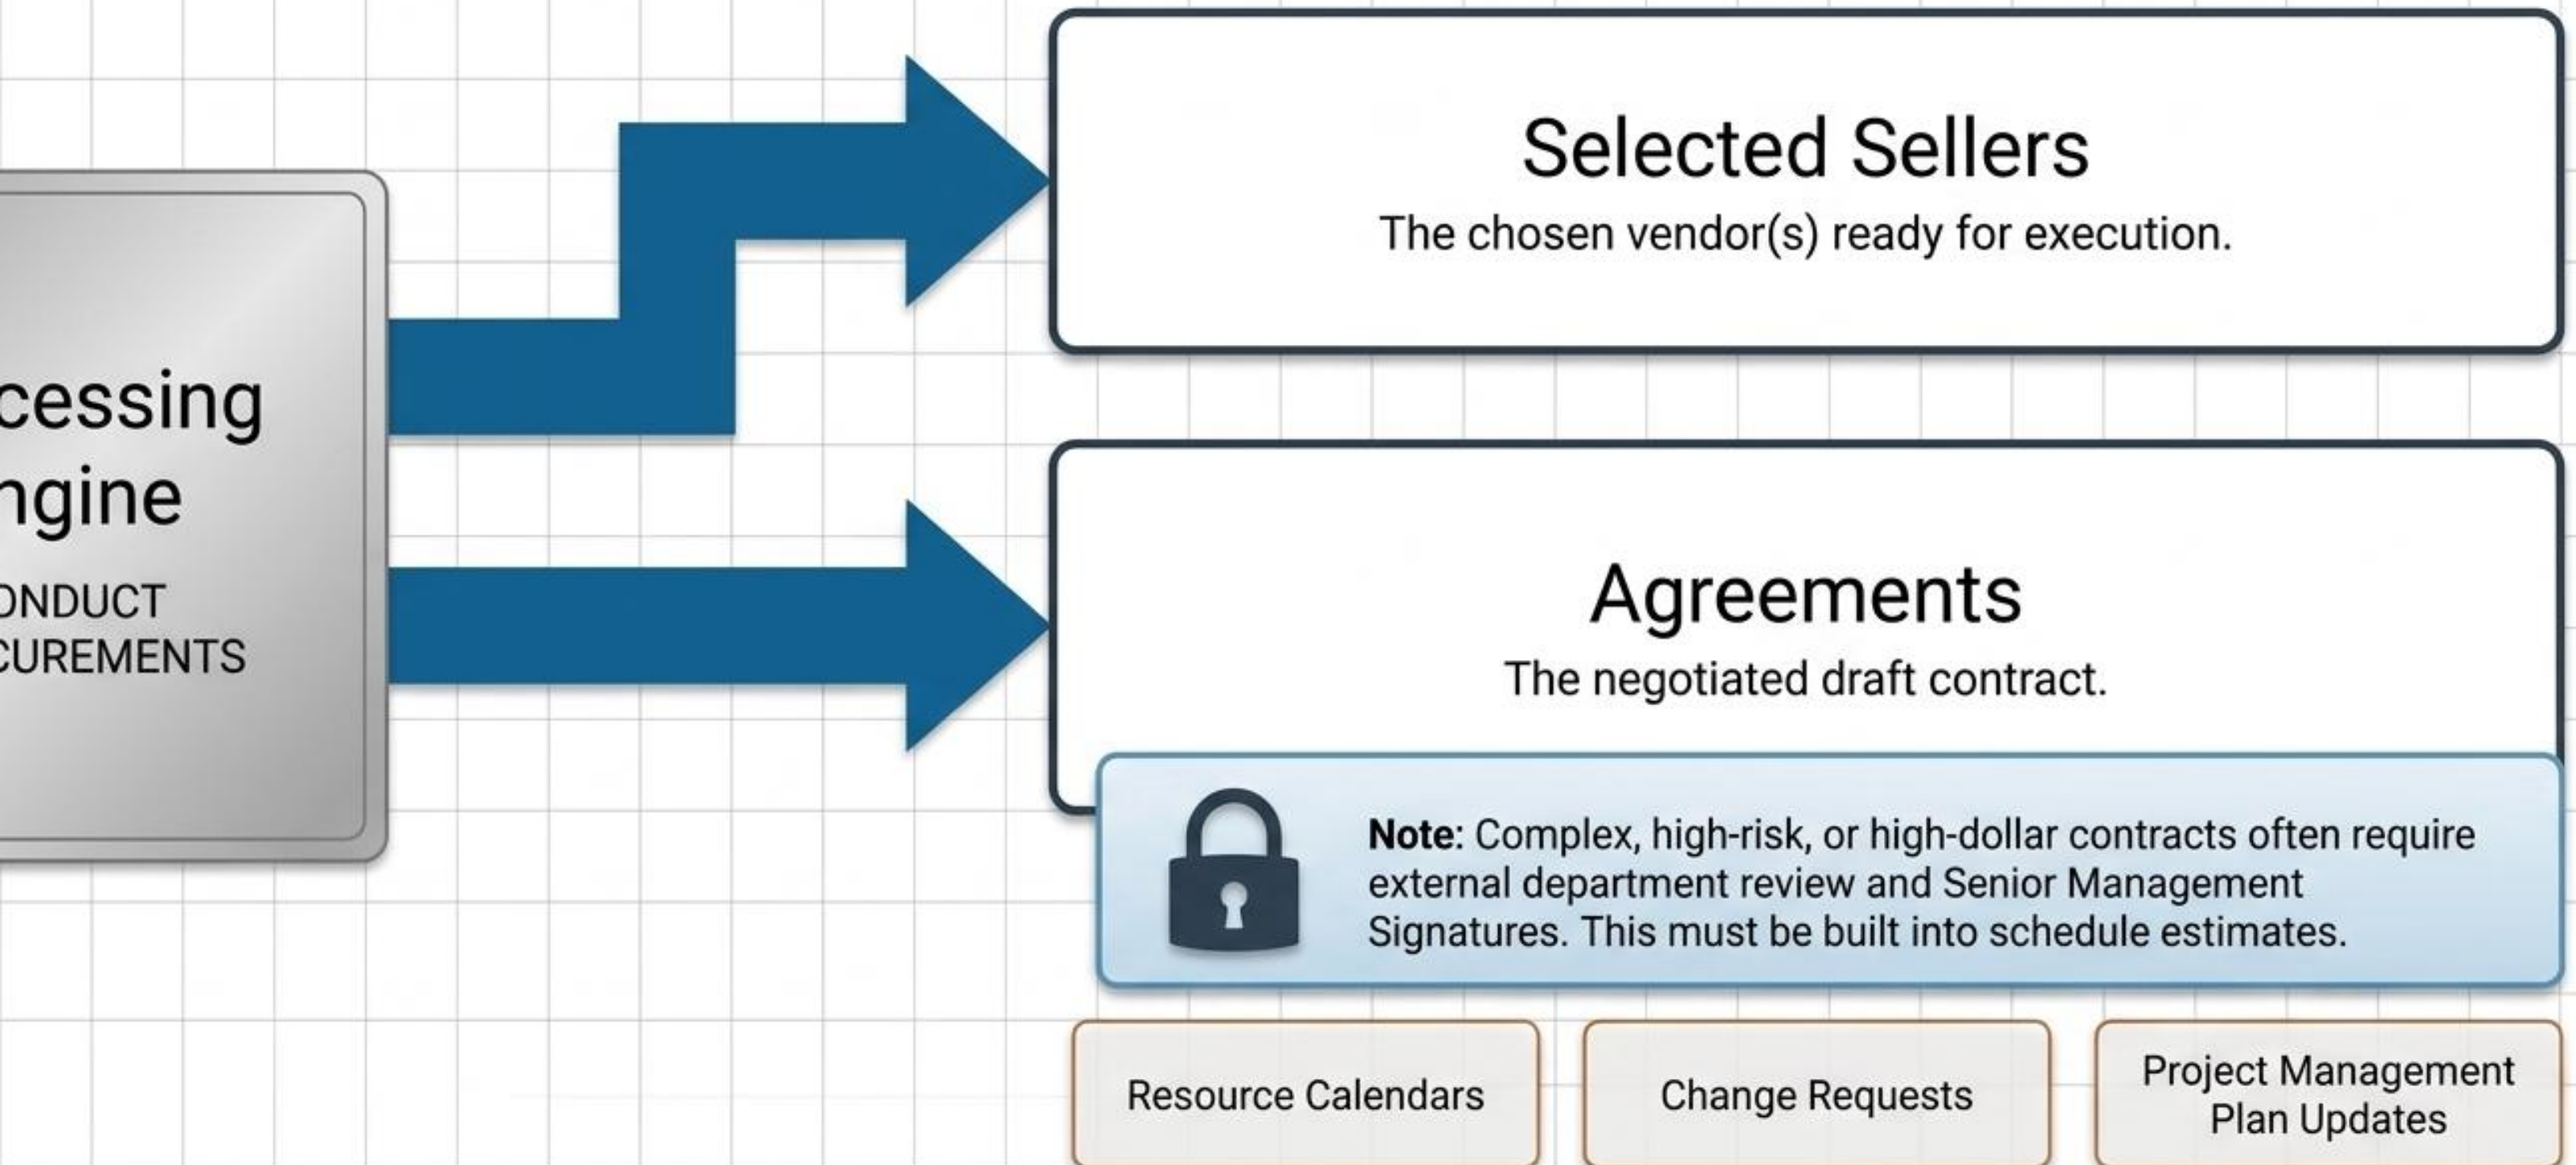

The Architecture of a Procurement Agreement

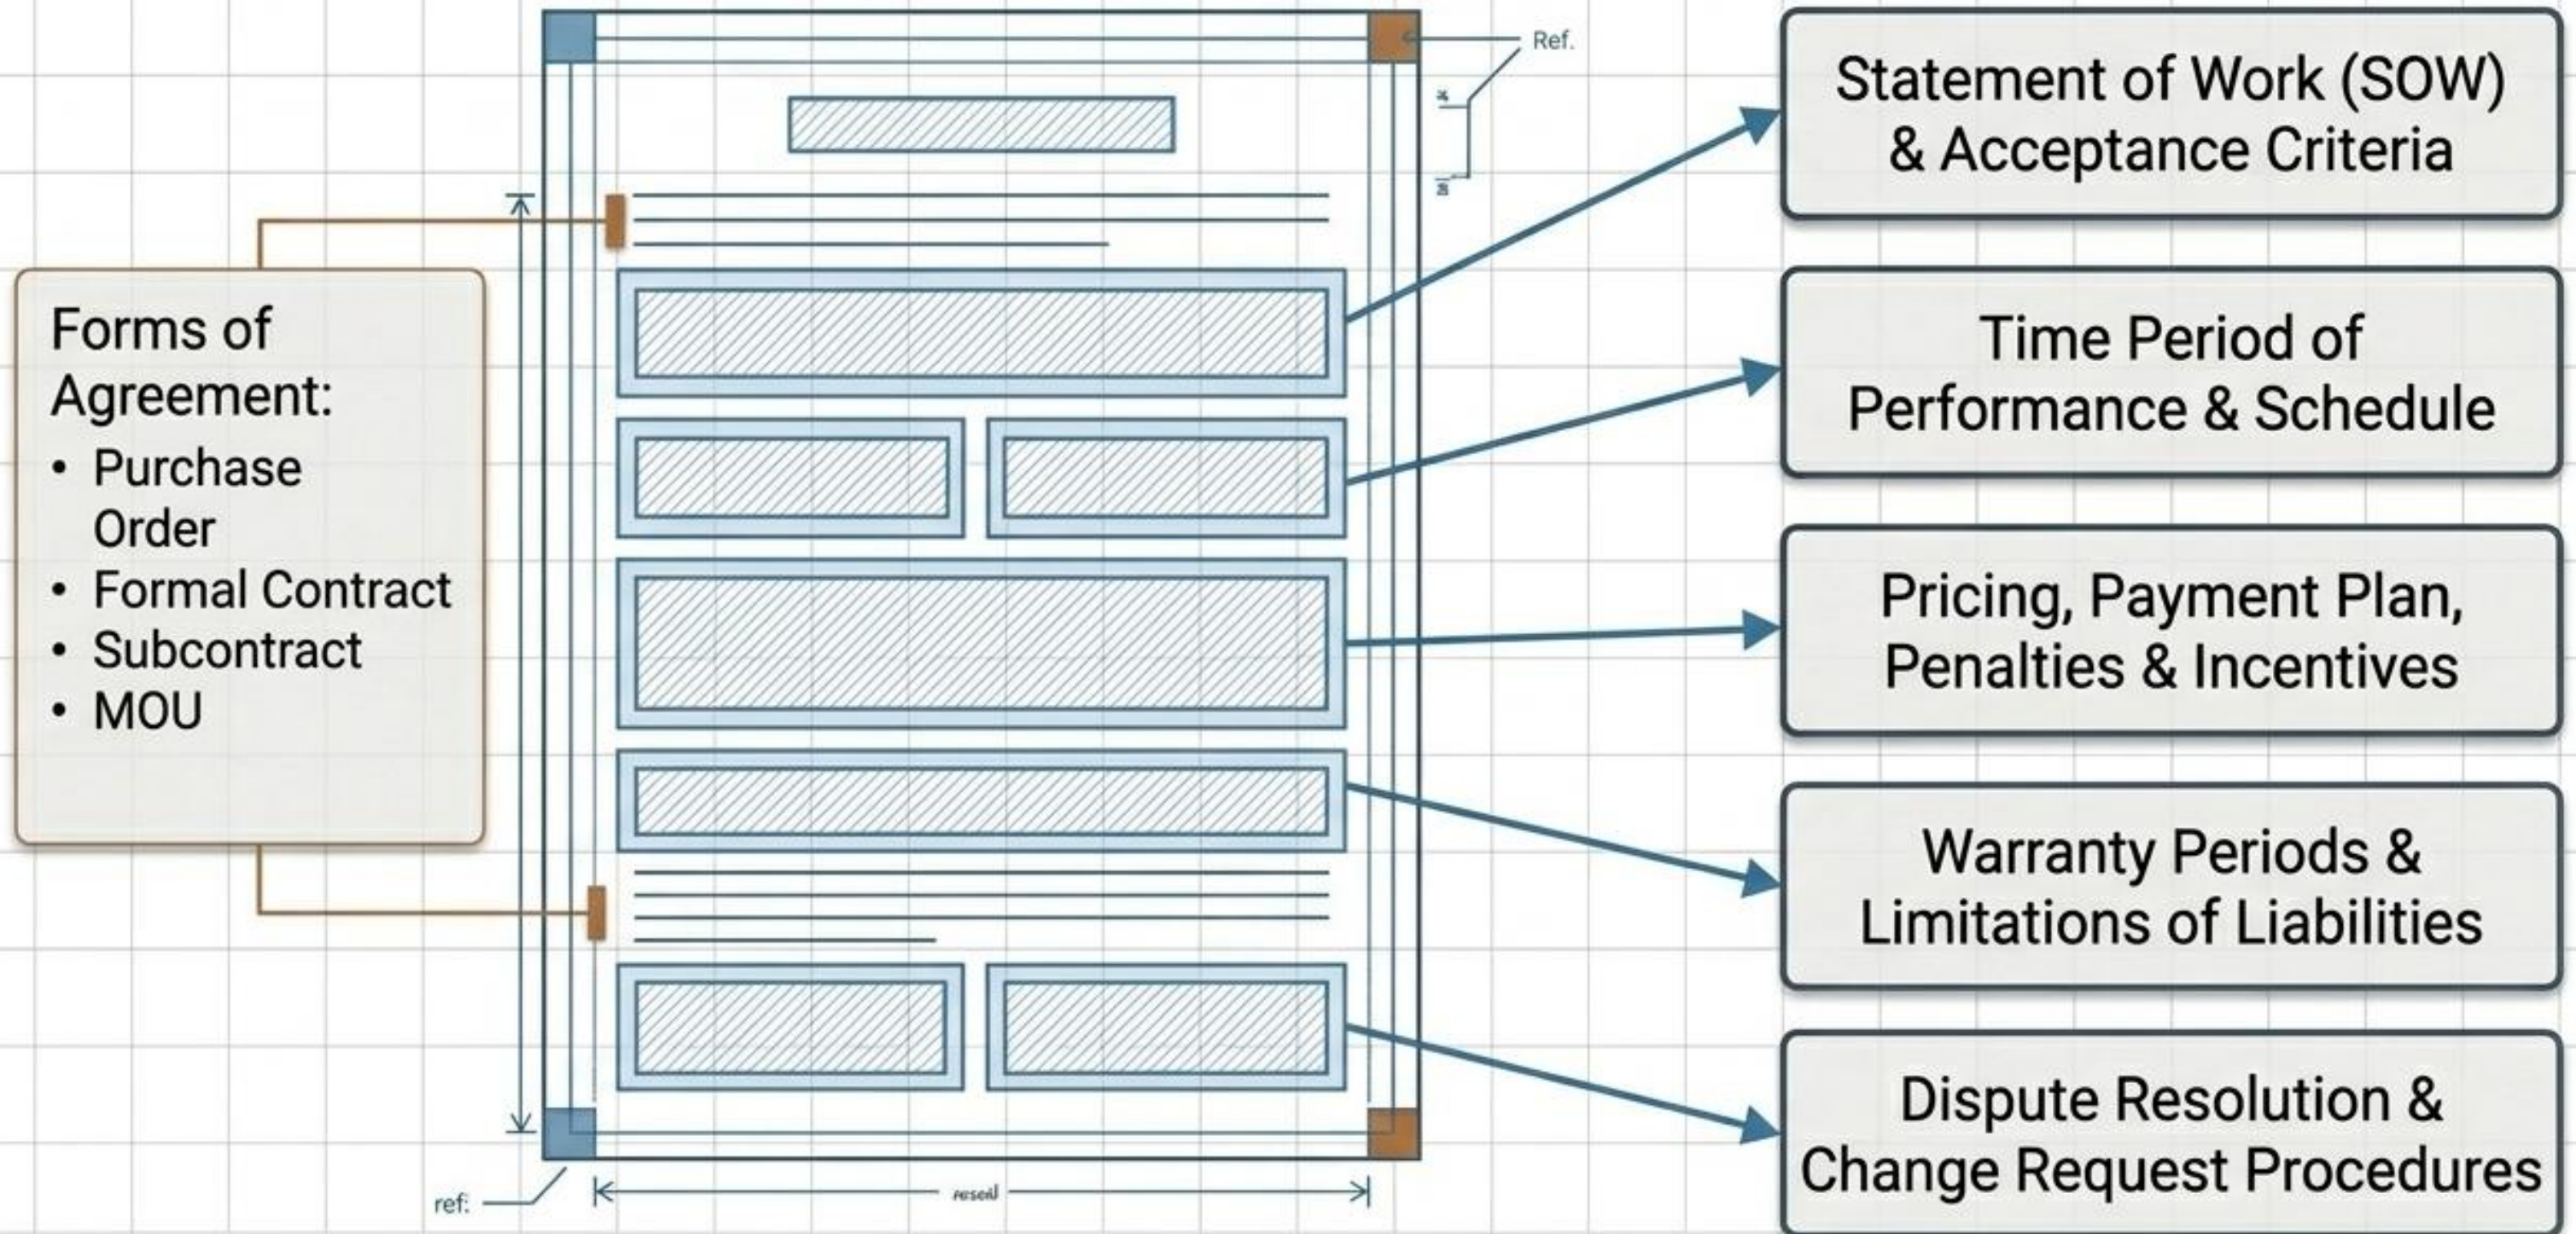

Synthesis: Mapping Contract Lifecycles to PMBOK®

