


# Certyfikat PMP: WBS Process


The Architecture of Project Planning: Subdividing scope into manageable, actionable components.



Author:  
dr Zbigniew Galar

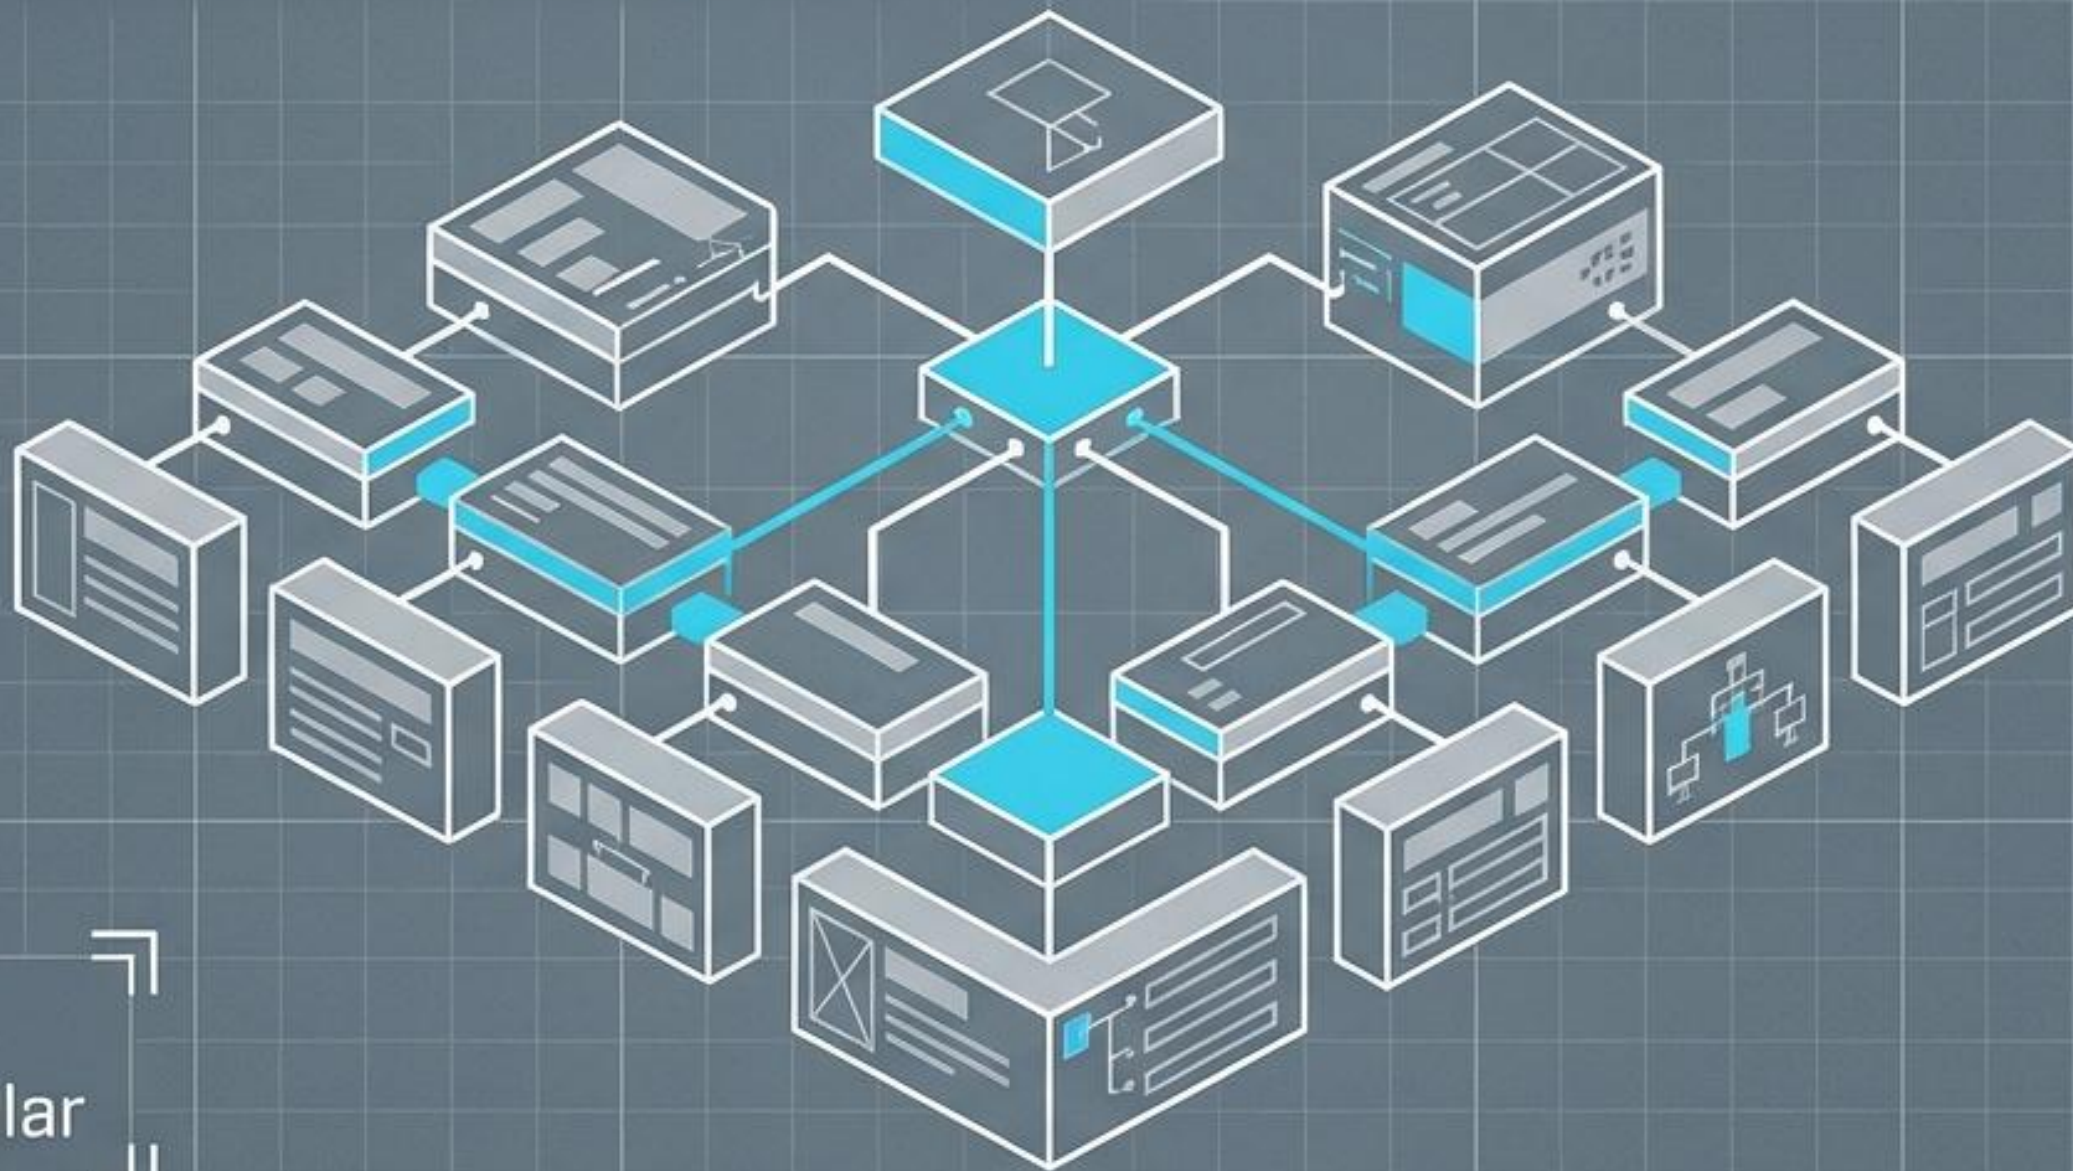


# The WBS bridges scope and execution

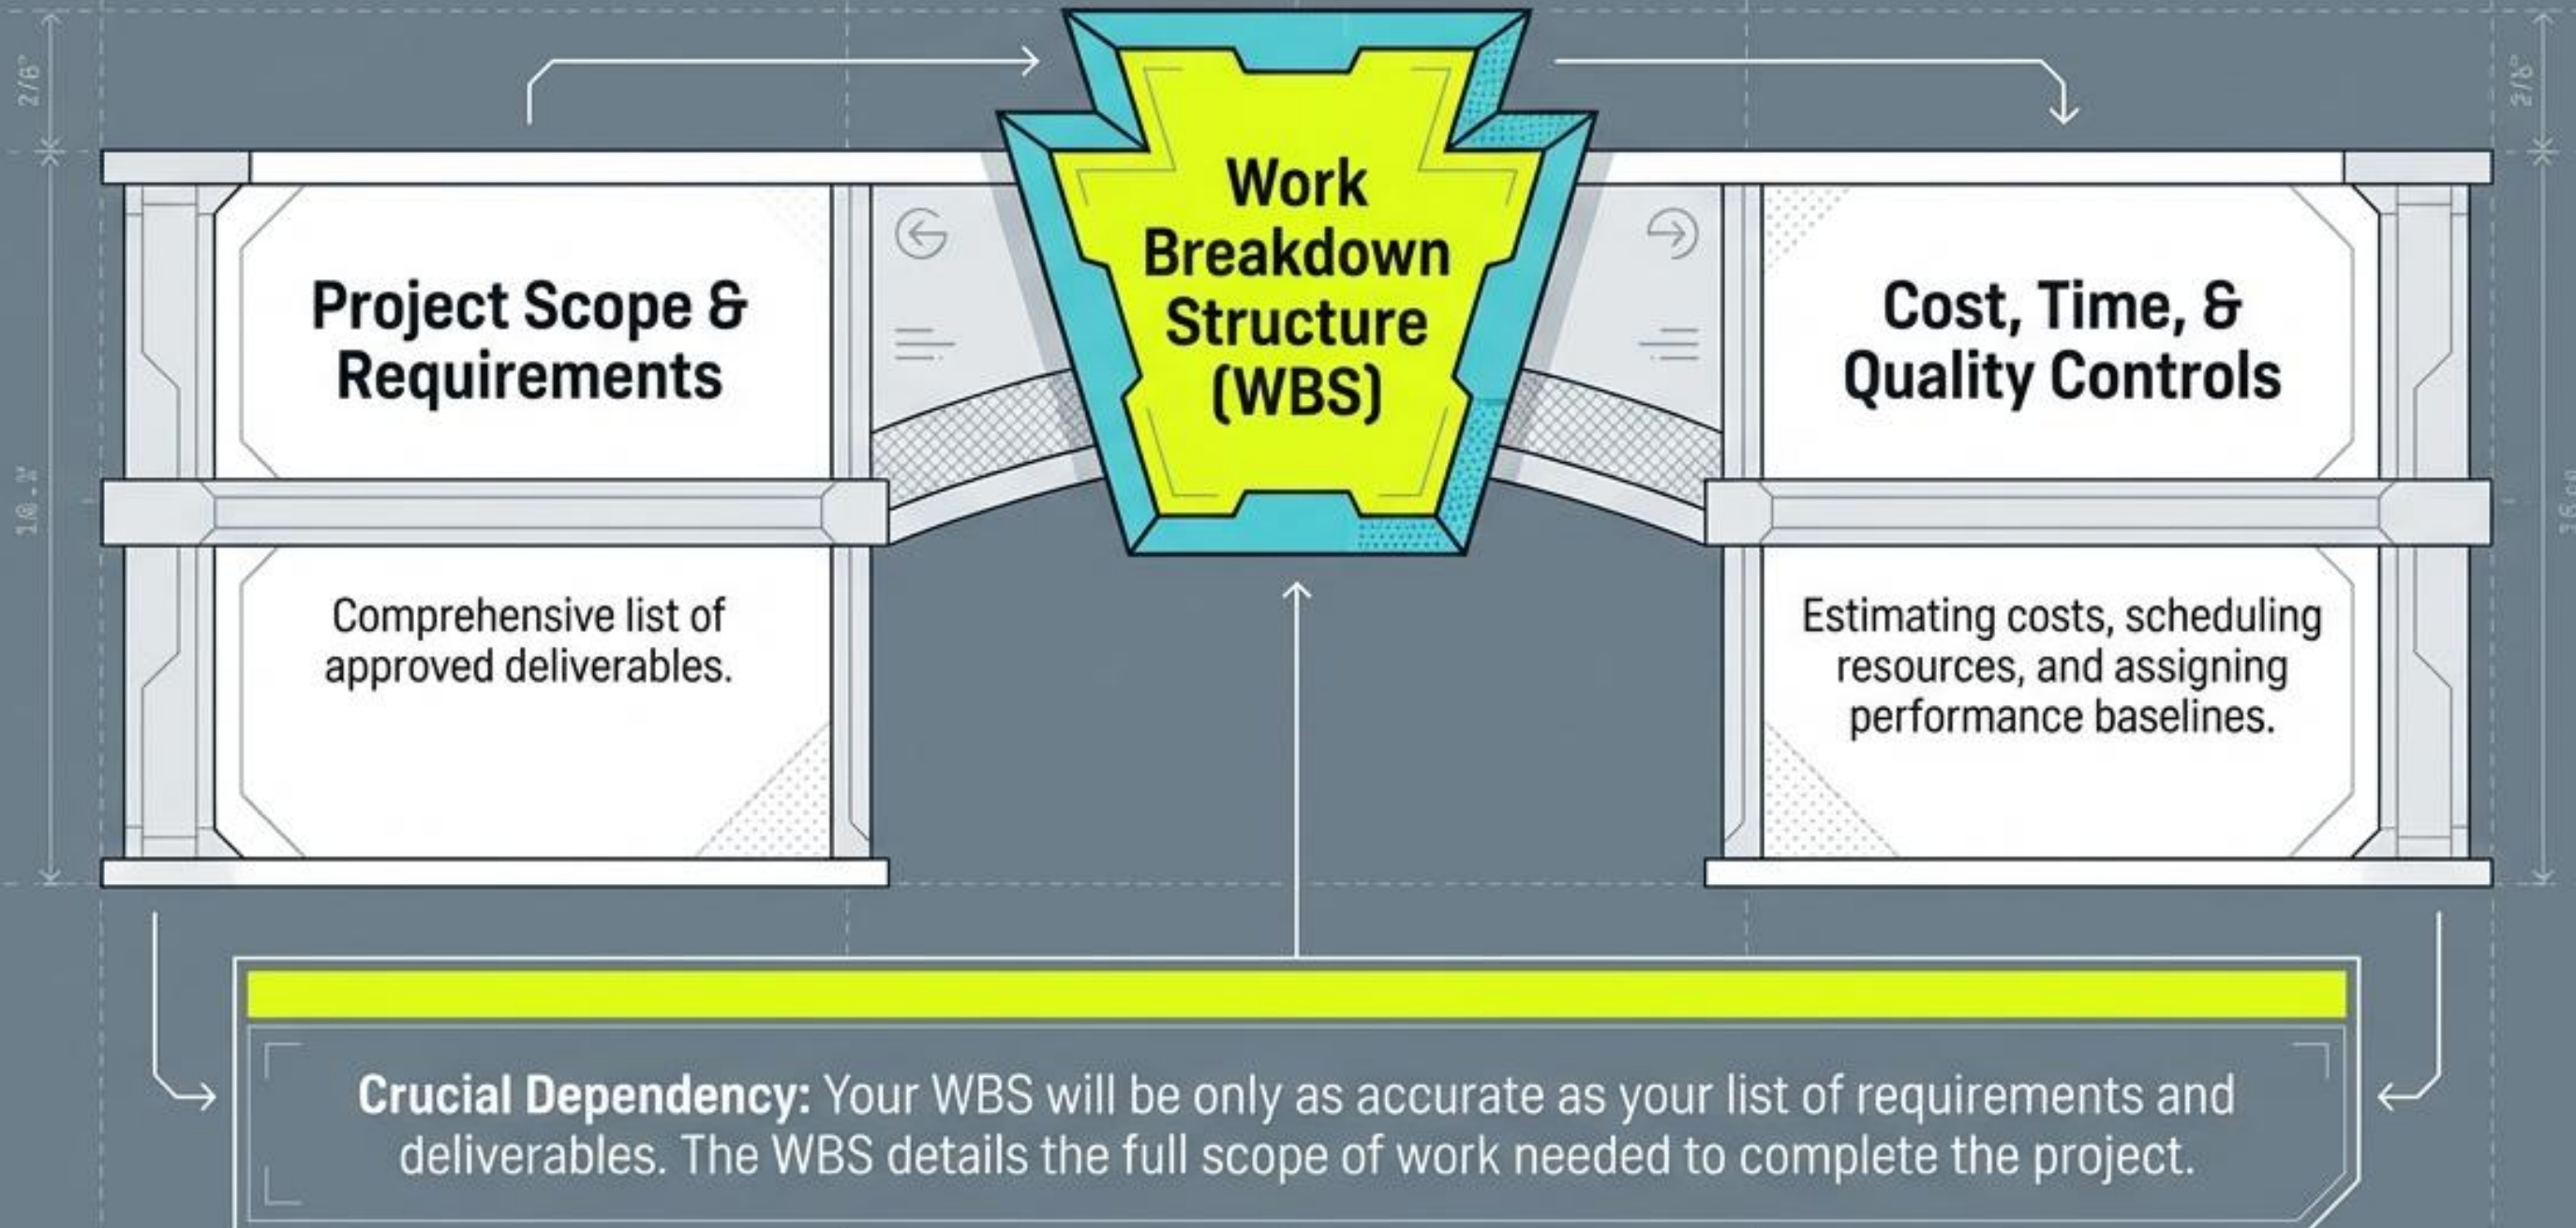



# Navigating the PMBOK® Process Architecture

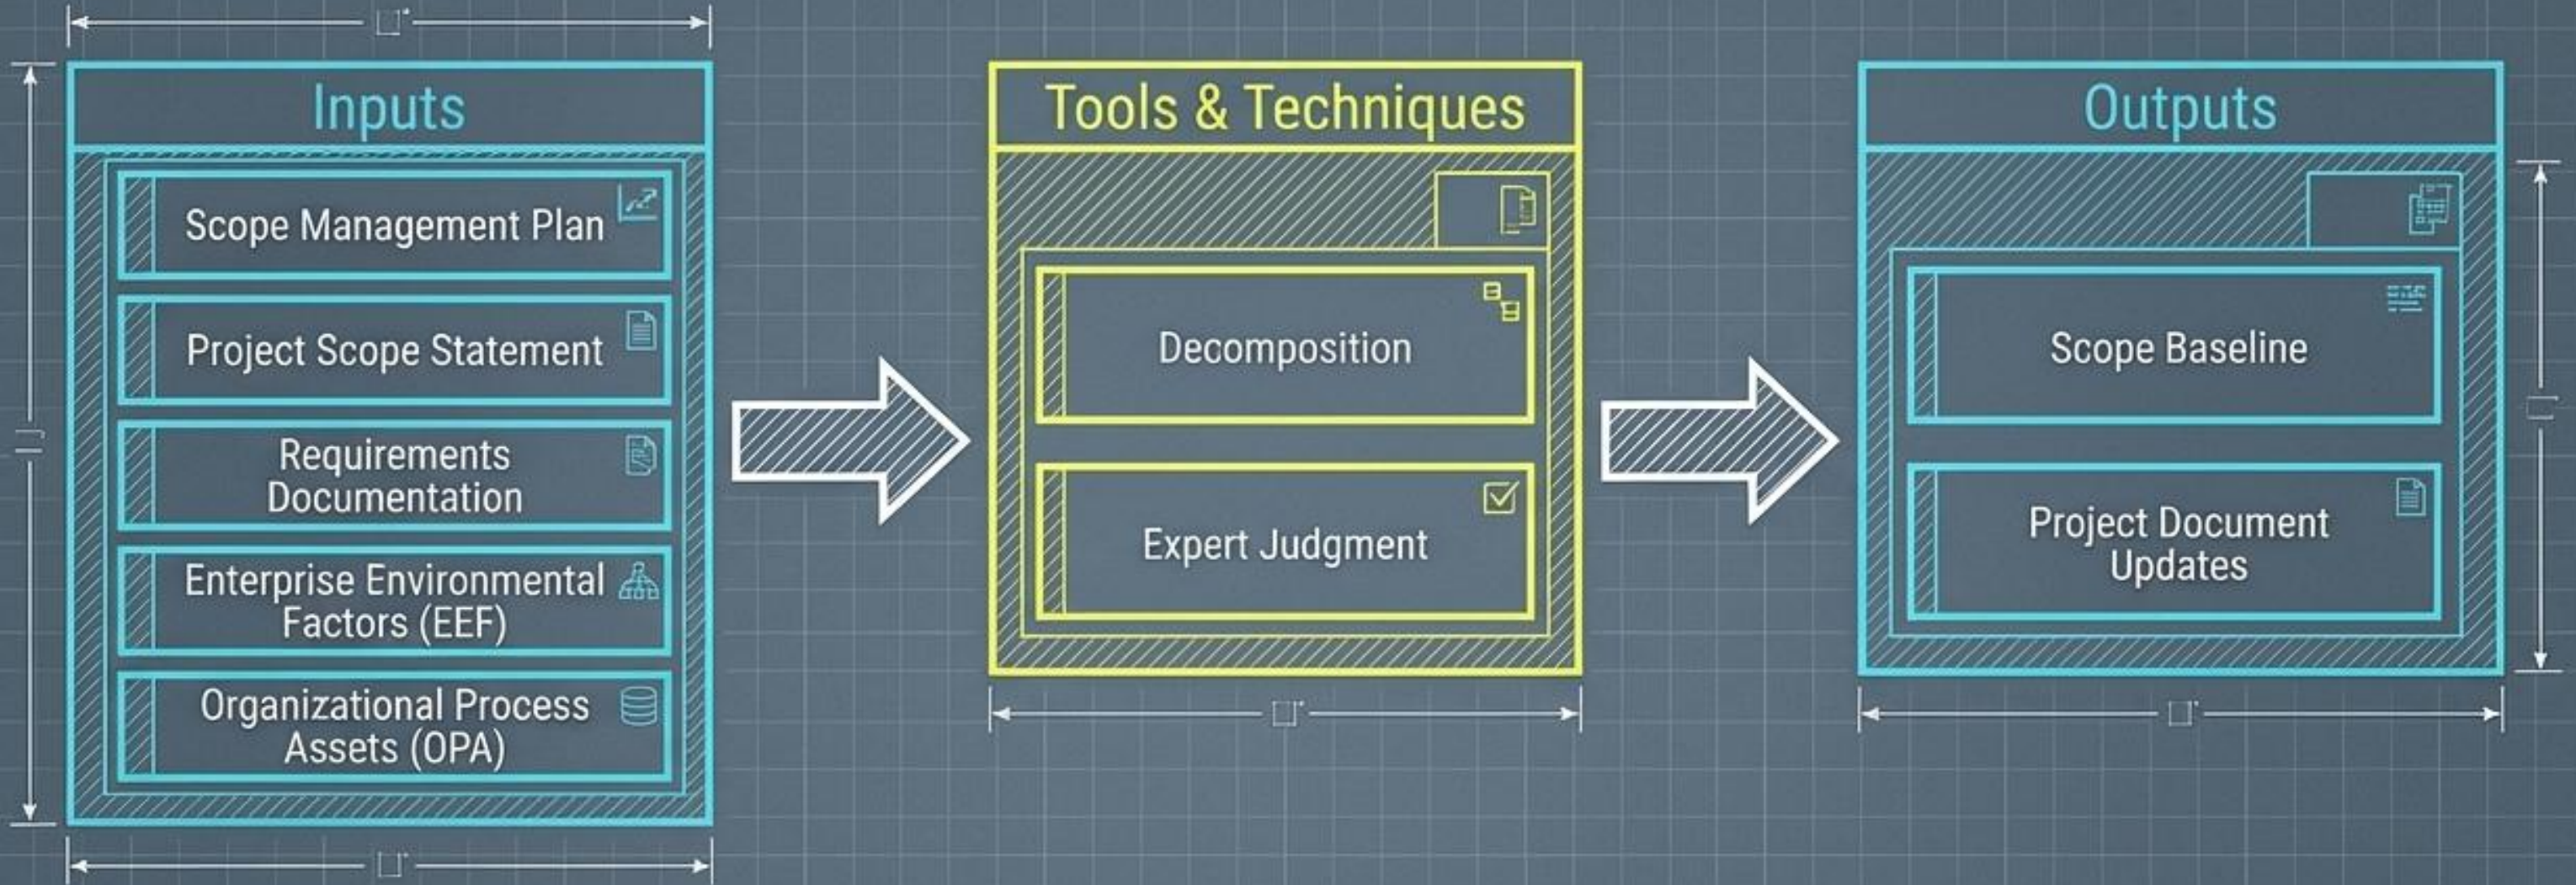


## Key Insight Banner

The approved Project Scope Statement is the primary foundation used to define and organize the work in the WBS. Make certain you are using the most current version.



# The Art of Decomposition: Breaking Down the Deliverables

Transforming broad deliverables into manageable units that can be easily planned, executed, monitored, and controlled.

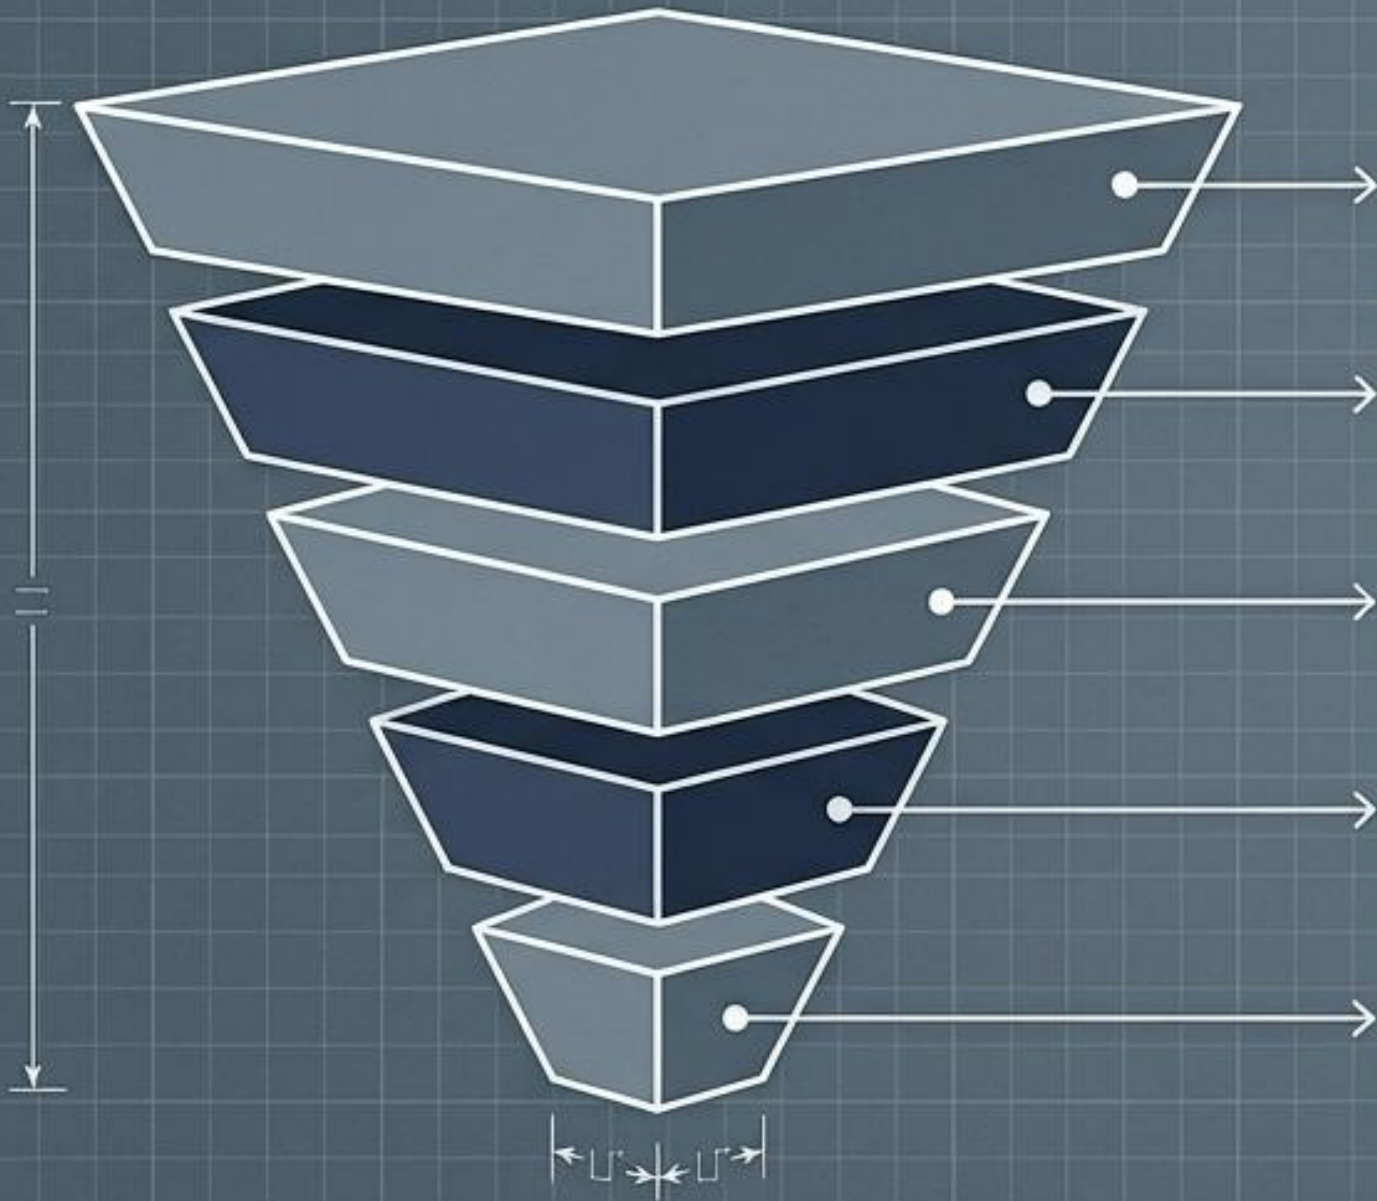

1. **Identify** deliverables and work.

2. **Organize** the WBS structure.


3. **Decompose** into lower-level, tangible components.

4. Assign unique identification codes.

5. Verify clarity, completeness, and necessity.




# Three frameworks for Level-1 decomposition

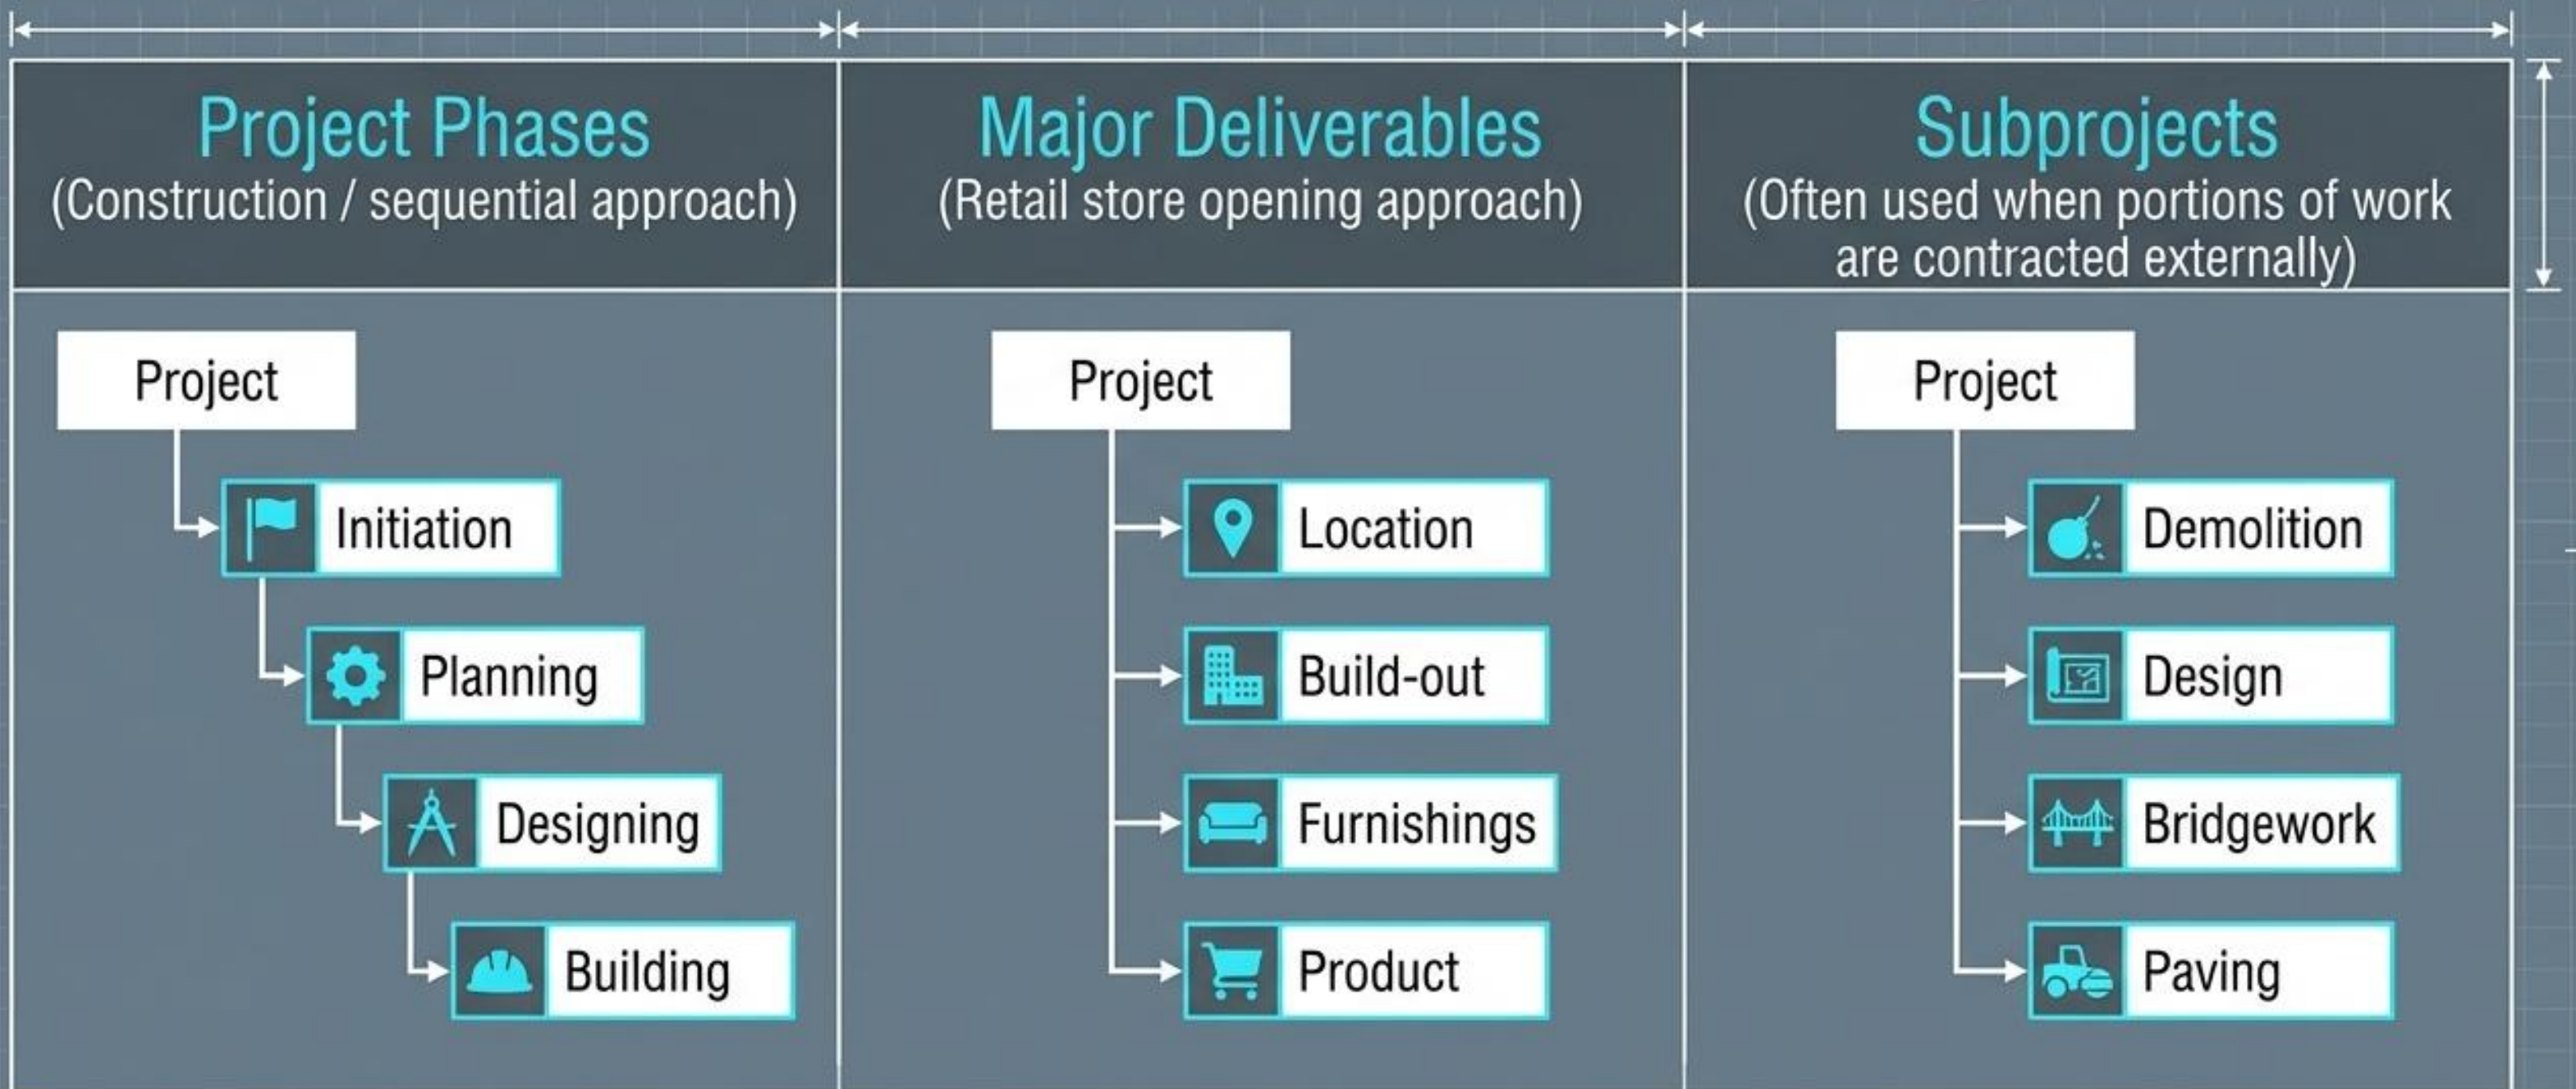

There is no single "right" way. The structure must reflect how the specific project will be managed.




# Anatomy of a WBS: The Macro View

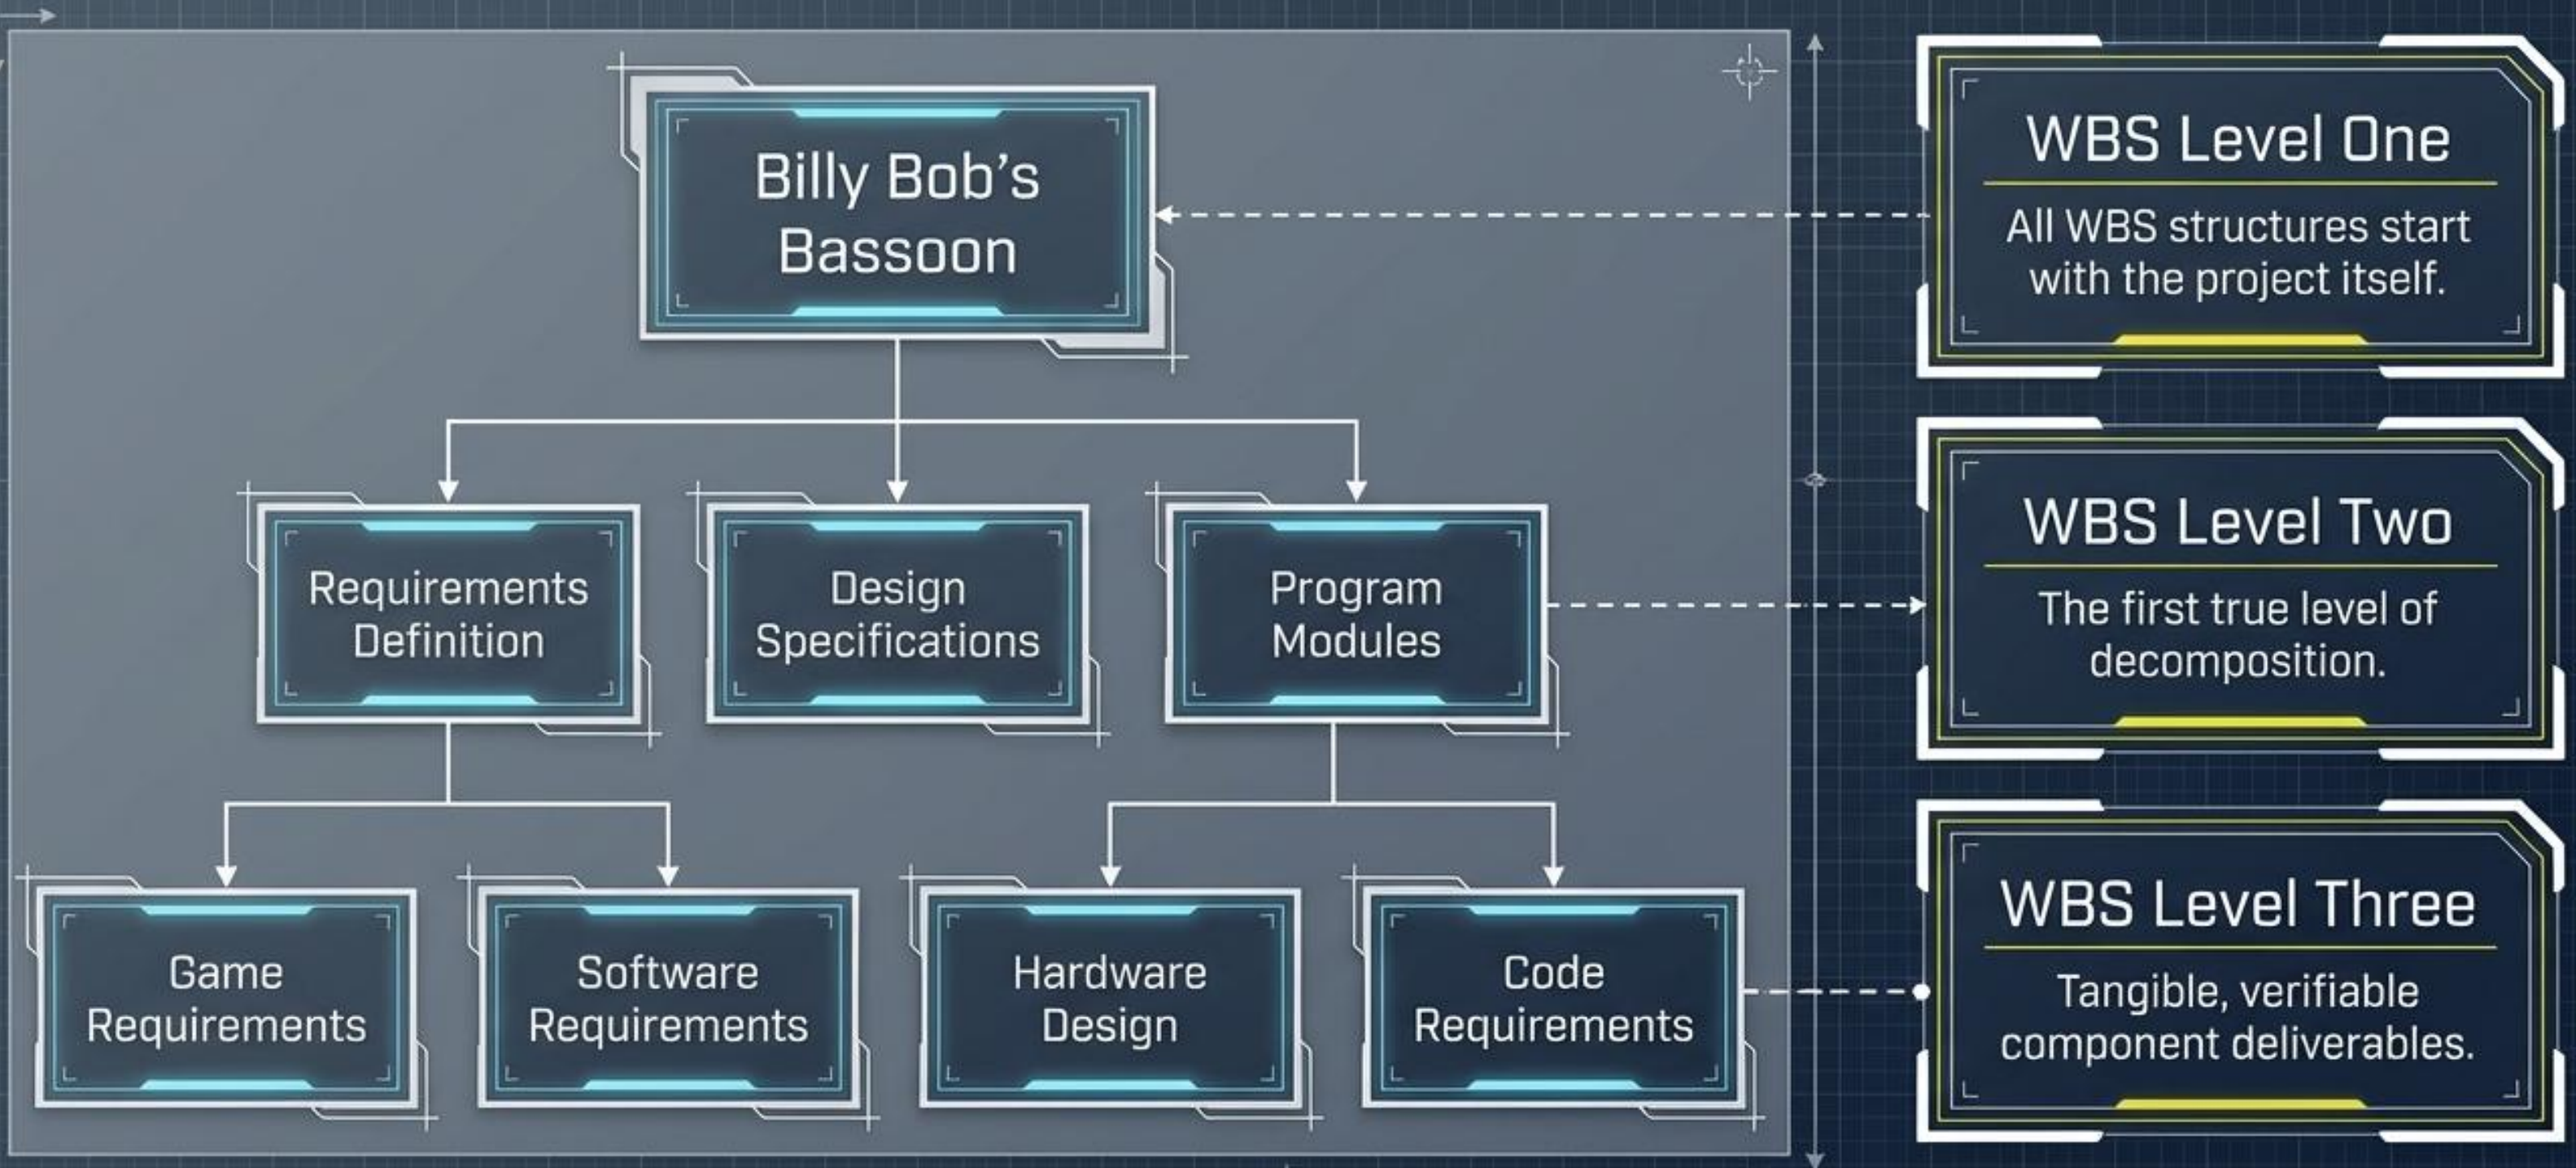



# The Micro View: Defining the Work Package

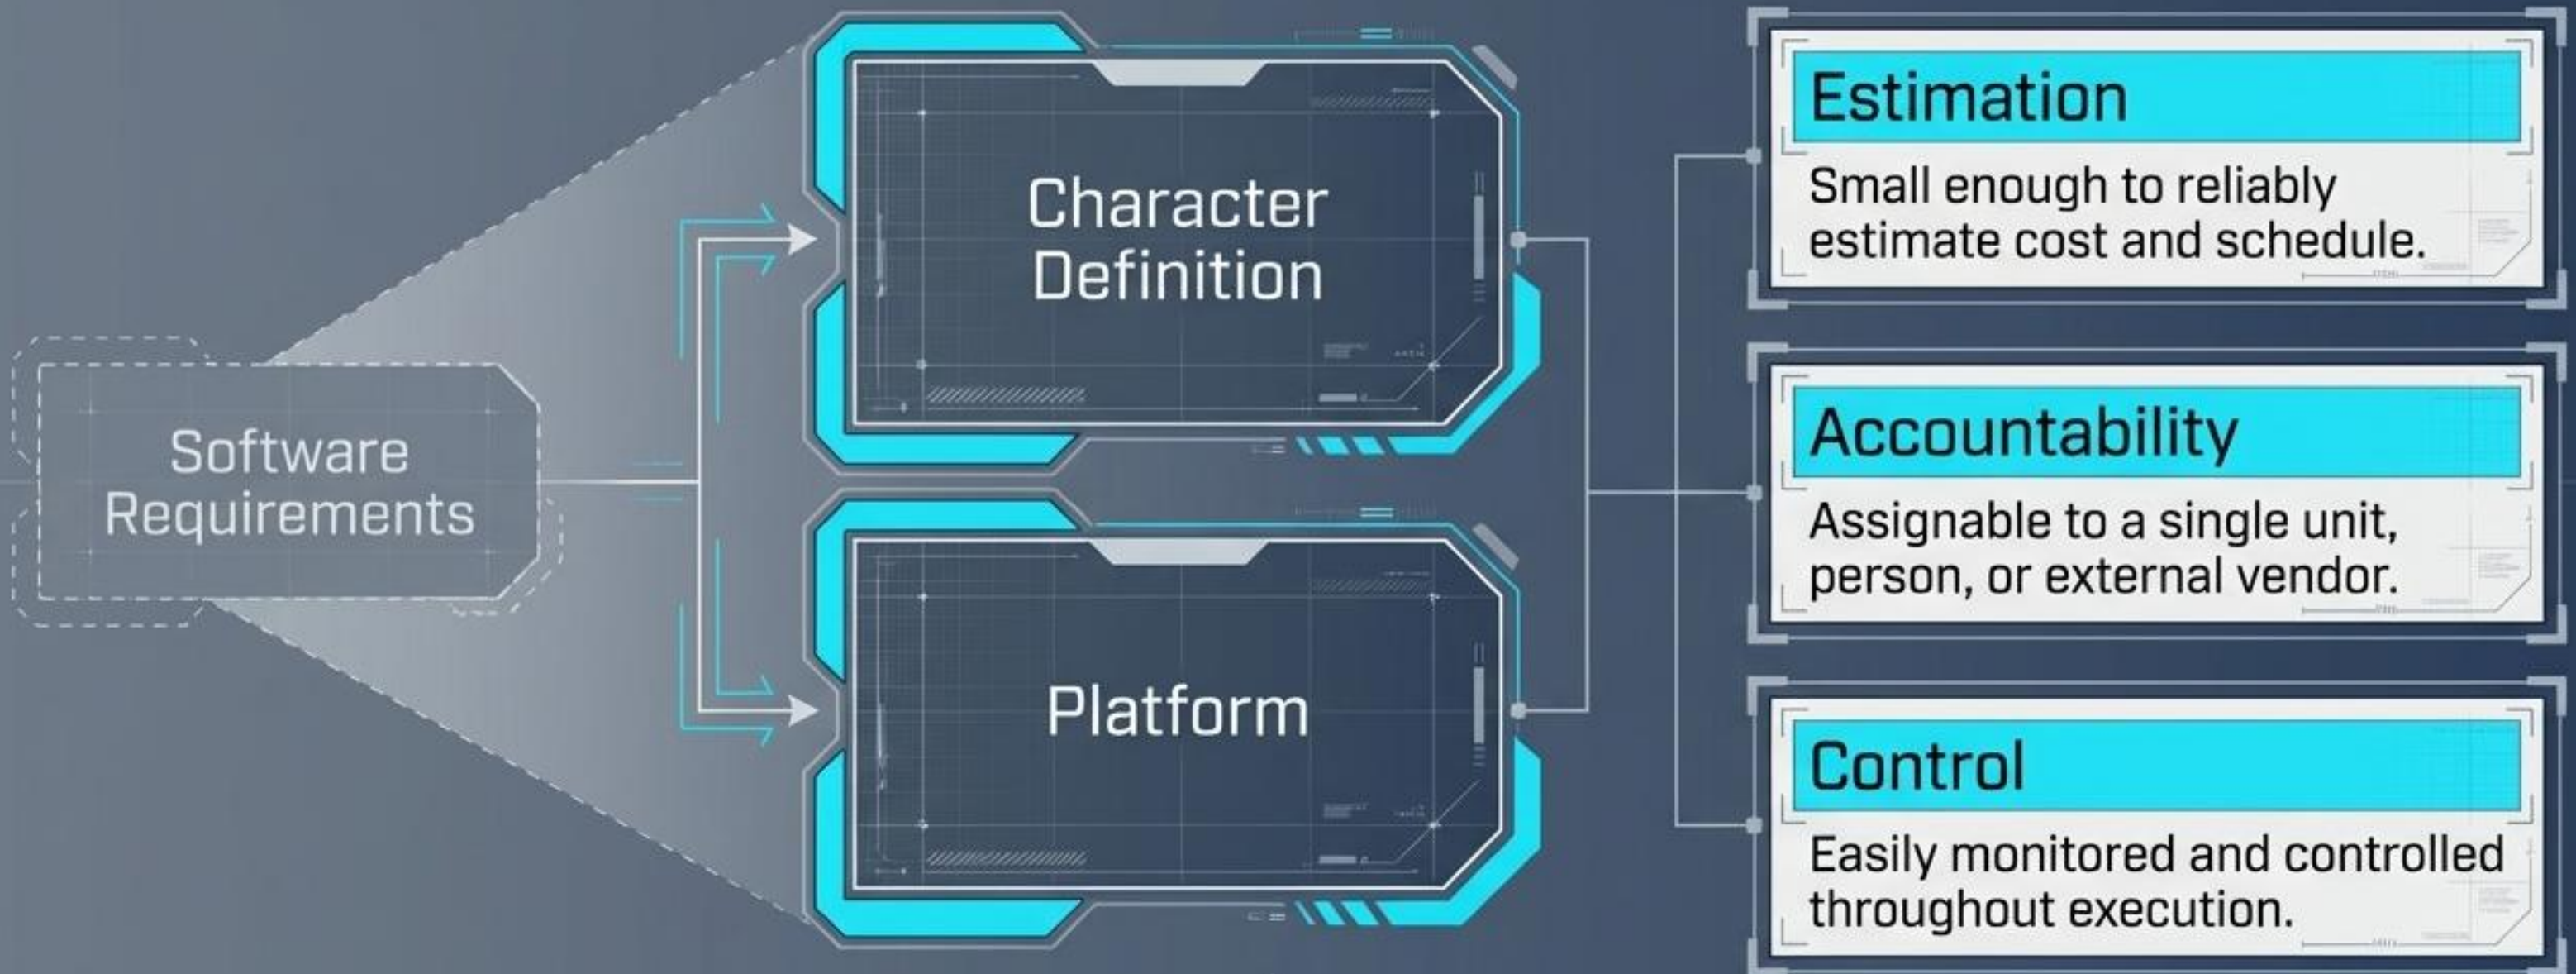


The lowest level of any WBS is always the Work Package. If you decompose to the point of listing individual activities, you have gone too far.




# The Golden Rules of WBS Construction

## The 100-Percent Rule.



Collectively, all levels roll up to the top. The WBS captures *all* project work. If a work package is not on the WBS, it is not in the project. No additional work is added.

## Nouns, Not Verbs.

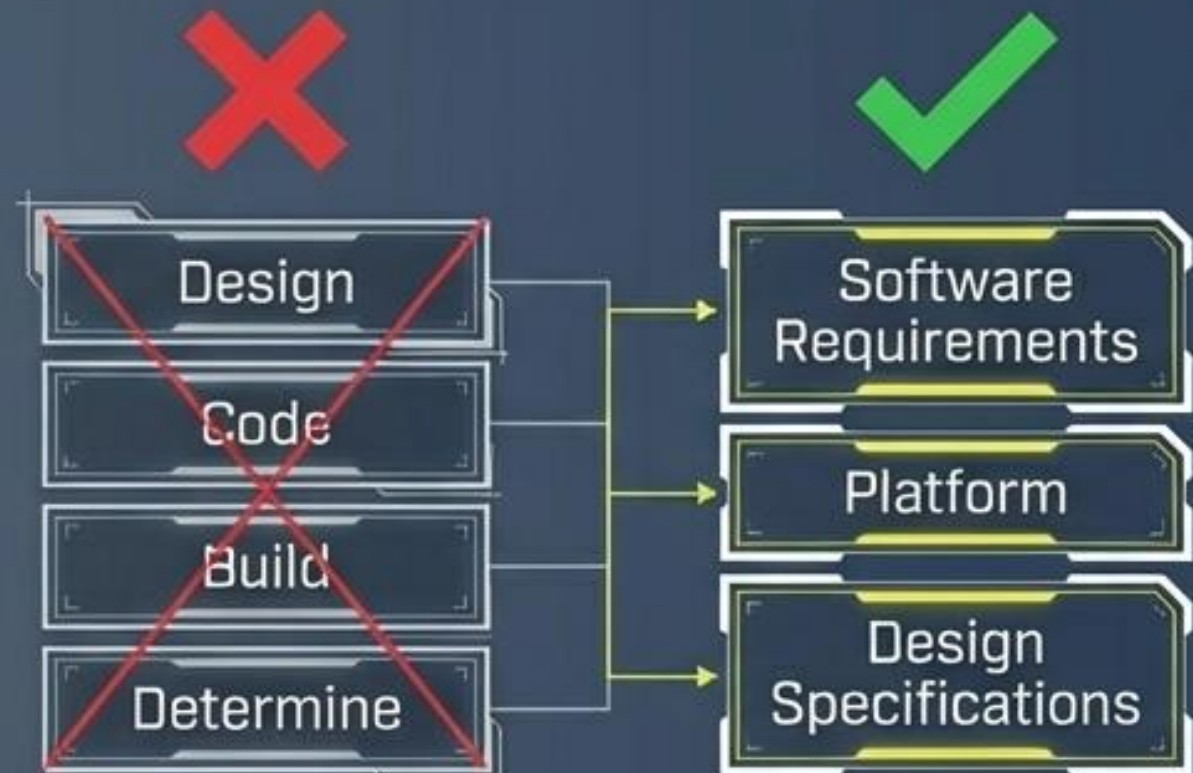


Large, complex projects do not include activities on the WBS. Deliverables are nouns [things]. Activities are verbs [actions], which are decomposed later during the Define Activities process.



# Handling uncertainty with Rolling Wave Planning


Elaborate the work to the level of detail known at the time.

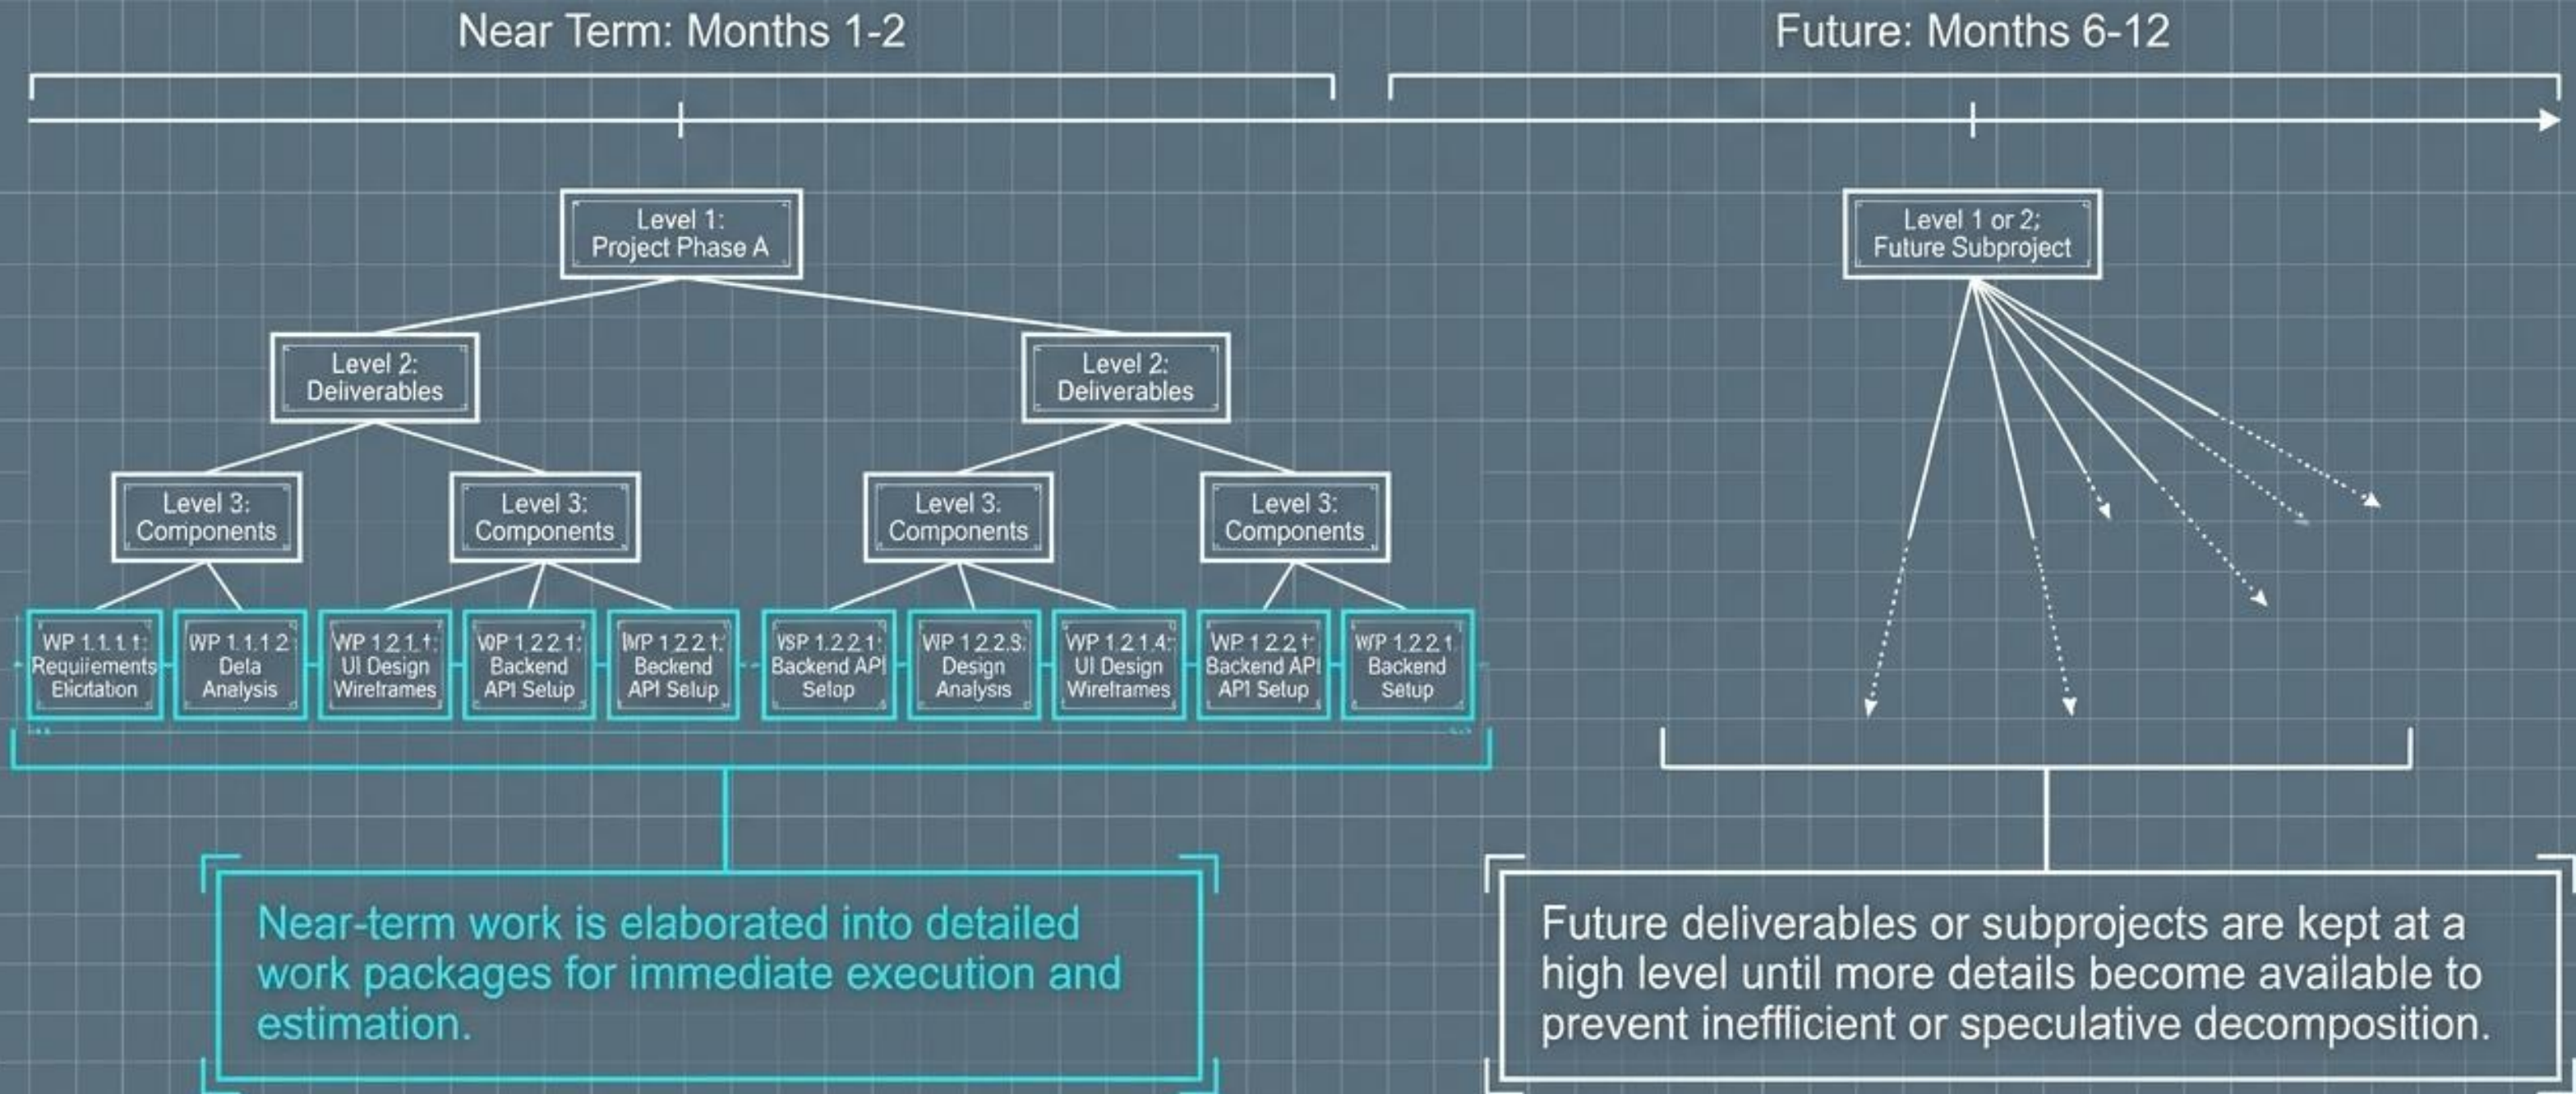



# The Code of Accounts: Unique Identifiers

Each element receives a unique identifier, typically a number.

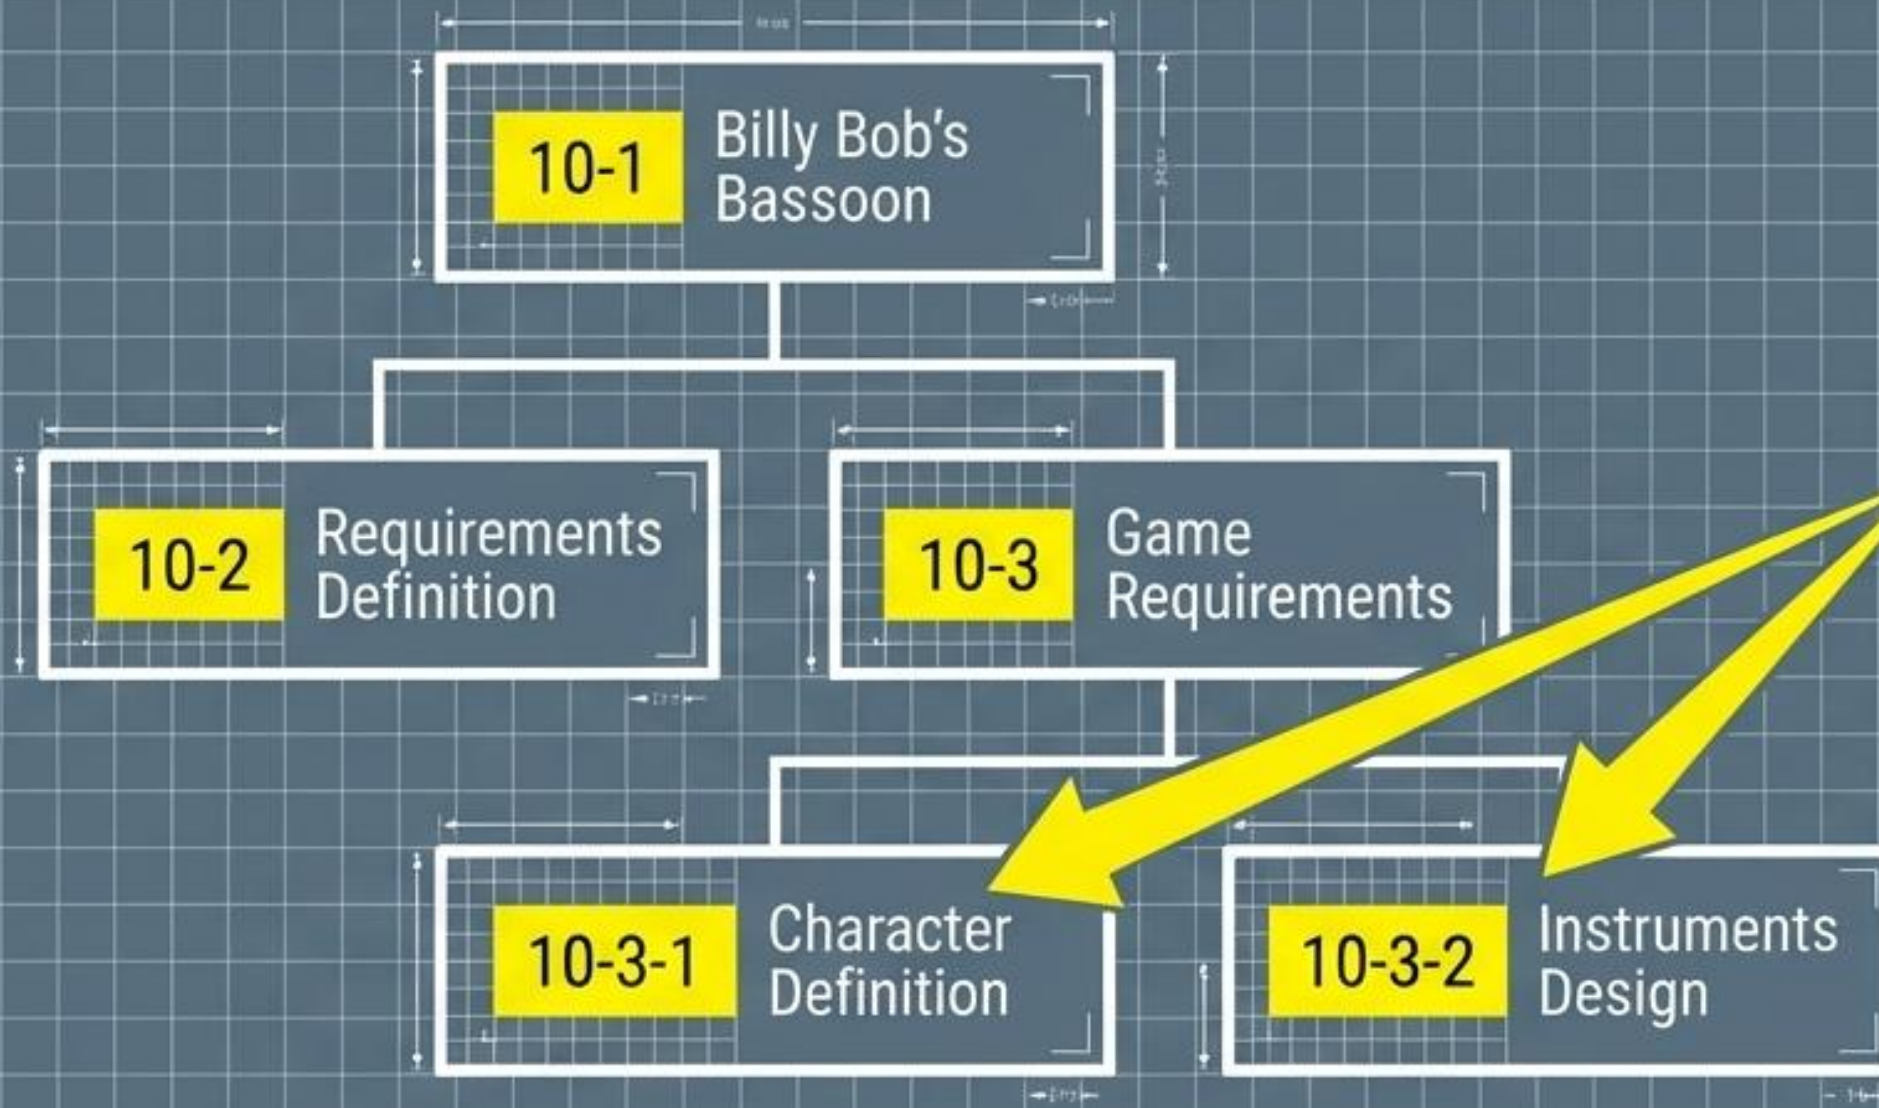

## Control Accounts

These identifiers sum and track costs, schedules, and resources. They map directly to the corporation's chart of accounts for categorical financial tracking.



# Behind the Node: The WBS Dictionary

The visual hierarchy.

WBS Node

## WBS Dictionary

- Code of accounts identifier
- Description of work
- Responsible organization
- Schedule milestones & activities
- Cost & resource estimates
- Acceptance criteria & quality requirements
- Contract information




# The Dictionary in Action: Lincoln Street Case Study



|                                                                                                                                       |                                                                                                   |
|---------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------|
| <b>WBS Code</b><br>3.1                                                                                                                | <b>Title: Inspection and Identification</b><br>(Asbestos Abatement)                               |
| <b>Description</b><br>Inspect historic building for asbestos and identify all areas where it is found. Update removal plan (WBS 2.2). | <b>Responsibility</b><br>Adrian (Facilities) to hire and oversee external contractor.             |
| <b>Milestones</b><br>Start after contractor hired (by <b>July 1</b> ). Complete no later than <b>Sept 15</b> .                        | <b>Contract Info</b><br>Two qualified contractors identified. Contracting closes <b>June 12</b> . |



# Synthesis Output: The Scope Baseline

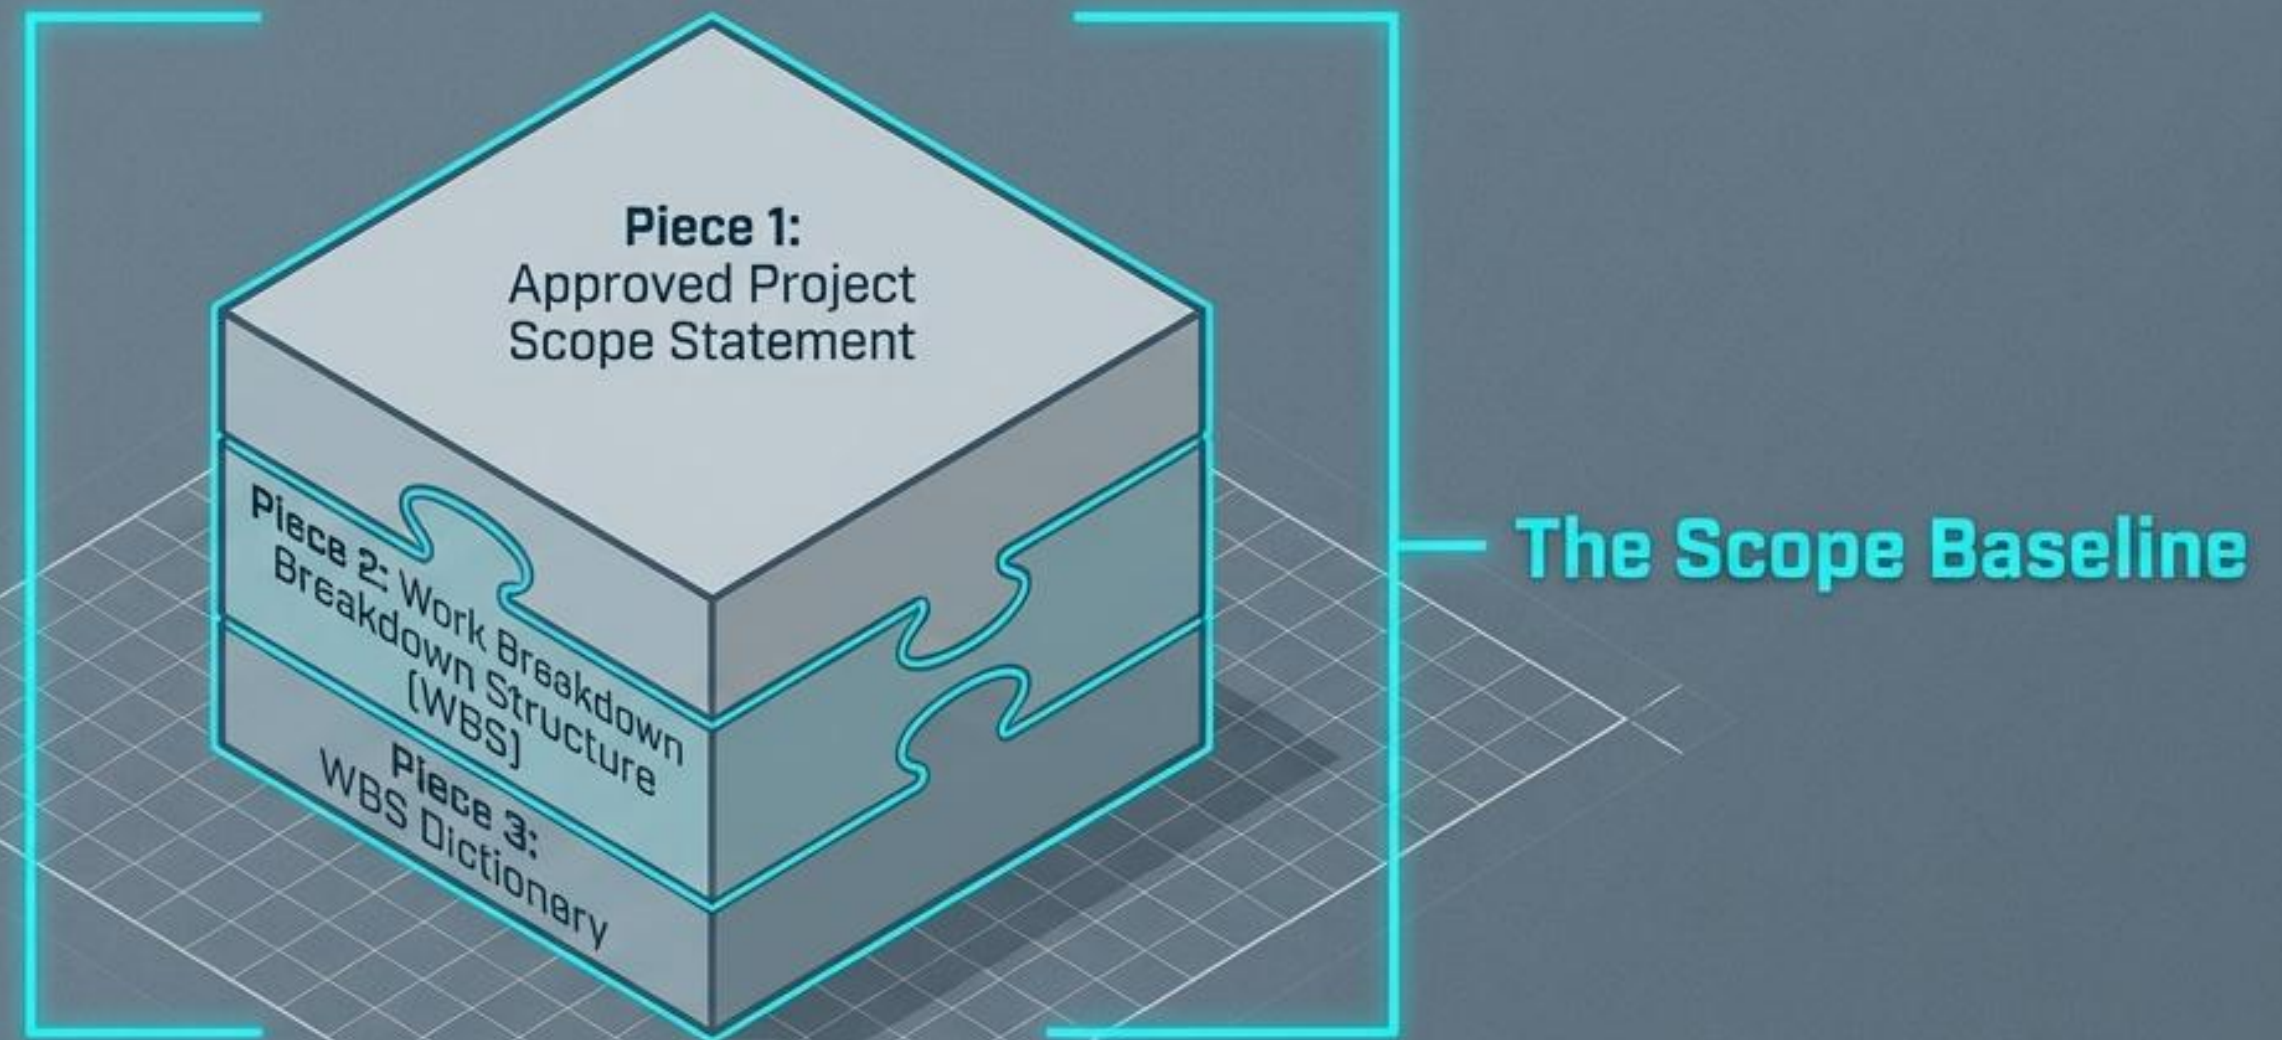


## Key Takeaway Banner

Together, these three documents form the **Scope Baseline**.

This is the **fixed, approved version** of the project's detailed work. From this unmoving foundation, the project manager will develop schedules, assign resources, and govern future changes to control scope creep.



# The Planning Domino Effect

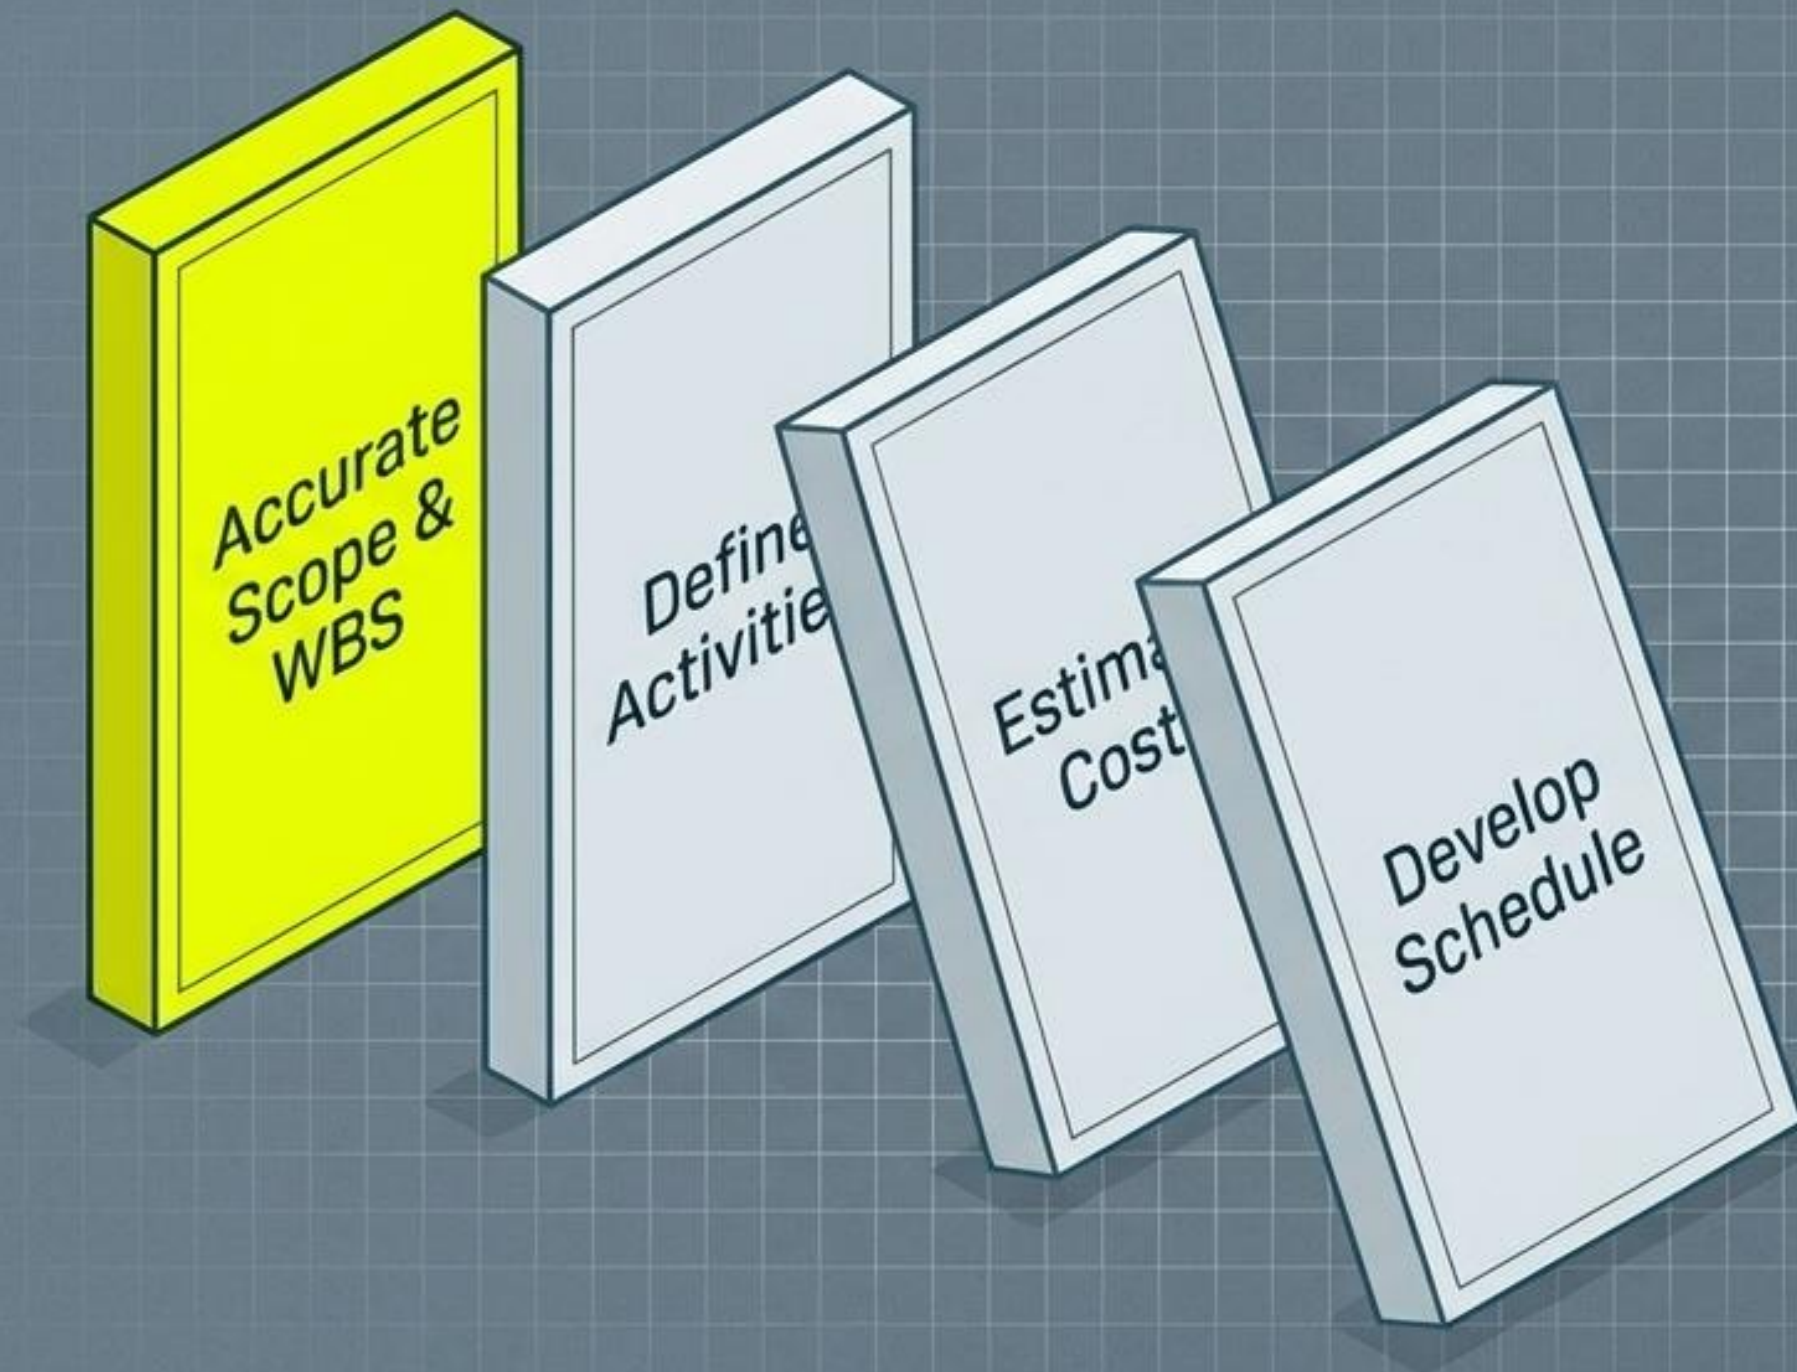

The WBS is essential for all remaining planning processes.

**A poorly constructed WBS leads to:**

Missing work requirements.

Inaccurate budget estimates.

Forced rework (late nights and weekends).

Premature project demise.



# PMP Exam Mastery Checklist



WBS contains only deliverables (nouns), never activities (verbs).



All levels roll up strictly adhering to the 100-Percent Rule.



The lowest level is always the Work Package, where time and cost are estimated.



Rolling Wave Planning elaborates near-term work in detail while keeping future work at macro levels.



The final output is the Scope Baseline = Scope Statement + WBS + WBS Dictionary.
